

ID		Task Mode	Task Name	Duration	Start	Finish	30, '26	Sep 6, '26	Sep 13, '26	Sep
							M T W T F S	S M T W T F S	S M T W T F S	S
1			Notice to Proceed	0 days	Tue 9/1/26	Tue 9/1/26				
2			Mobilization & Temporary Facilities	20 days	Tue 9/1/26	Wed 9/23/26				
3			Survey / Setting Out	15 days	Mon 9/7/26	Wed 9/23/26				
4			Review IFC Drawings / Interfaces	30 days	Tue 9/1/26	Mon 10/5/26				
5			Method Statements & Material	45 days	Sat 9/12/26	Tue 11/3/26				
6			Long-Lead M&E Procurement	300 days	Wed 11/4/26	Tue 10/19/27				
7			SCADA / Instrumentation Procurement	260 days	Wed 11/4/26	Thu 9/2/27				
8			Electrical / Receiving Equipment Procurement	240 days	Wed 11/4/26	Tue 8/10/27				
9			Site Clearing / Excavation / Dewatering	35 days	Thu 9/24/26	Tue 11/3/26				
10			Ground Preparation / Blinding	15 days	Wed 11/4/26	Fri 11/20/26				
11			WTP Foundations / Base Slabs	60 days	Sat 11/21/26	Fri 1/29/27				
12			Mixing / Flocculation Basin RC Works	70 days	Sat 1/30/27	Wed 4/21/27				

Project: Michael_FutoI_Chinaim

Date: Sun 8/30/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline

Progress

Manual Progress

ID		Task Mode	Task Name	Duration	Start	Finish	30, '26 M T W T F S							Sep 6, '26 S M T W T F S							Sep 13, '26 S M T W T F S							Sep S
13			Sedimentation Basin RC Works	100 days	Tue 2/23/27	Fri 6/18/27																						
14			Rapid Sand Filter Structure	80 days	Sat 6/19/27	Mon 9/20/27																						
15			Internal Channels / Pipe Galleries	45 days	Tue 9/21/27	Thu 11/11/27																						
16			Waterproofing / Prot	30 days	Fri 11/12/27	Thu 12/16/27																						
17			Hydrostatic / Structur	14 days	Fri 12/17/27	Sat 1/1/28																						
18			10,000 m³ Reservoir	140 days	Thu 9/24/26	Mon 11/9/26																						
19			Reservoir Foundation	60 days	Tue 11/10/26	Mon 1/18/27																						
20			Reservoir Walls / Col	100 days	Tue 1/19/27	Fri 5/14/27																						
21			Reservoir Roof Slab	60 days	Sat 5/15/27	Fri 7/23/27																						
22			Reservoir Waterproof	30 days	Sat 7/24/27	Fri 8/27/27																						
23			Reservoir Hydrostatic	14 days	Sat 8/28/27	Mon 9/13/27																						
24			Pump Room Civil / Sti	75 days	Tue 12/15/26	Thu 3/11/27																						
25			Chemical Building Civ	90 days	Sat 12/26/26	Fri 4/9/27																						
26			Administration & Lab	120 days	Wed 11/4/26	Tue 3/23/27																						
27			Building MEP / Archit	70 days	Wed 3/24/27	Sat 6/12/27																						
28			Process Piping Install	100 days	Mon 1/3/28	Thu 4/27/28																						
29			Pumps & Mechanical	90 days	Wed 10/20/27	Tue 2/1/28																						
30			Chemical Dosing Equi	70 days	Wed 10/20/27	Sat 1/8/28																						
31			Filter Media / Underd	50 days	Mon 1/3/28	Tue 2/29/28																						
32			Electrical Installation	100 days	Wed 8/11/27	Sat 12/4/27																						
33			Instrumentation & SC	90 days	Fri 4/28/28	Thu 8/10/28																						

Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	30, '26 M T W T F S							Sep 6, '26 S M T W T F S							Sep 13, '26 S M T W T F S							Sep S
34			Salakham Site Prepar	40 days	Thu 9/24/26	Mon 11/9/26																						
35			7,100 m³ Reservoir R	180 days	Tue 11/10/26	Mon 6/7/27																						
36			Salakham Pump Roor	90 days	Thu 10/29/26	Wed 2/10/27																						
37			Salakham M&E Instal	80 days	Wed 10/20/27	Thu 1/20/28																						
38			22-kV Route Survey /	45 days	Thu 9/24/26	Sat 11/14/26																						
39			Pole / Foundation Wc	100 days	Mon 11/16/27	Thu 3/11/27																						
40			22-kV Line Installati	120 days	Fri 3/12/27	Thu 7/29/27																						
41			Receiving Equipment	30 days	Wed 8/11/27	Tue 9/14/27																						
42			Mechanical Pre-Comr	25 days	Fri 4/28/28	Fri 5/26/28																						
43			Electrical / I&C Pre-Cc	25 days	Fri 8/11/28	Fri 9/8/28																						
44			Dry Commissioning	20 days	Sat 9/9/28	Mon 10/2/28																						
45			Wet Commissioning /	30 days	Tue 10/3/28	Mon 11/6/28																						
46			Performance / Water	30 days	Tue 11/7/28	Mon 12/11/28																						
47			Punch List / Rectificat	30 days	Tue 12/12/28	Mon 1/15/29																						
48			Training / O&M Docu	20 days	Tue 10/3/28	Wed 10/25/28																						
49			Taking Over / Comple	0 days	Mon 1/15/29	Mon 1/15/29																						

Project: Michael_FutoI_Chinaim
Date: Sun 8/30/26

Task

Split


Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only
















External Tasks

External Milestone

Deadline

Progress

Manual Progress


















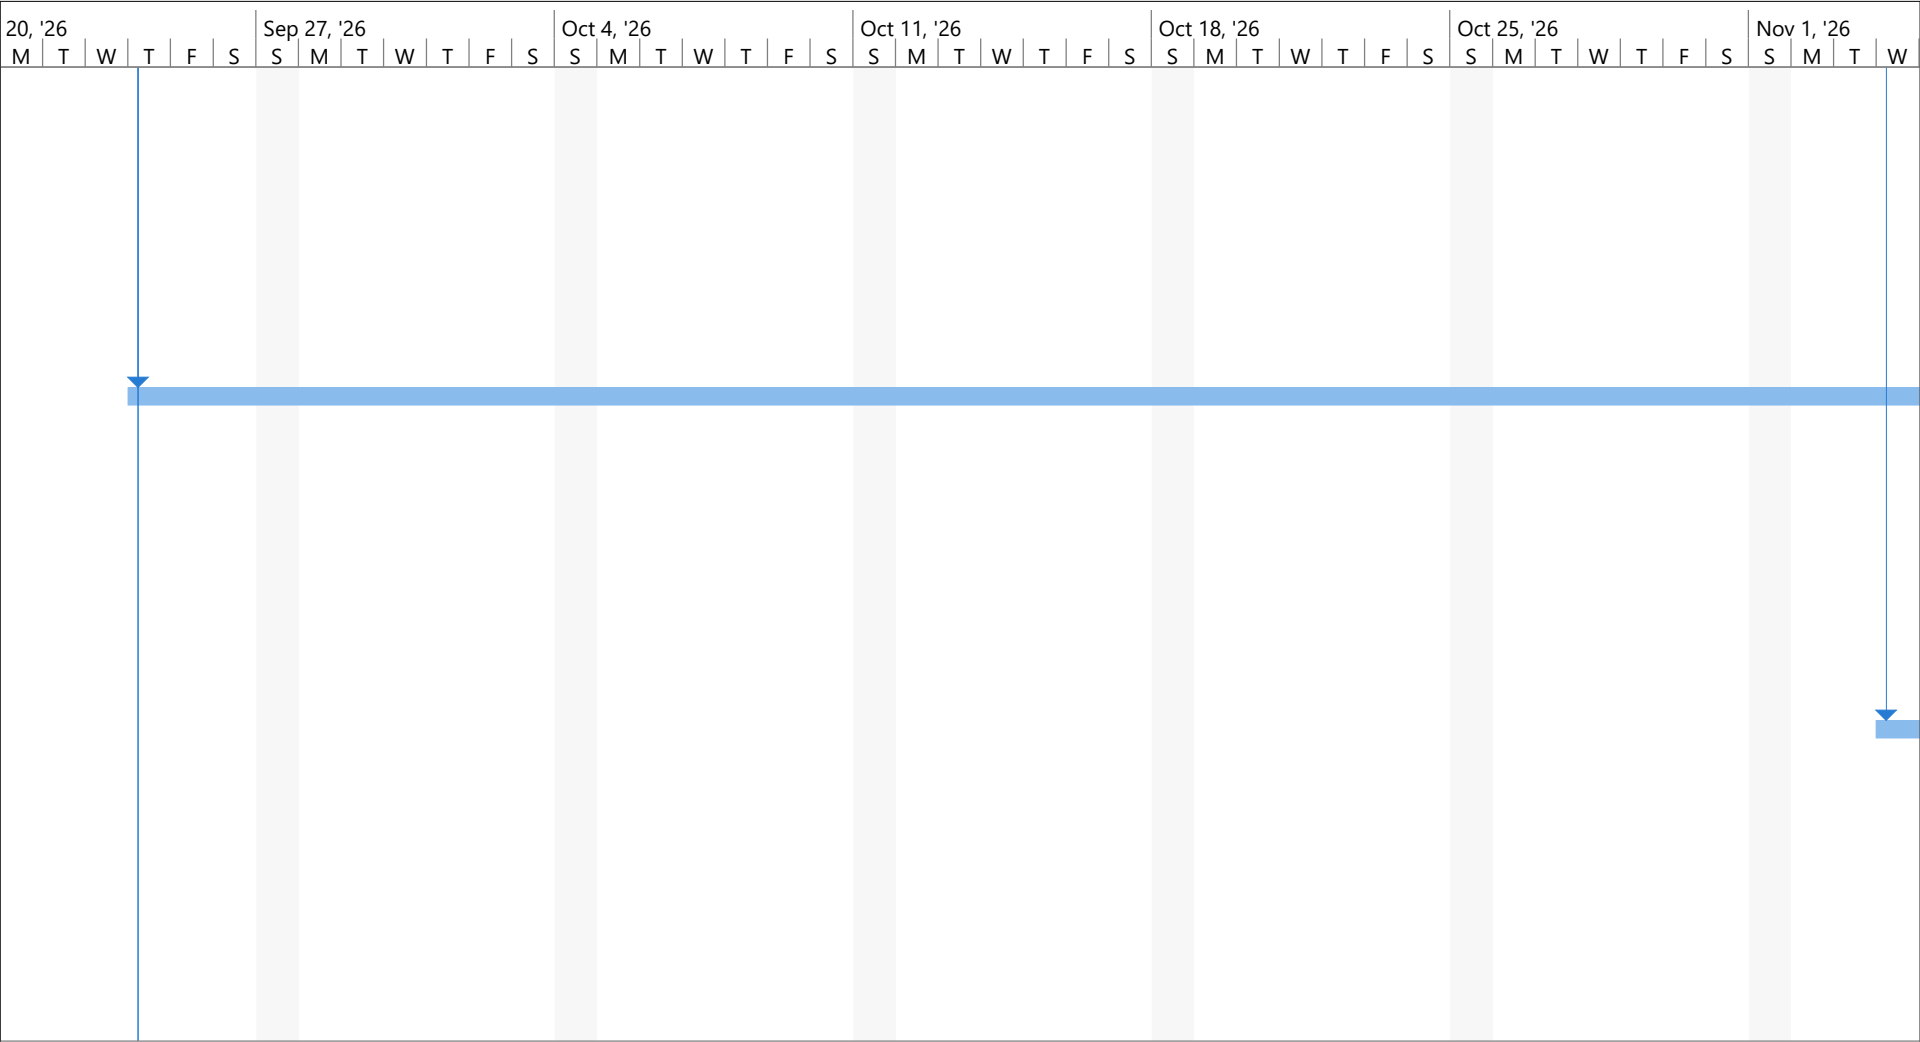


Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

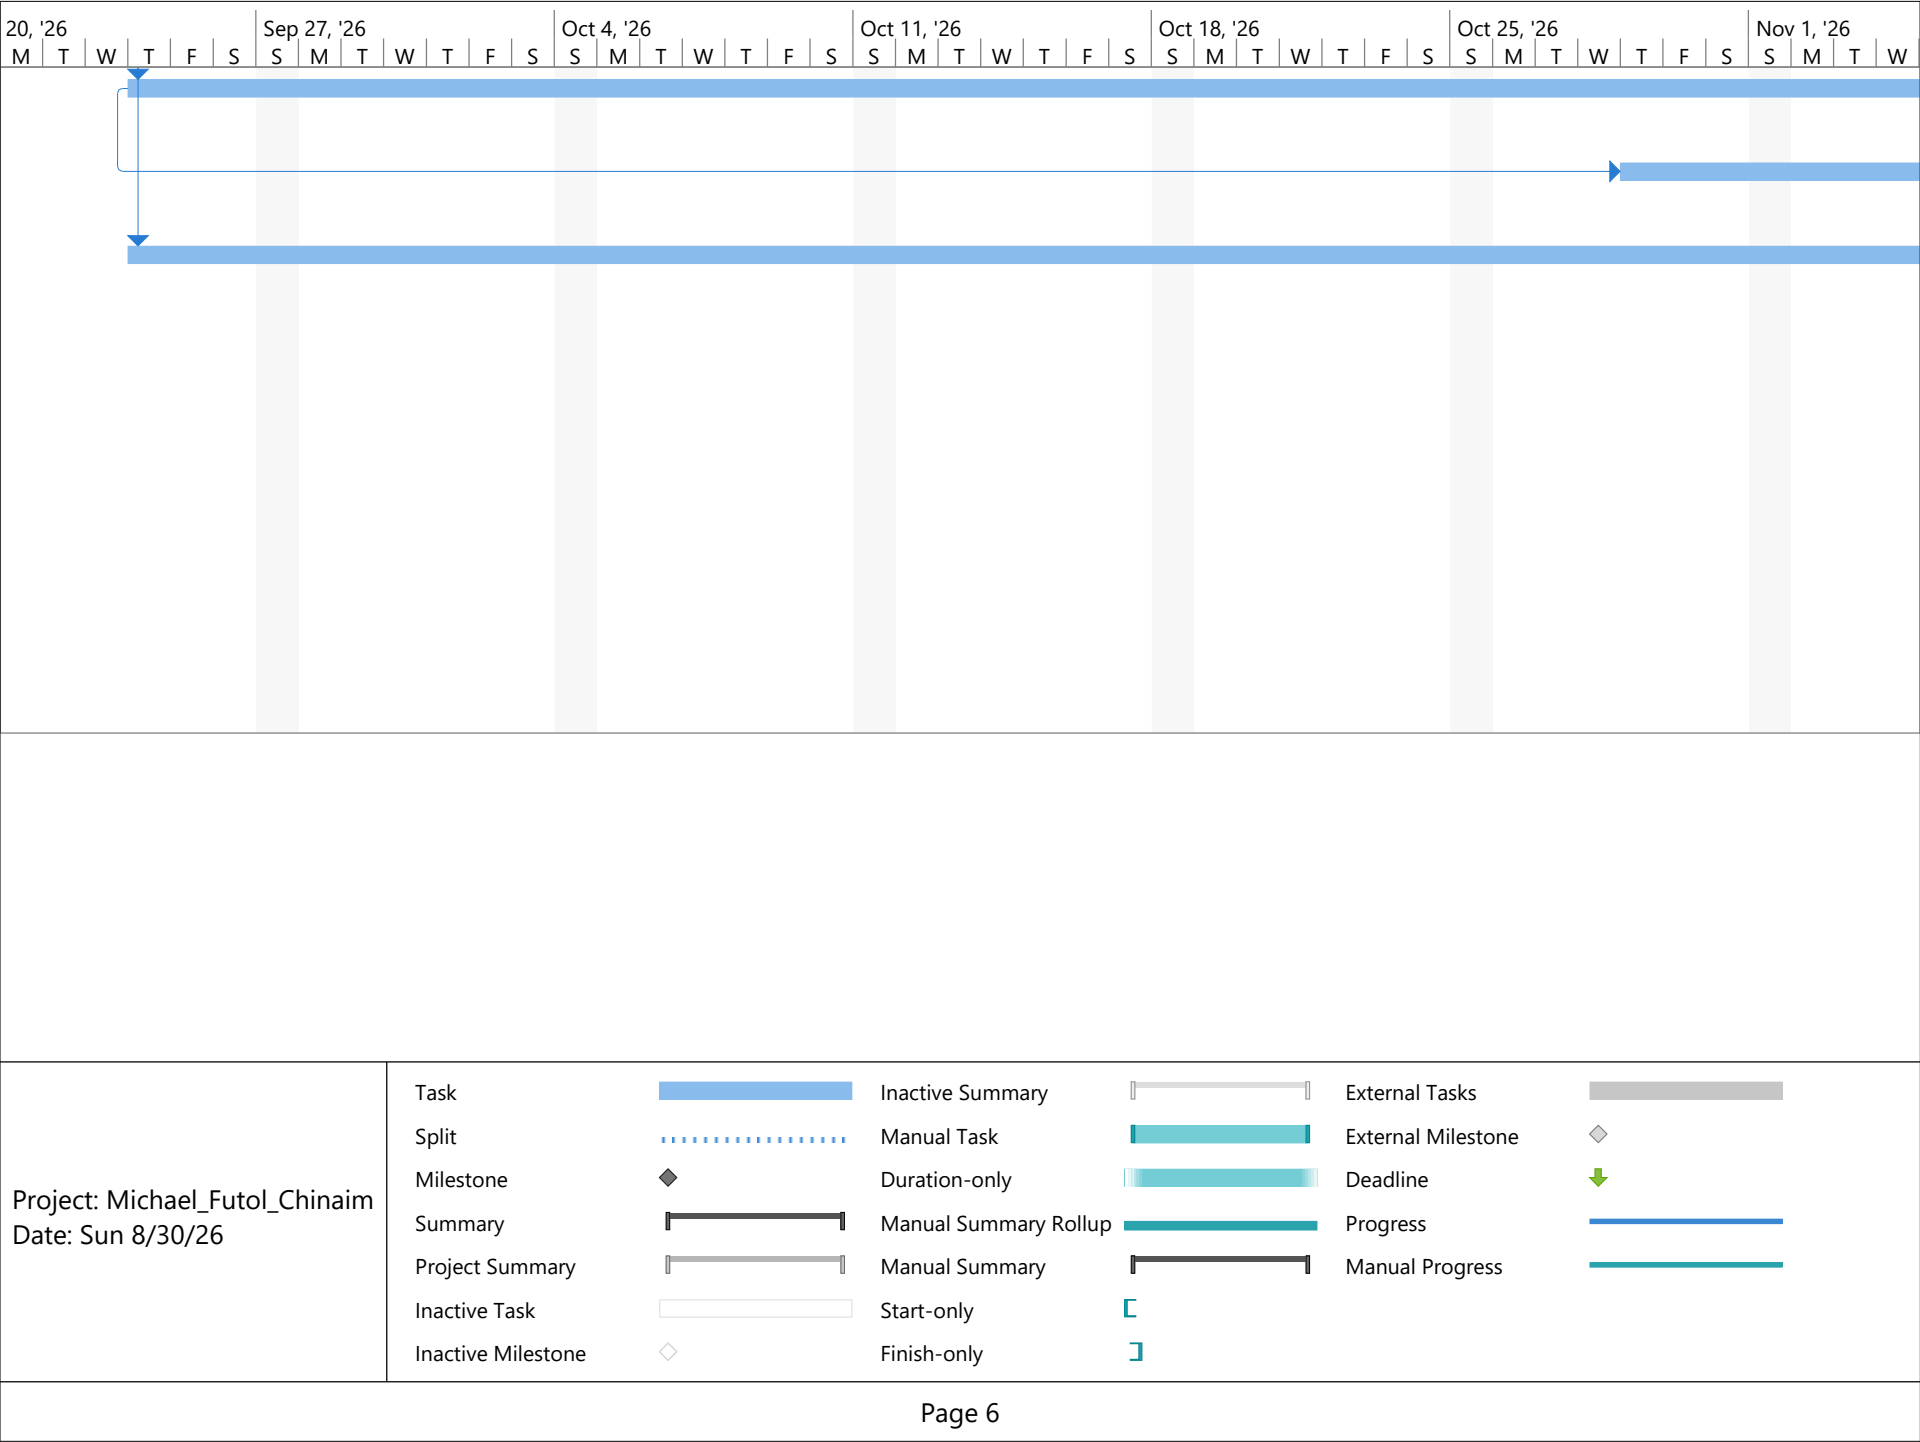


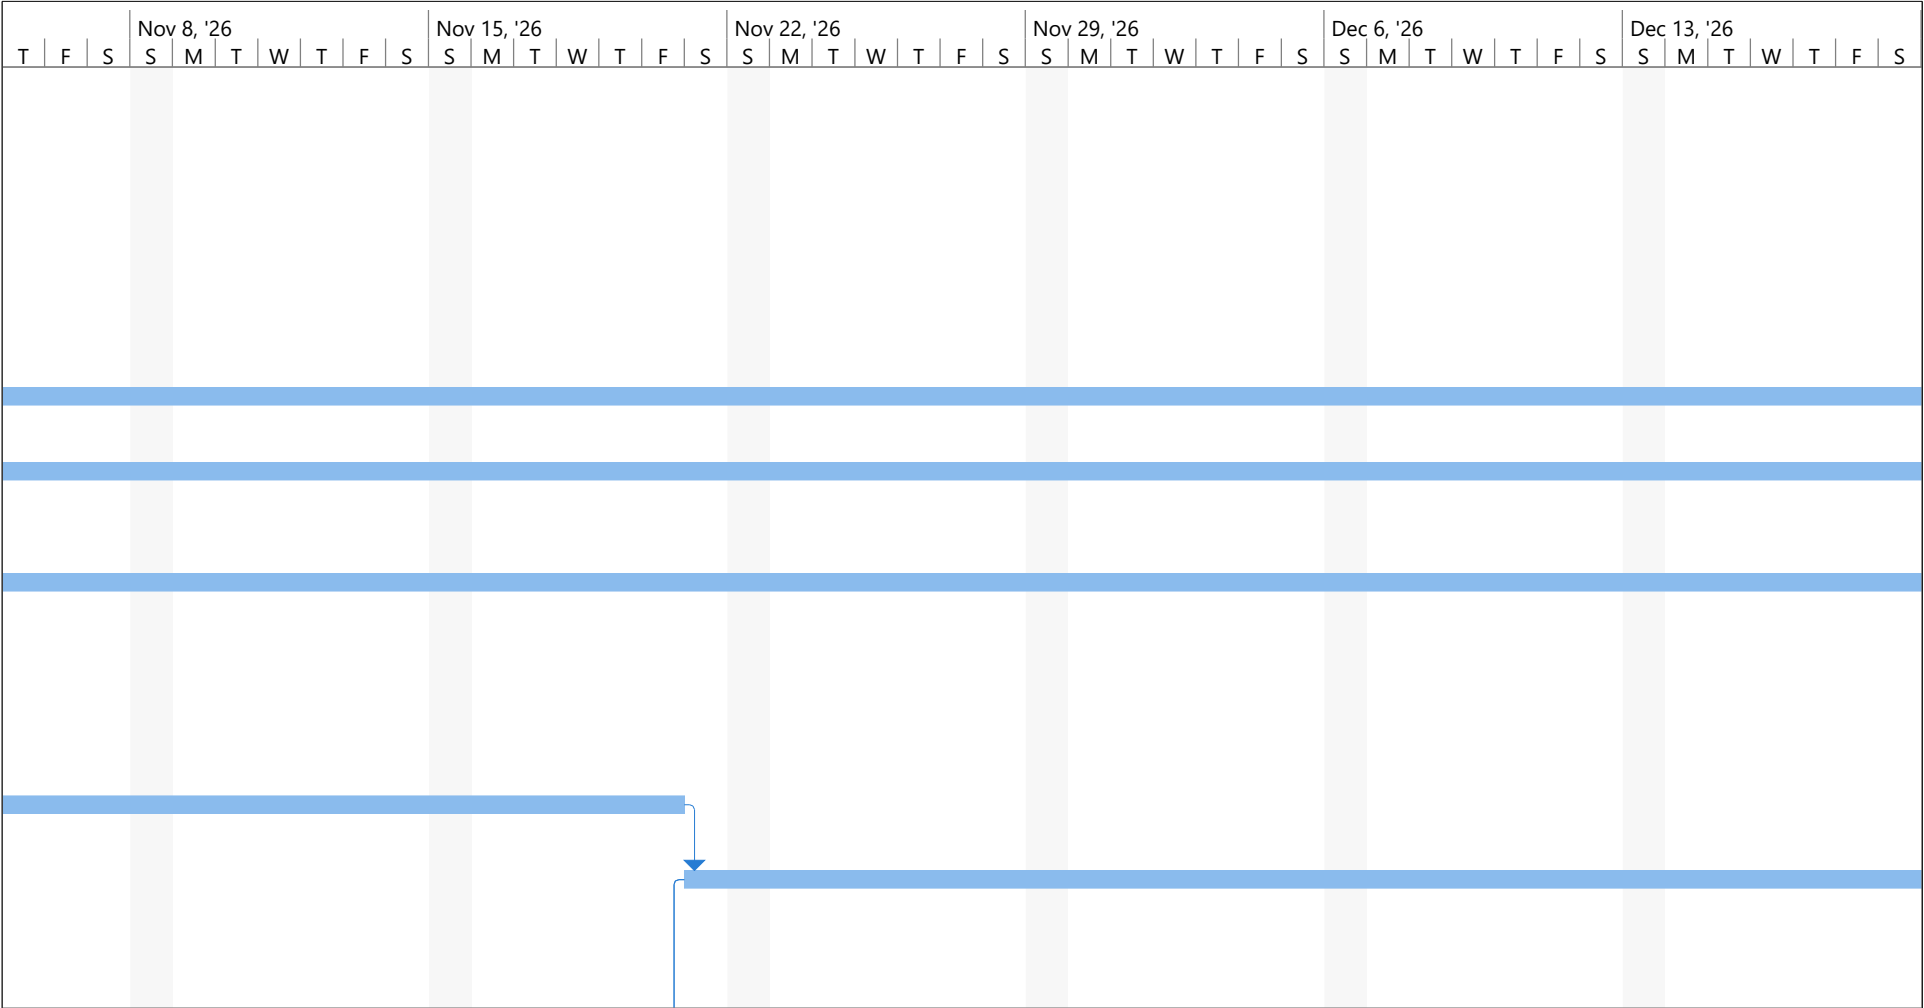

Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

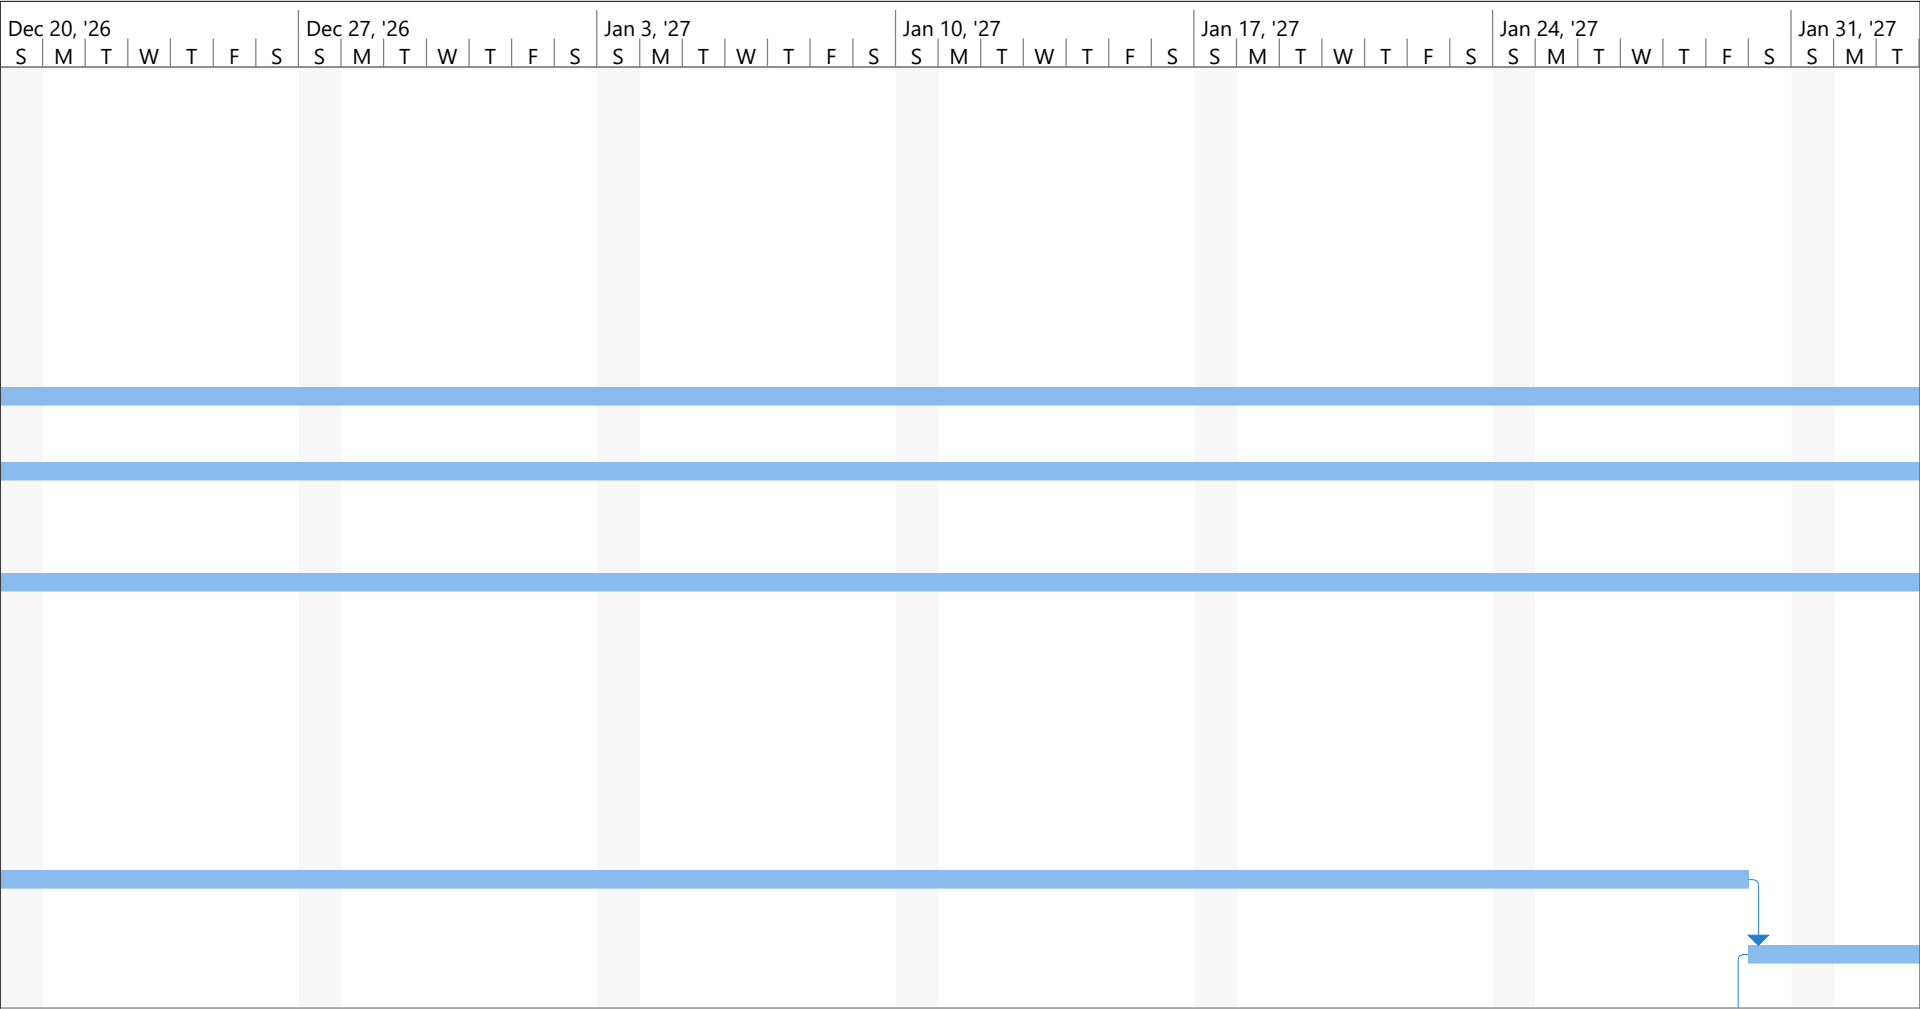


Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

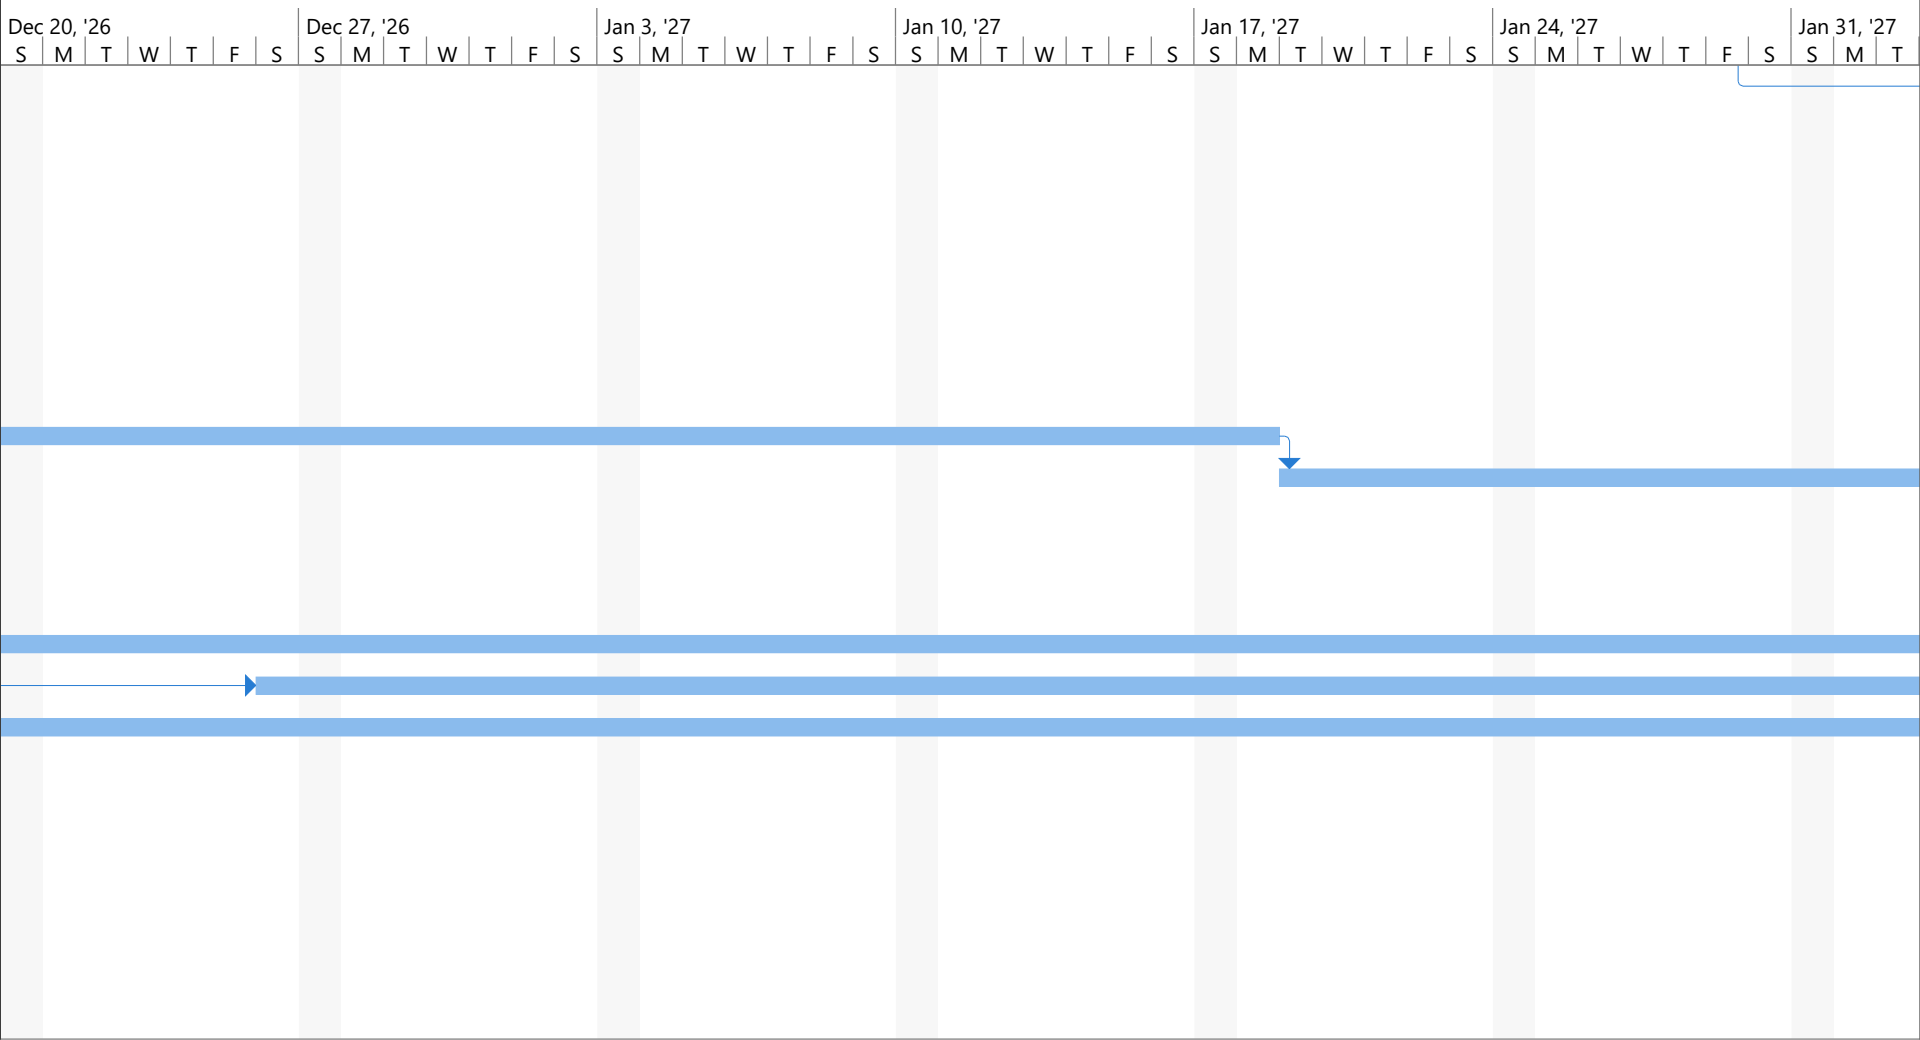




Project: Michael_FutoI_Chinaim


Date: Sun 8/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

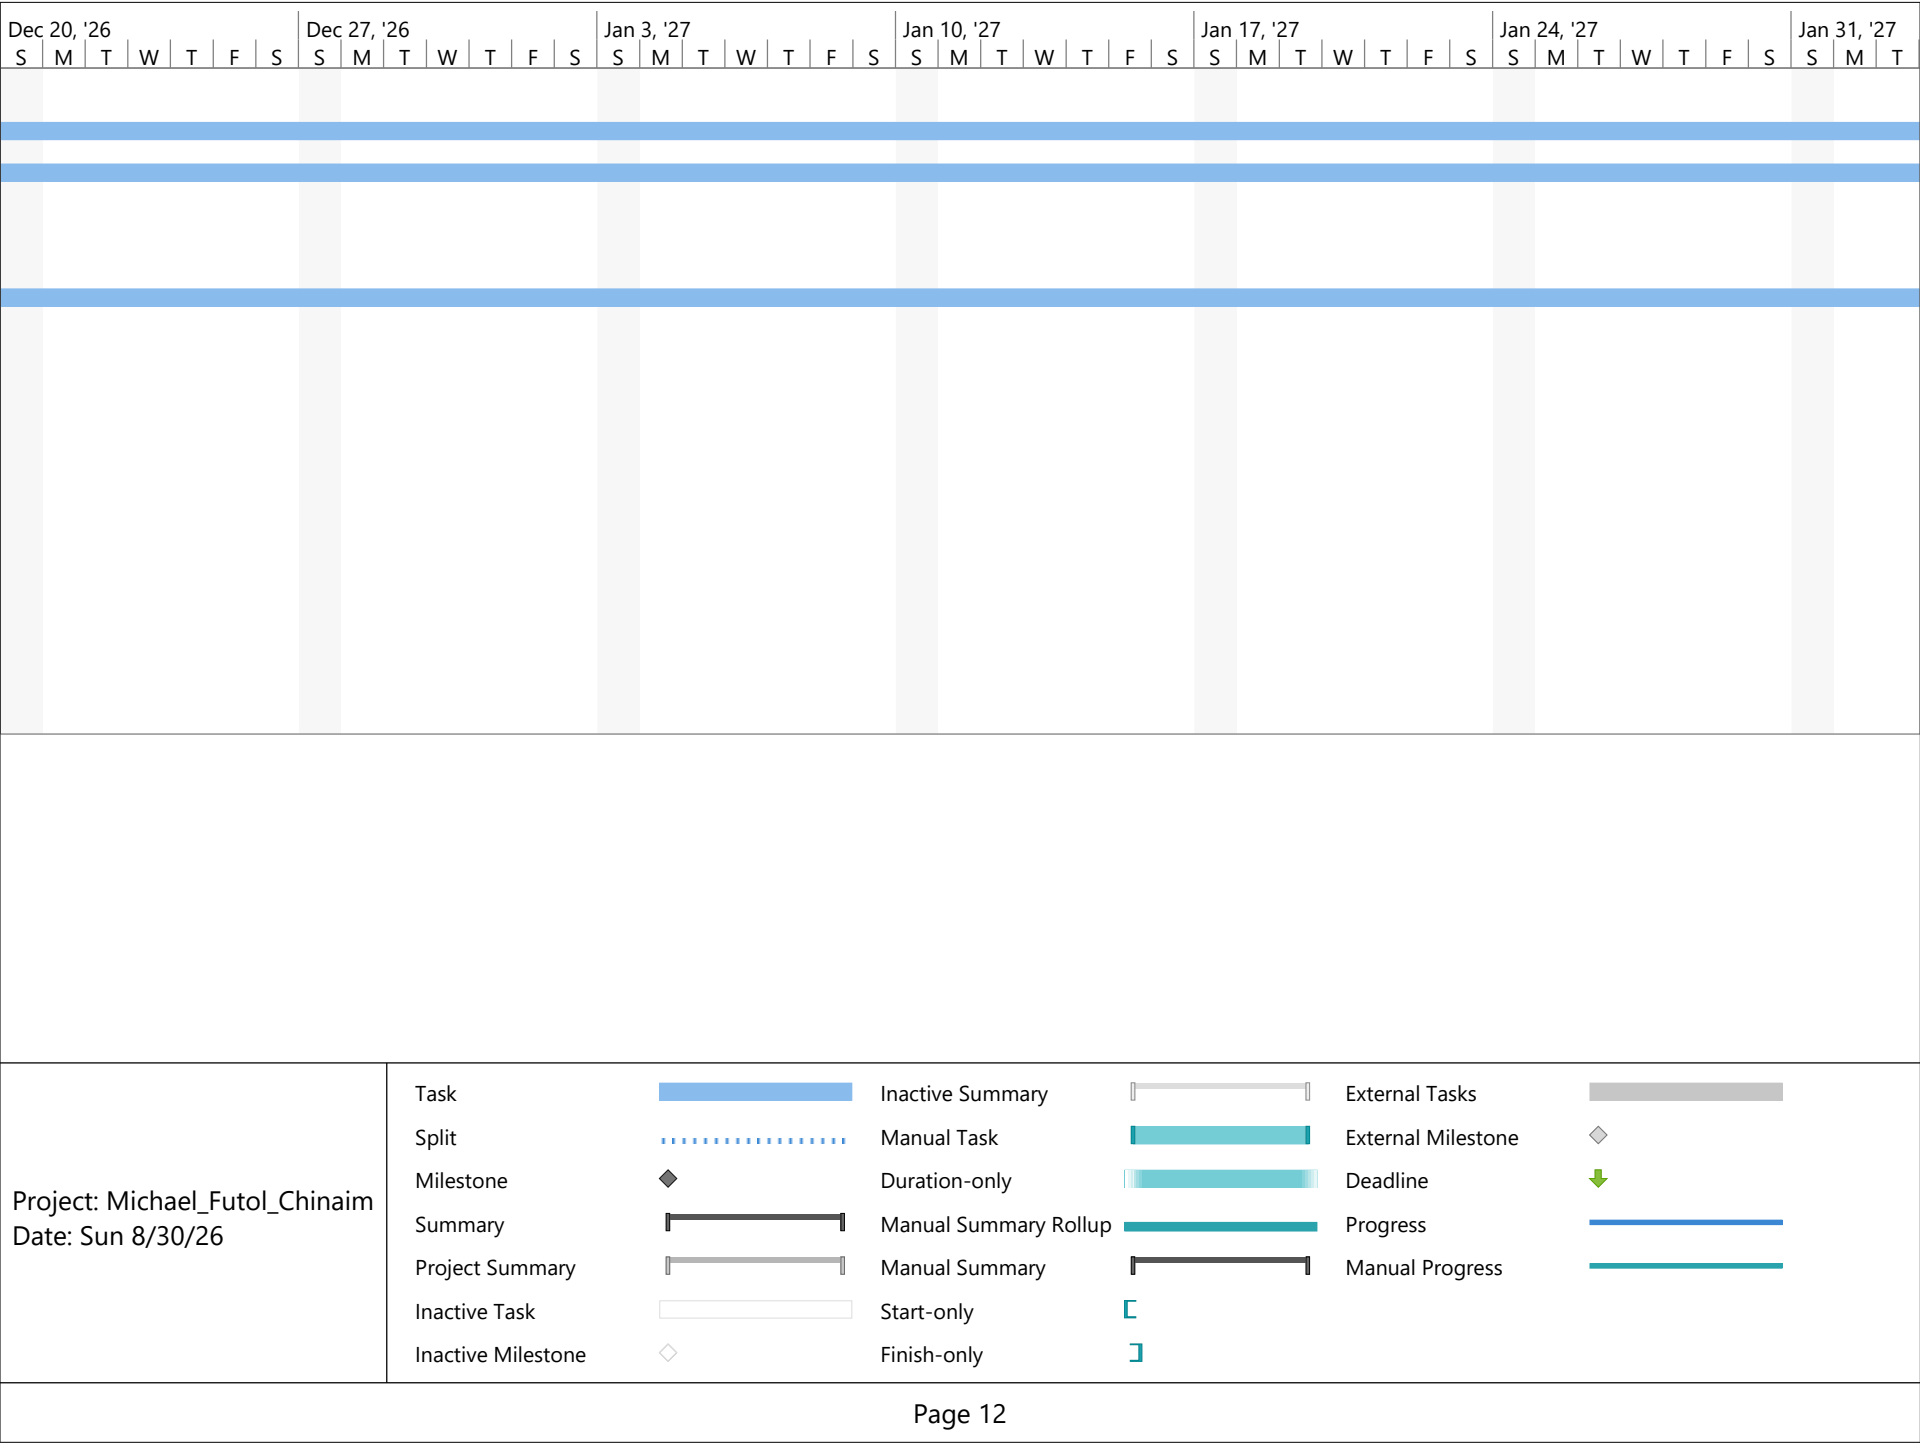



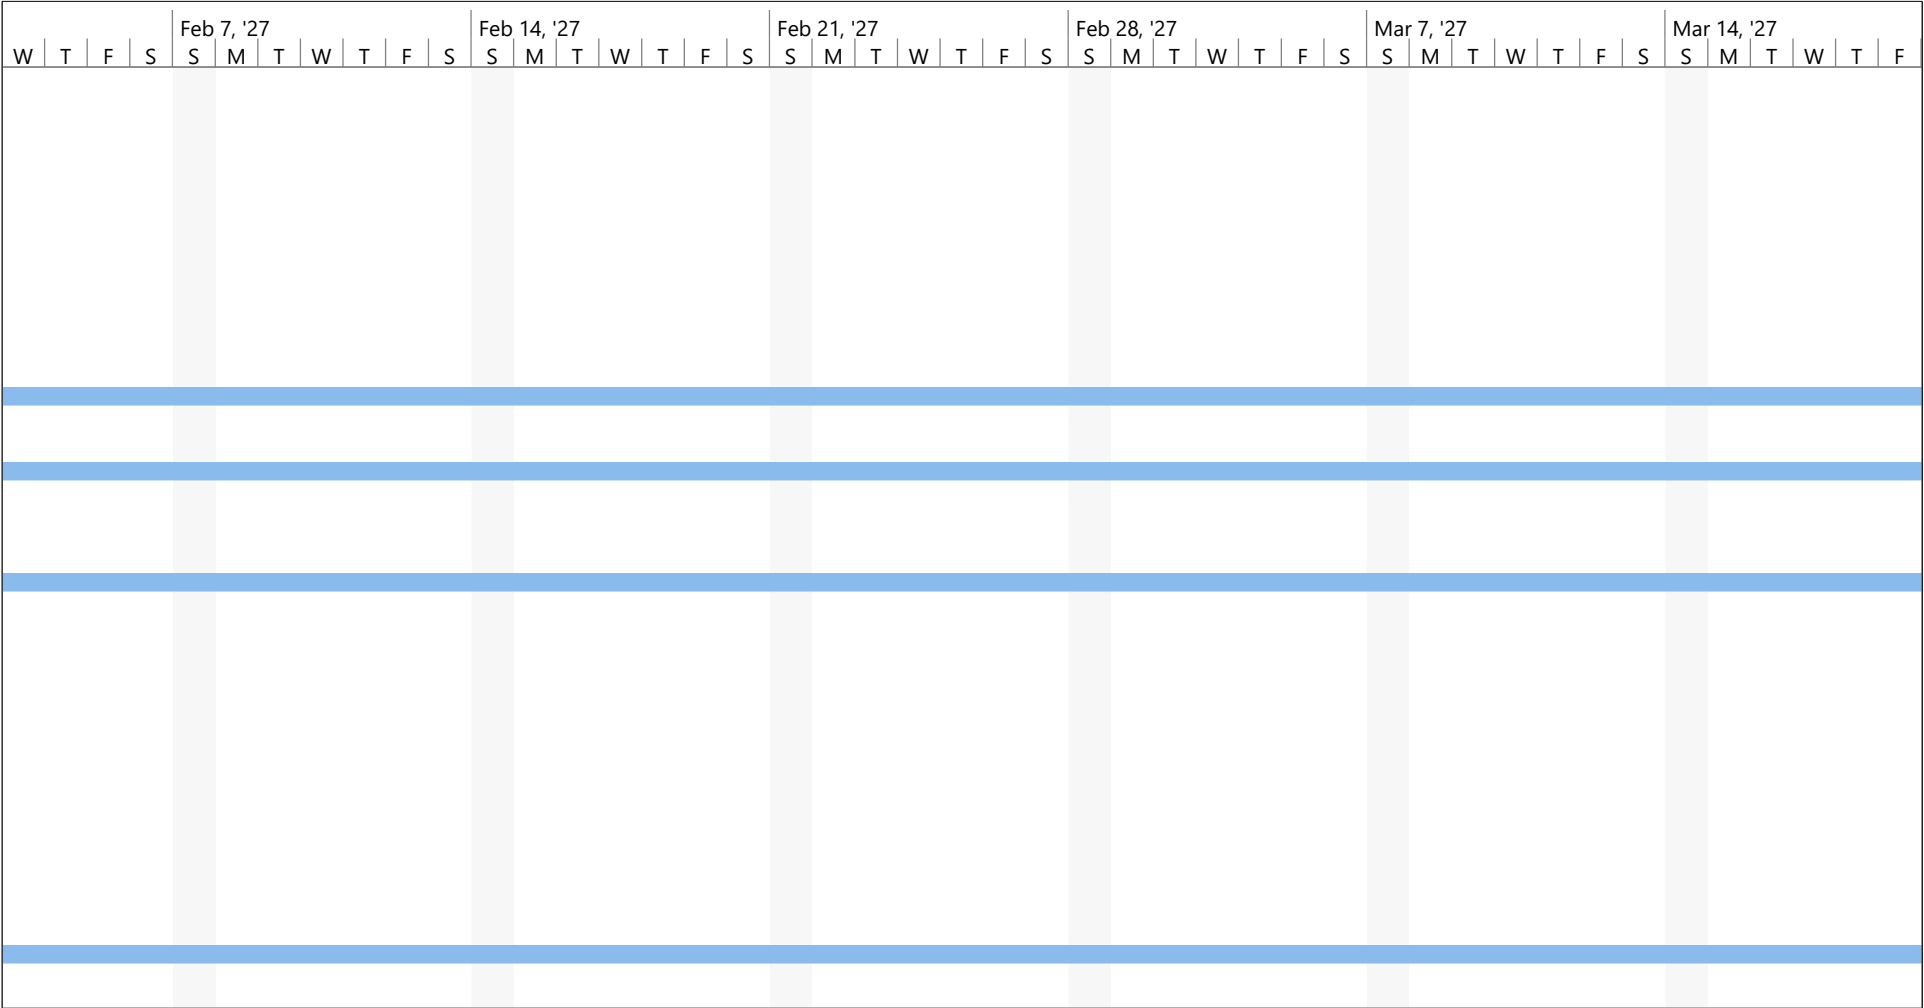



Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

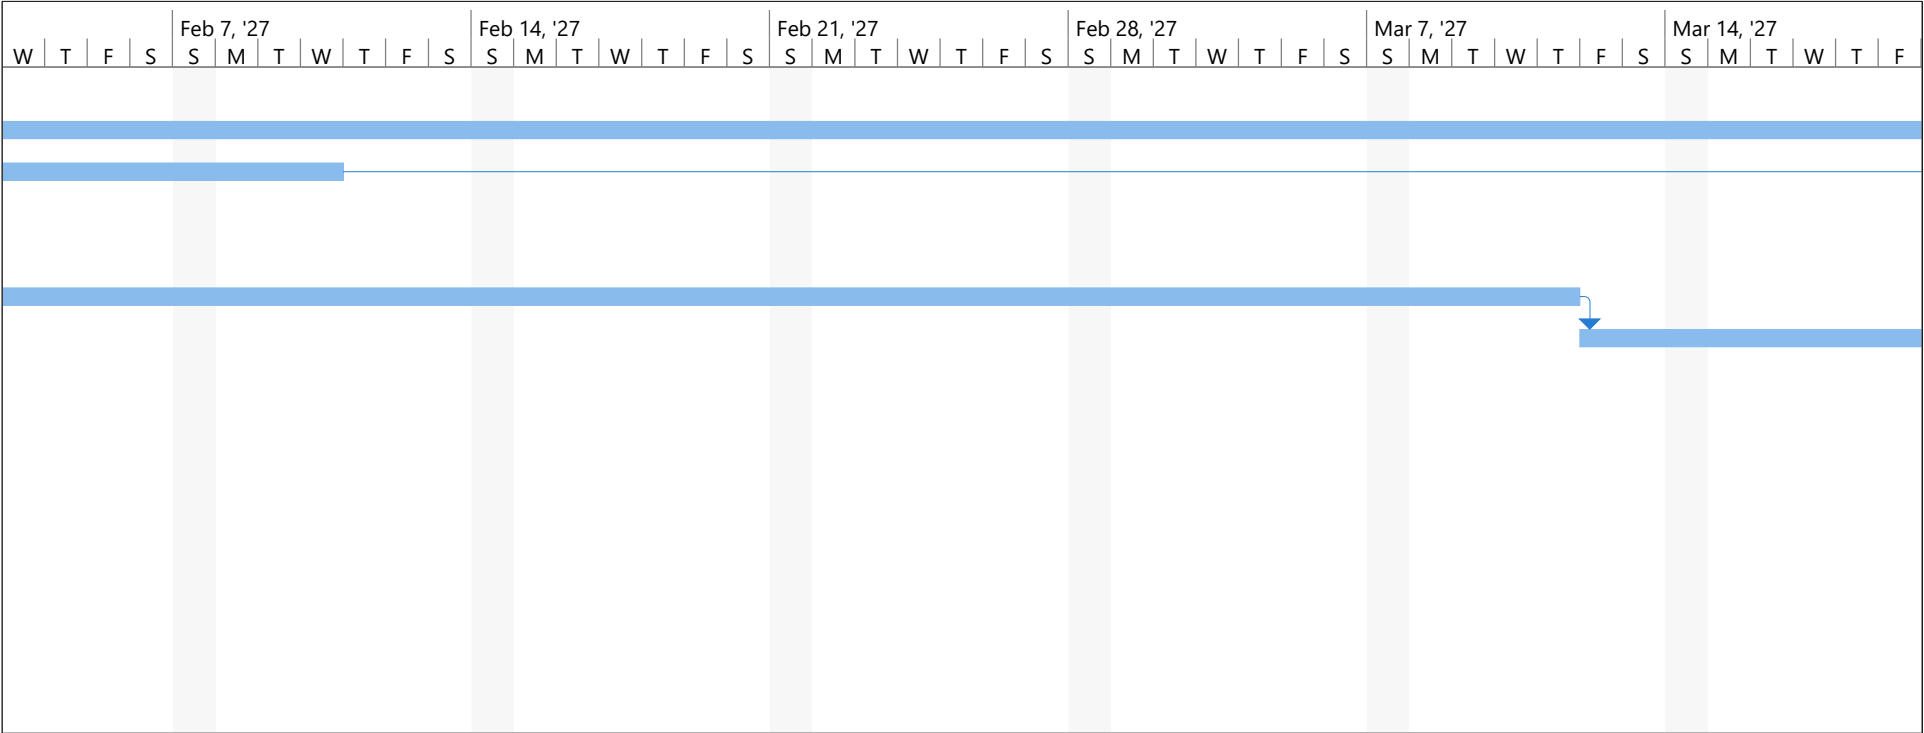



Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


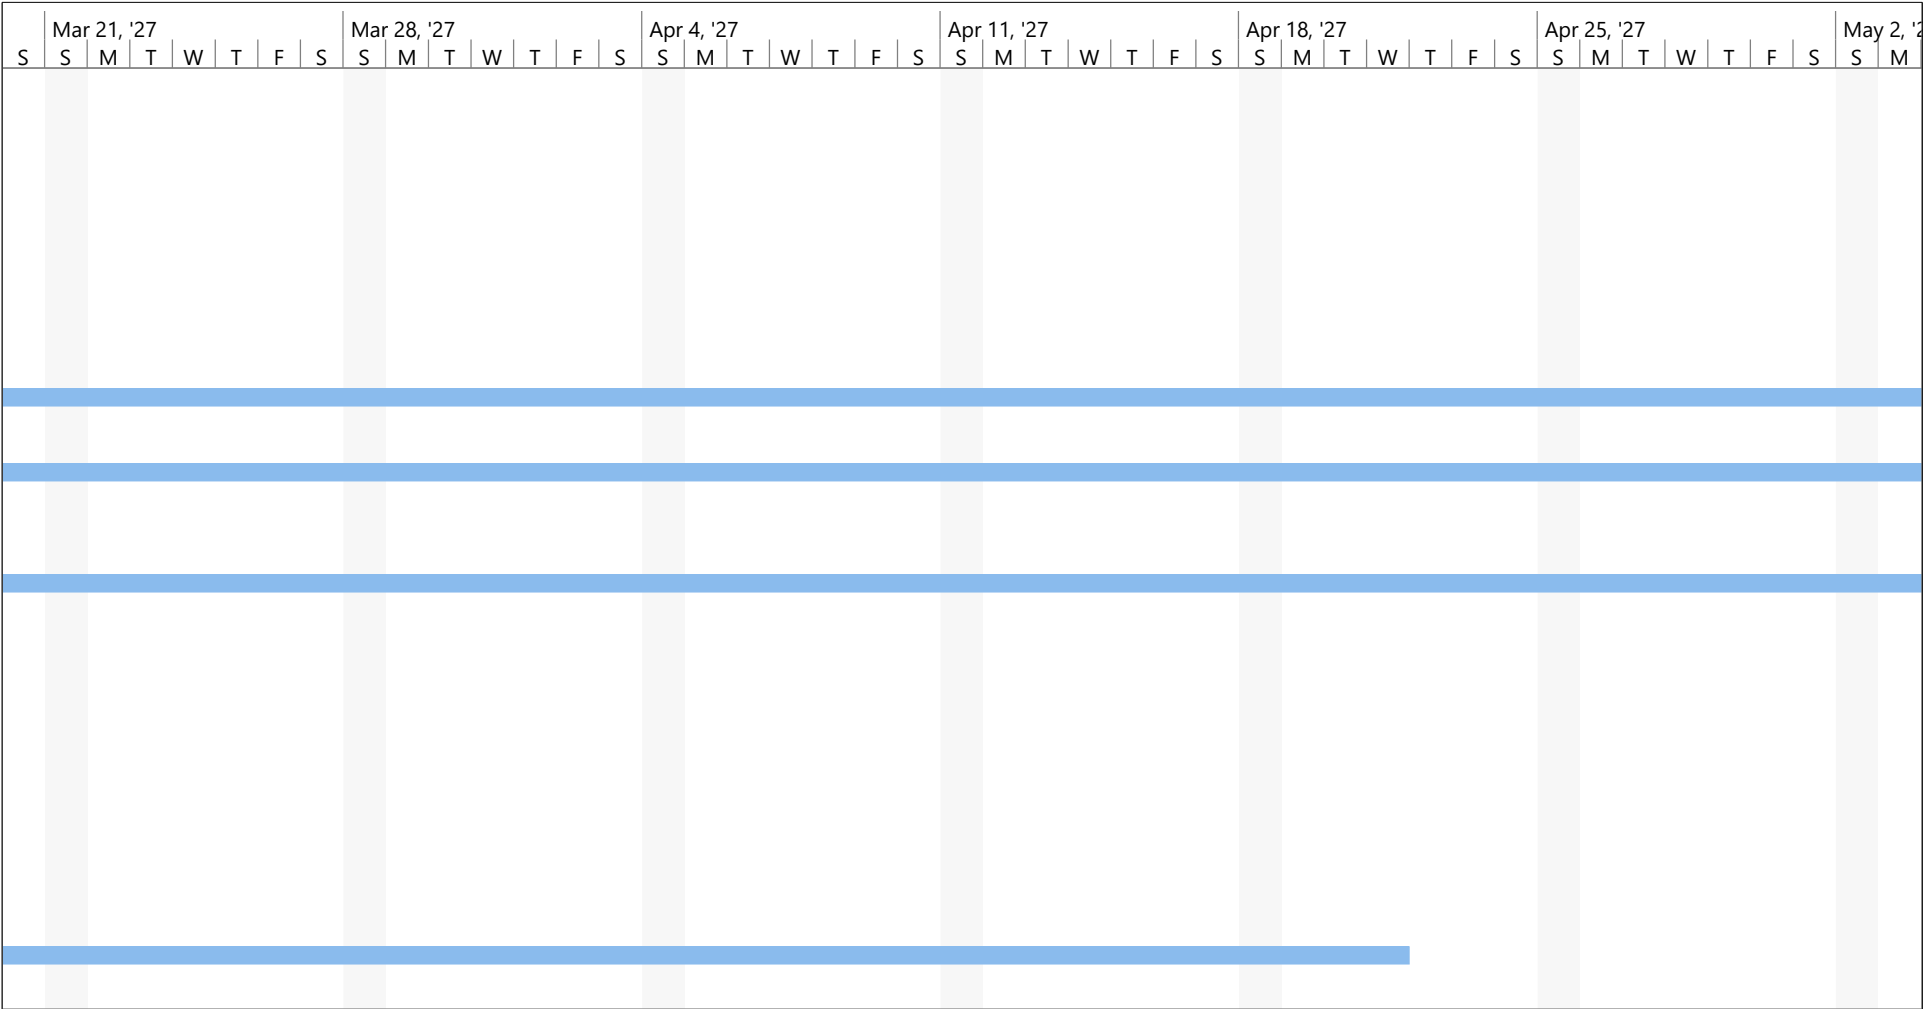



Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

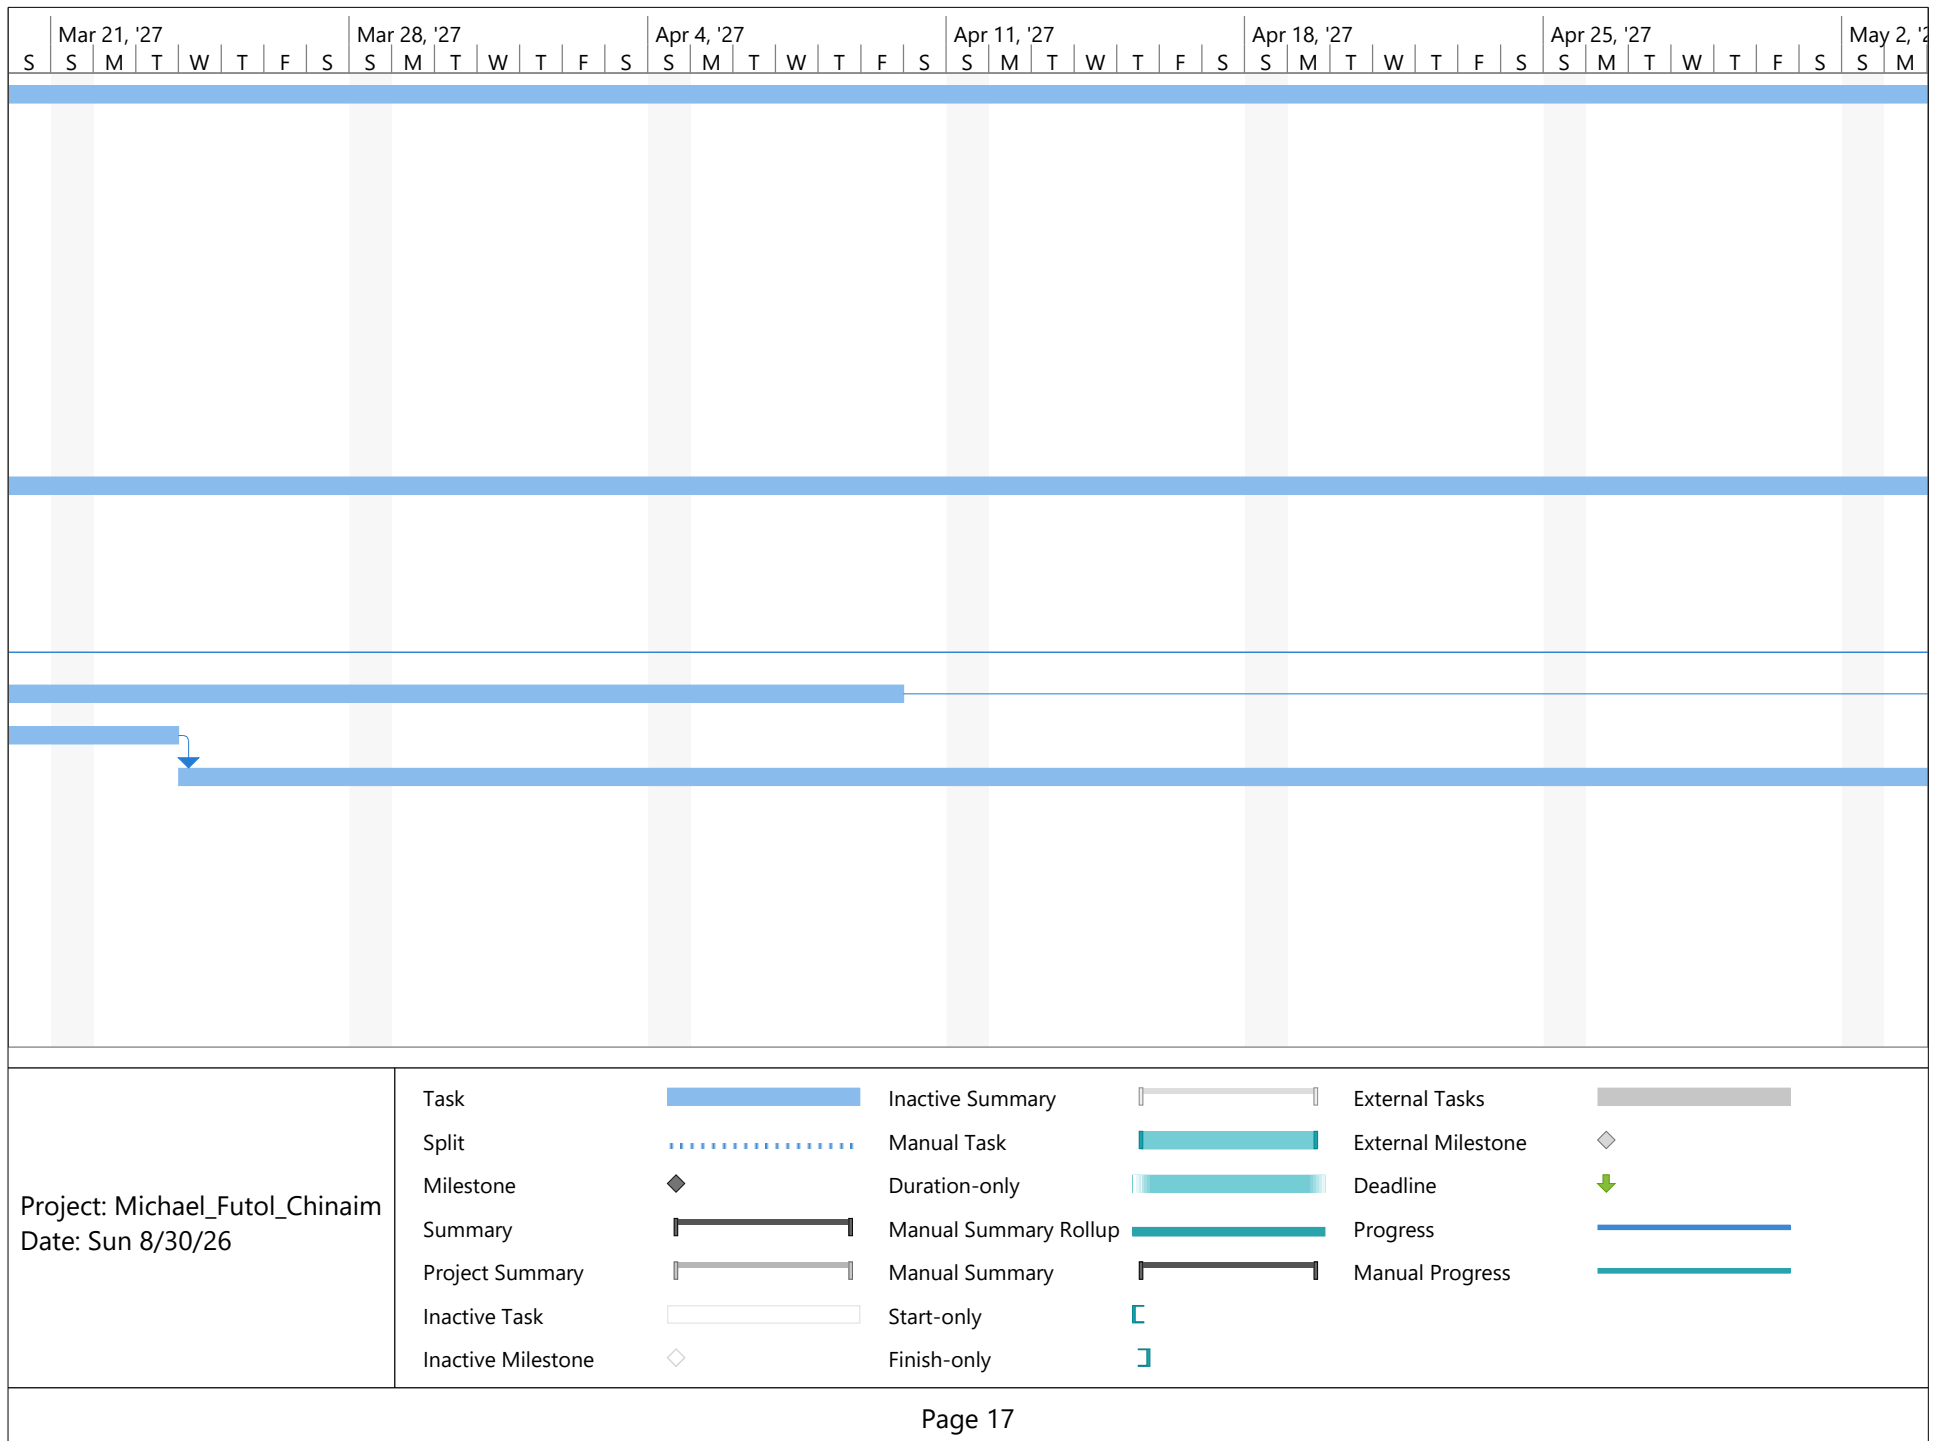

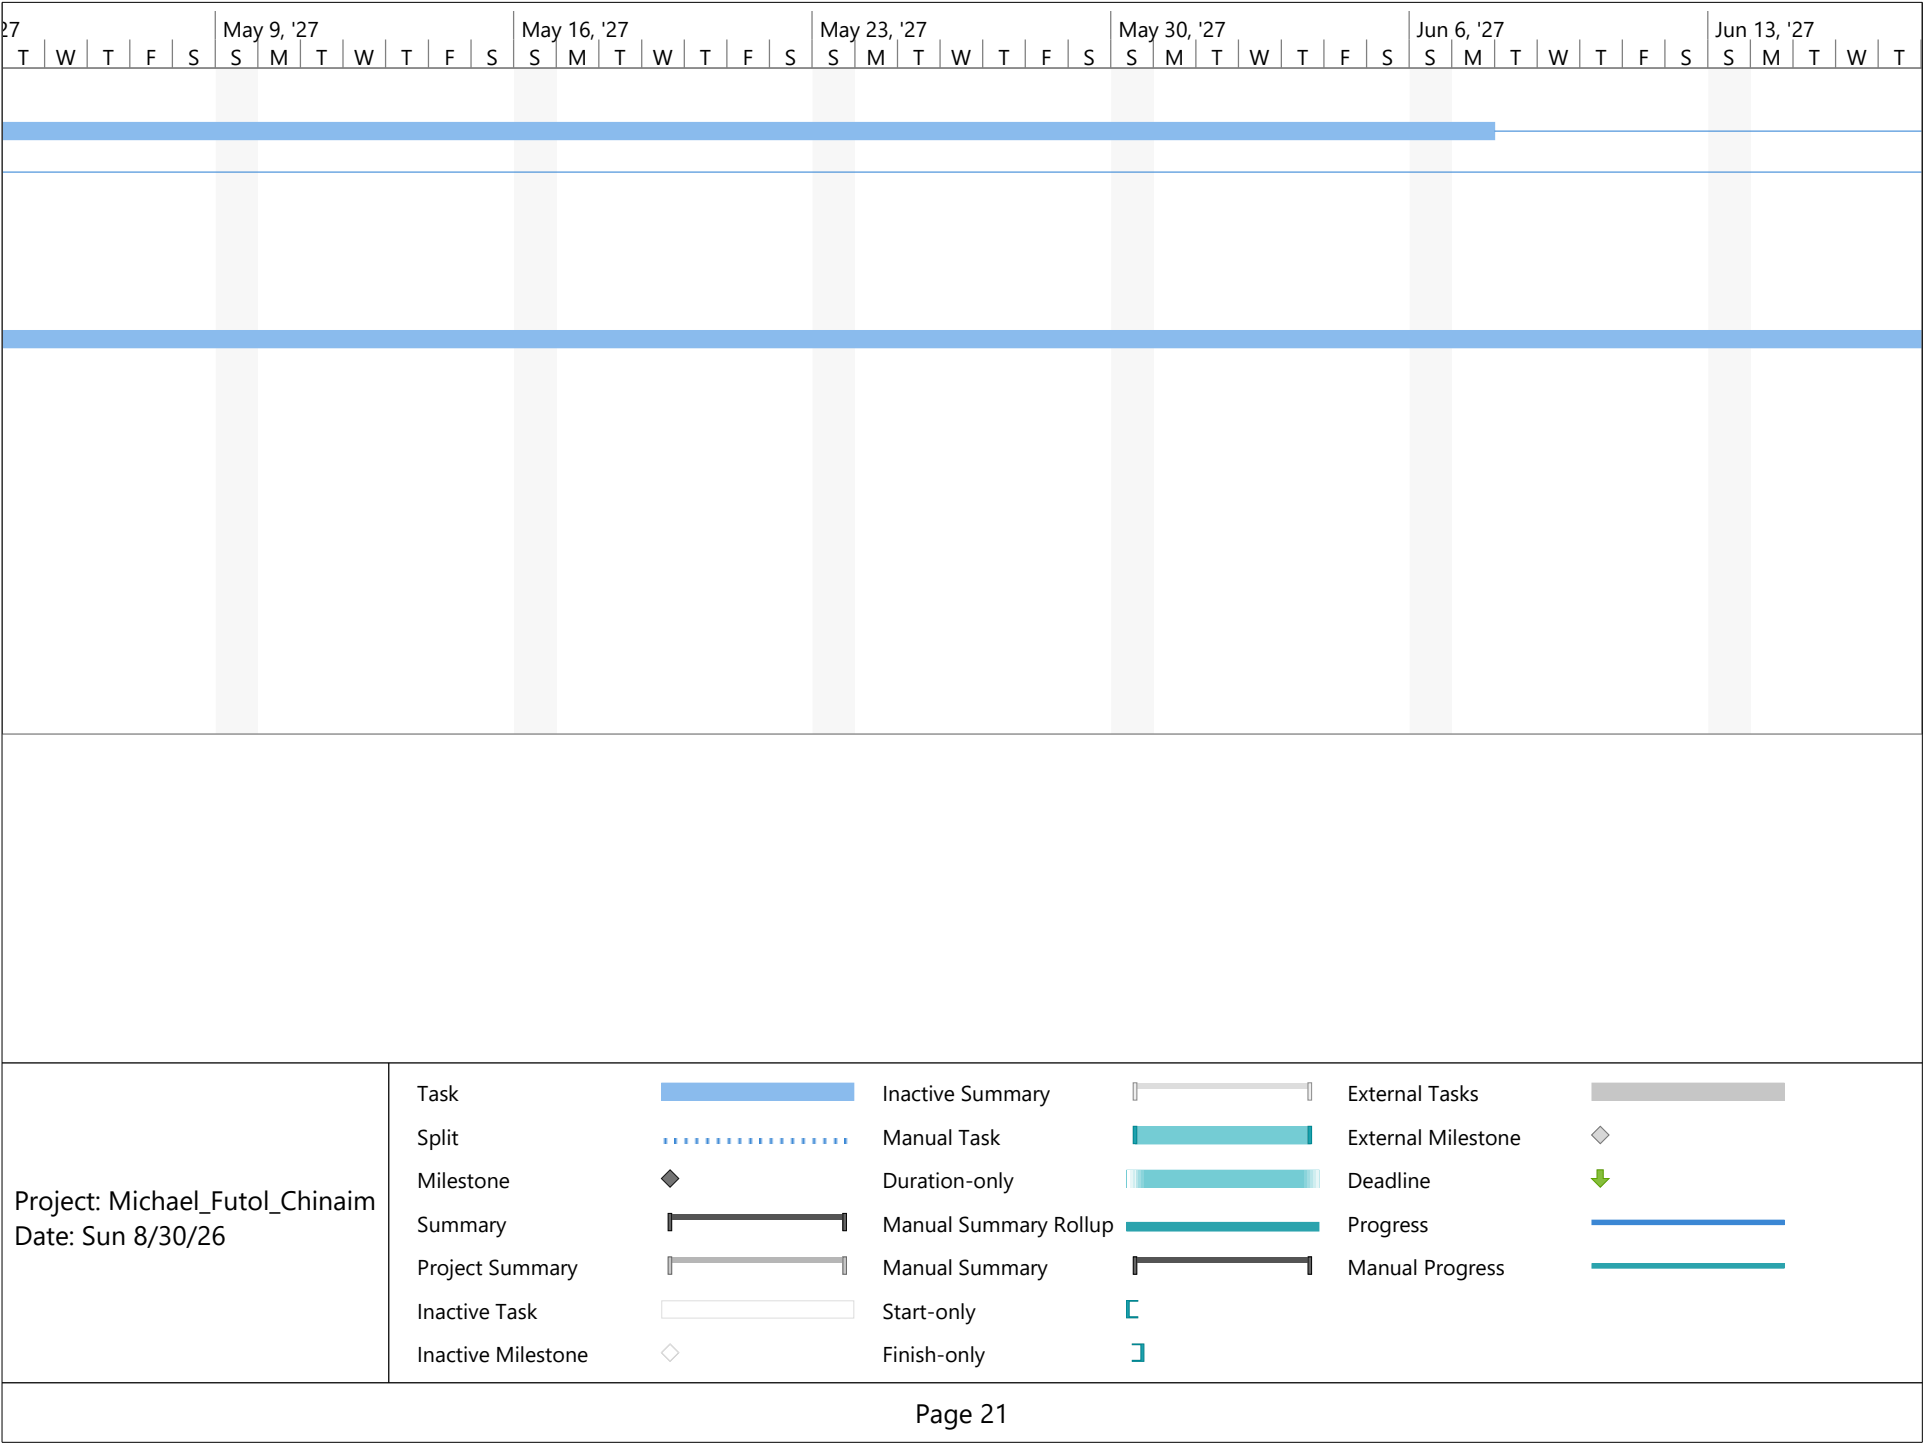


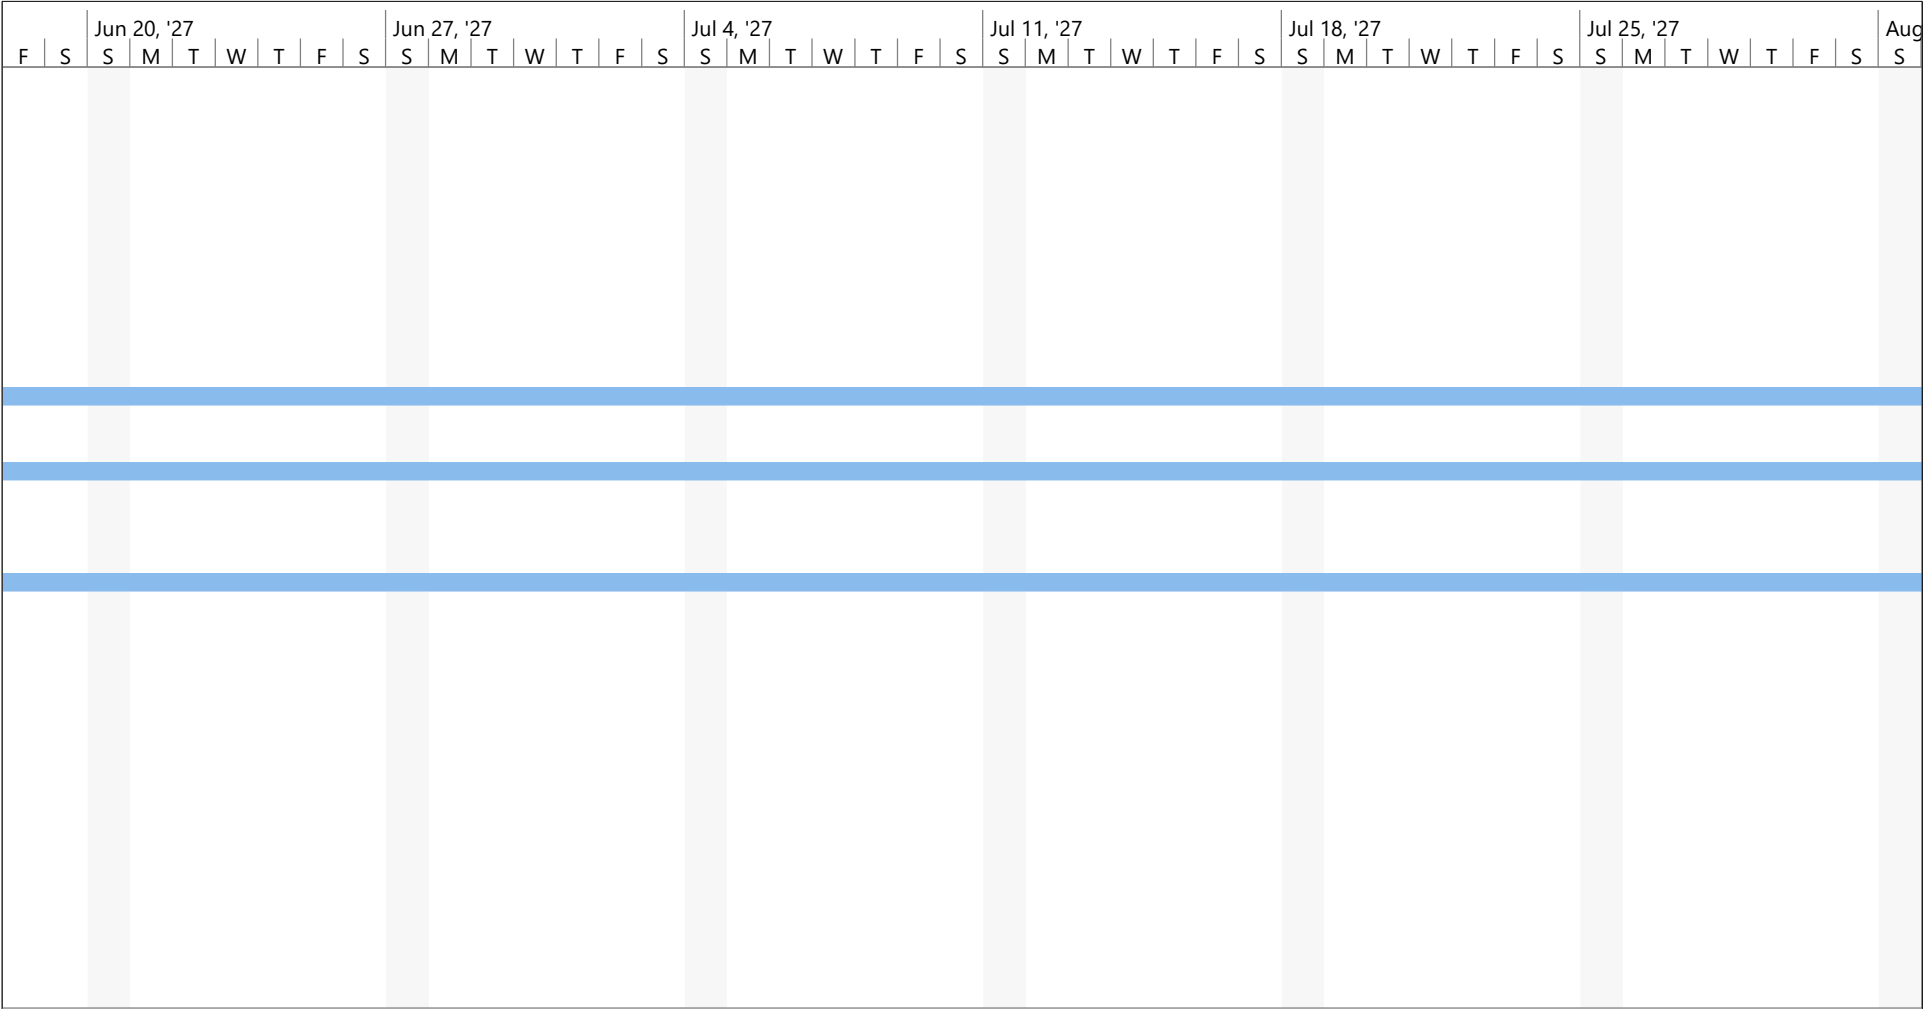



Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

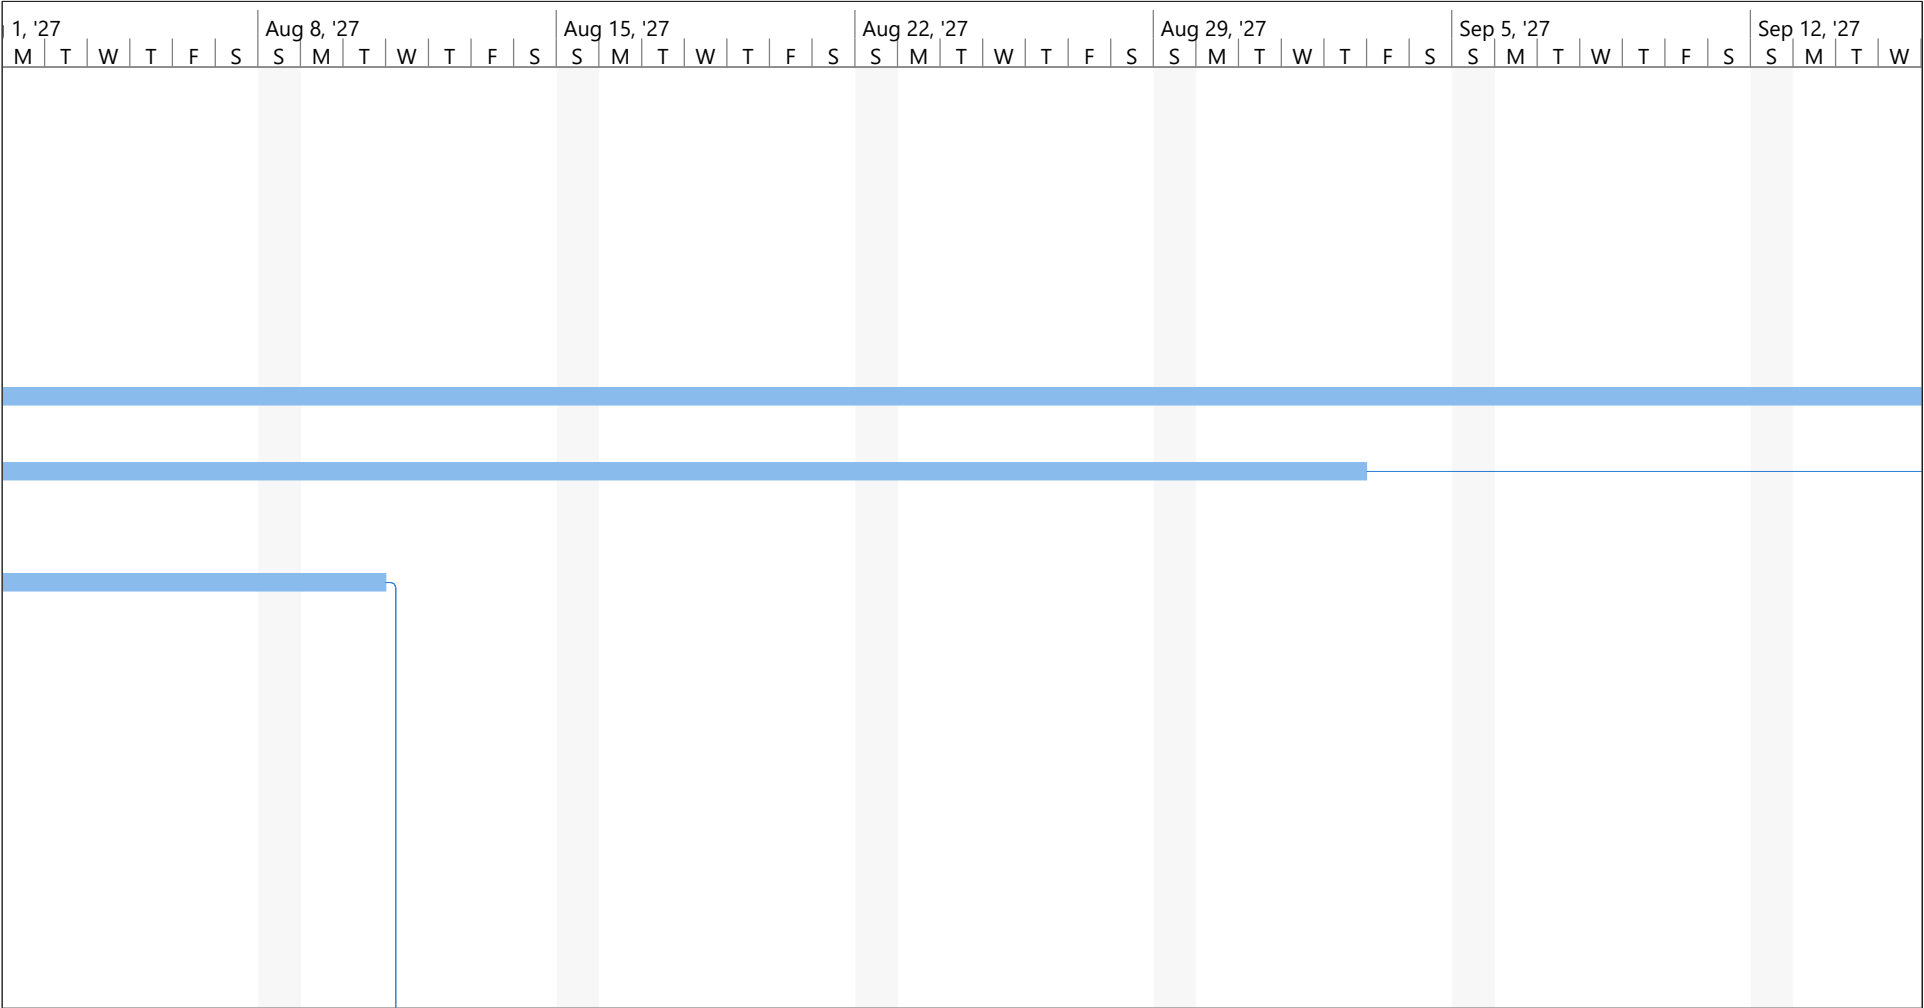



Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

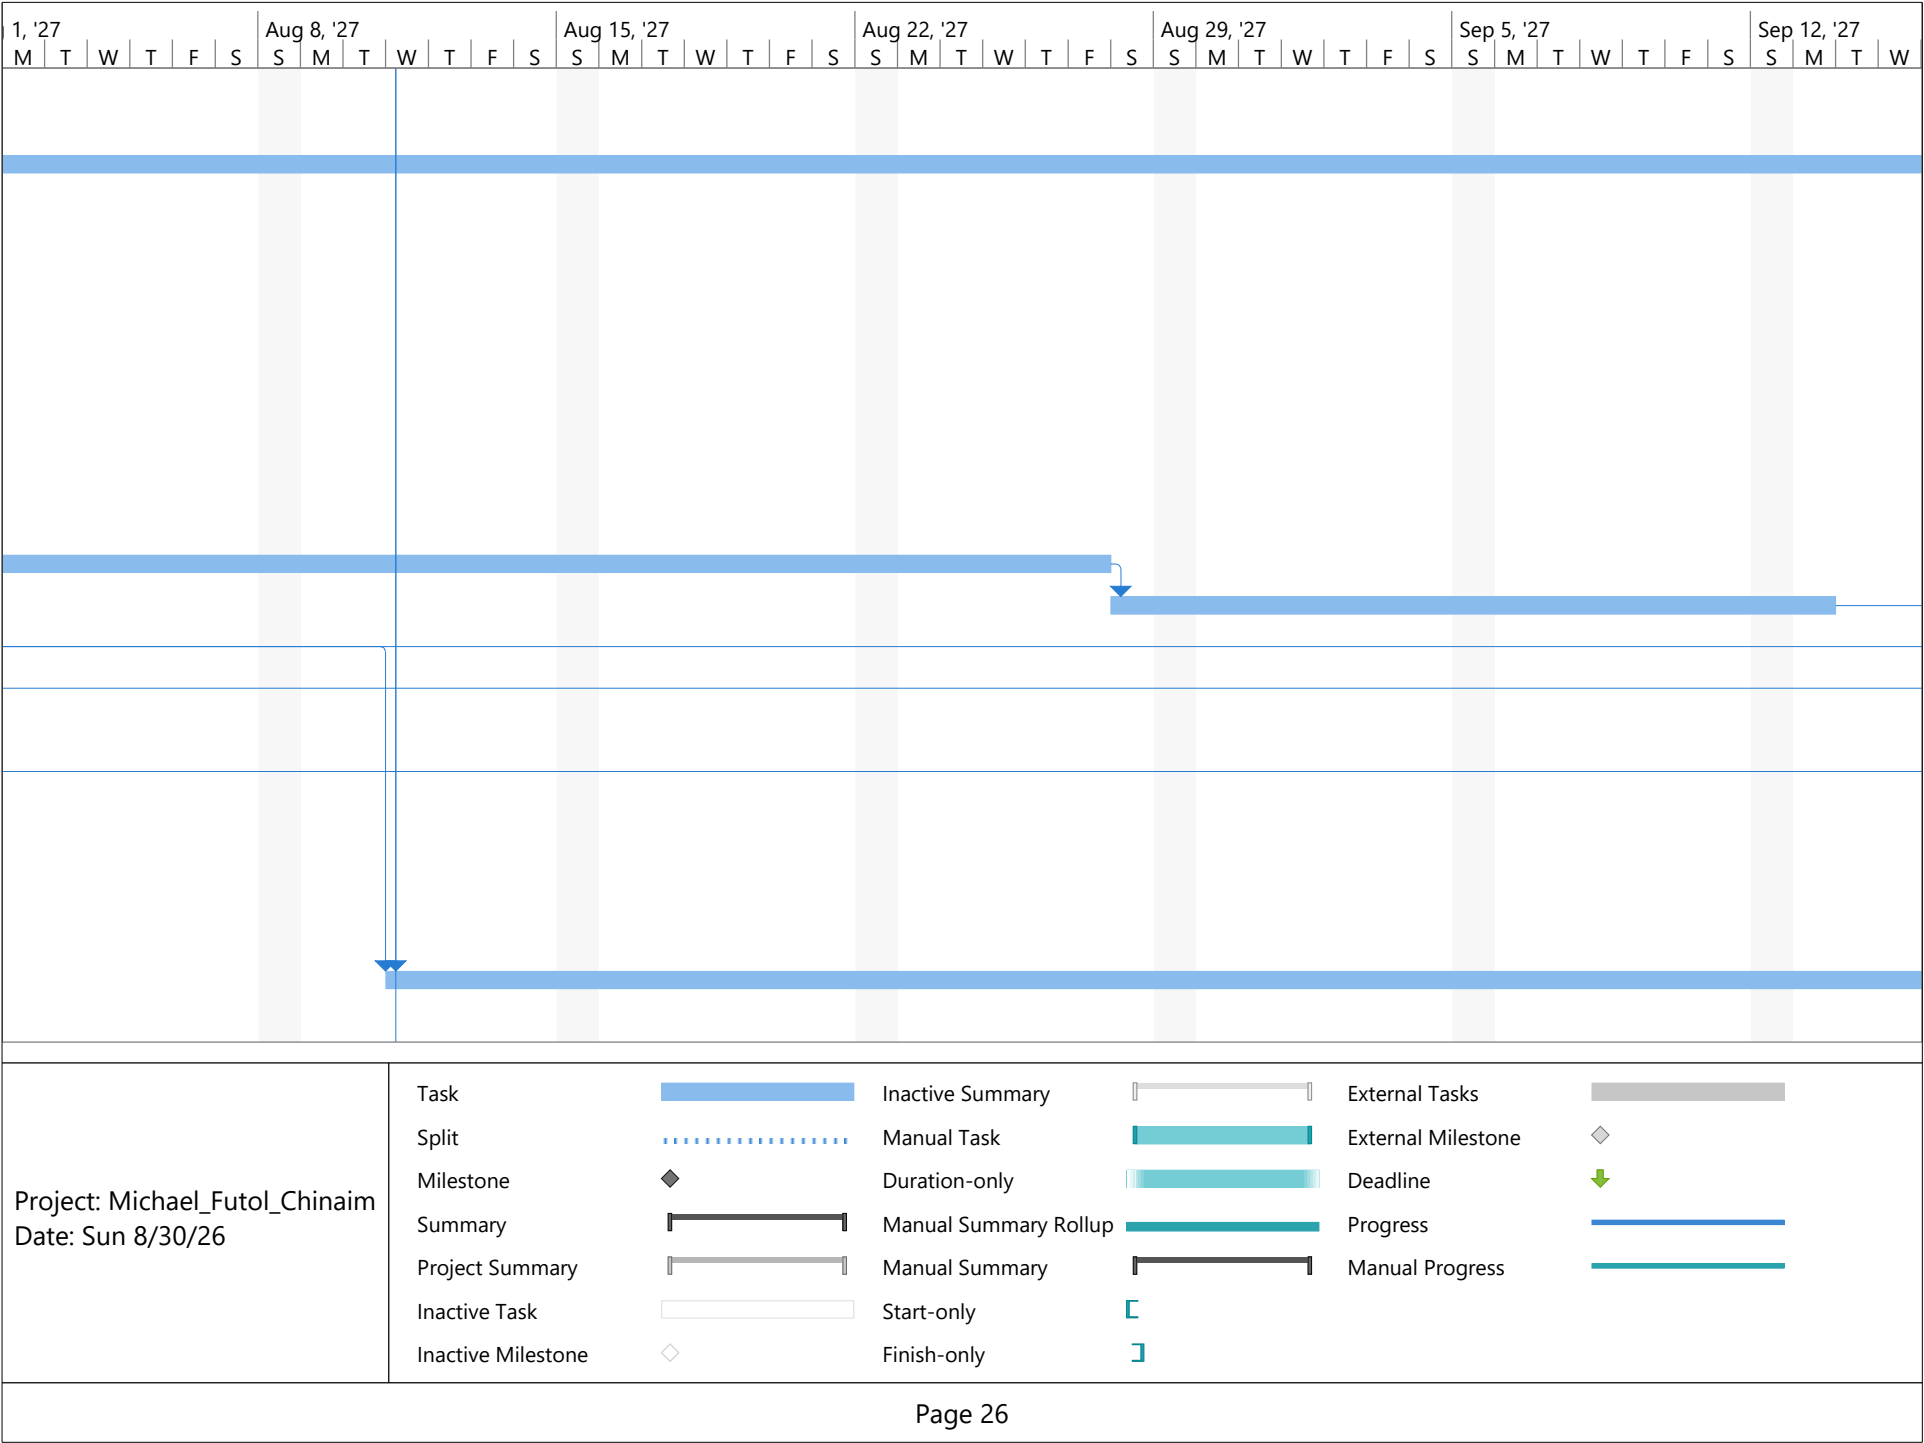

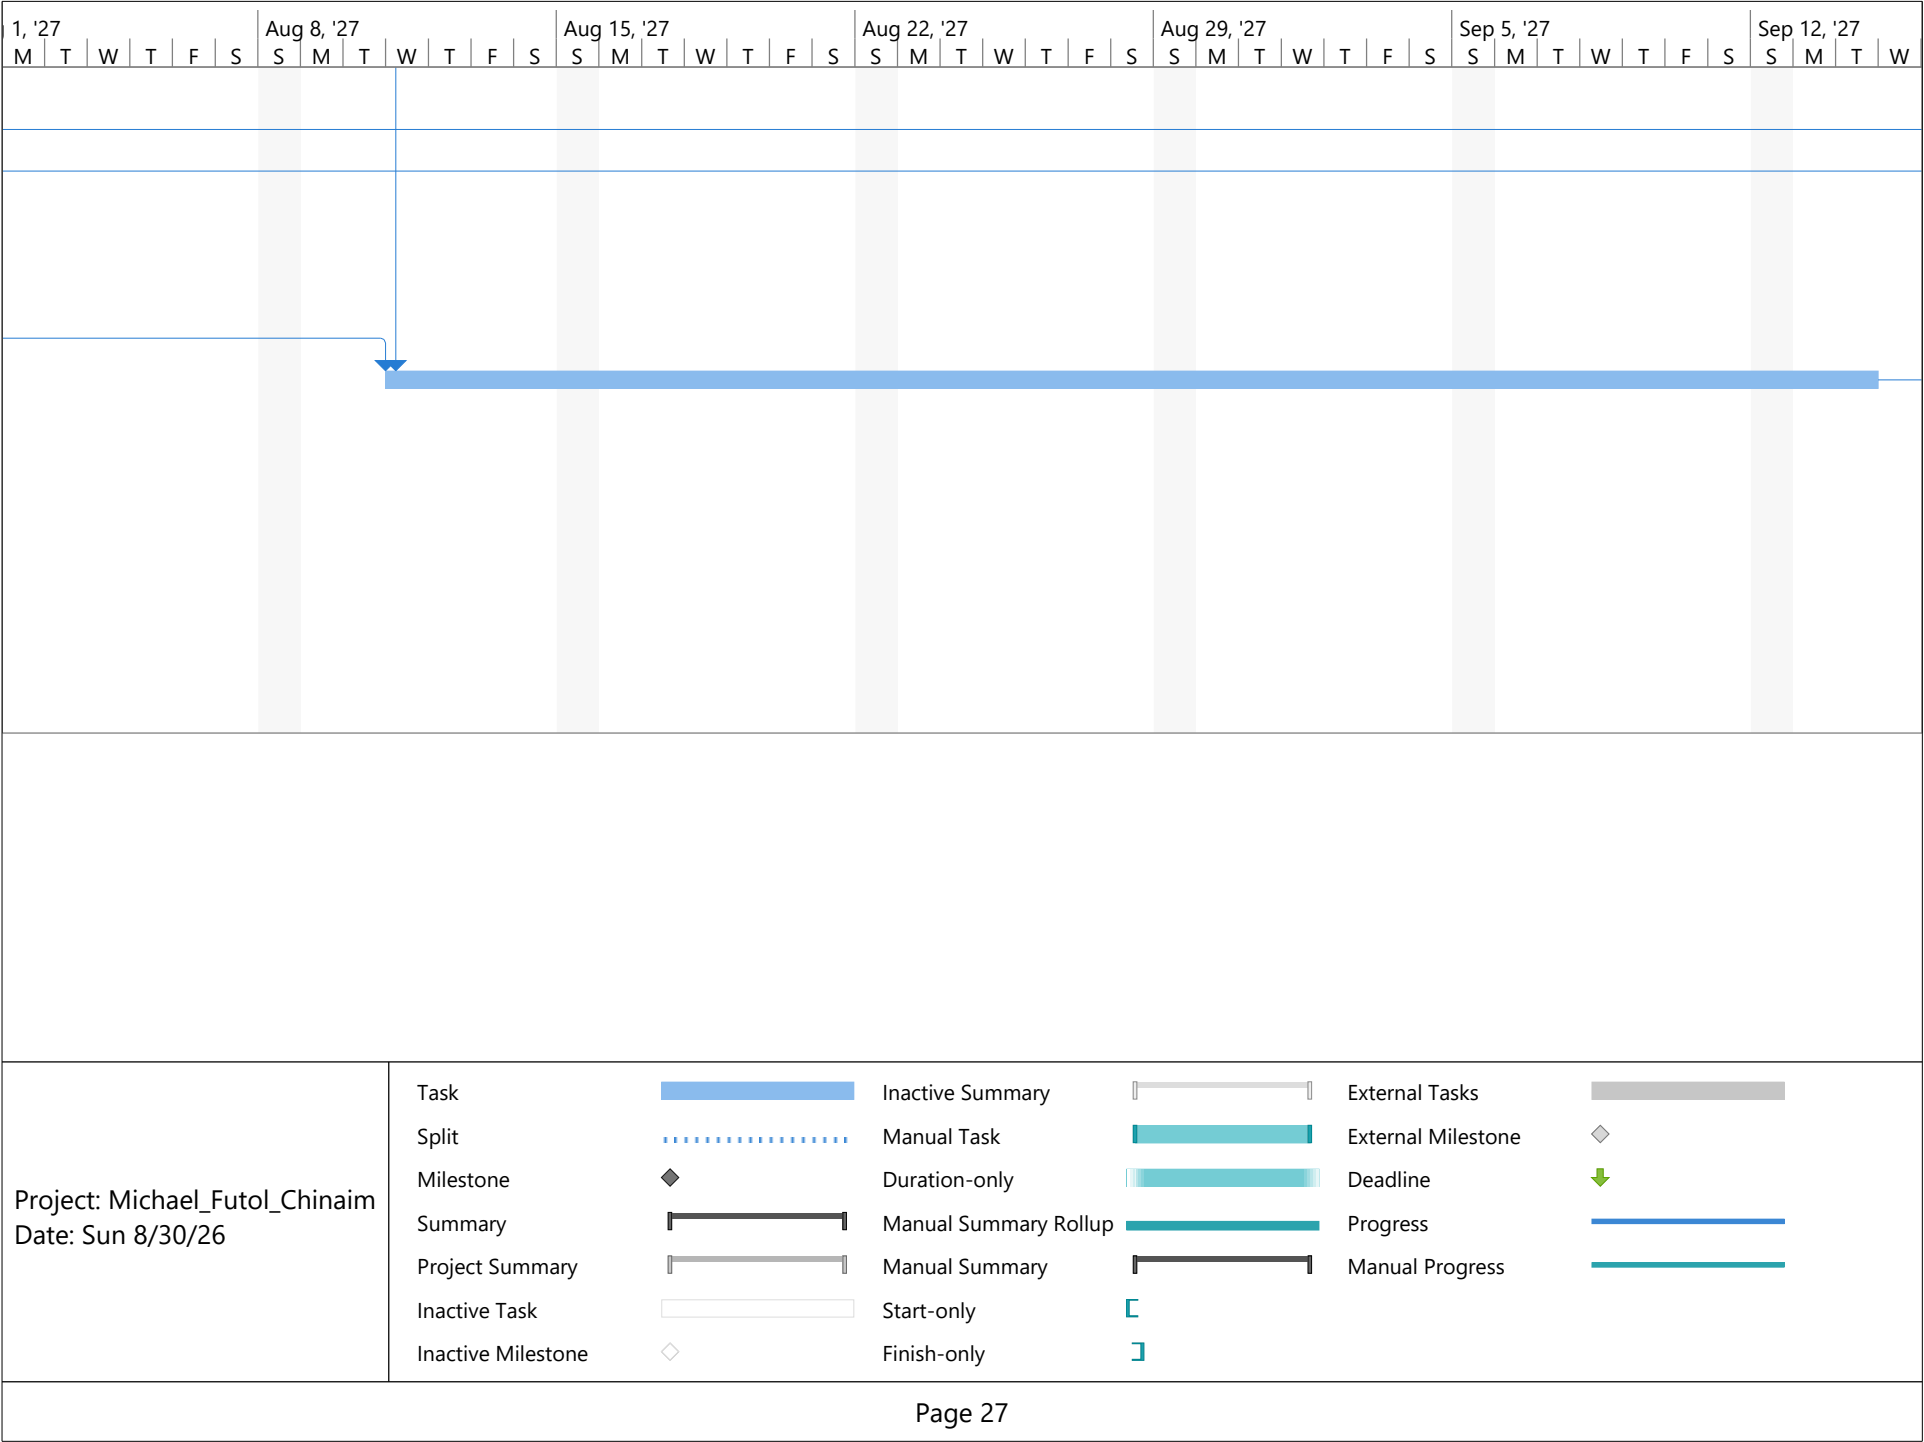

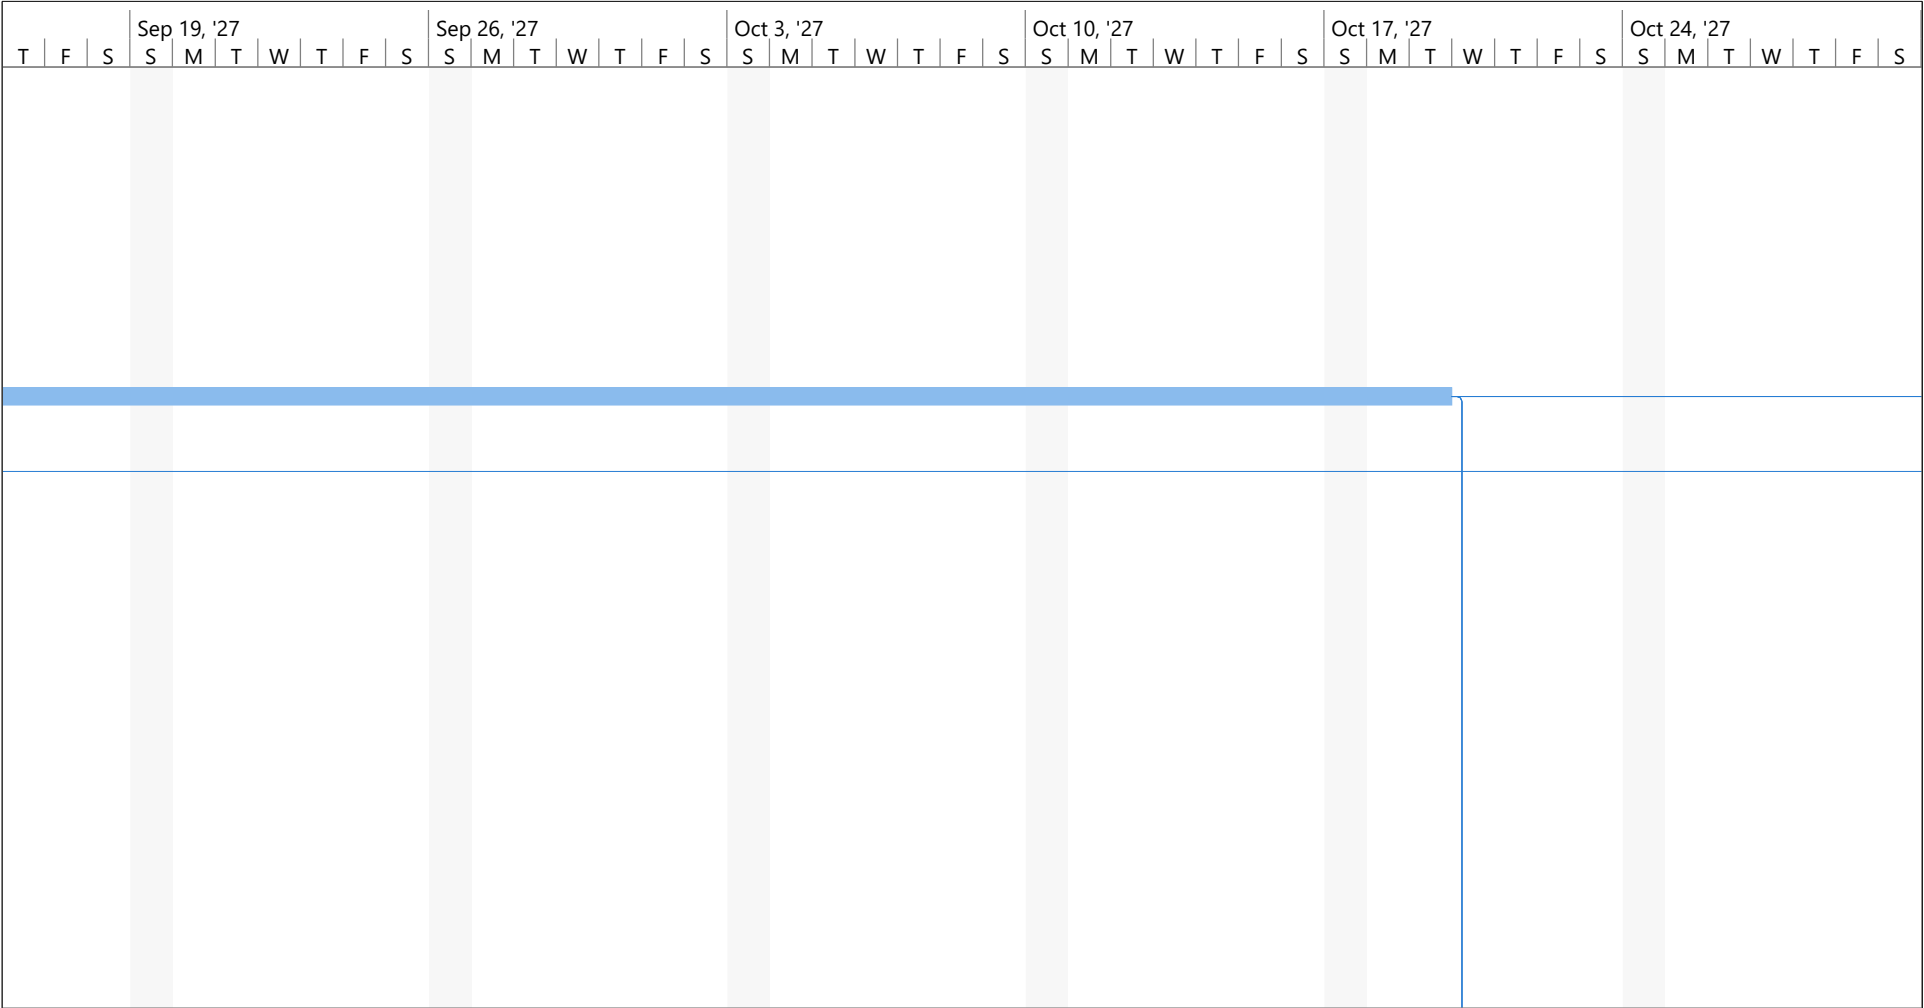


Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

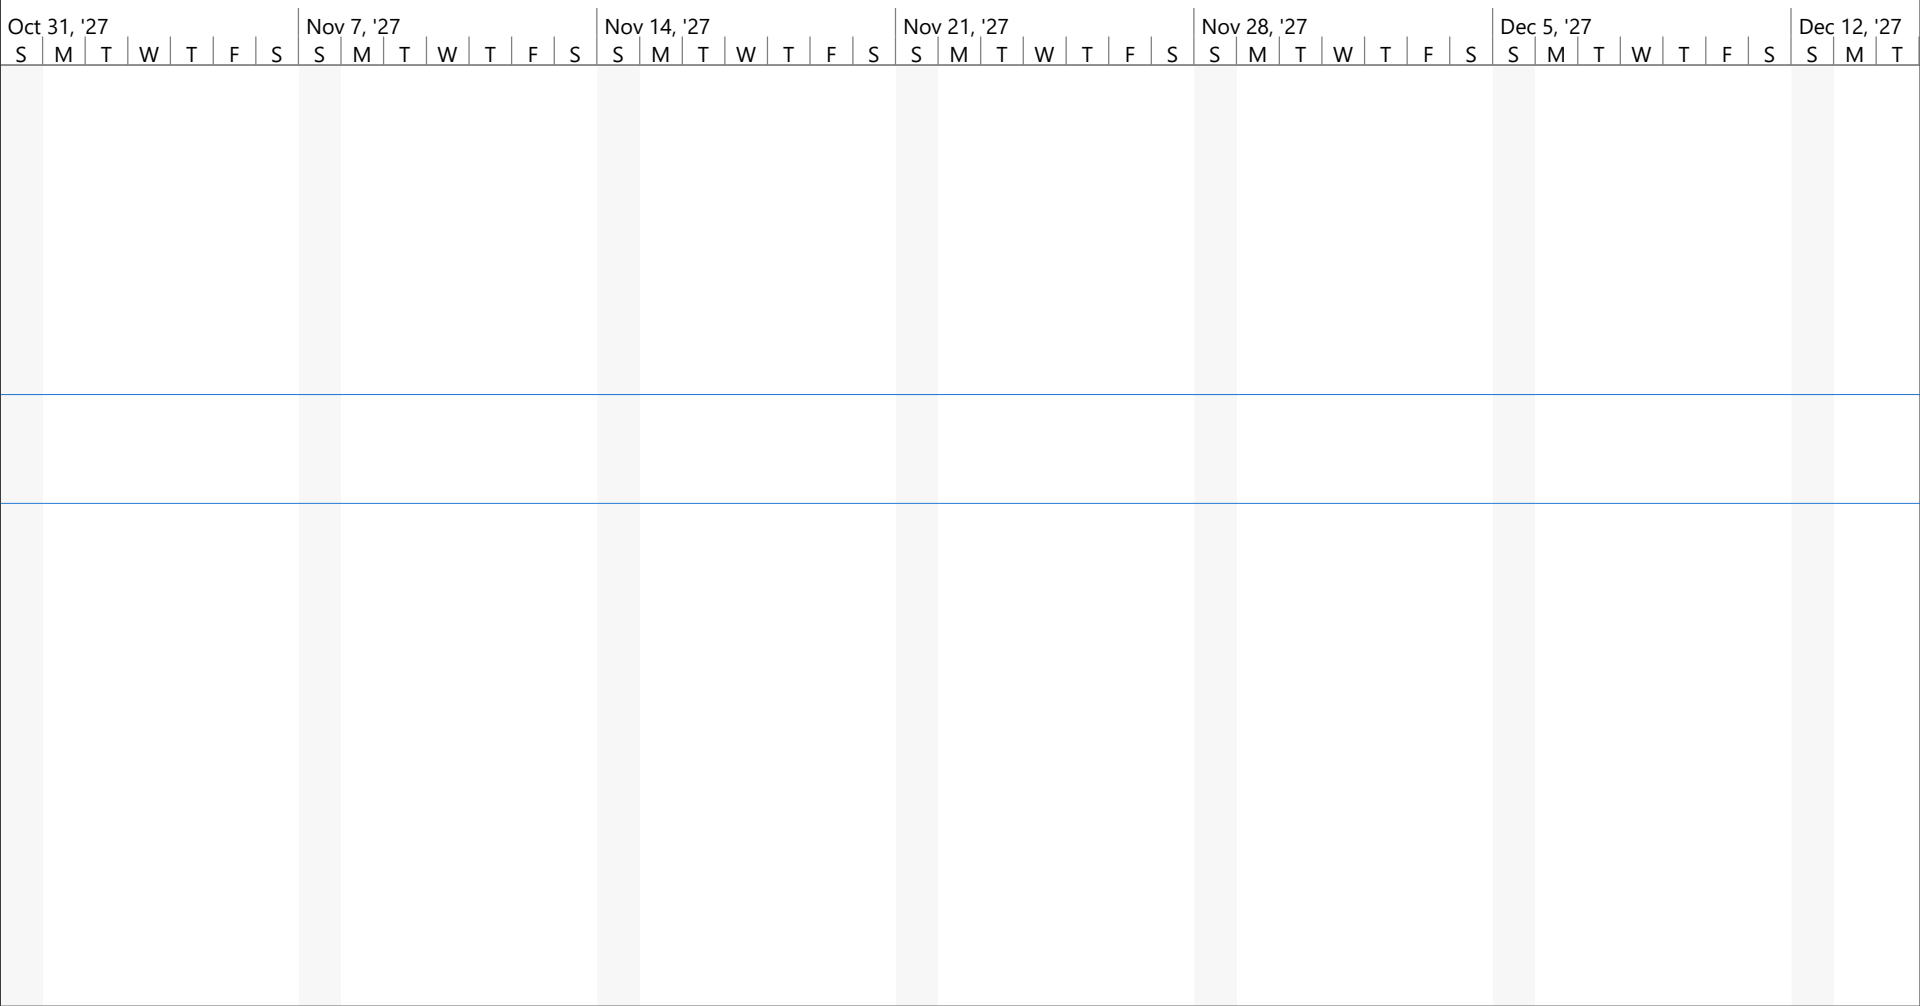

Project: Michael_FutoI_Chinaim
Date: Sun 8/30/26


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

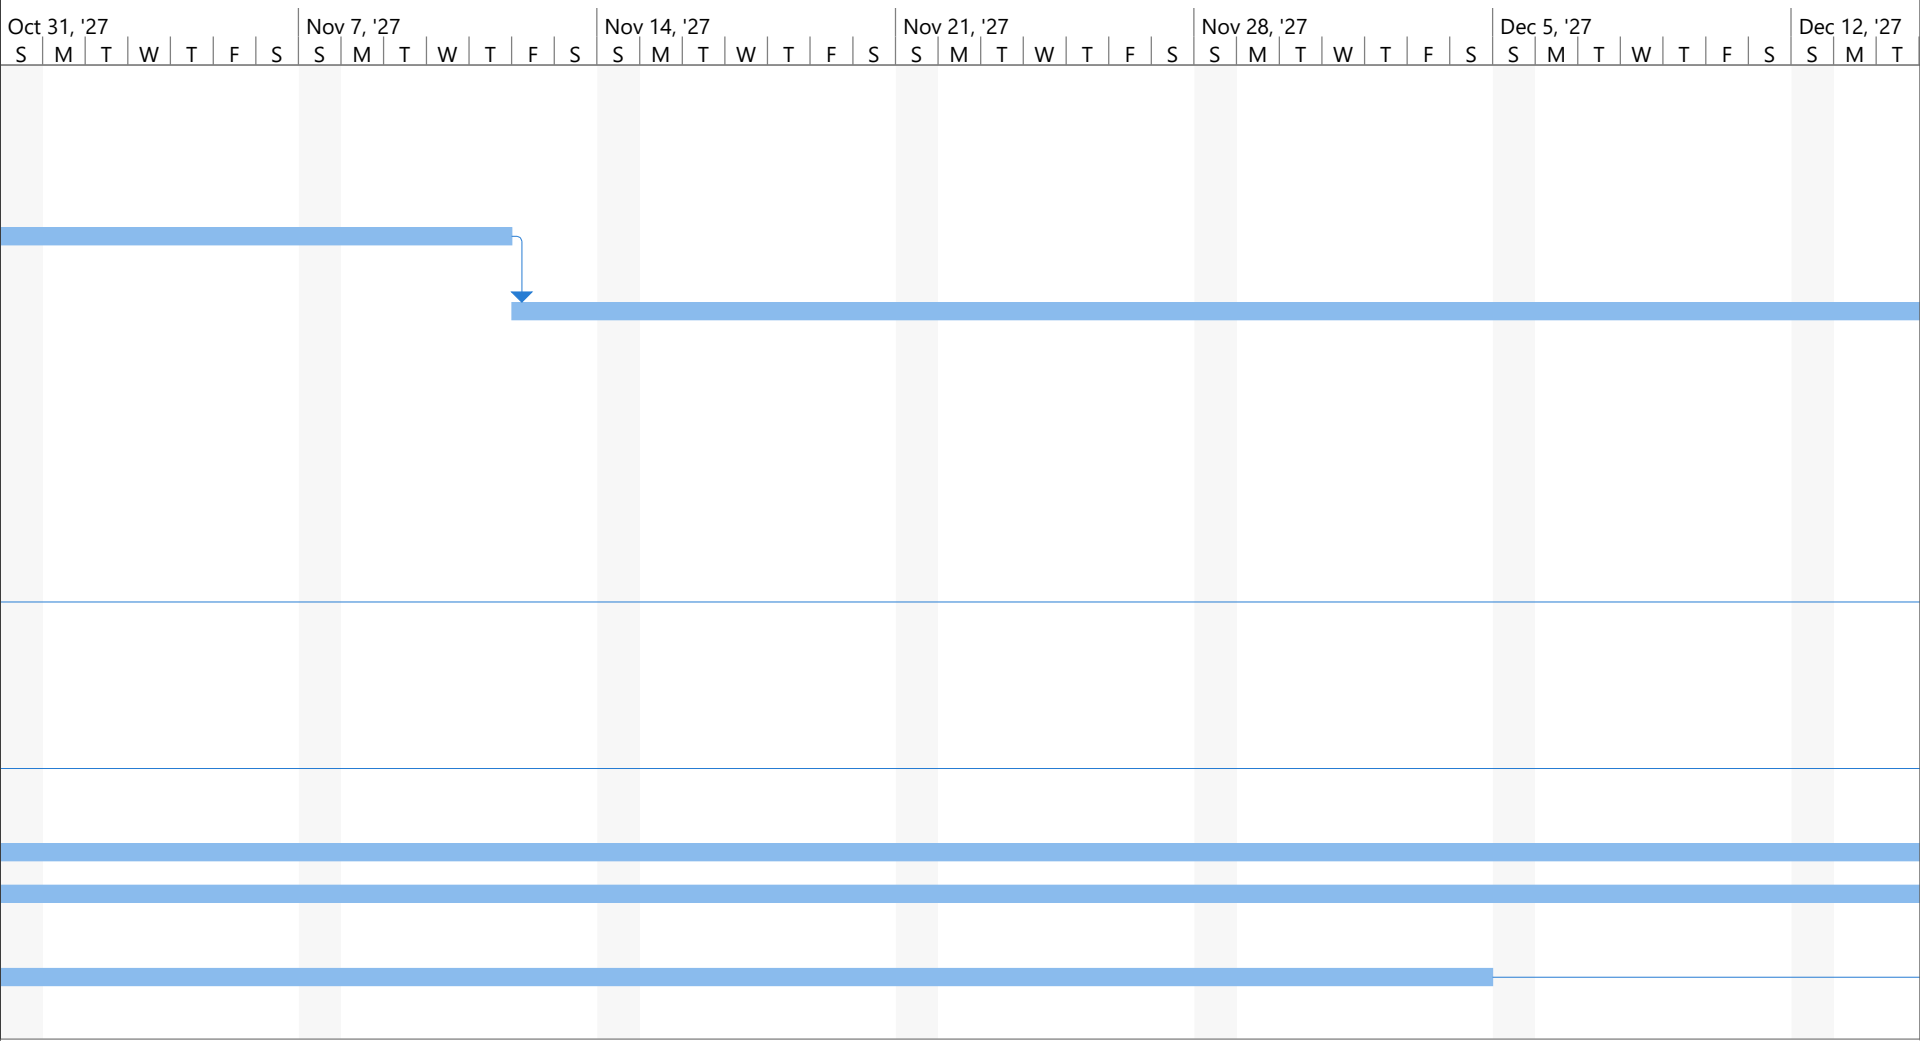


Project: Michael_FutoI_Chinaim


Date: Sun 8/30/26


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

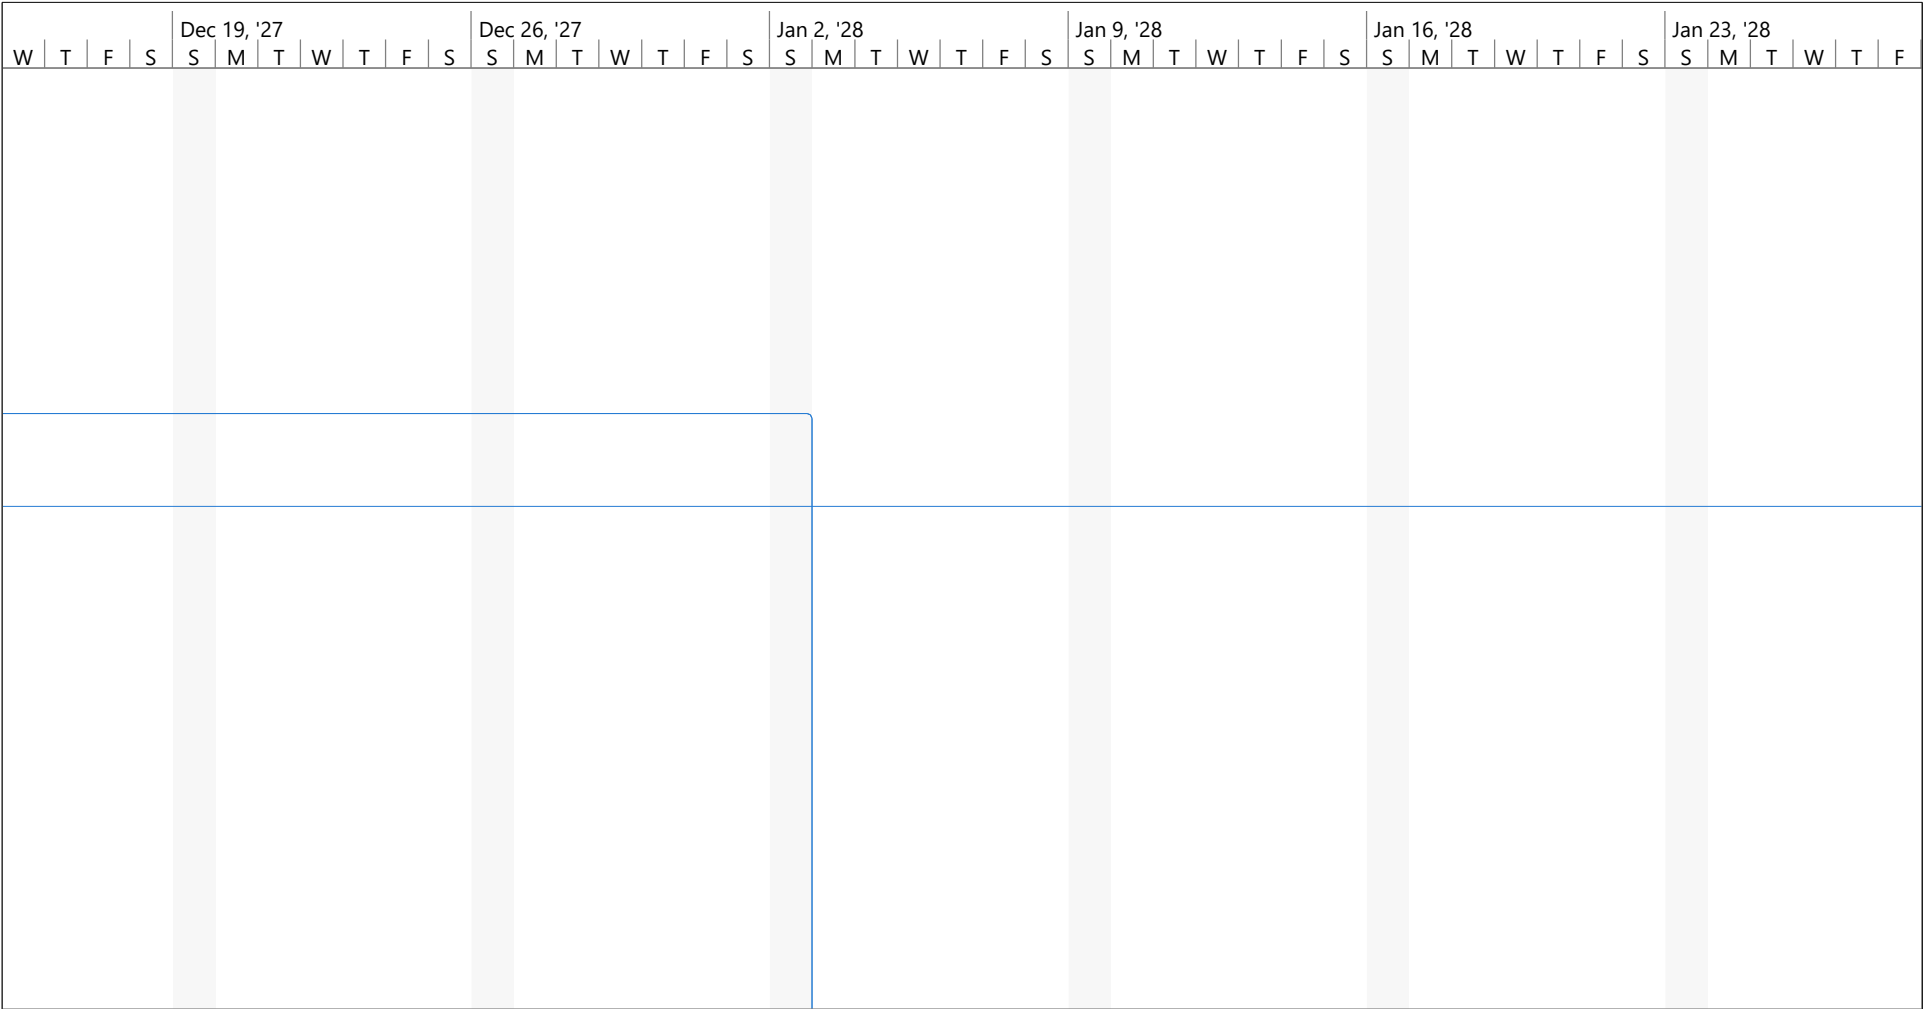

Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

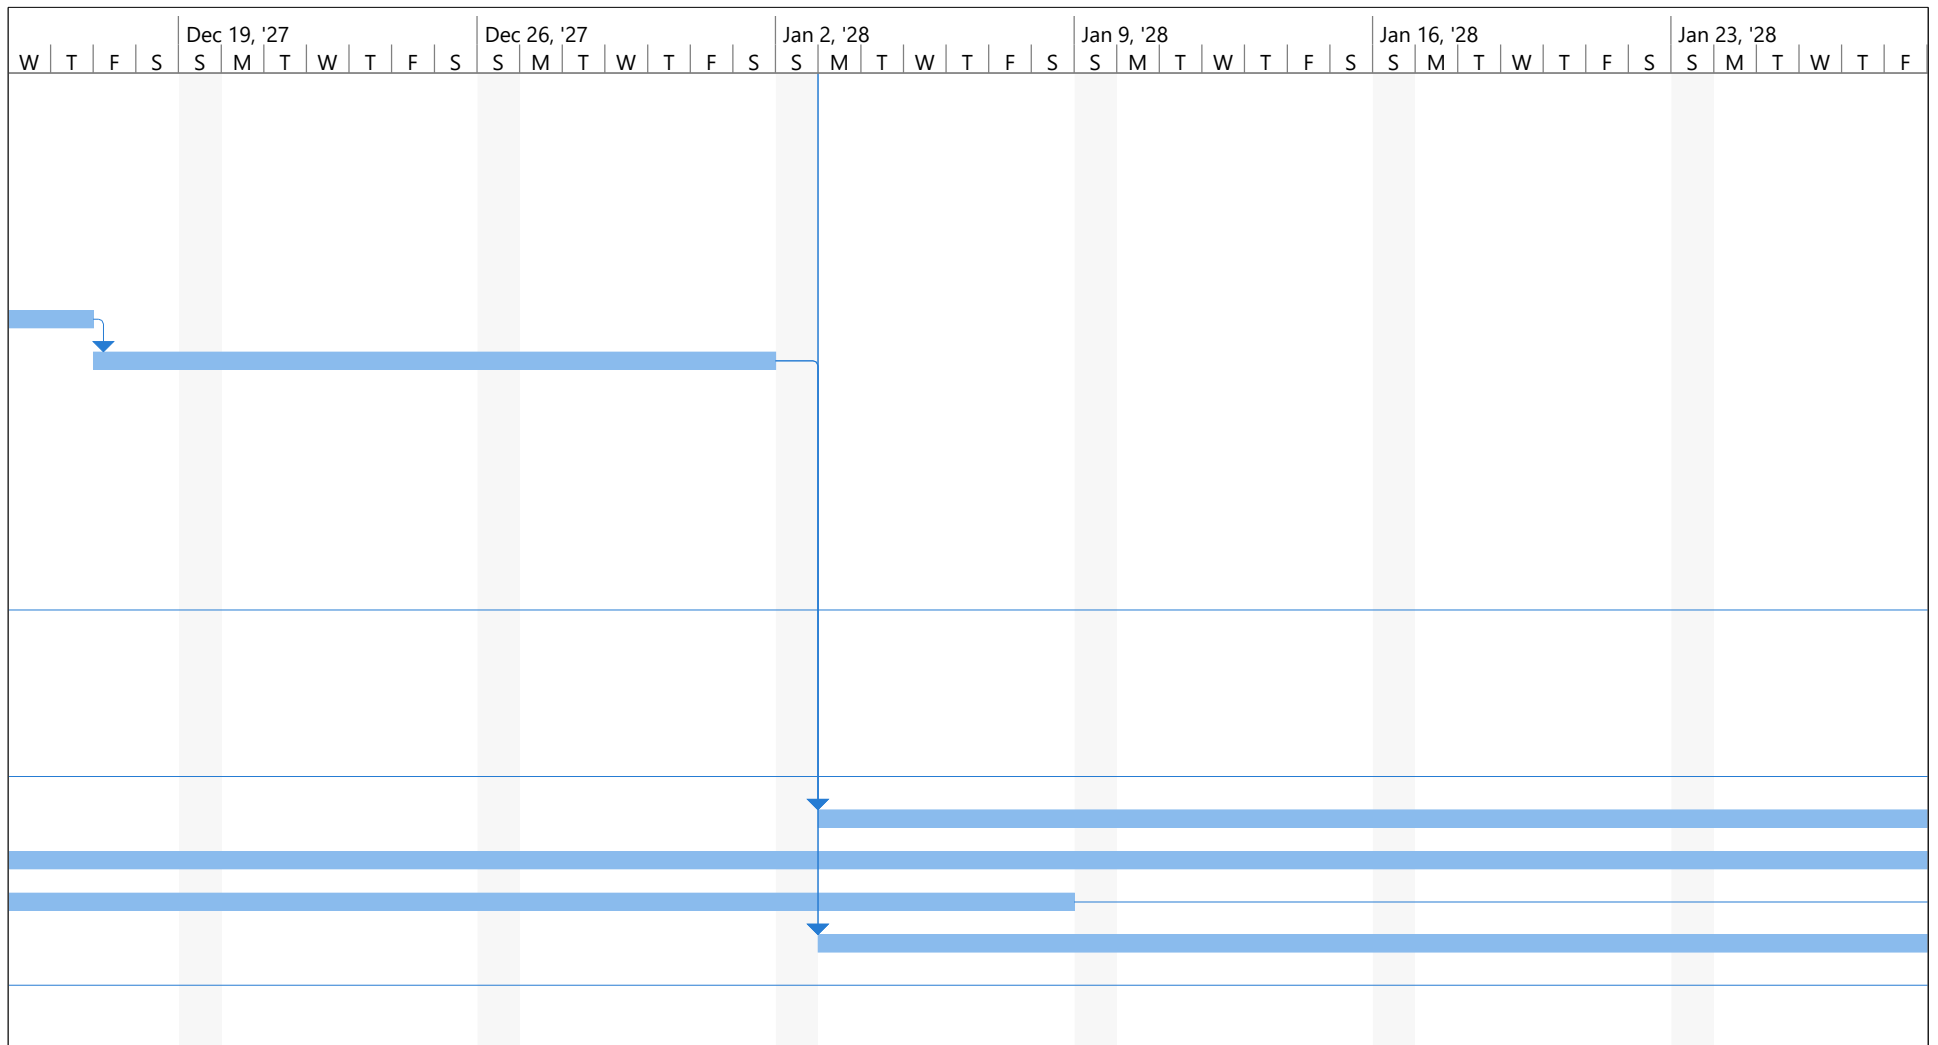


Project: Michael_Futol_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

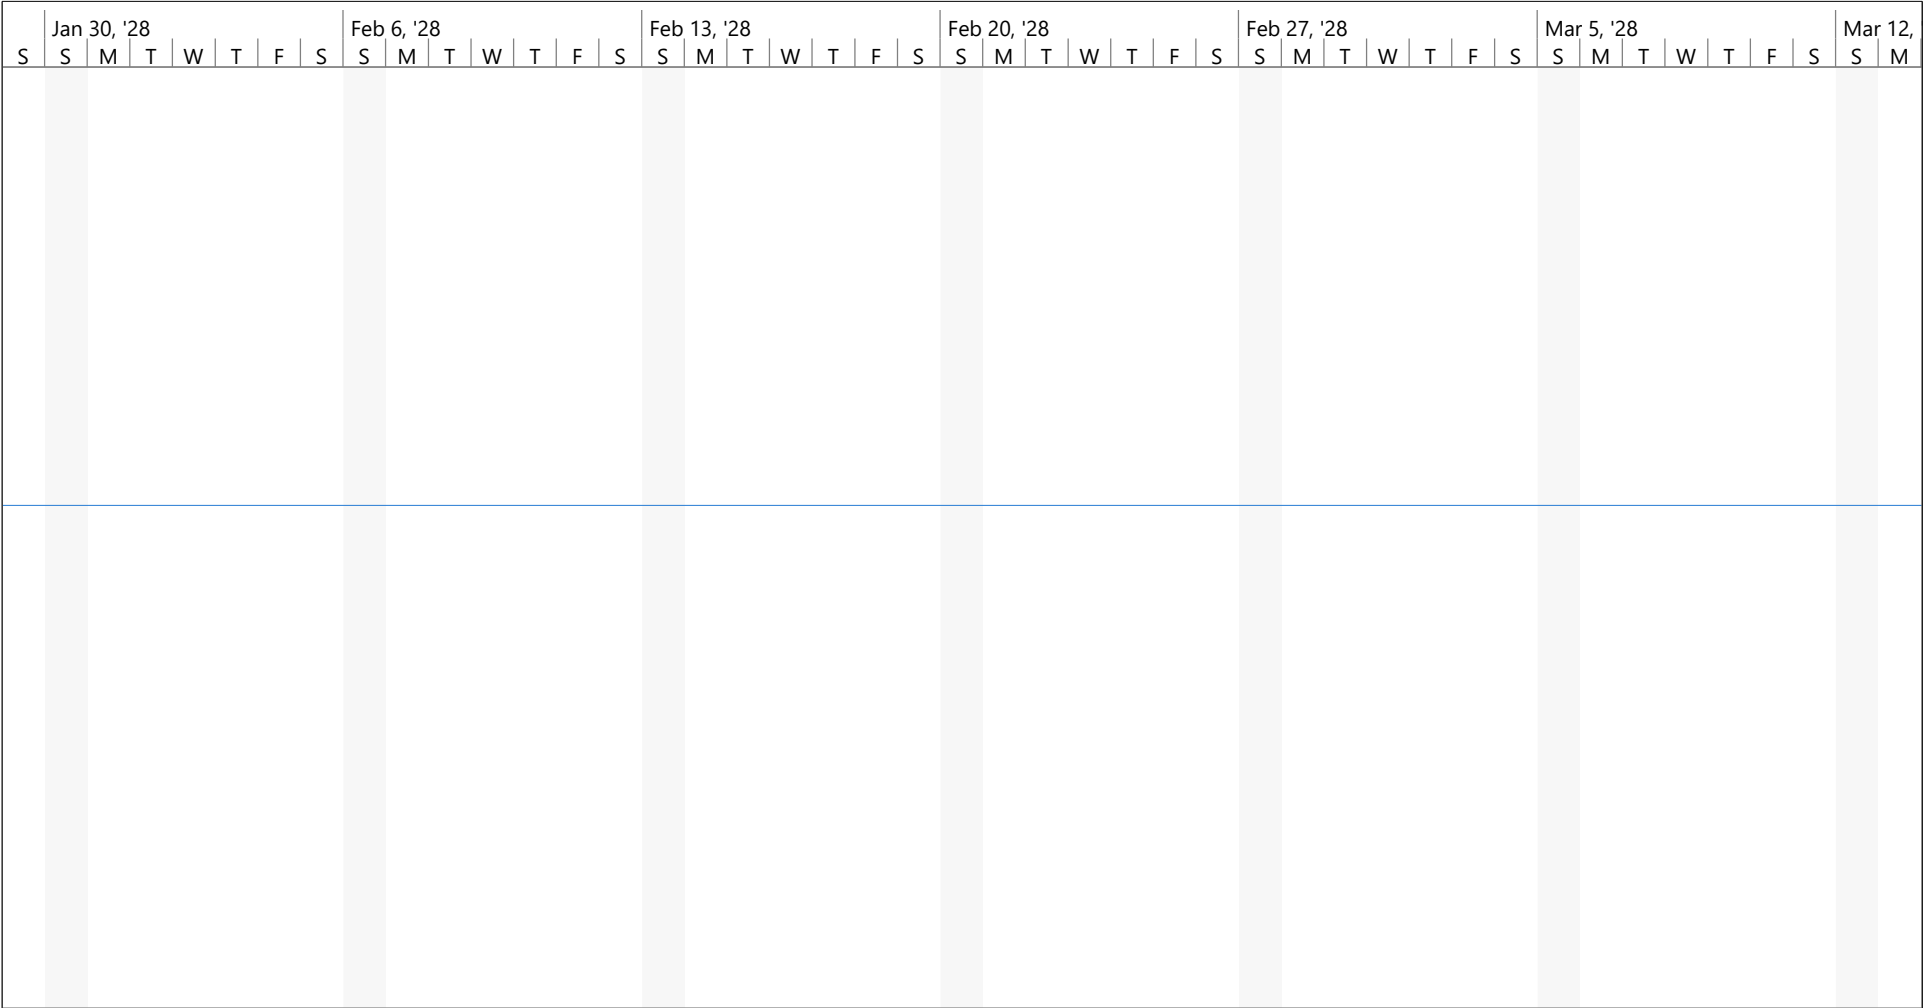


Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Project: Michael_FutoI_Chinaim
Date: Sun 8/30/26

Task	Visual Representation	Task	Visual Representation	Task	Visual Representation
Task	Solid blue bar	Inactive Summary	Thin grey bar	External Tasks	Grey bar
Split	Dotted blue bar	Manual Task	Teal bar with black ends	External Milestone	Grey diamond
Milestone	Diamond	Duration-only	Teal bar with gradient	Deadline	Green arrow
Summary	Thick black bar	Manual Summary Rollup	Teal bar with black ends	Progress	Blue bar
Project Summary	Thin grey bar	Manual Summary	Thin grey bar	Manual Progress	Teal bar
Inactive Task	Thin white bar	Start-only	Teal bracket		
Inactive Milestone	White diamond	Finish-only	Teal bracket		

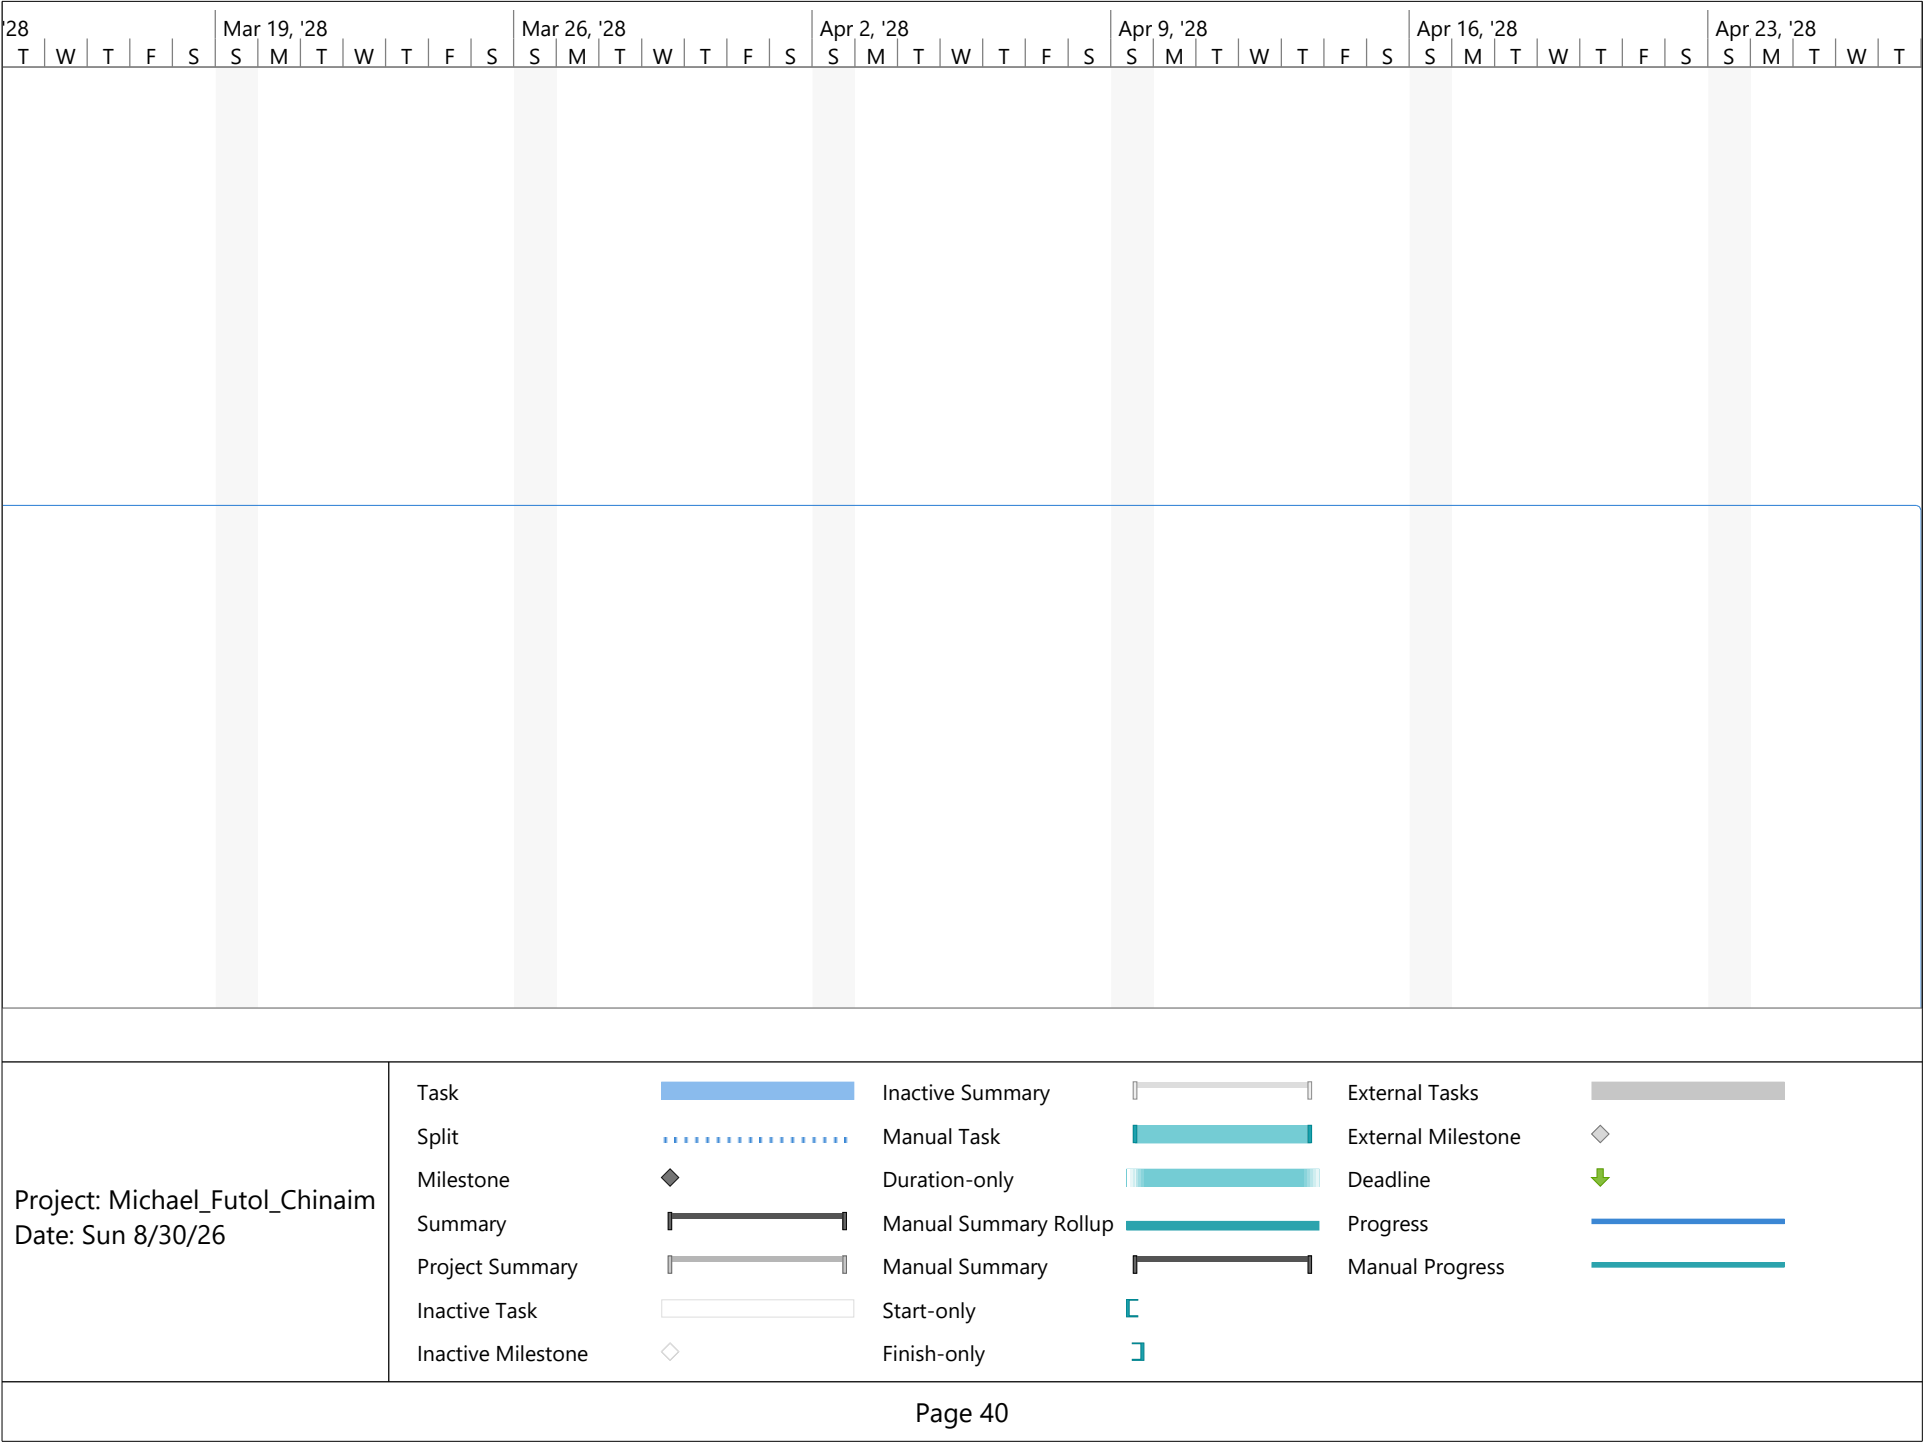

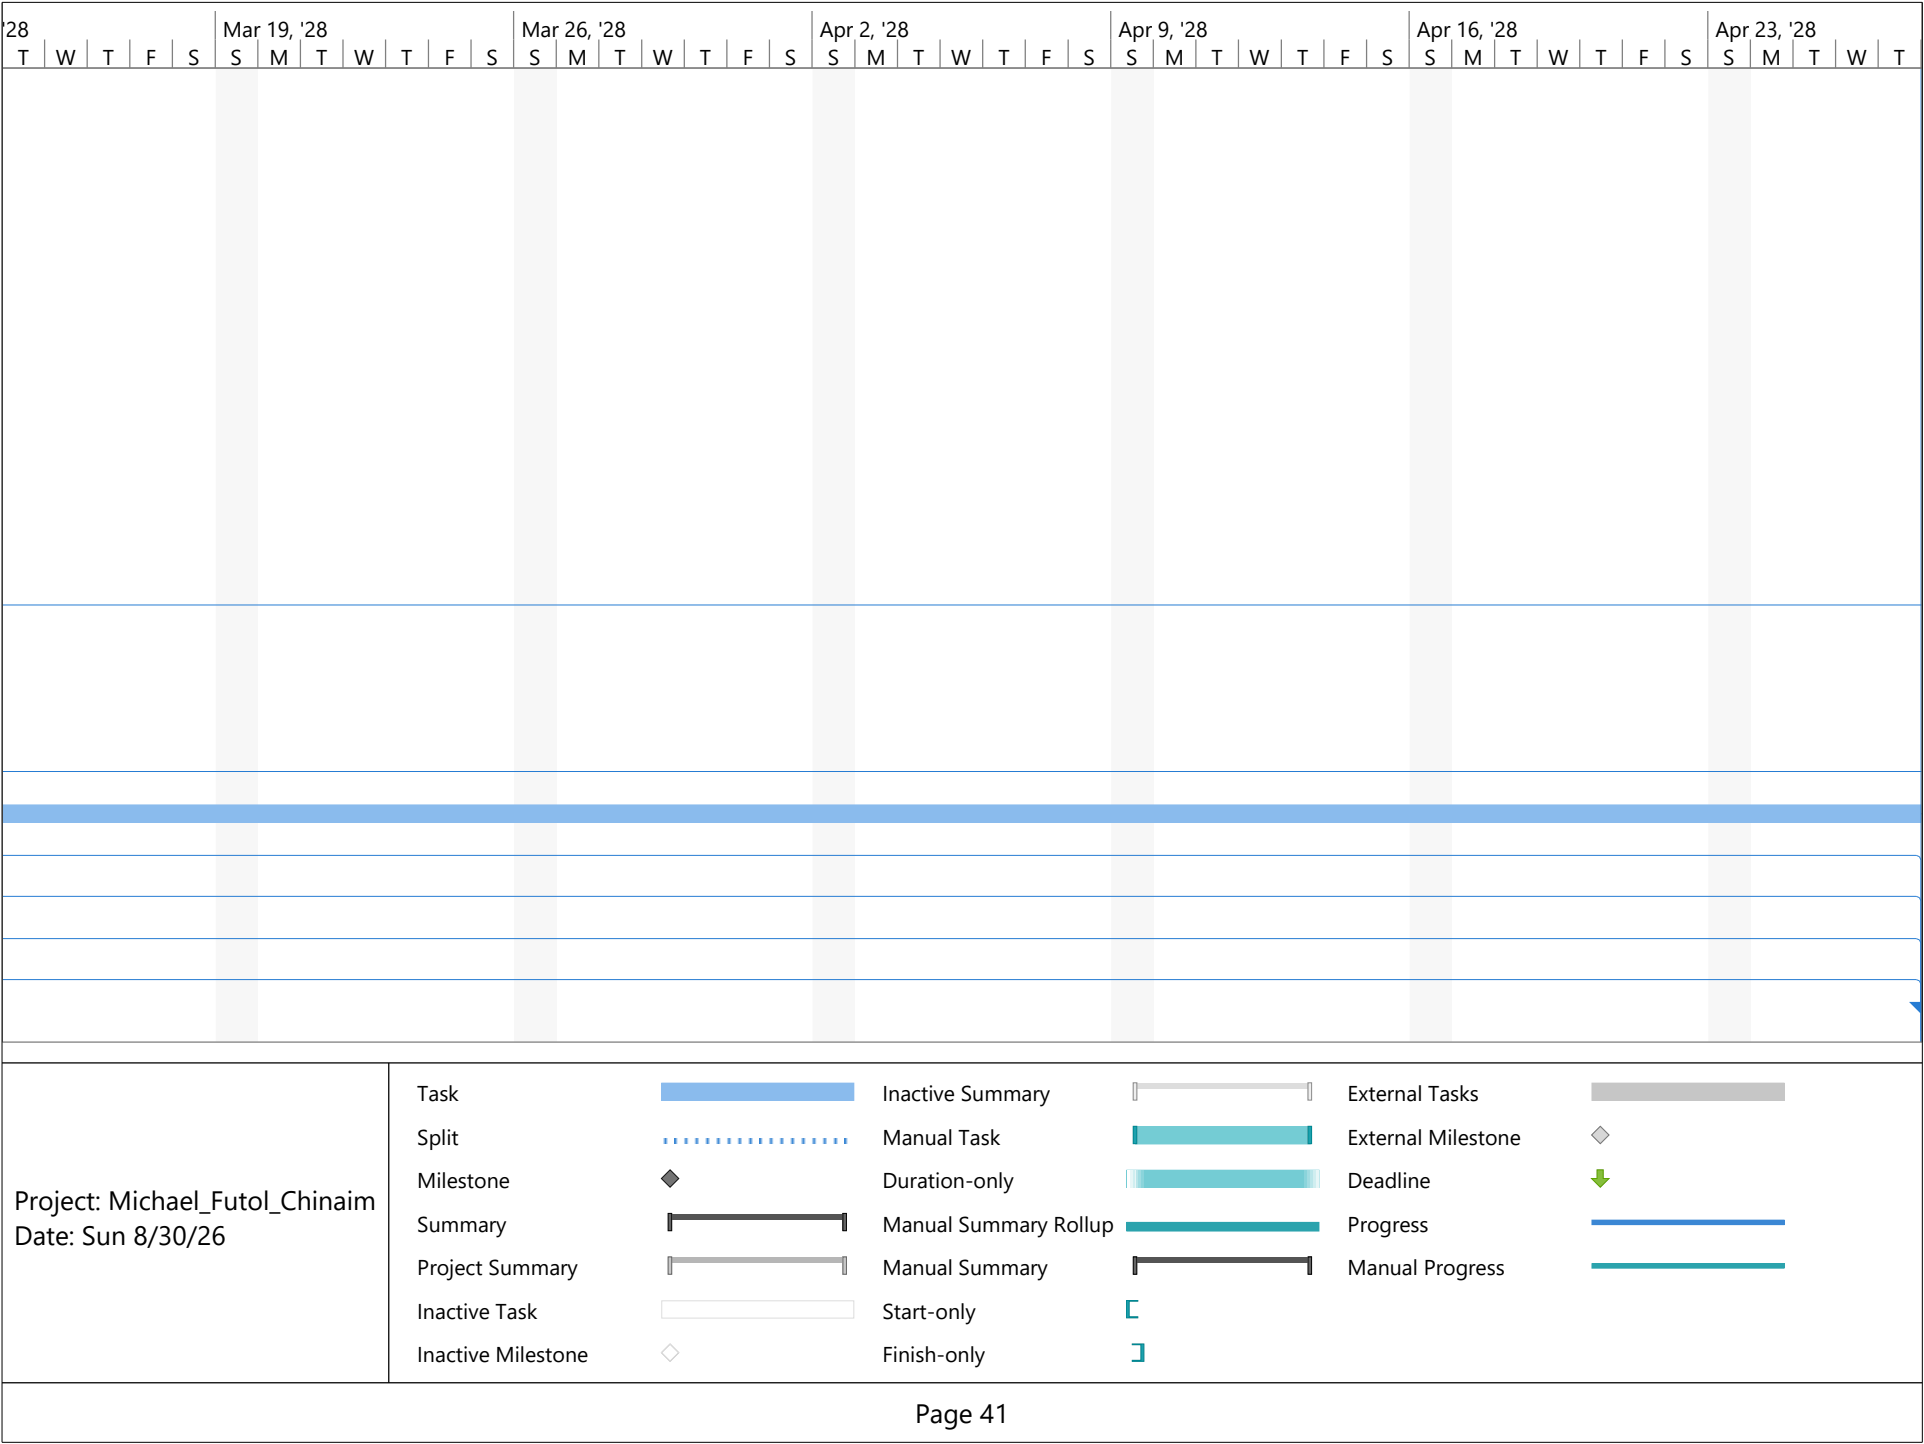

28

T

W

T

F

S

Mar 19, '28

S

M

T

W

T

F

S

Mar 26, '28

S

M

T

W

T

F

S

Apr 2, '28

S

M

T

W

T

F

S

Apr 9, '28

S

M

T

W

T

F

S

Apr 16, '28

S

M

T

W

T

F

S

Apr 23, '28

S

M

T

W

T

Project: Michael_FutoI_Chinaim

Date: Sun 8/30/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone



Deadline

Progress



Manual Progress


Page 42





Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			






Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

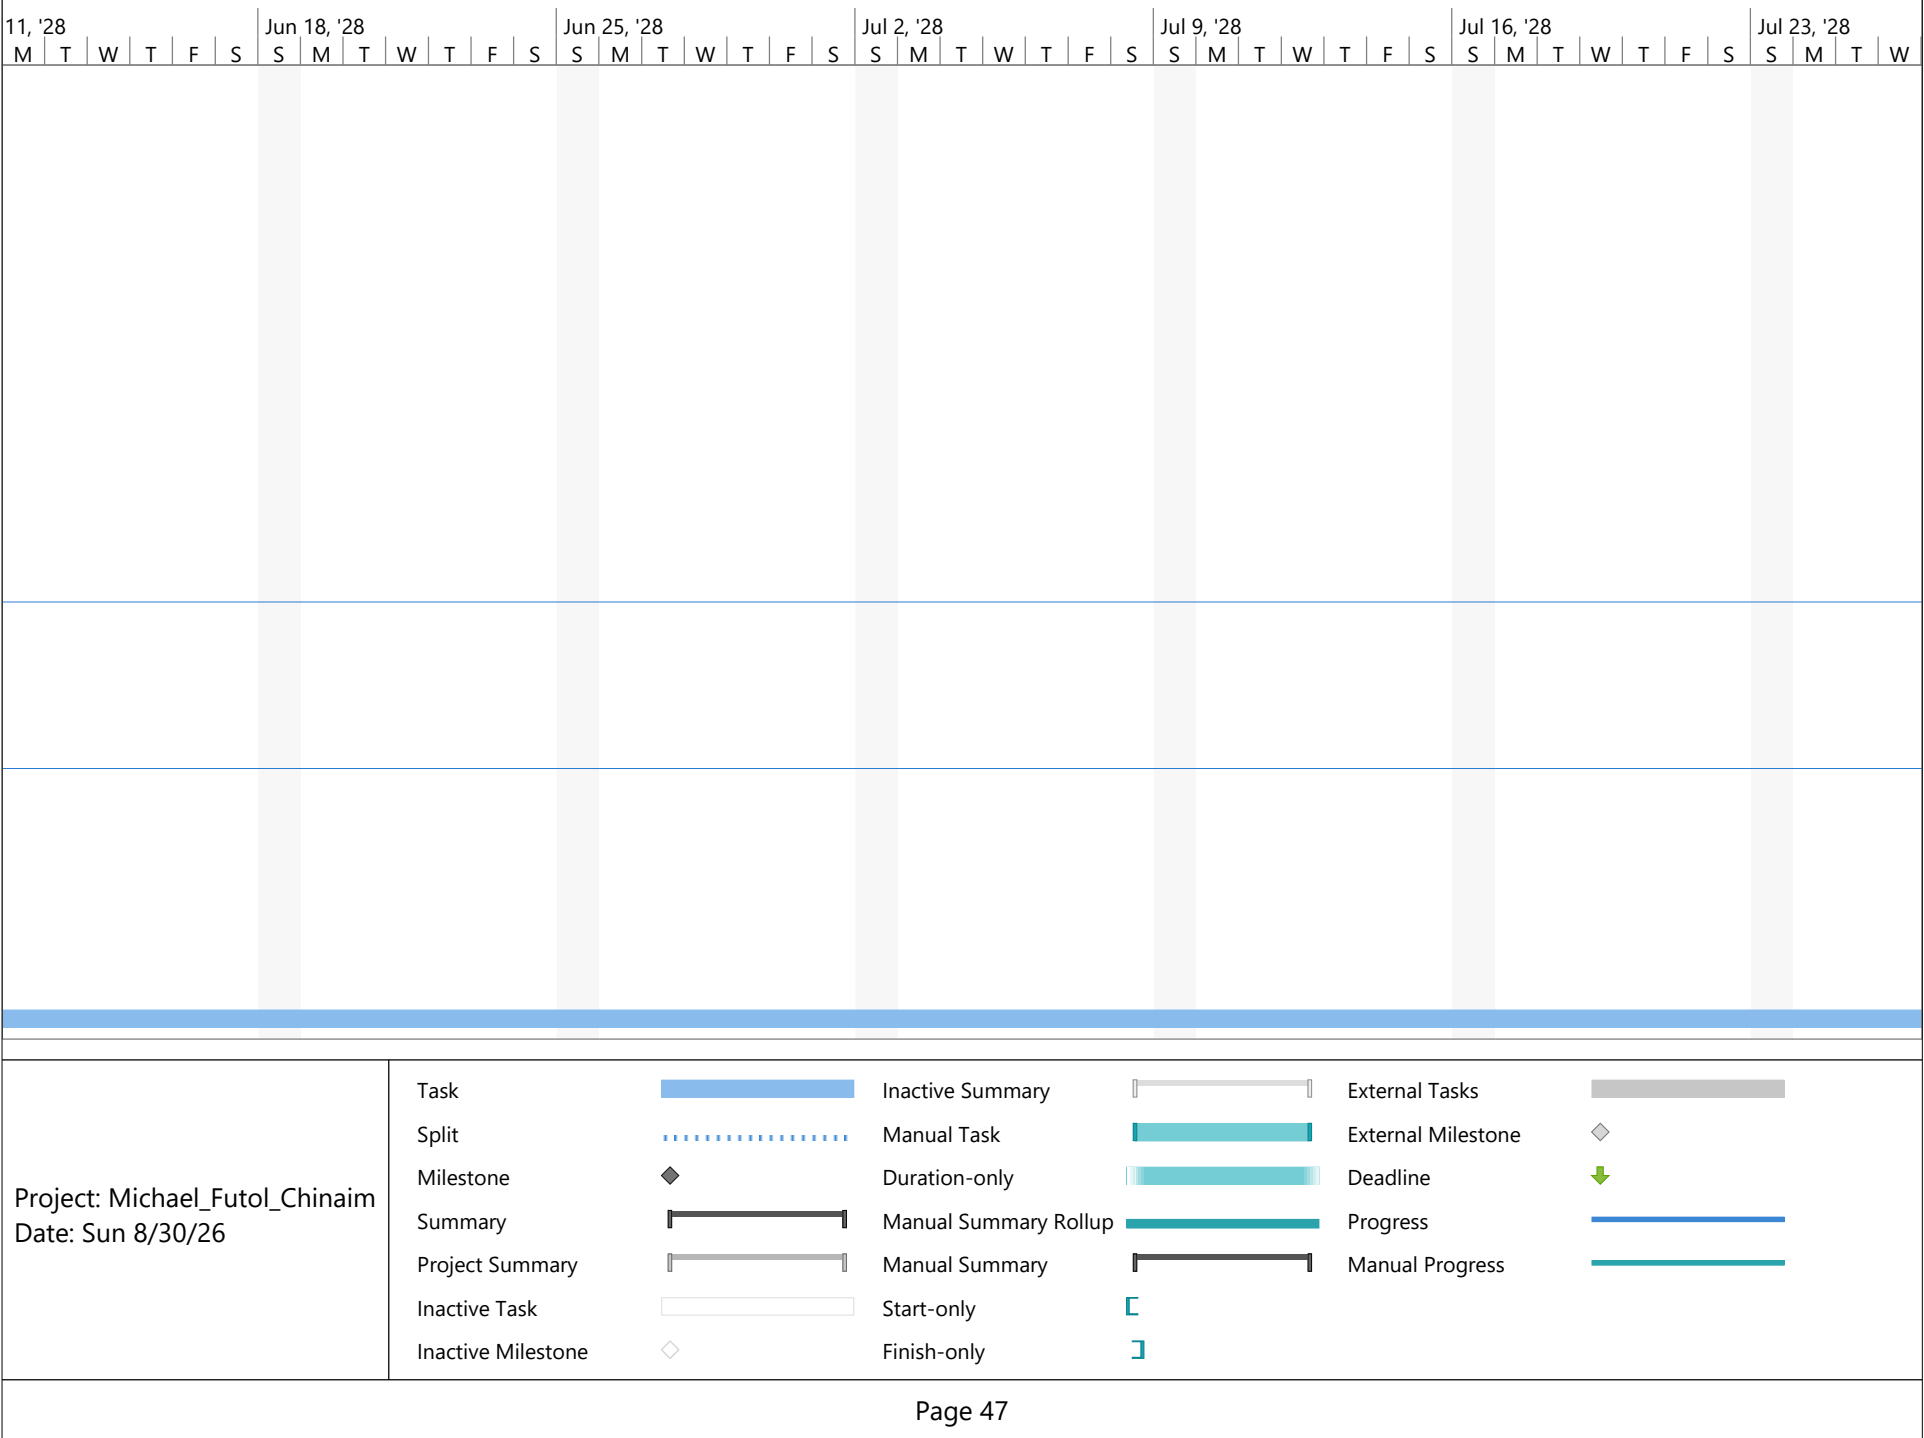


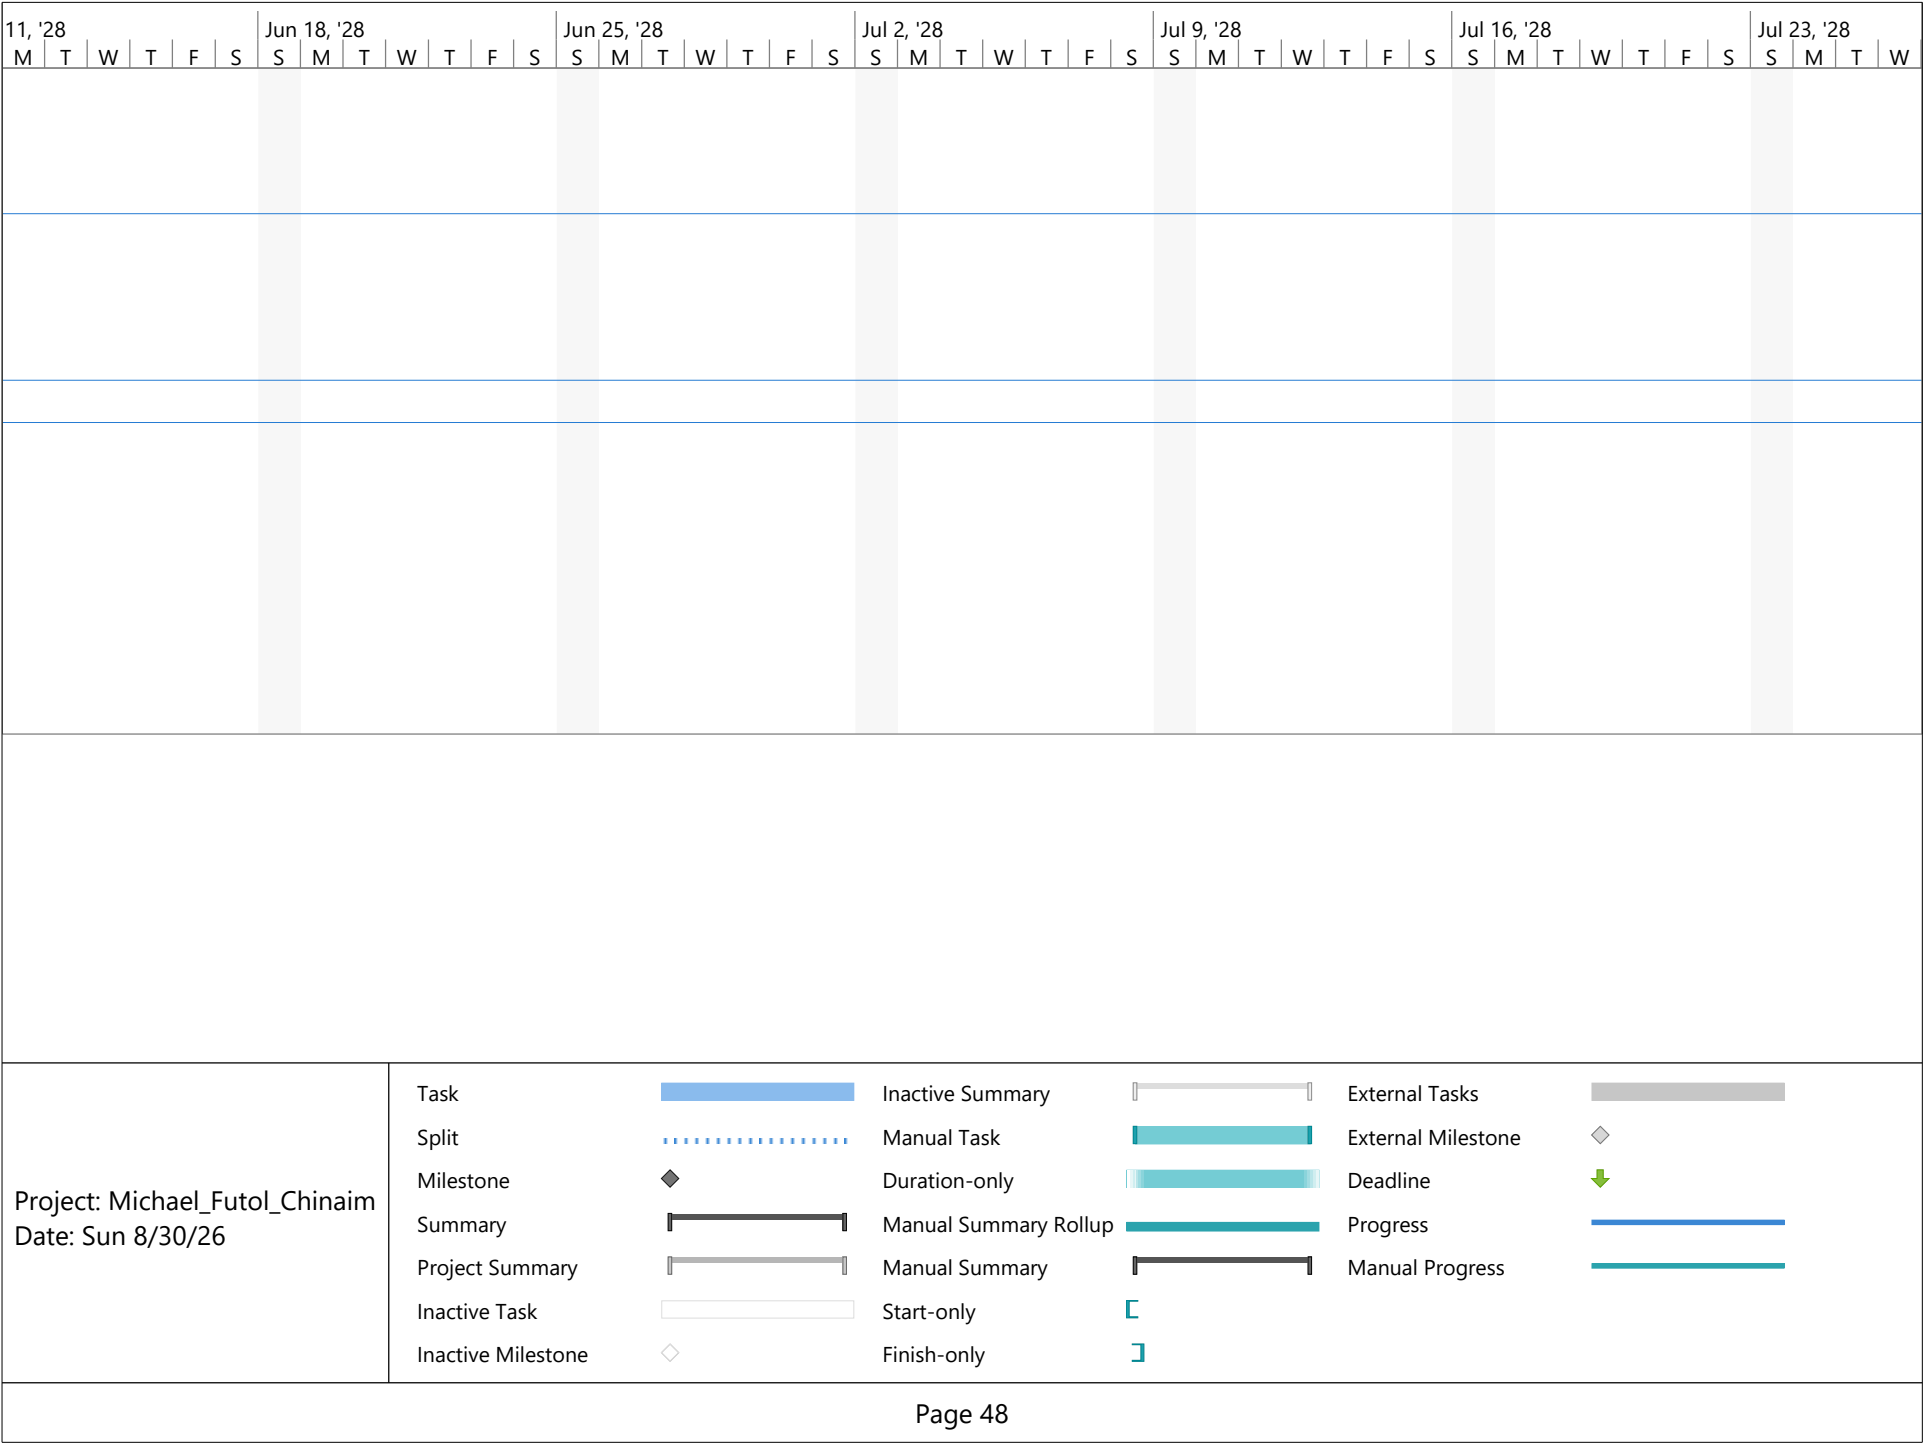

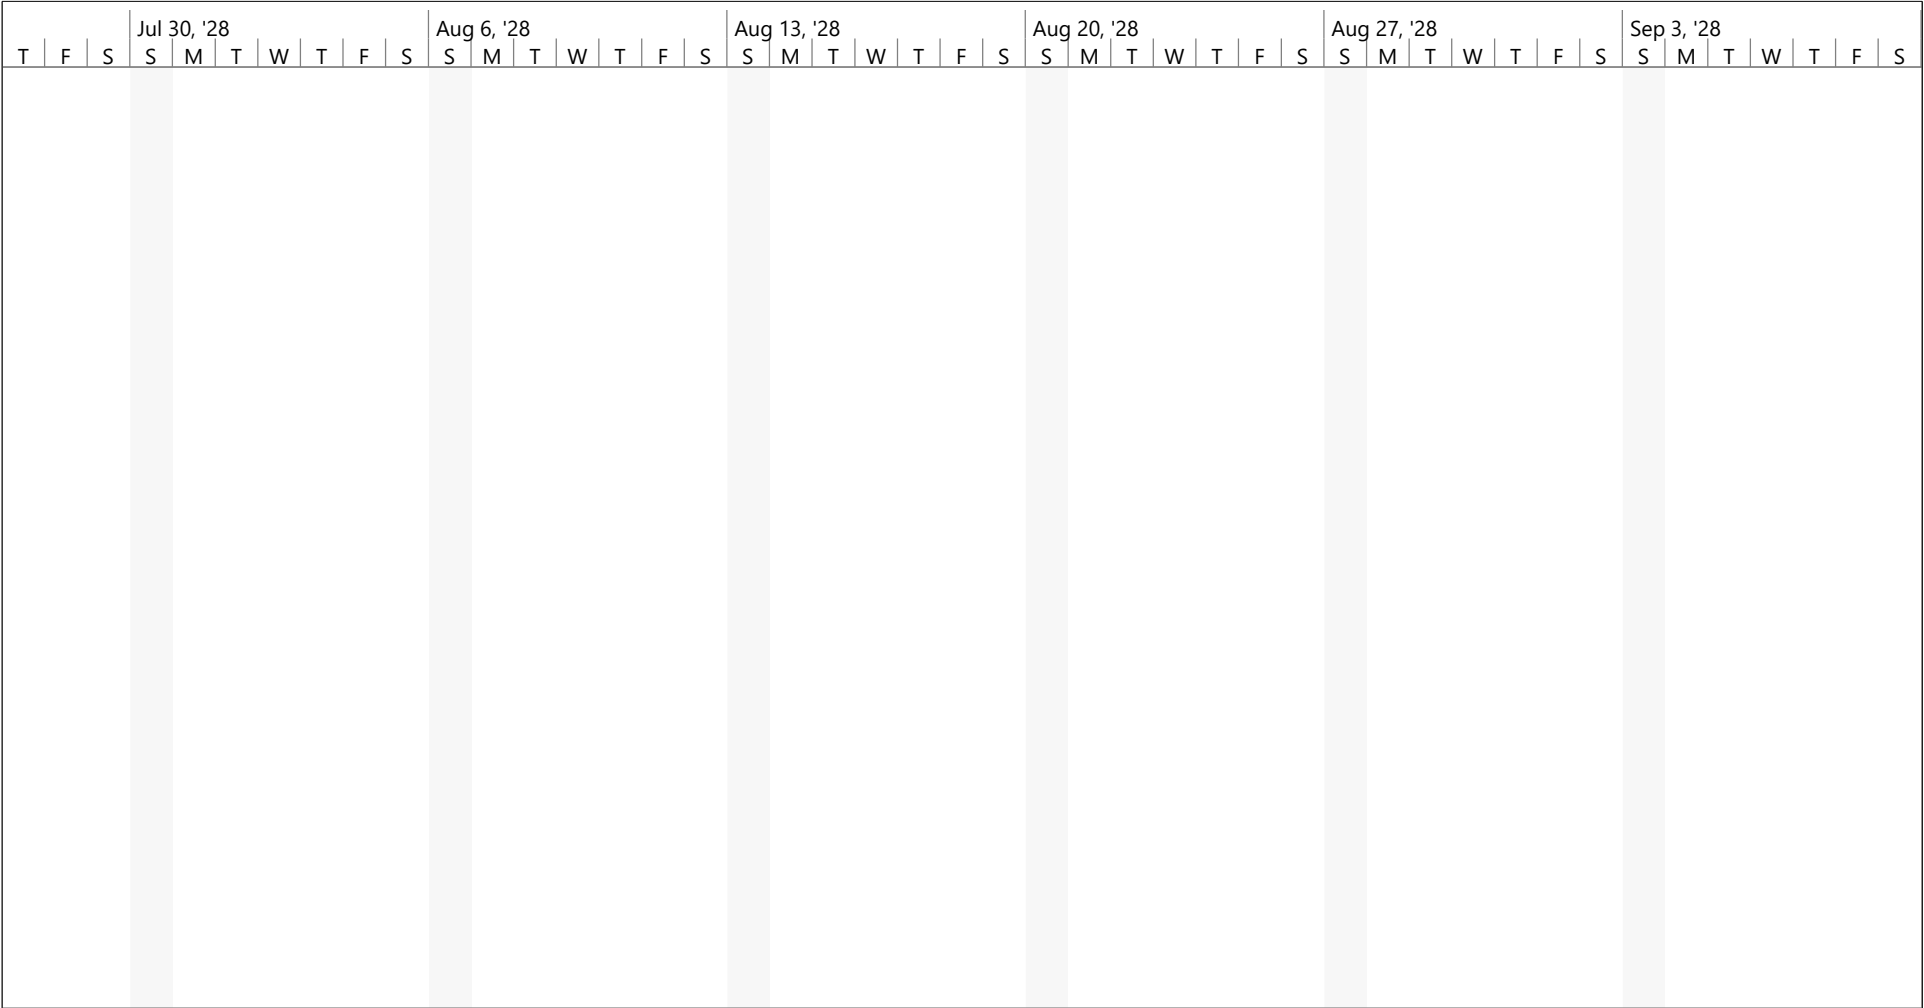


Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

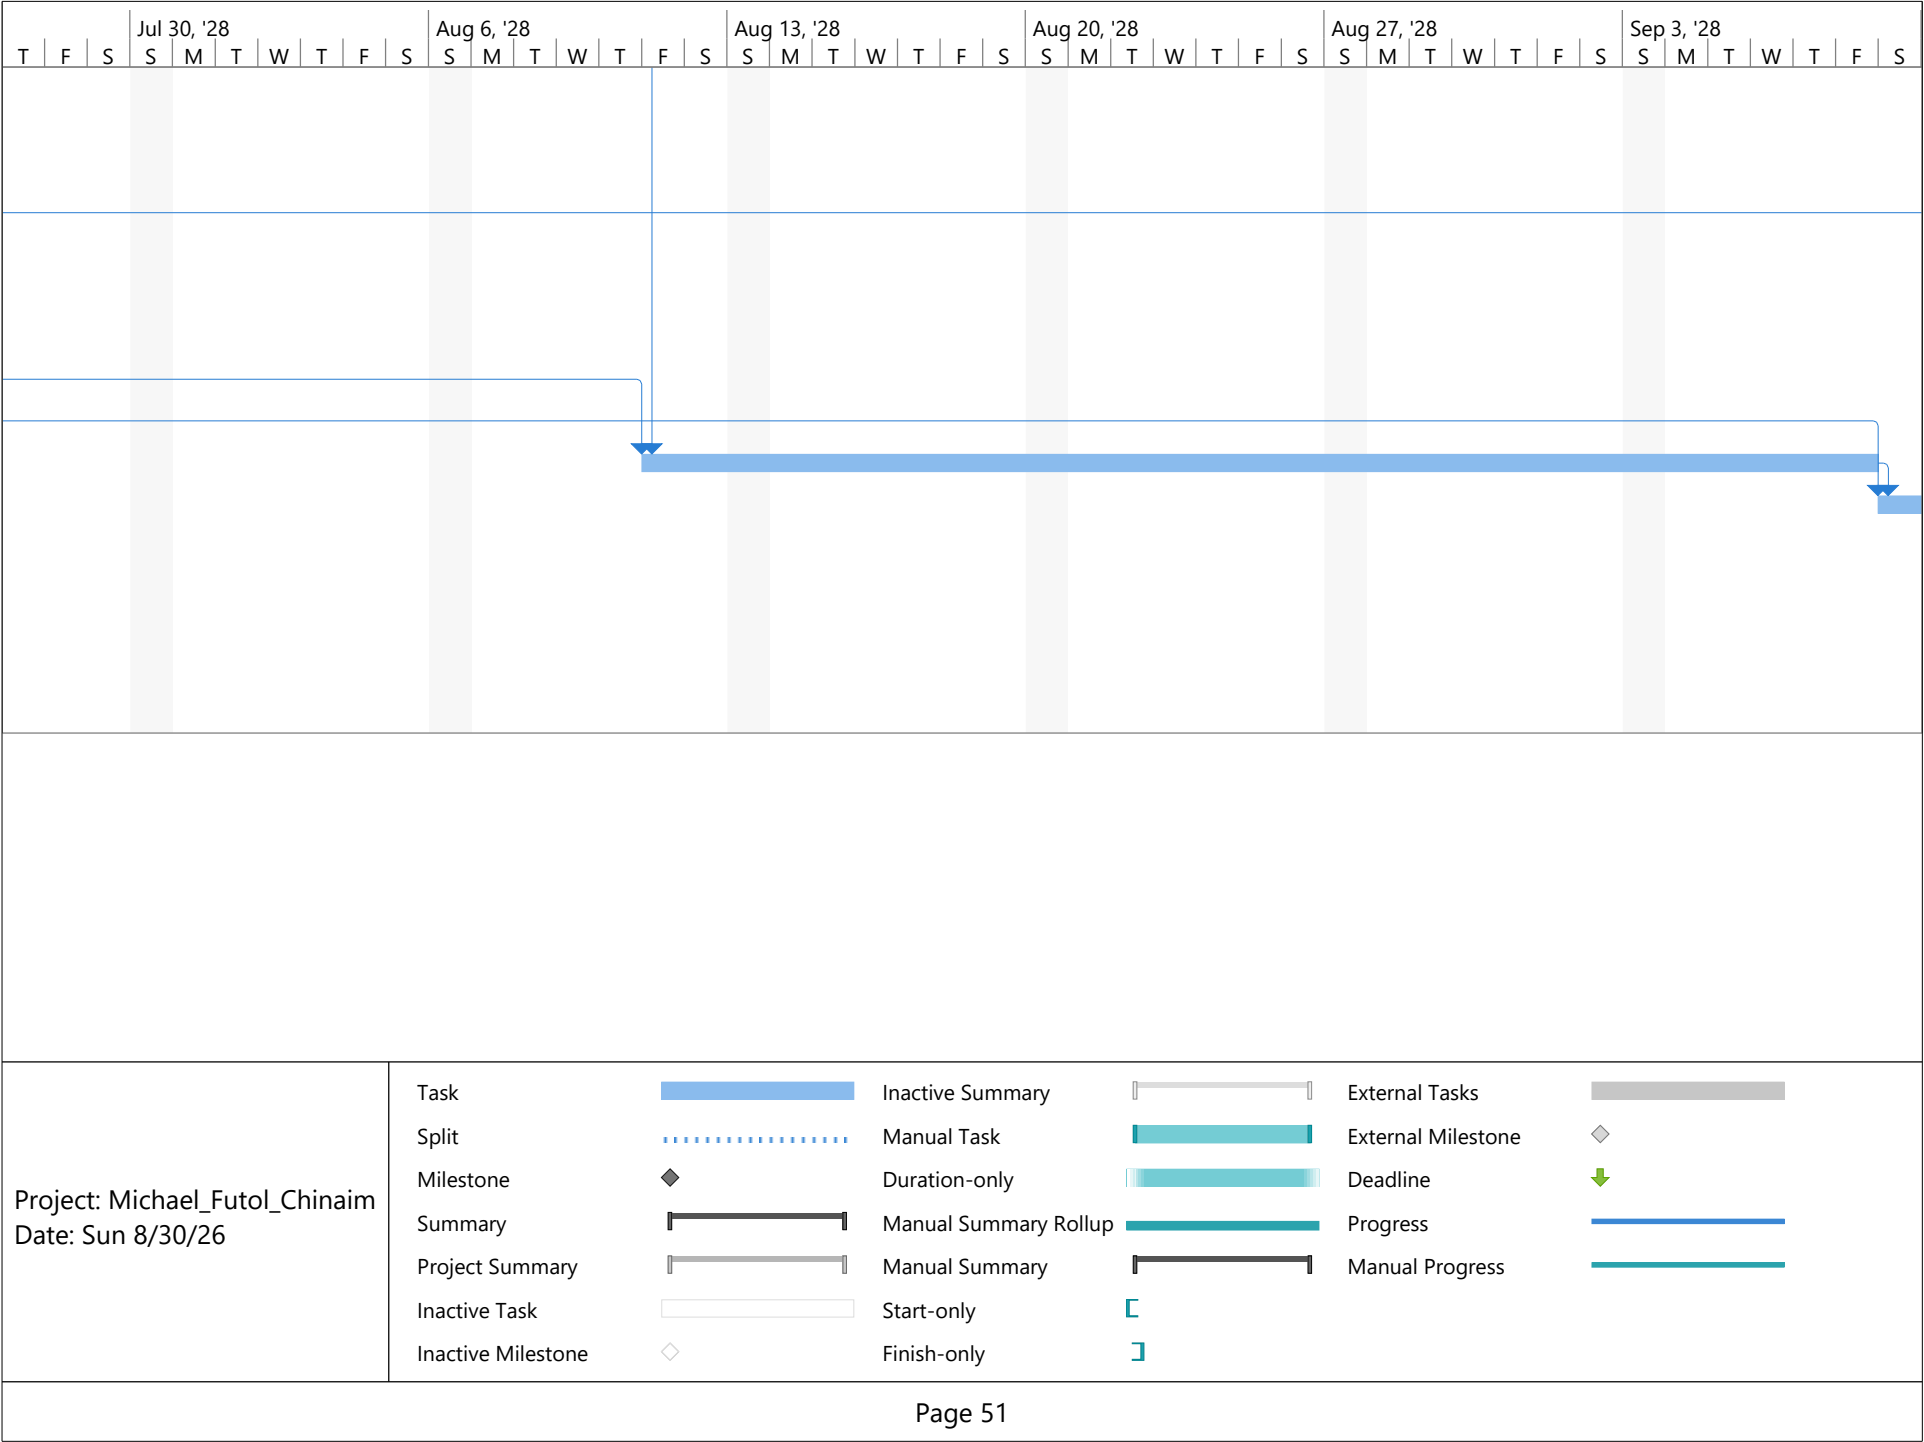

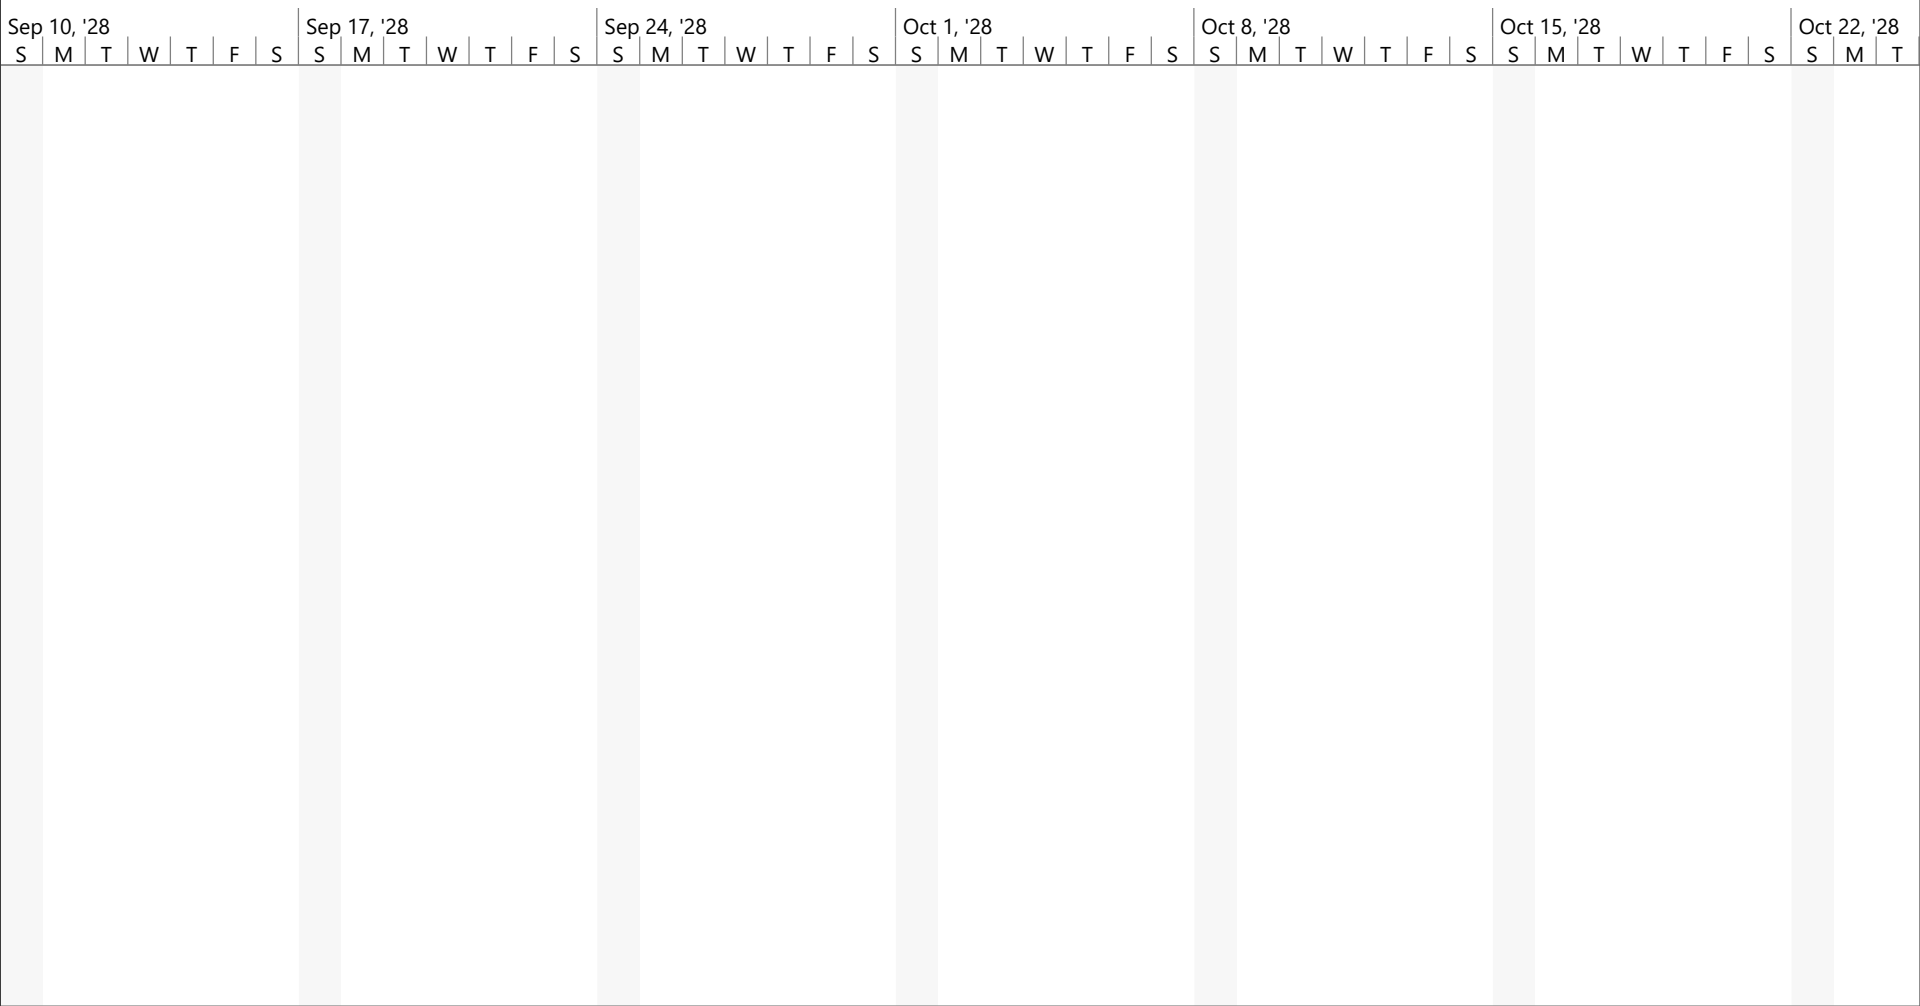

Project: Michael_FutoI_Chinaim
Date: Sun 8/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

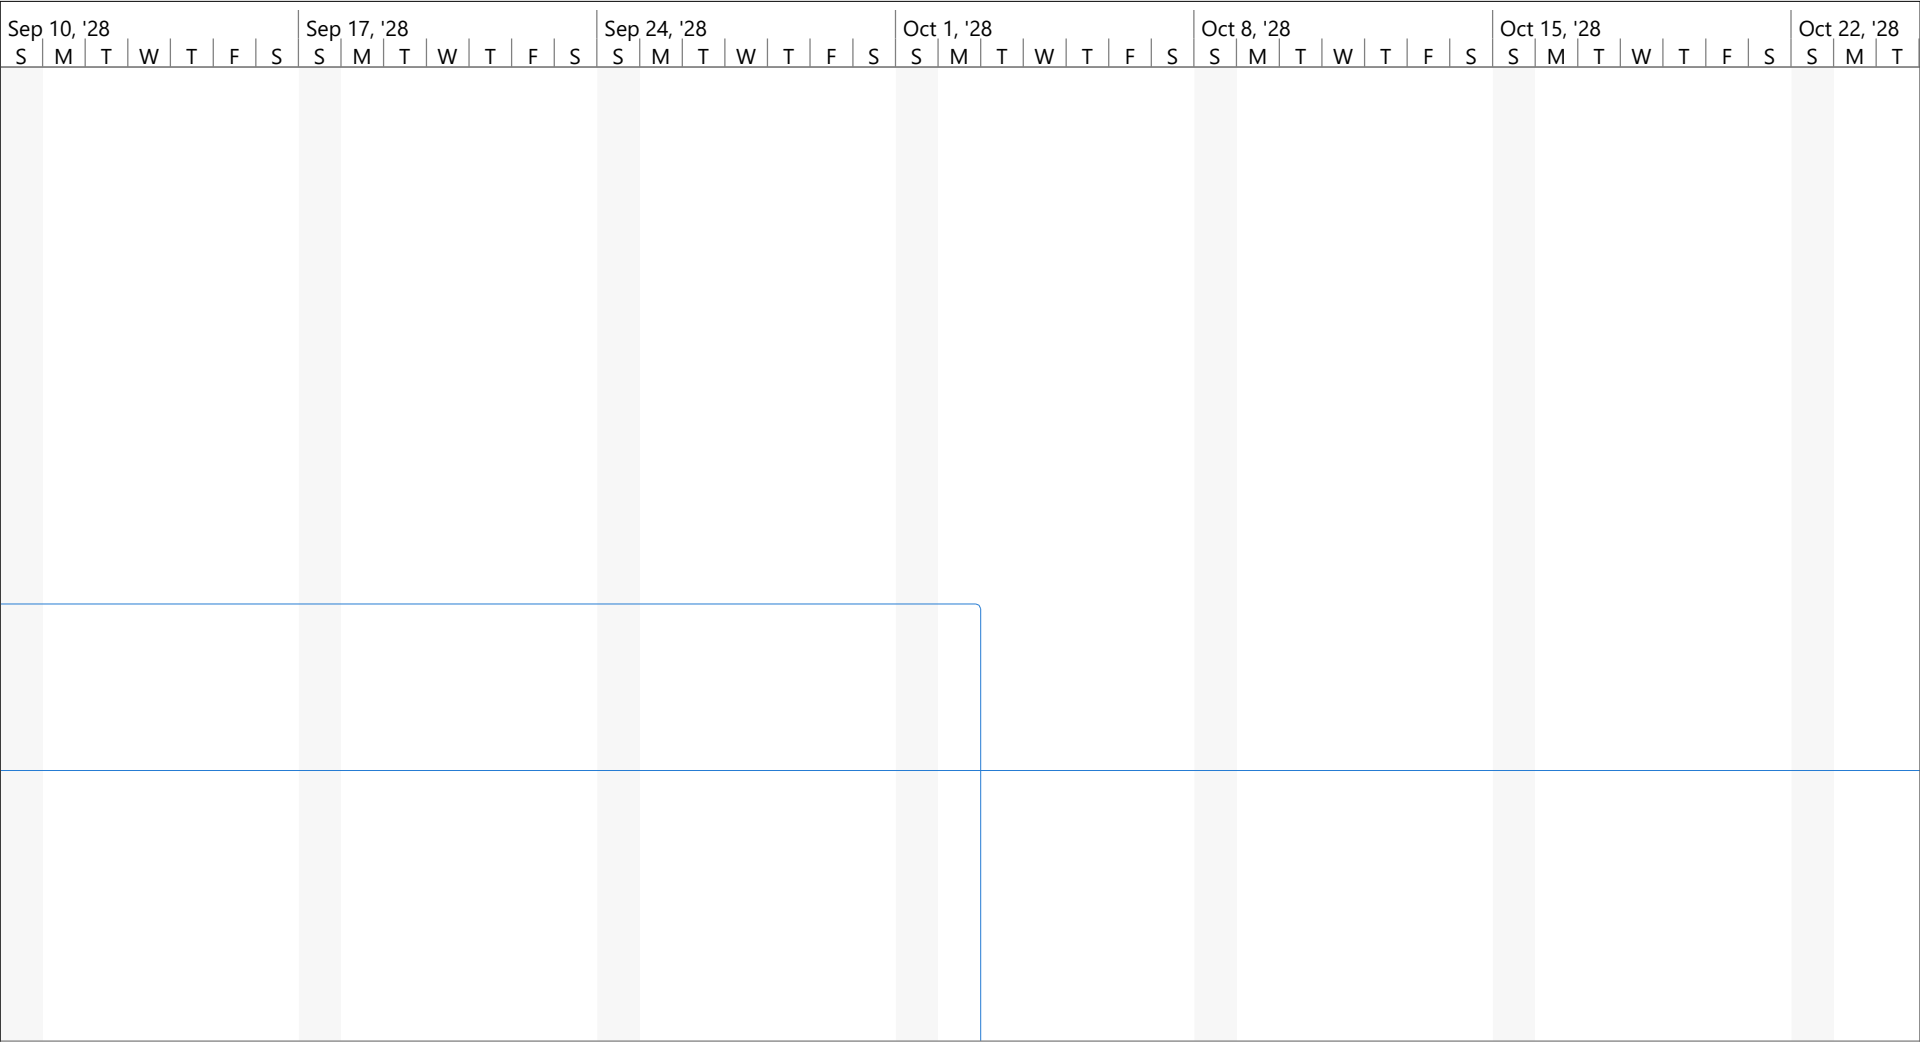

Project: Michael_FutoI_Chinaim
Date: Sun 8/30/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone



Deadline


Progress


Manual Progress


Page 53

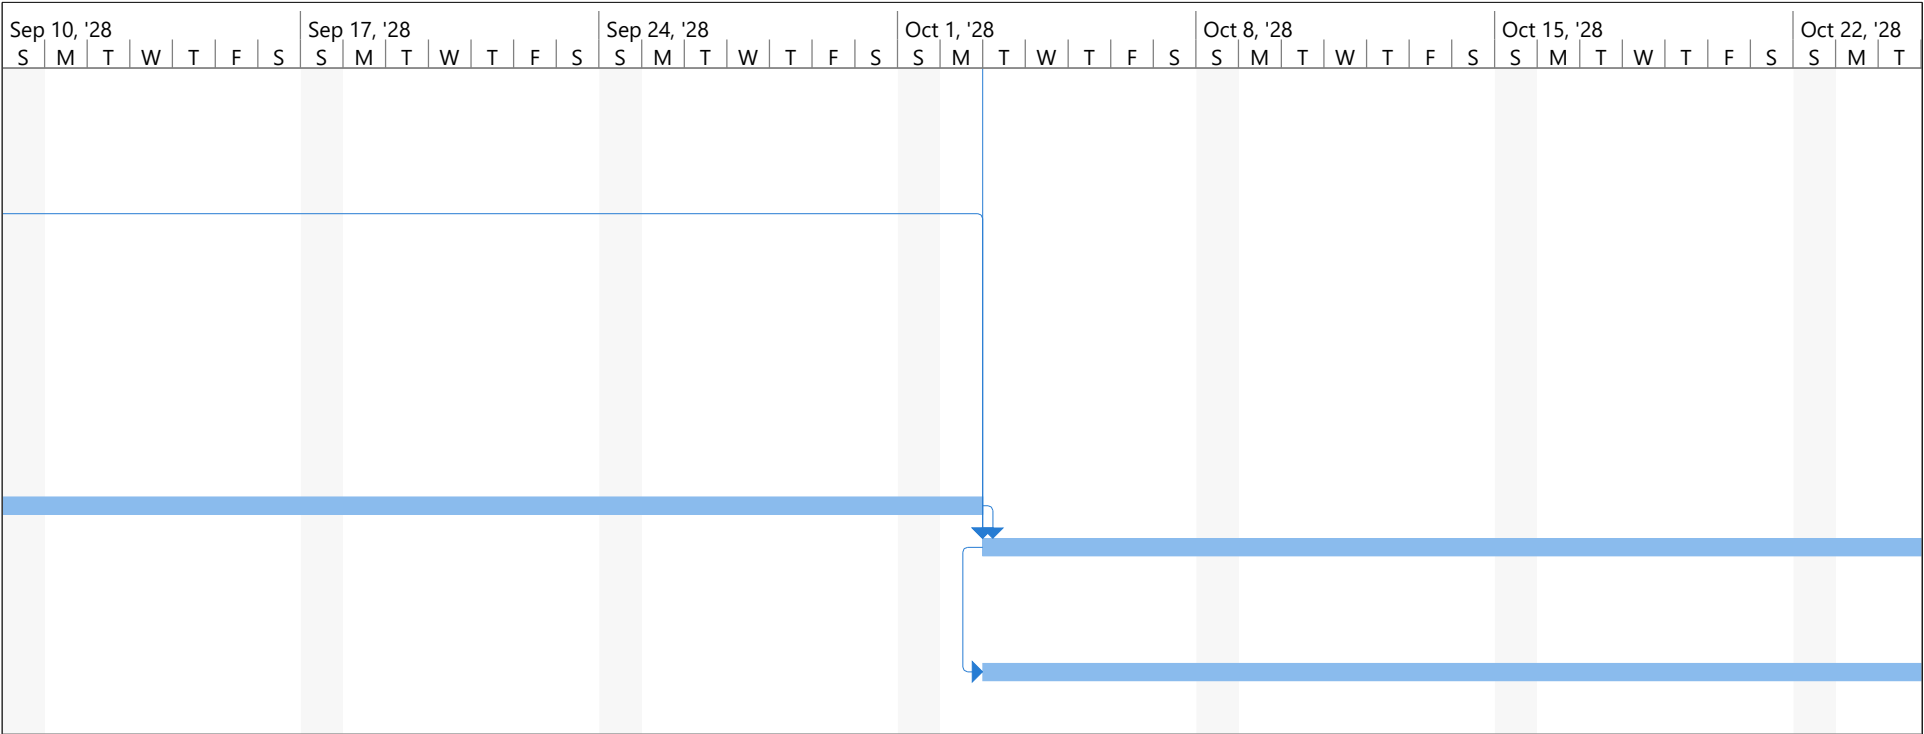


Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

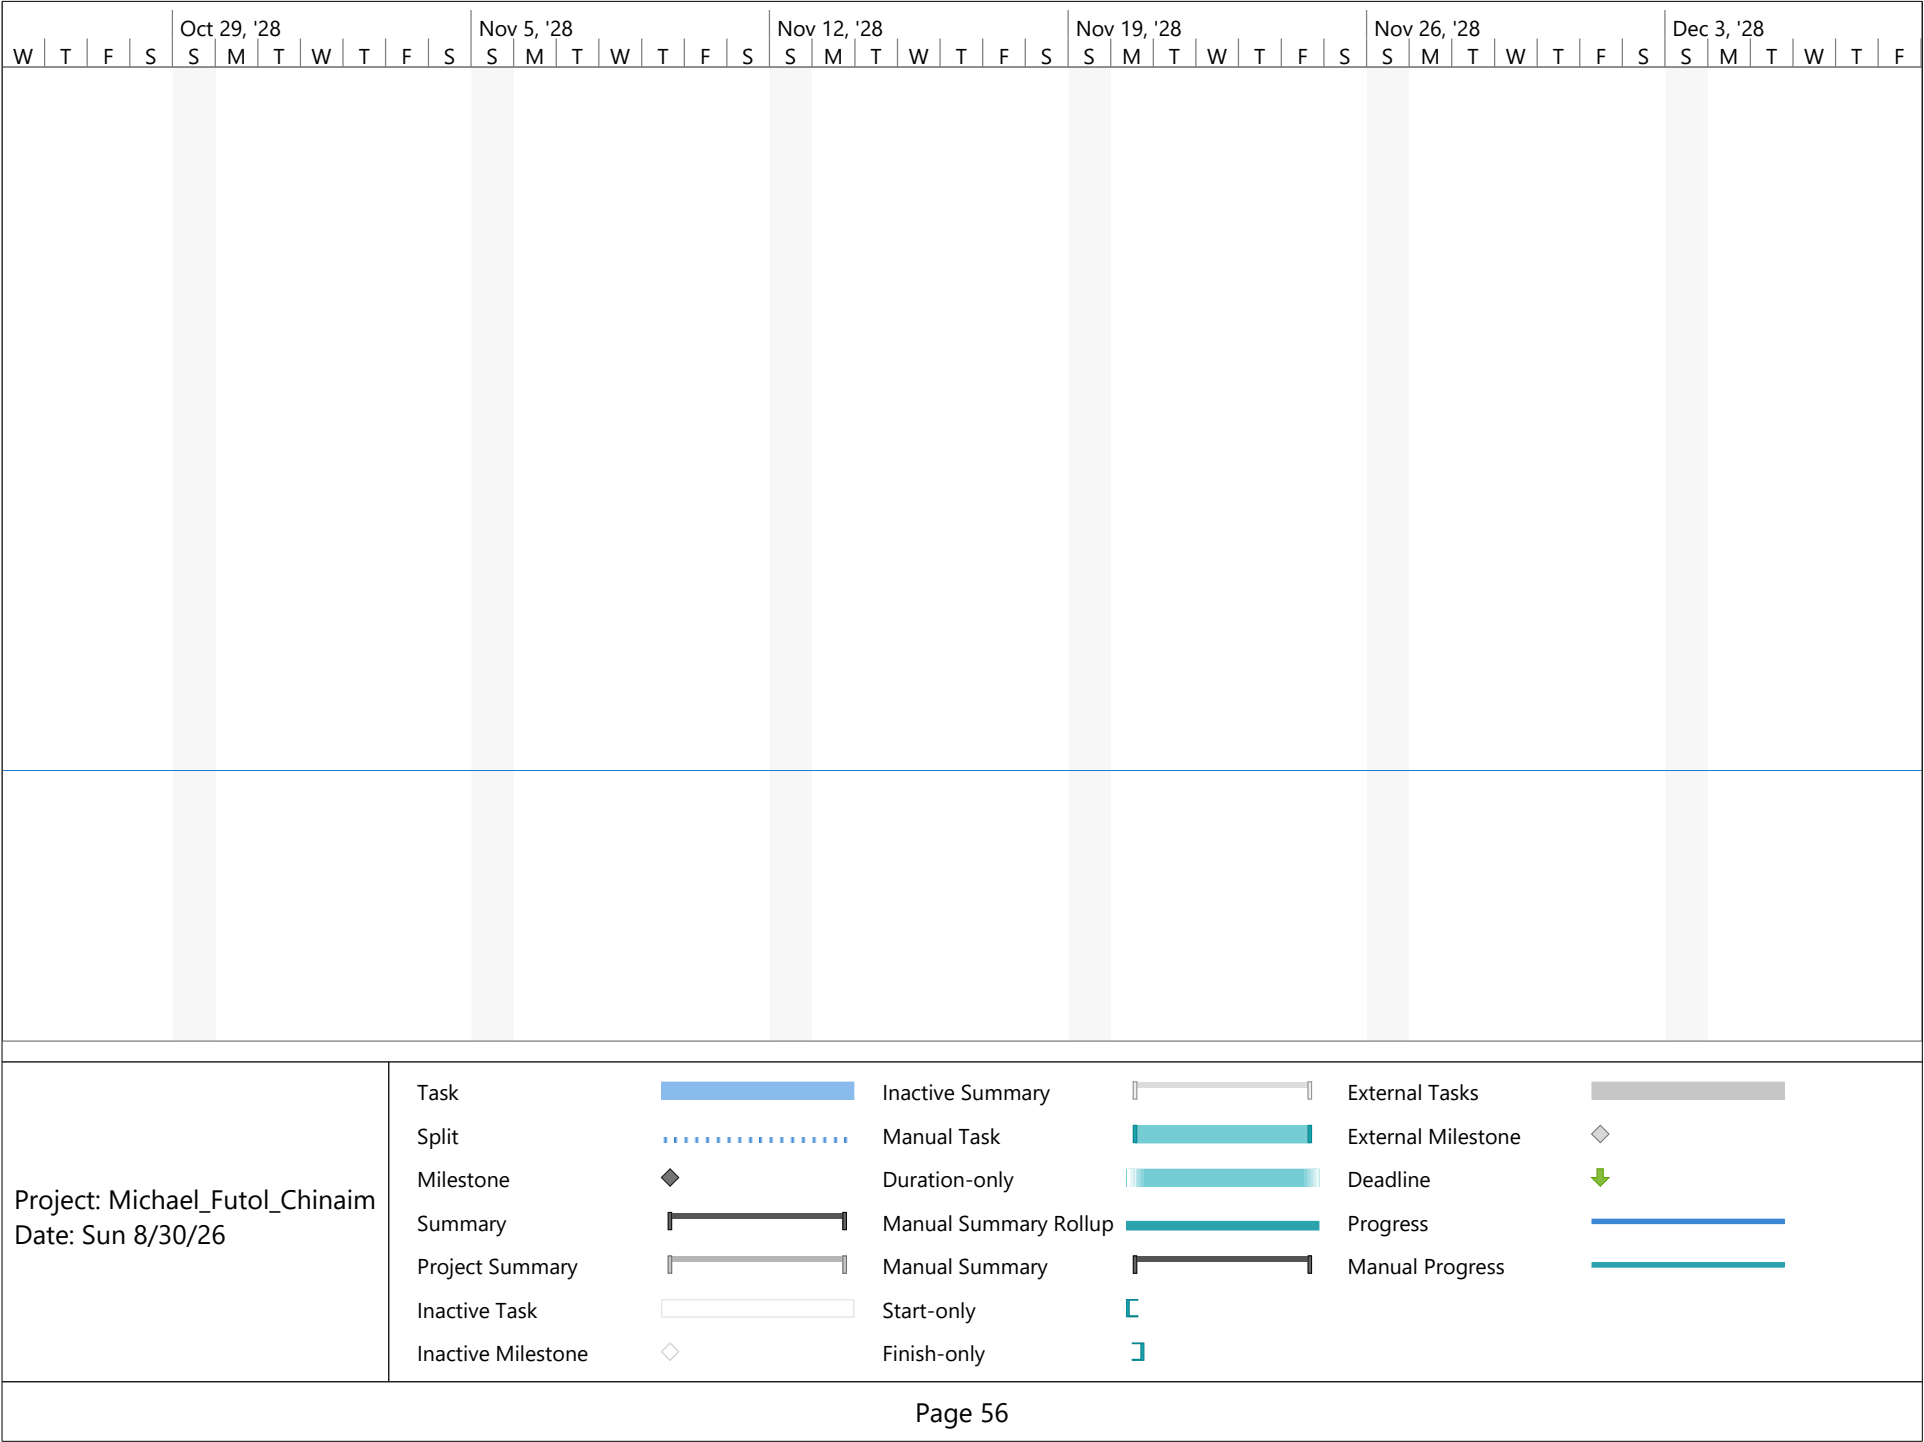

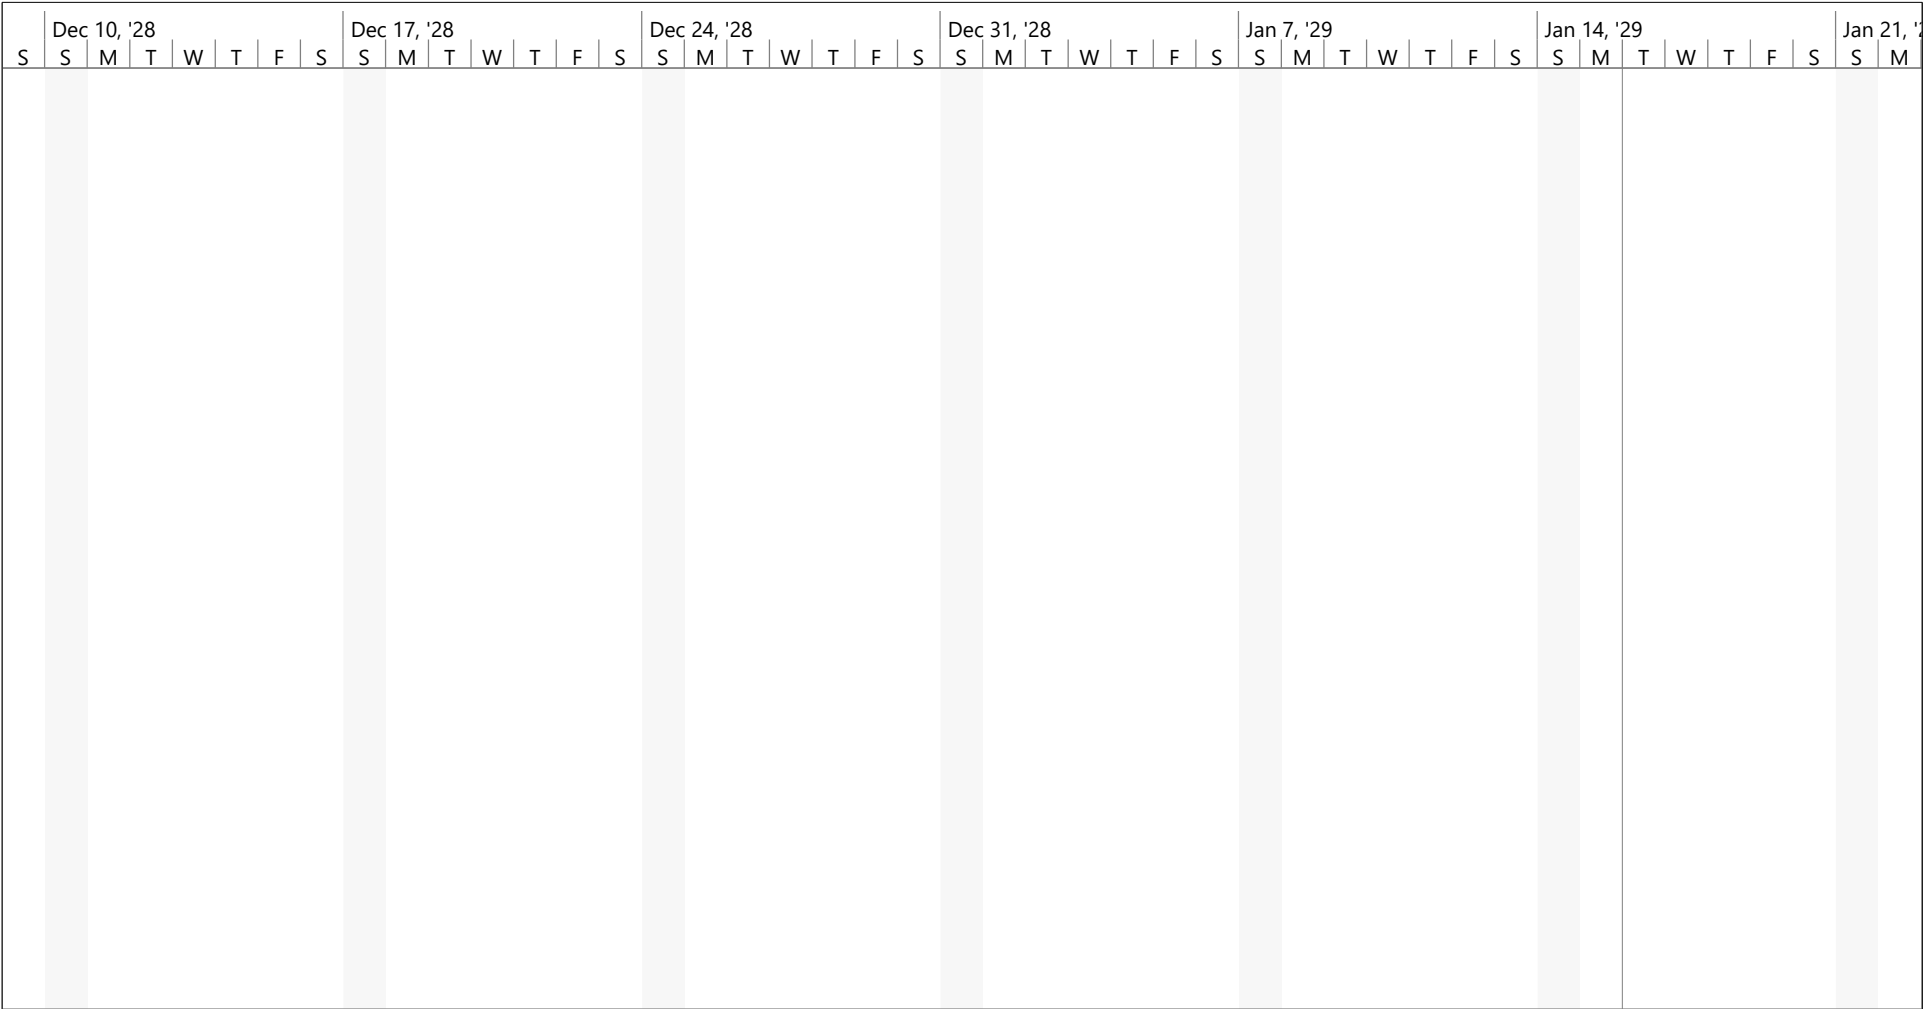

Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

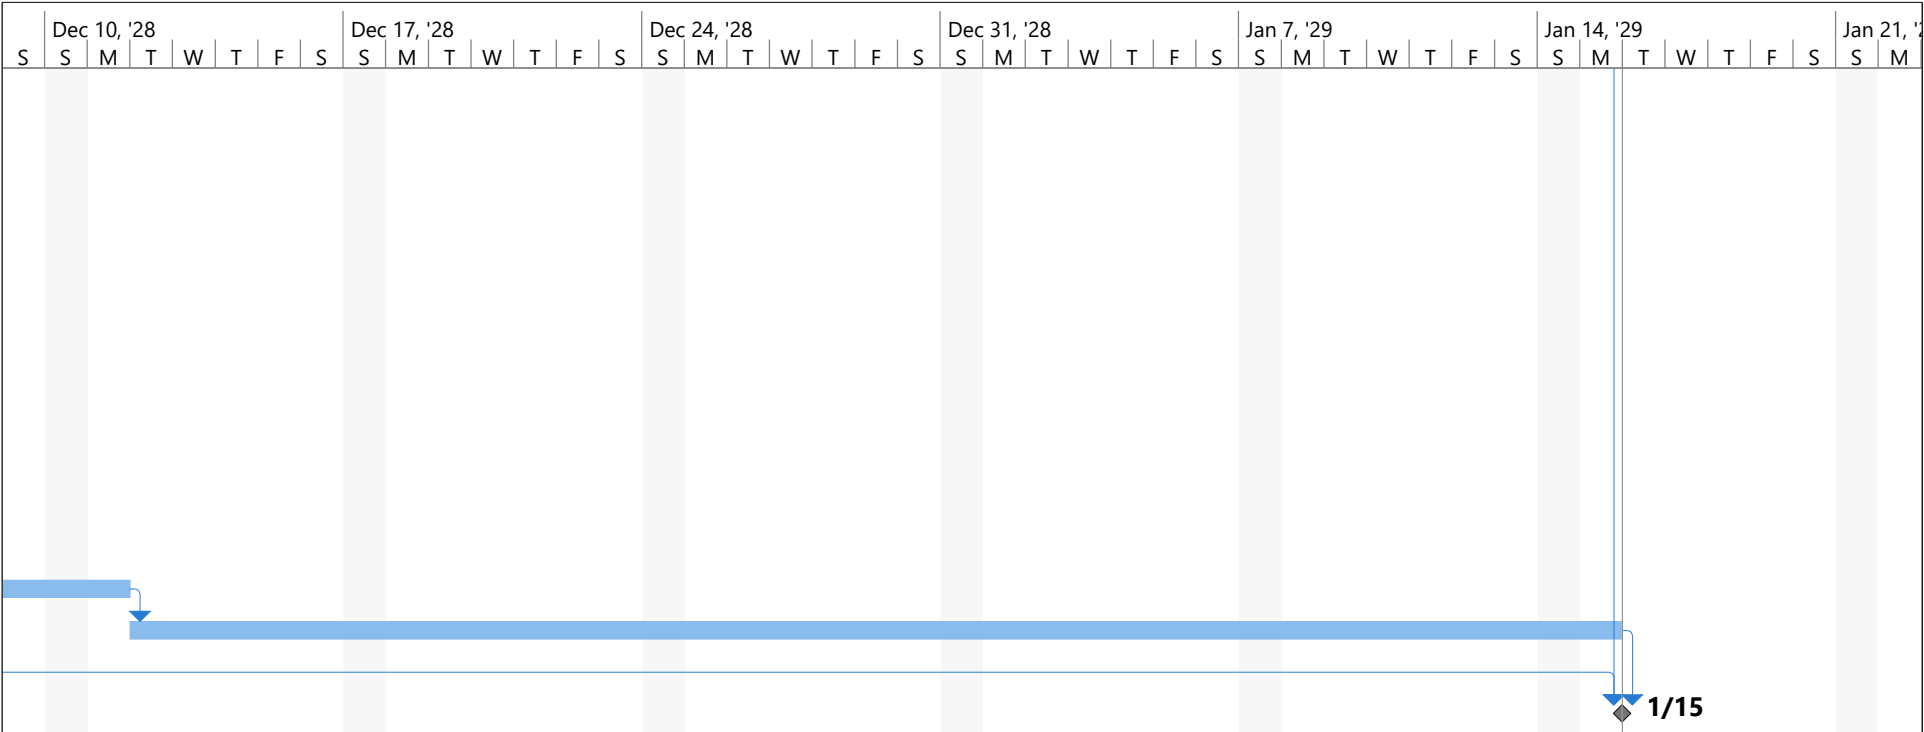

Project: Michael_FutoI_Chinaim Date: Sun 8/30/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
