

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

ID		Task Mode	Task Name	Duration	Start	Finish	30, '26	Sep 6, '26	Sep 13, '26	Sep 20, '26
							M T W T F S	S M T W T F S	S M T W T F S	S M
1			Notice to Proceed	0 days	Tue 9/1/26	Tue 9/1/26	9/1			
2			Mobilization & Temp	20 days	Tue 9/1/26	Wed 9/23/26				
3			Survey / Setting Out	15 days	Mon 9/7/26	Wed 9/23/26				
4			Review IFC Drawings	30 days	Tue 9/1/26	Mon 10/5/26				
5			Method Statements &	45 days	Sat 9/12/26	Tue 11/3/26				
6			Long-Lead M&E Proci	300 days	Wed 11/4/26	Tue 10/19/27				
7			SCADA / Instrumenta	260 days	Wed 11/4/26	Thu 9/2/27				
8			Electrical / Receiving	240 days	Wed 11/4/26	Tue 8/10/27				
9			Site Clearing / Excava	35 days	Thu 9/24/26	Tue 11/3/26				
10			Ground Preparation /	15 days	Wed 11/4/26	Fri 11/20/26				
11			WTP Foundations / B	60 days	Sat 11/21/26	Fri 1/29/27				
12			Mixing / Flocculation	70 days	Sat 1/30/27	Wed 4/21/27				
13			Sedimentation Basin	100 days	Tue 2/23/27	Fri 6/18/27				
14			Rapid Sand Filter Stru	90 days	Sat 6/19/27	Fri 10/1/27				
15			Internal Channels / Pi	45 days	Sat 10/2/27	Tue 11/23/27				
16			Waterproofing / Prot	30 days	Wed 11/24/27	Tue 12/28/27				
17			Hydrostatic / Structur	14 days	Wed 12/29/27	Thu 1/13/28				
18			10,000 m³ Reservoir f	40 days	Thu 9/24/26	Mon 11/9/26				
19			Reservoir Foundation	60 days	Tue 11/10/26	Mon 1/18/27				
20			Reservoir Walls / Col	100 days	Tue 1/19/27	Fri 5/14/27				
21			Reservoir Roof Slab	60 days	Sat 5/15/27	Fri 7/23/27				

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

ID		Task Mode	Task Name	Duration	Start	Finish	30, '26					Sep 6, '26					Sep 13, '26					Sep 20					
							M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T					
22			Reservoir Waterproof	30 days	Sat 7/24/27	Fri 8/27/27																					
23			Reservoir Hydrostatic	14 days	Sat 8/28/27	Mon 9/13/27																					
24			Pump Room Civil / Str	75 days	Tue 12/15/26	Thu 3/11/27																					
25			Chemical Building Civ	90 days	Sat 12/26/26	Fri 4/9/27																					
26			Administration & Lab	120 days	Wed 11/4/26	Tue 3/23/27																					
27			Building MEP / Archit	70 days	Wed 3/24/27	Sat 6/12/27																					
28			Process Piping Install	100 days	Fri 1/14/28	Tue 5/9/28																					
29			Pumps & Mechanical	90 days	Wed 10/20/27	Tue 2/1/28																					
30			Chemical Dosing Equi	70 days	Wed 10/20/27	Sat 1/8/28																					
31			Filter Media / Underd	50 days	Fri 1/14/28	Sat 3/11/28																					
32			Electrical Installation	100 days	Wed 8/11/27	Sat 12/4/27																					
33			Instrumentation & SC	90 days	Wed 5/10/28	Tue 8/22/28																					
34			Salakham Site Prepar	40 days	Thu 9/24/26	Mon 11/9/26																					
35			7,100 m³ Reservoir R	180 days	Tue 11/10/26	Mon 6/7/27																					
36			Salakham Pump Room	90 days	Thu 10/29/26	Wed 2/10/27																					
37			Salakham M&E Instal	80 days	Wed 10/20/27	Thu 1/20/28																					
38			22-kV Route Survey /	45 days	Thu 9/24/26	Sat 11/14/26																					
39			Pole / Foundation Wc	100 days	Mon 11/16/27	Thu 3/11/27																					
40			22-kV Line Installati	120 days	Fri 3/12/27	Thu 7/29/27																					
41			Receiving Equipment	30 days	Wed 8/11/27	Tue 9/14/27																					
42			Mechanical Pre-Comr	25 days	Wed 5/10/28	Wed 6/7/28																					

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp																													
ID		Task Mode	Task Name	Duration	Start	Finish	30, '26							Sep 6, '26							Sep 13, '26							Sep 20, '26	
							M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	
43			Electrical / I&C Pre-Commissioning	25 days	Wed 8/23/28	Wed 9/20/28																							
44			Dry Commissioning	20 days	Thu 9/21/28	Fri 10/13/28																							
45			Wet Commissioning / Performance	30 days	Sat 10/14/28	Fri 11/17/28																							
46			Water / Rectification	30 days	Sat 11/18/28	Fri 12/22/28																							
47			Punch List / Rectification	30 days	Sat 12/23/28	Fri 1/26/29																							
48			Training / O&M Documentation	20 days	Sat 10/14/28	Mon 11/6/28																							
49			Taking Over / Completion	0 days	Fri 1/26/29	Fri 1/26/29																							

Critical

Finish-only

Manual Summary

Critical Split

Duration-only

Project Summary

Critical Progress

Baseline

External Tasks

Task

Baseline Split

External Milestone

Split

Baseline Milestone

Inactive Task

Task Progress

Milestone

Inactive Milestone

Manual Task

Summary Progress

Inactive Summary


Start-only

Summary

Deadline

Page 3

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

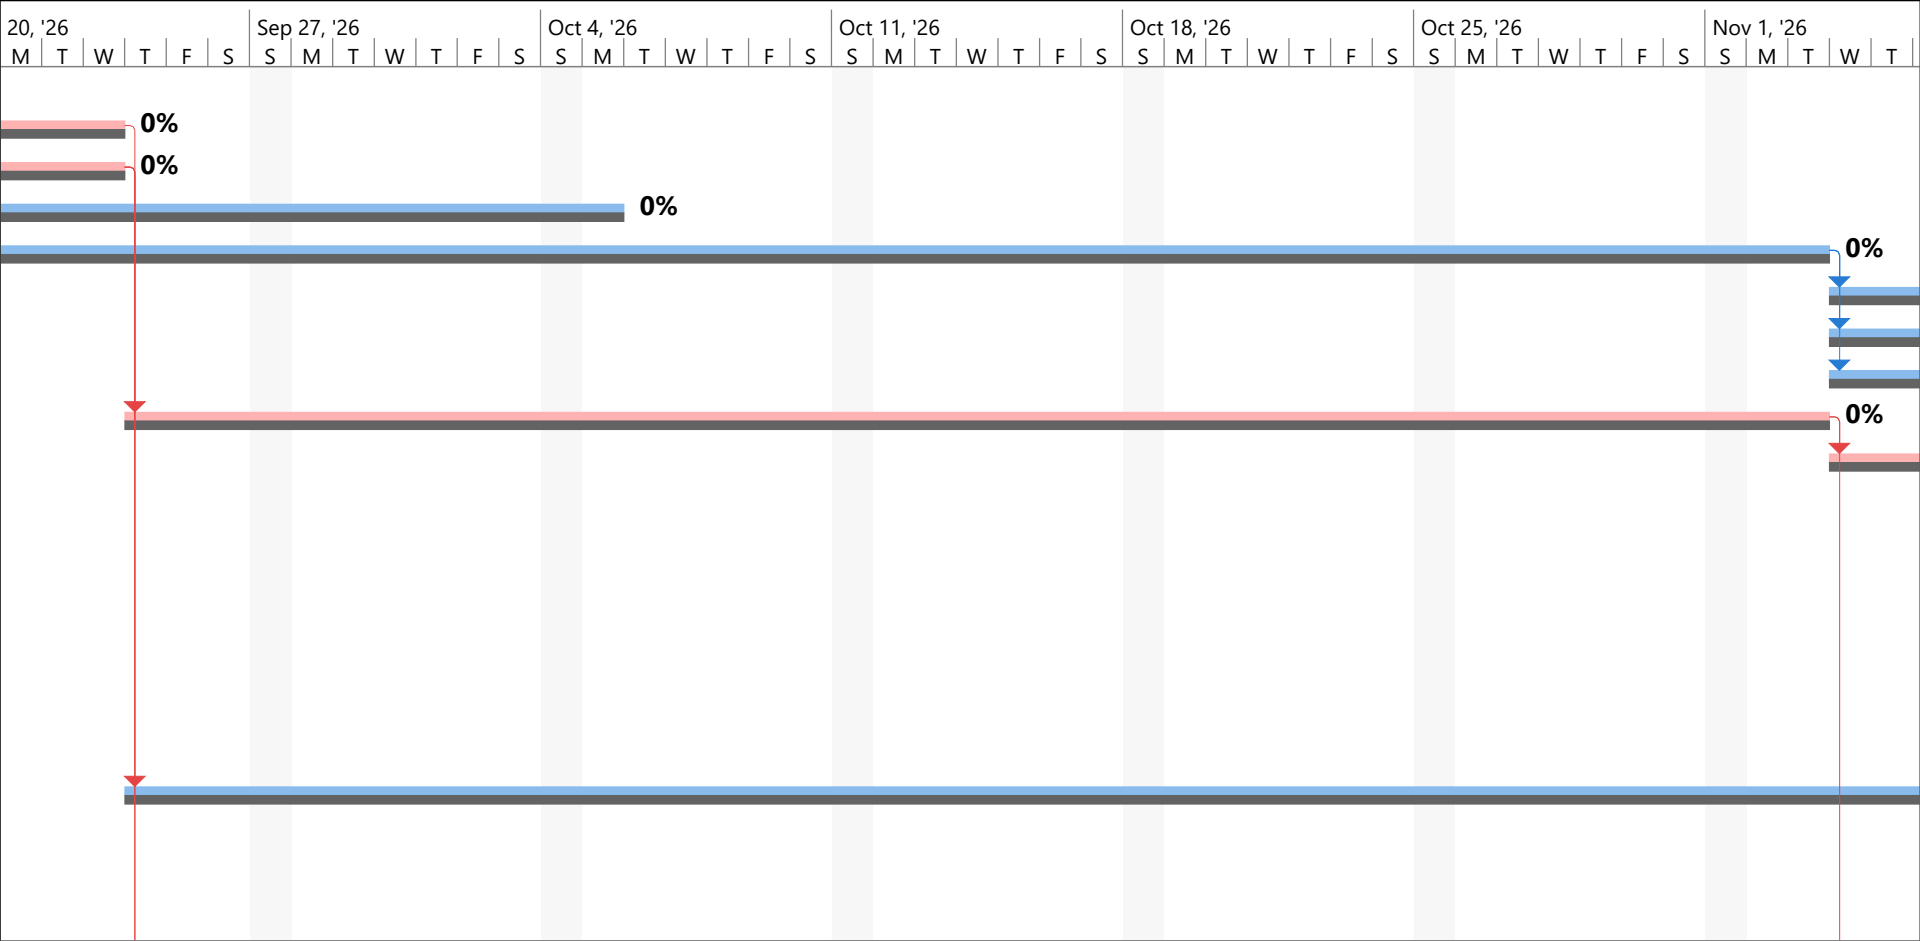

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

20, '26
M T W T F S

Sep 27, '26
S M T W T F S

Oct 4, '26
S M T W T F S

Oct 11, '26
S M T W T F S

Oct 18, '26
S M T W T F S

Oct 25, '26
S M T W T F S

Nov 1, '26
S M T W T

Legend:

Task Type	Symbol	Task Type	Symbol	Task Type	Symbol
Critical	Red solid line	Finish-only	Blue square	Manual Summary	Black line with square
Critical Split	Red dotted line	Duration-only	Teal line	Project Summary	Grey line with square
Critical Progress	Red solid line	Baseline	Black line	External Tasks	Grey line
Task	Blue solid line	Baseline Split	Black dotted line	External Milestone	Grey diamond
Split	Blue dotted line	Baseline Milestone	Black diamond	Inactive Task	Grey line
Task Progress	Blue solid line	Milestone	Black diamond	Inactive Milestone	Grey diamond
Manual Task	Teal line	Summary Progress	Black line	Inactive Summary	Grey line with square
Start-only	Blue square	Summary	Black line with square	Deadline	Green arrow


Page 5

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

20, '26							Sep 27, '26							Oct 4, '26							Oct 11, '26							Oct 18, '26							Oct 25, '26							Nov 1, '26						
M	T	W	T	F	S		S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T		


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

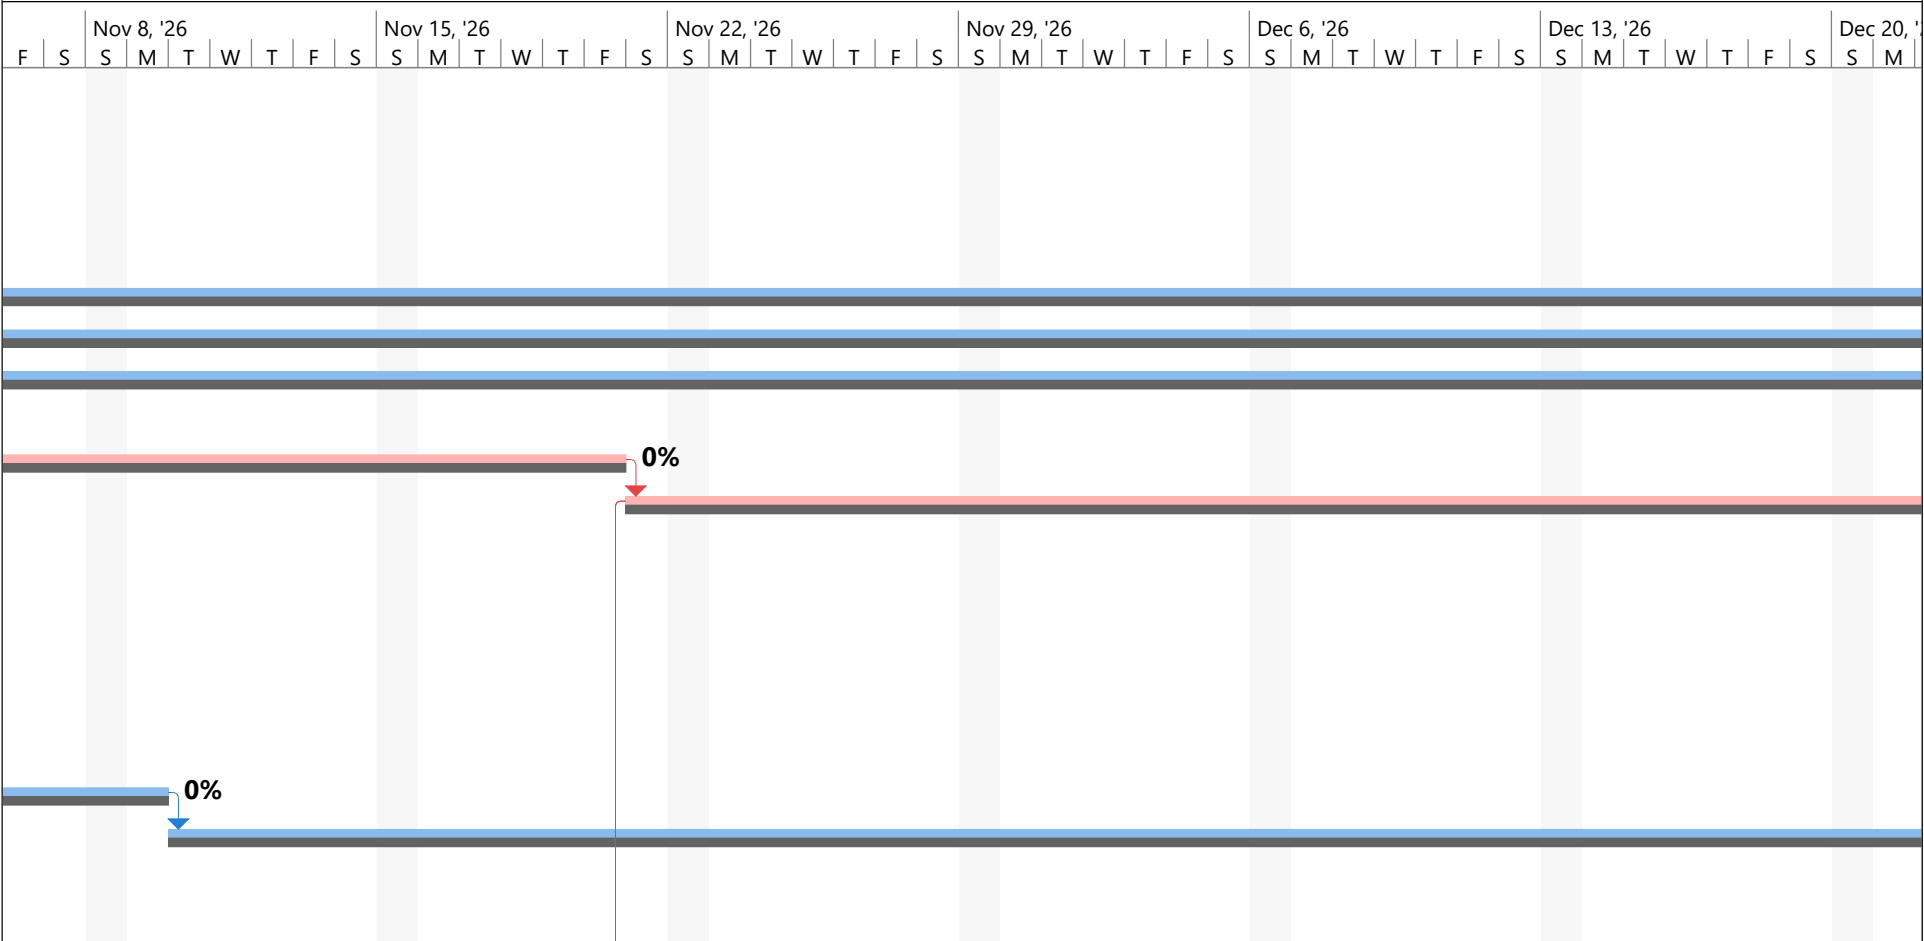

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	


Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

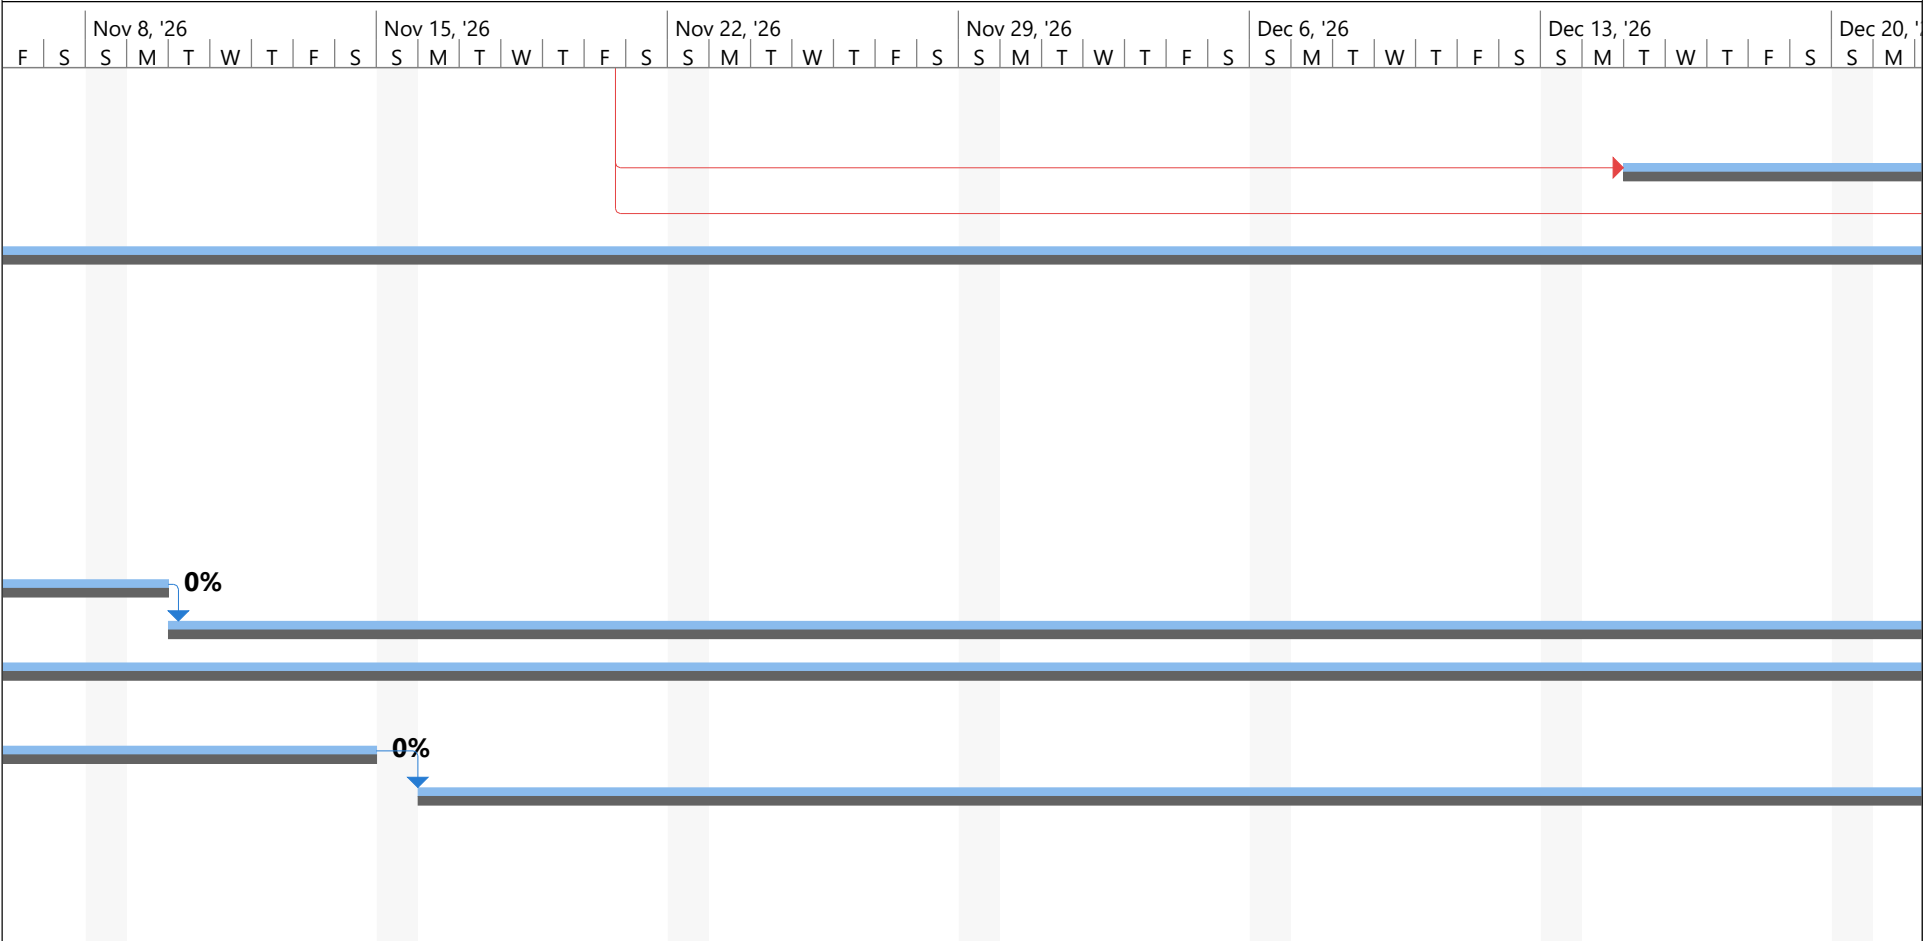

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	


[illegible]

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

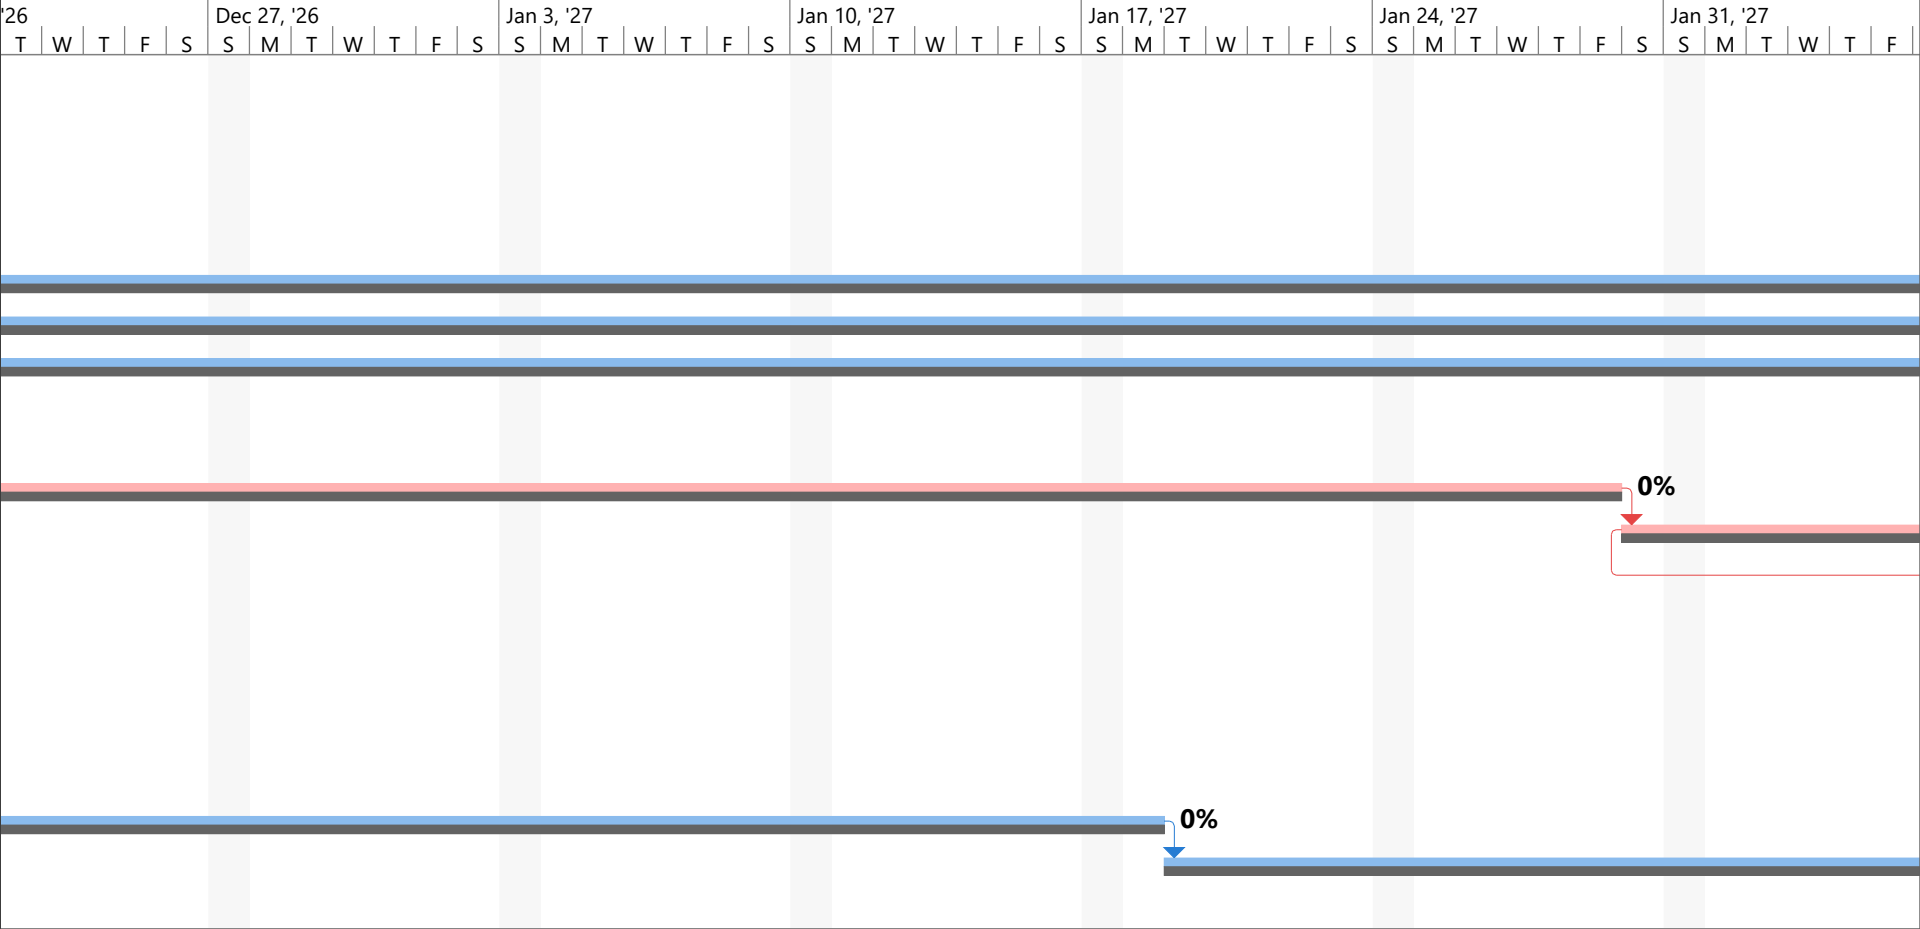

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

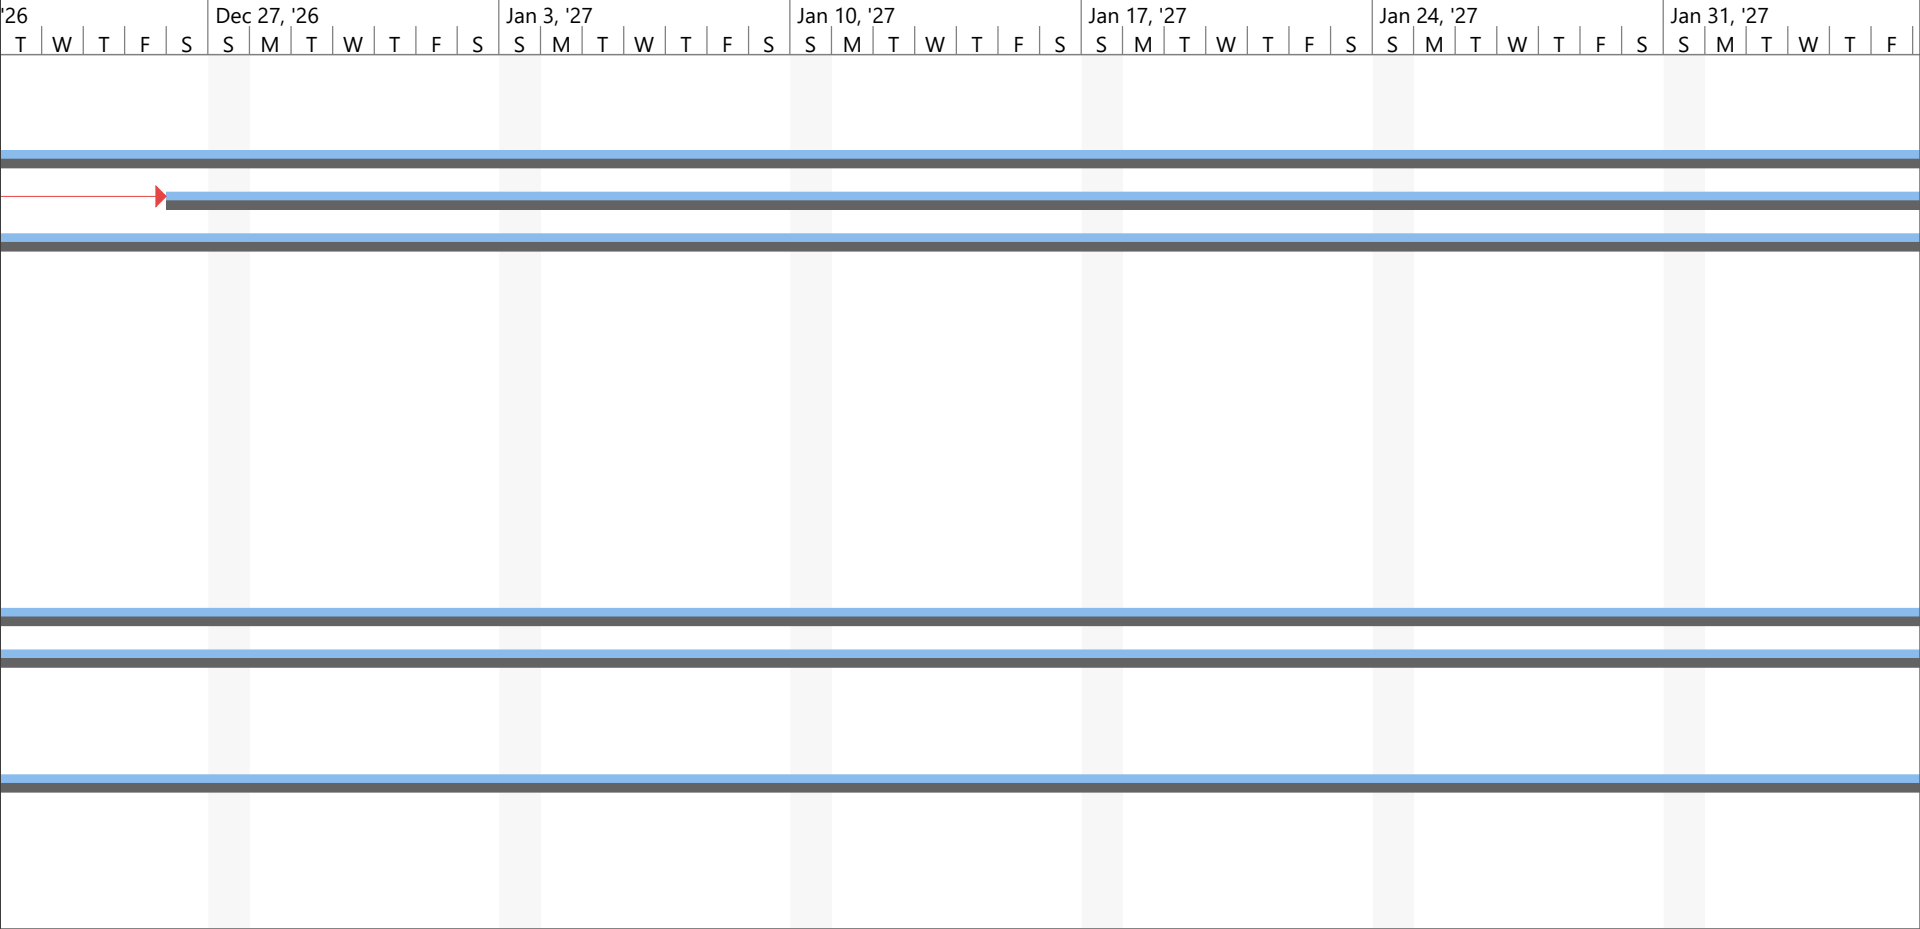

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

26

T

W

T

F

S

Dec 27, '26

S

M

T

W

T

F

S

Jan 3, '27

S

M

T

W

T

F

S

Jan 10, '27

S

M

T

W

T

F

S

Jan 17, '27

S

M

T

W

T

F

S

Jan 24, '27

S

M

T

W

T

F

S

Jan 31, '27

S



M

T

W

T

F



Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

The Gantt chart displays a project schedule from February 7, 2027, to March 21, 2027. The timeline is marked with weekly intervals. The chart shows several tasks, with a critical path highlighted in red. A task is shown starting on February 21 and ending on March 14, 2027. The legend defines the symbols used in the chart, including task types (Critical, Task, Manual Task), progress indicators (Progress, Split, Progress), and summary types (Manual Summary, Project Summary, External Tasks, External Milestone, Inactive Task, Inactive Milestone, Inactive Summary, Deadline).

Task Type	Symbol	Task Type	Symbol	Task Type	Symbol
Critical	Red solid line	Finish-only	Blue square	Manual Summary	Black bar with end cap
Critical Split	Red dotted line	Duration-only	Teal bar	Project Summary	Grey bar with end cap
Critical Progress	Red solid line	Baseline	Black bar	External Tasks	Grey bar
Task	Blue bar	Baseline Split	Black dotted line	External Milestone	Grey diamond
Split	Blue dotted line	Baseline Milestone	Black diamond	Inactive Task	White bar
Task Progress	Blue solid line	Milestone	Black diamond	Inactive Milestone	White diamond
Manual Task	Teal bar	Summary Progress	Black bar	Inactive Summary	Grey bar with end cap
Start-only	Blue square	Summary	Black bar with end cap	Deadline	Green arrow pointing down

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp


The Gantt chart displays a project schedule with tasks, milestones, and progress bars. The timeline is marked with dates from February 7, '27 to March 21, '27. The chart shows several tasks, including 'Critical', 'Task', 'Split', 'Manual Task', and 'Start-only'. The progress bars indicate the current status of each task, with some showing 0% completion. The legend defines the symbols used in the chart, such as 'Critical' (red bar), 'Task' (blue bar), 'Split' (dotted blue bar), 'Manual Task' (teal bar), 'Start-only' (cyan bar), 'Finish-only' (red bar), 'Duration-only' (dotted red bar), 'Baseline' (black bar), 'Baseline Split' (dotted black bar), 'Baseline Milestone' (diamond), 'Milestone' (black diamond), 'Summary Progress' (black bar), 'Summary' (black bar), 'Manual Summary' (black bar), 'Project Summary' (grey bar), 'External Tasks' (grey bar), 'External Milestone' (diamond), 'Inactive Task' (grey bar), 'Inactive Milestone' (grey diamond), 'Inactive Summary' (grey bar), and 'Deadline' (green arrow).

Task Type	Symbol
Critical	Red bar
Critical Split	Dotted red bar
Critical Progress	Red bar
Task	Blue bar
Split	Dotted blue bar
Task Progress	Blue bar
Manual Task	Teal bar
Start-only	Cyan bar
Finish-only	Red bar
Duration-only	Dotted red bar
Baseline	Black bar
Baseline Split	Dotted black bar
Baseline Milestone	Diamond
Milestone	Black diamond
Summary Progress	Black bar
Summary	Black bar
Manual Summary	Black bar
Project Summary	Grey bar
External Tasks	Grey bar
External Milestone	Diamond
Inactive Task	Grey bar
Inactive Milestone	Grey diamond
Inactive Summary	Grey bar
Deadline	Green arrow

Page 14


Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

Feb 7, '27							Feb 14, '27							Feb 21, '27							Feb 28, '27							Mar 7, '27							Mar 14, '27							Mar 21, '27		
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T						




Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

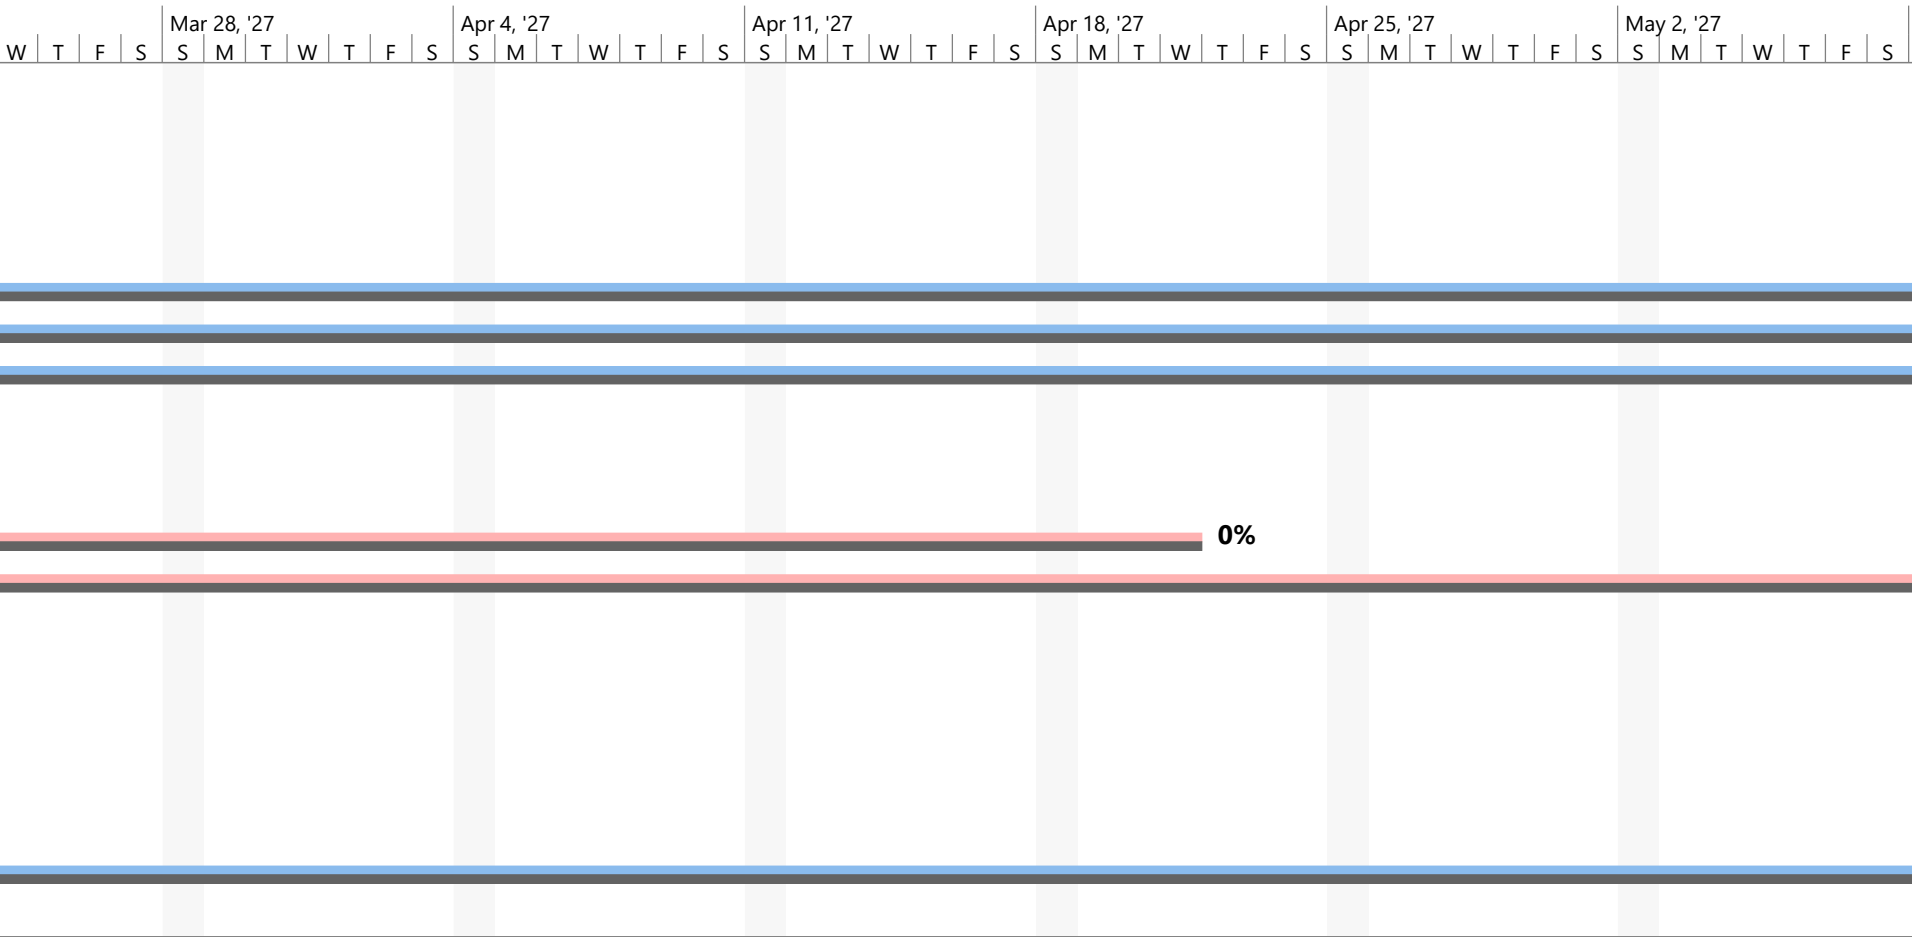


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

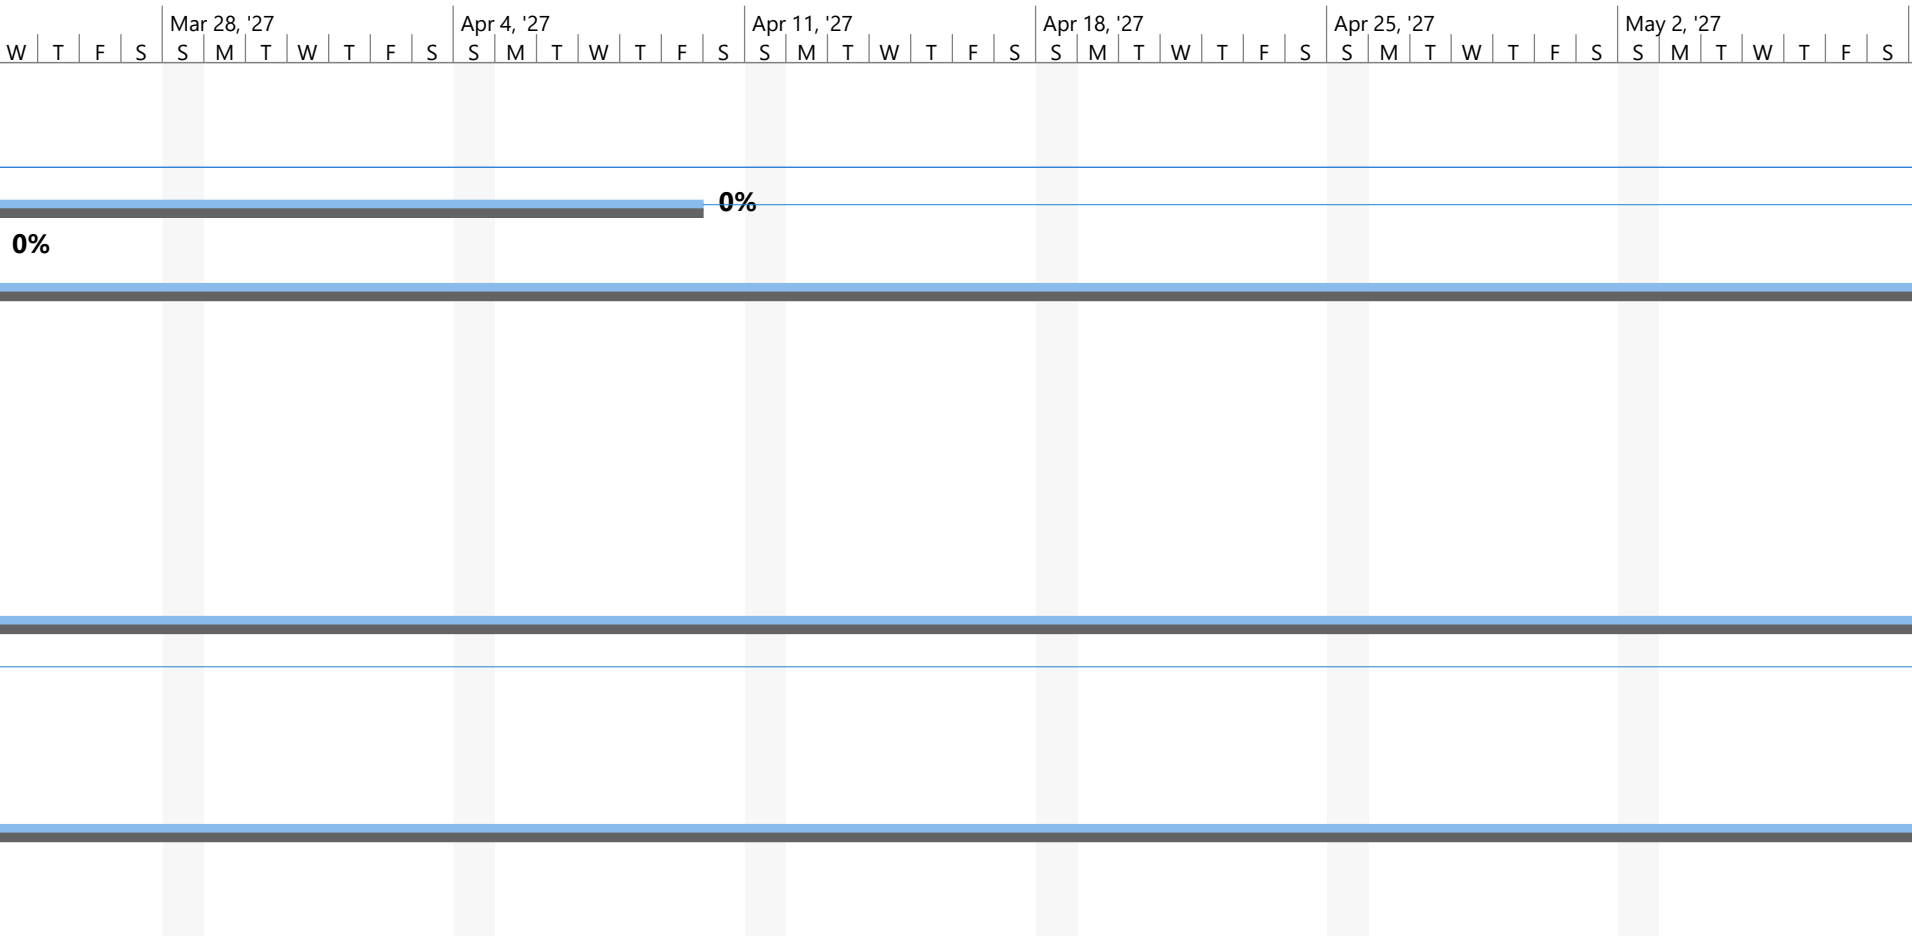


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	



Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

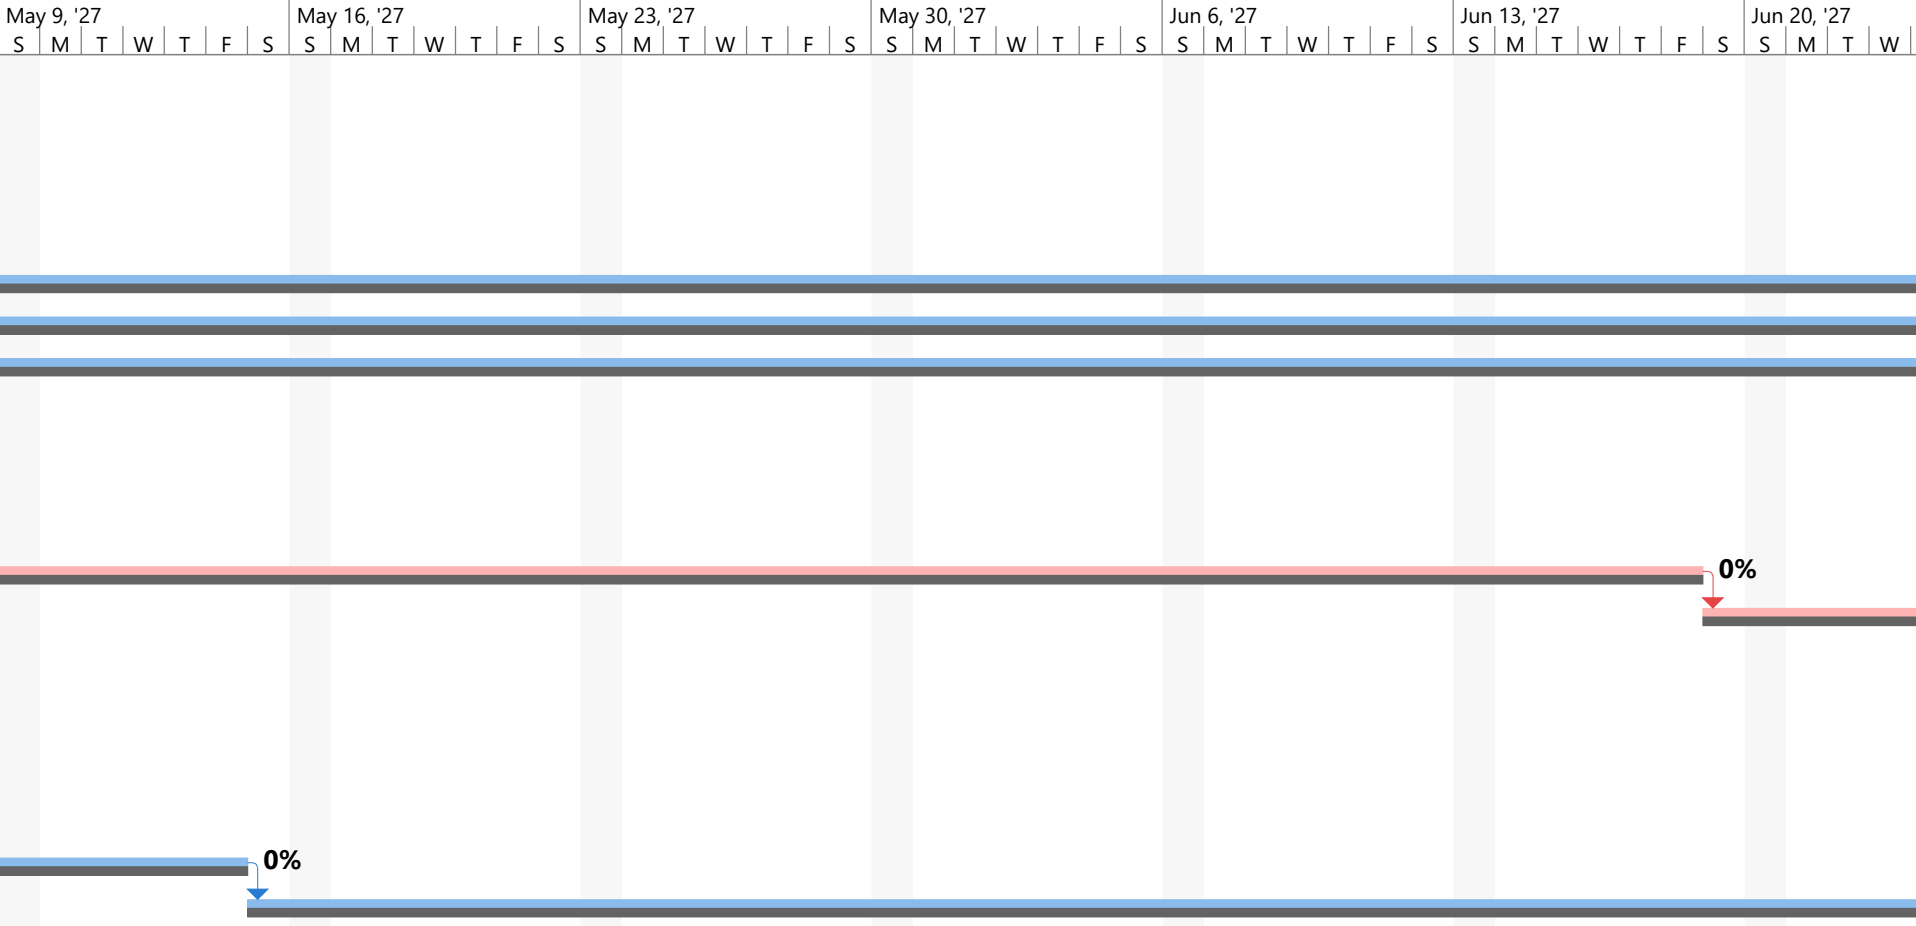


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

[illegible]

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

May 9, '27							May 16, '27							May 23, '27							May 30, '27							Jun 6, '27							Jun 13, '27							Jun 20, '27			
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W							



Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

The Gantt chart displays a project schedule from June 27, '27 to August 1, '27. The timeline is marked with days of the week (T, F, S) and specific dates. The chart shows several tasks, including Critical, Task, Split, Manual Task, and Start-only. A legend at the bottom explains the symbols used:

- Critical: Solid red line
- Critical Split: Dotted red line
- Critical Progress: Solid red line with a red arrow
- Task: Solid blue line
- Split: Dotted blue line
- Task Progress: Solid blue line with a blue arrow
- Manual Task: Solid teal line
- Start-only: Solid teal line with a teal arrow
- Finish-only: Solid black line with a black arrow
- Duration-only: Solid black line
- Baseline: Solid black line
- Baseline Split: Dotted black line
- Baseline Milestone: Solid black line with a black diamond
- Milestone: Solid black line with a black diamond
- Summary Progress: Solid black line with a black arrow
- Summary: Solid black line with a black arrow
- Manual Summary: Solid black line with a black arrow
- Project Summary: Solid black line with a black arrow
- External Tasks: Solid black line with a black arrow
- External Milestone: Solid black line with a black diamond
- Inactive Task: Solid black line with a black arrow
- Inactive Milestone: Solid black line with a black diamond
- Inactive Summary: Solid black line with a black arrow
- Deadline: Solid black line with a green arrow

0%


Page 22

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

The Gantt chart displays a project timeline from June 27, '27 to August 1, '27. The timeline is marked with weekly intervals and specific dates. A single task bar is shown at the bottom, indicating 0% completion. The legend defines various task types and their visual representations.


Task Type	Visual Representation
Critical	Thick red line
Critical Split	Dotted red line
Critical Progress	Thick red line with black outline
Task	Blue line
Split	Dotted blue line
Task Progress	Blue line with black outline
Manual Task	Thick blue line
Start-only	Blue line with open square
Finish-only	Blue line with open square
Duration-only	Thick blue line
Baseline	Thick black line
Baseline Split	Dotted black line
Baseline Milestone	Open diamond
Milestone	Filled diamond
Summary Progress	Thick black line
Summary	Thick black line with open square
Manual Summary	Thick black line with open square
Project Summary	Thick black line with open square
External Tasks	Thick grey line
External Milestone	Open diamond
Inactive Task	Thin grey line
Inactive Milestone	Open diamond
Inactive Summary	Thin grey line with open square
Deadline	Green arrow pointing down

T	F	S	Jun 27, '27					Jul 4, '27					Jul 11, '27					Jul 18, '27					Jul 25, '27					Aug 1, '27					Aug		
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S




Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

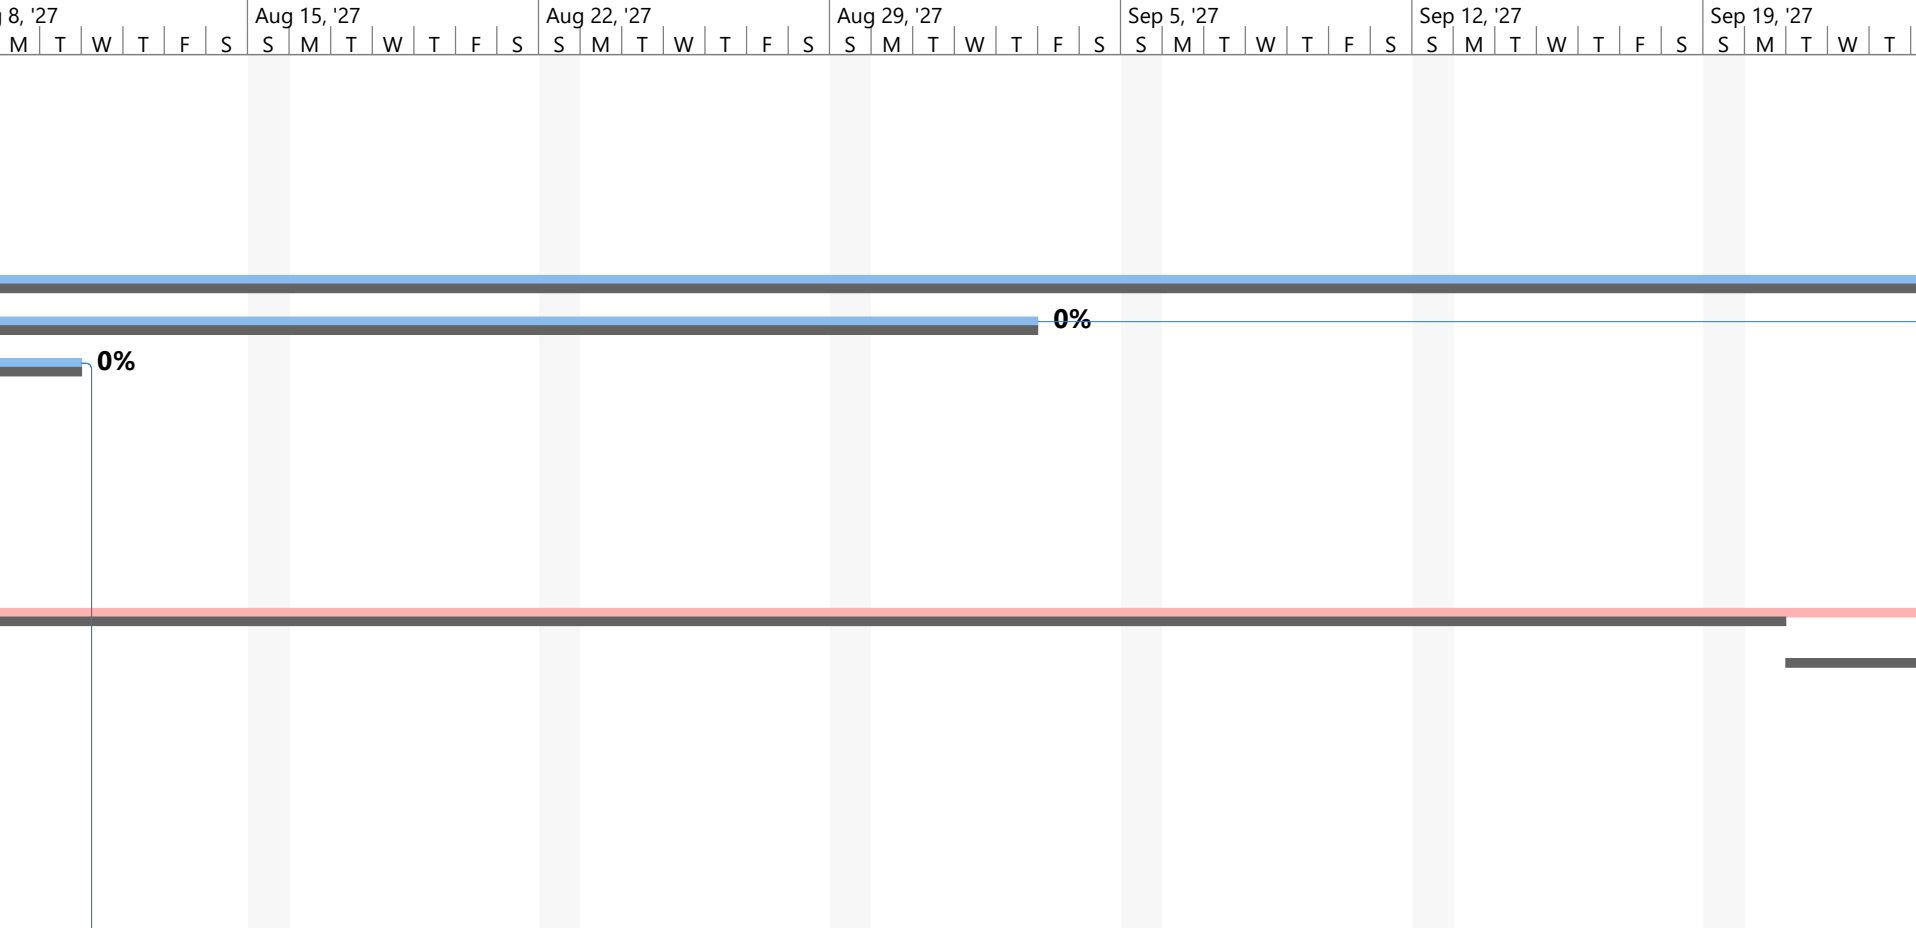

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

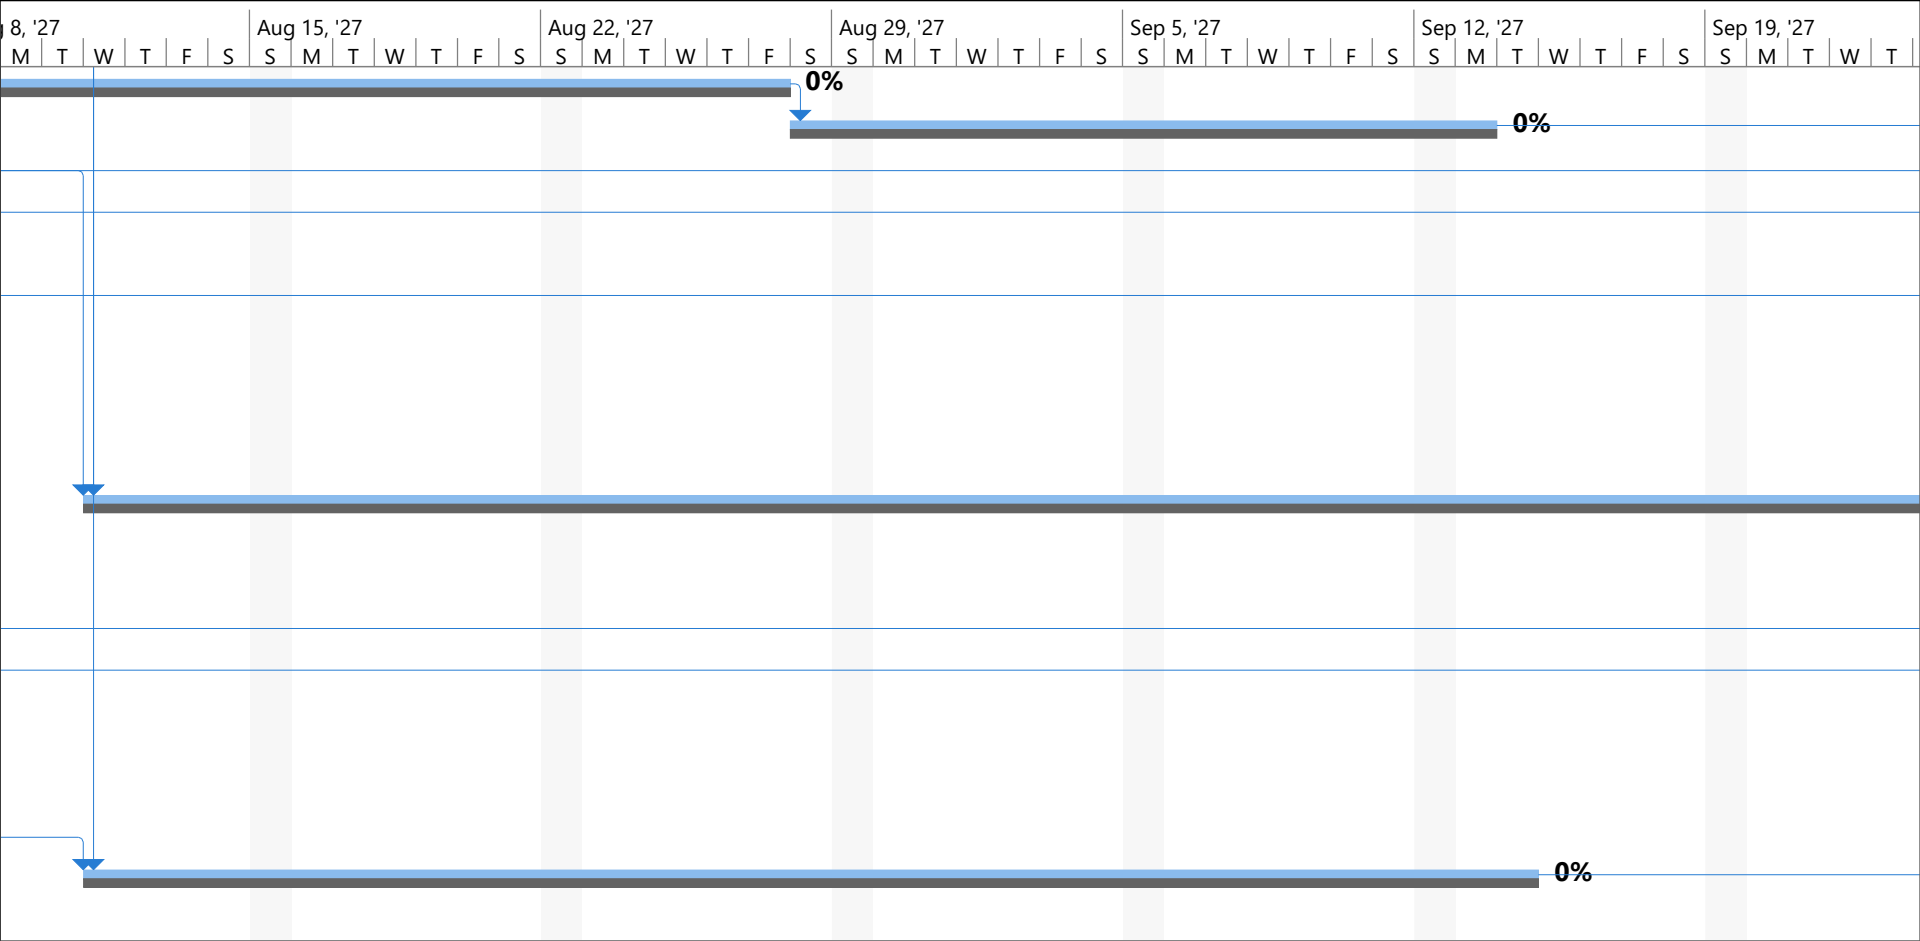


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

8, '27							Aug 15, '27							Aug 22, '27							Aug 29, '27							Sep 5, '27							Sep 12, '27							Sep 19, '27				
M	T	W	T	F	S		S	M	T	W	T	F	S		S	M	T	W	T	F	S		S	M	T	W	T	F	S		S	M	T	W	T	F	S		S	M	T	W	T			


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

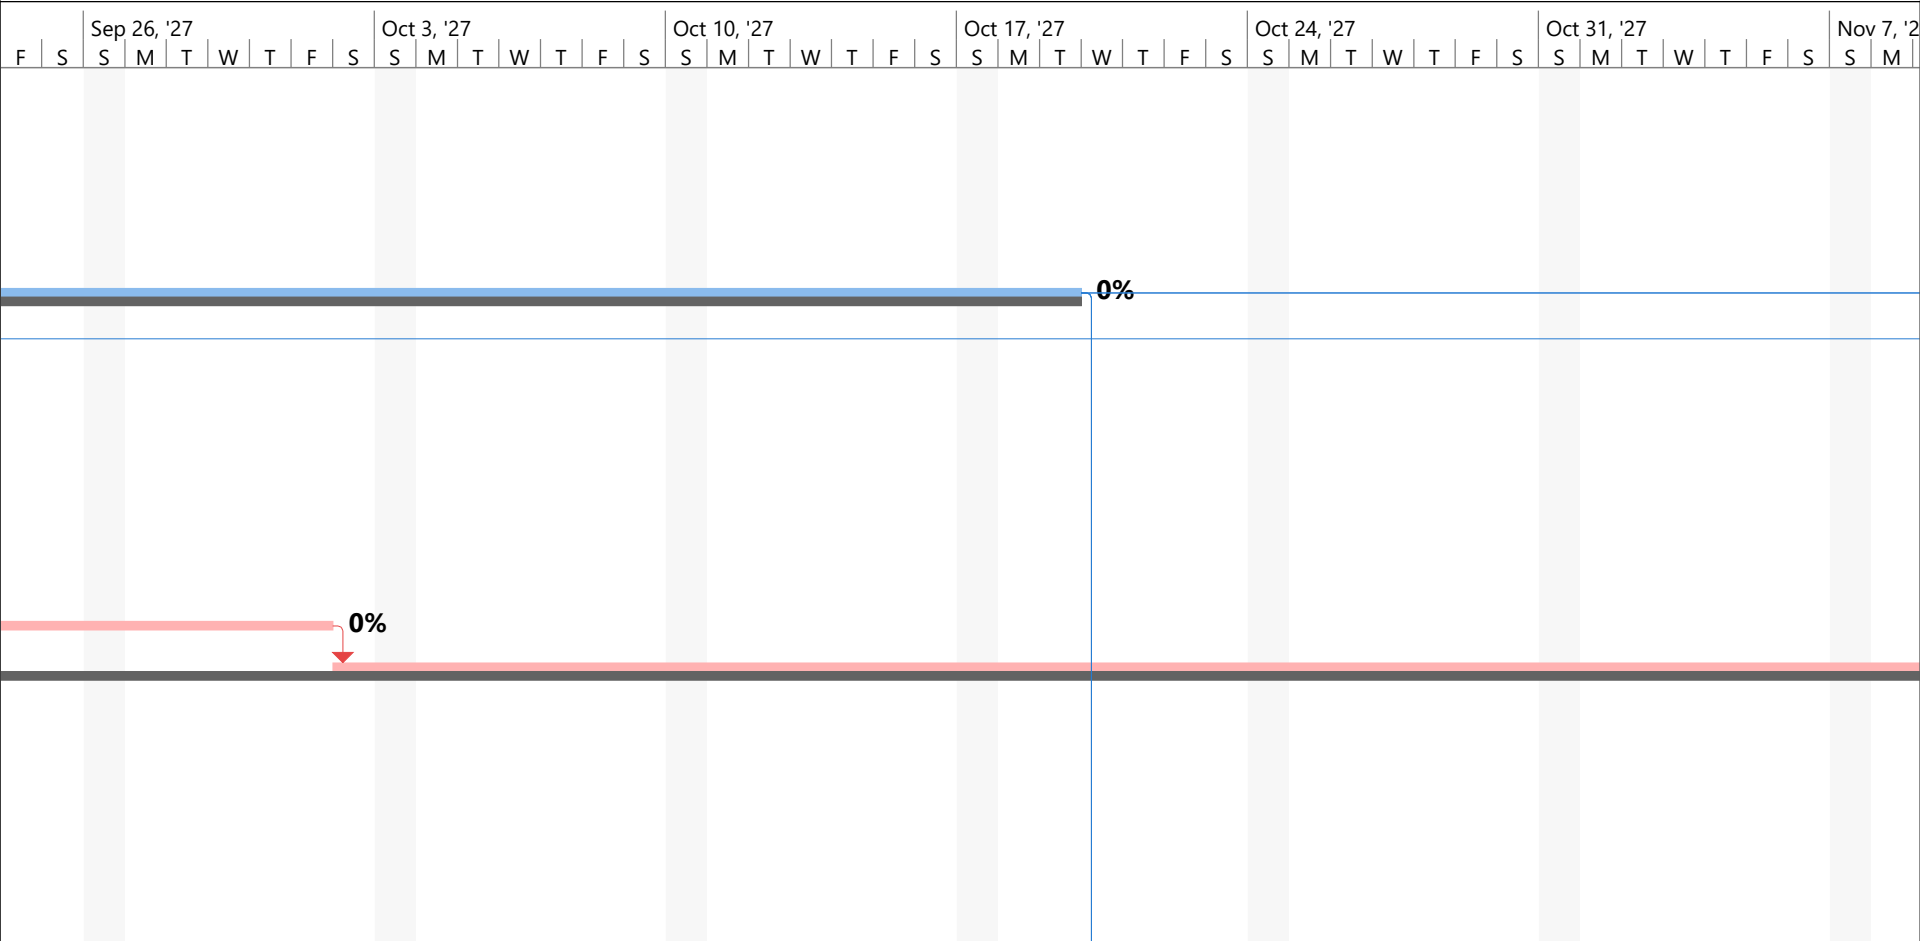

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	


Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

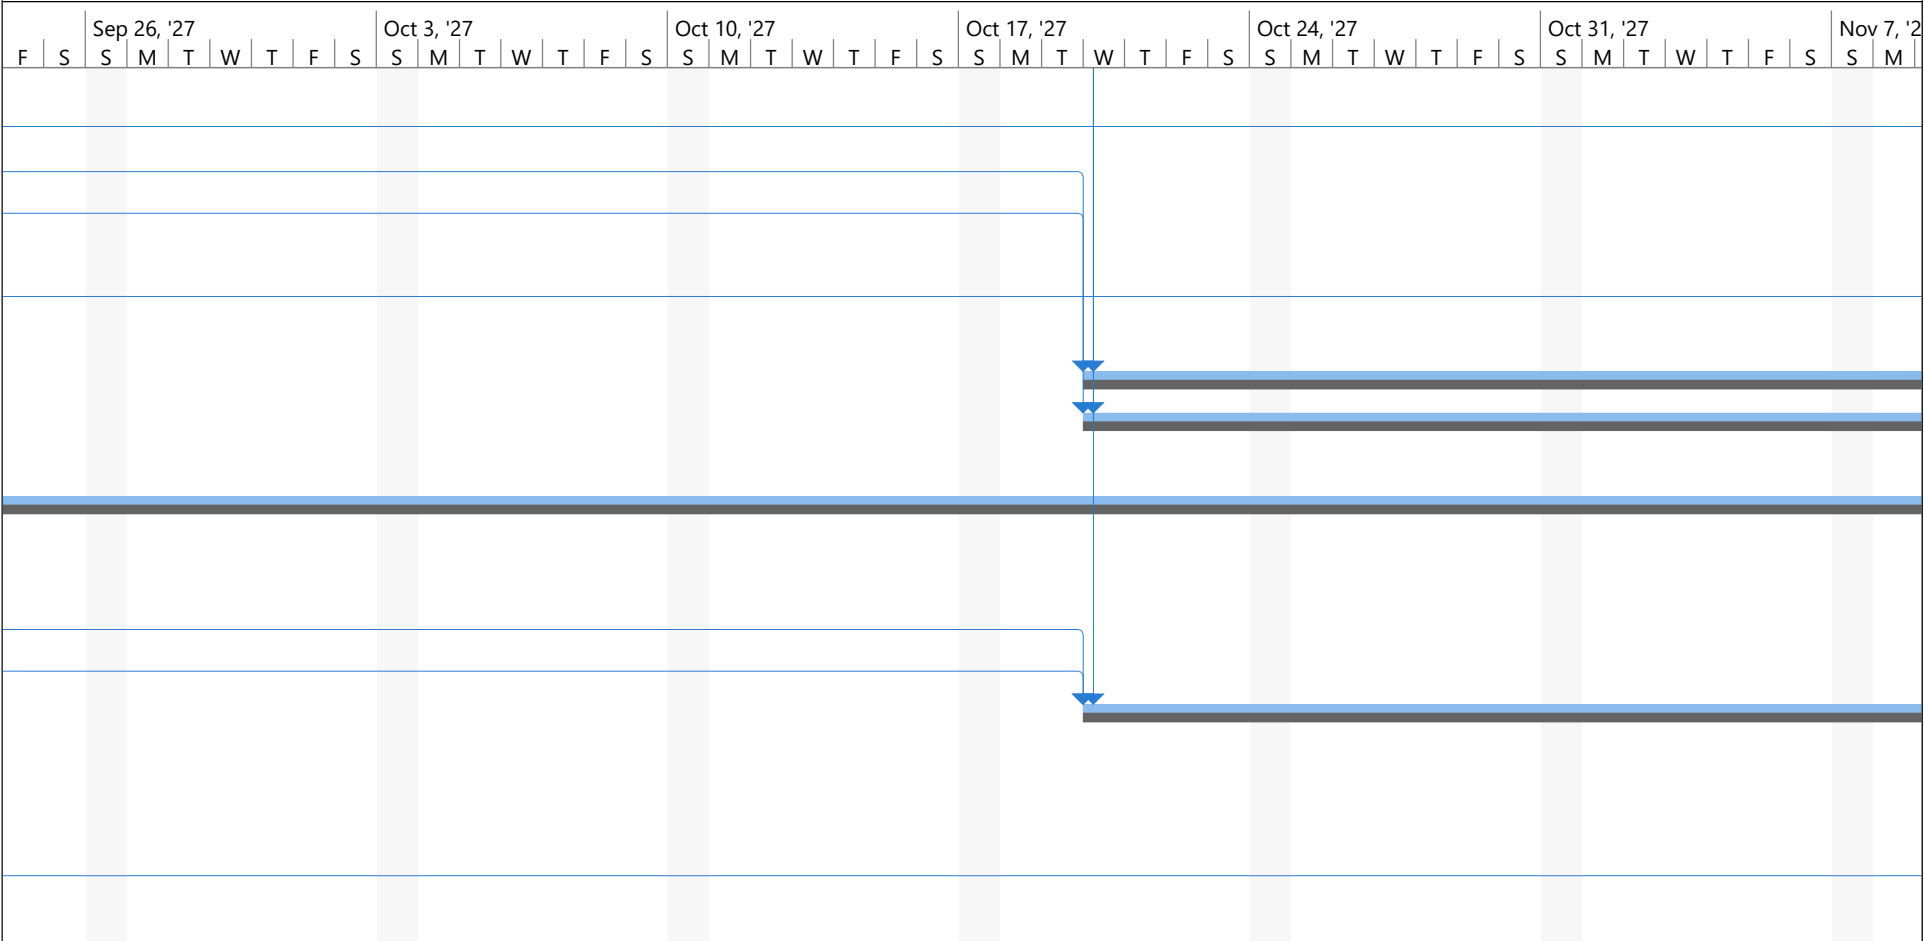

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	


[illegible]

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

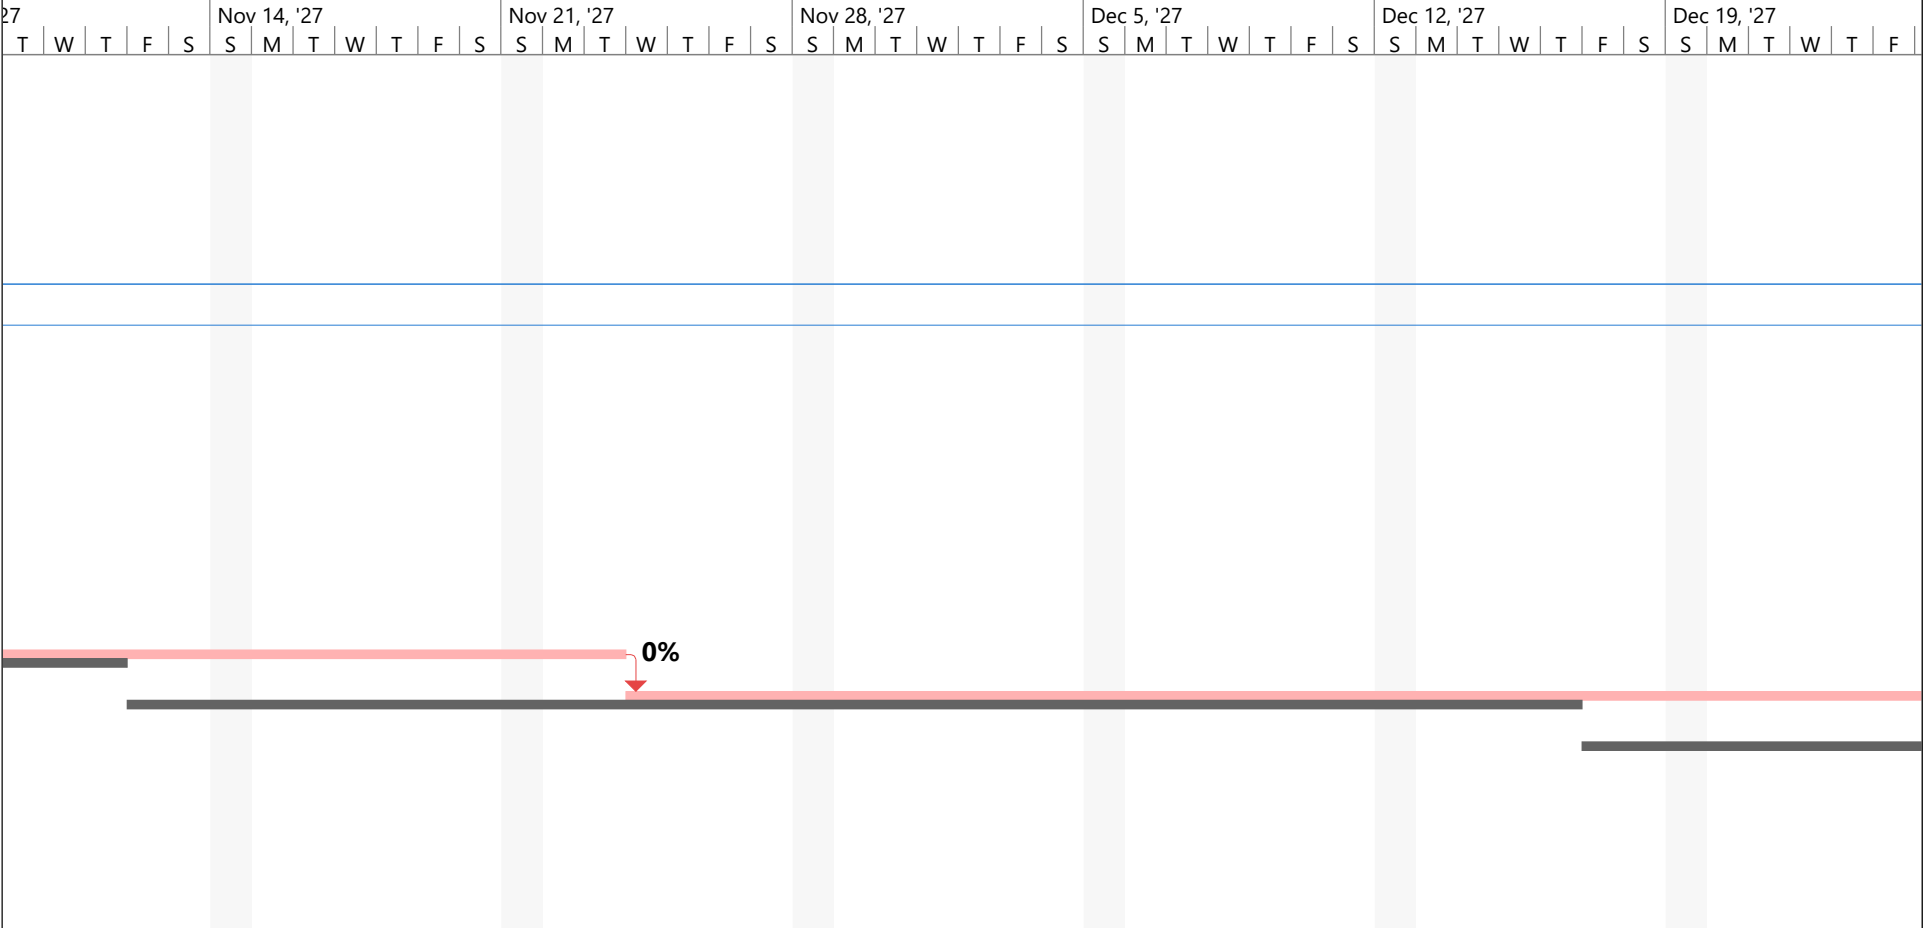

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

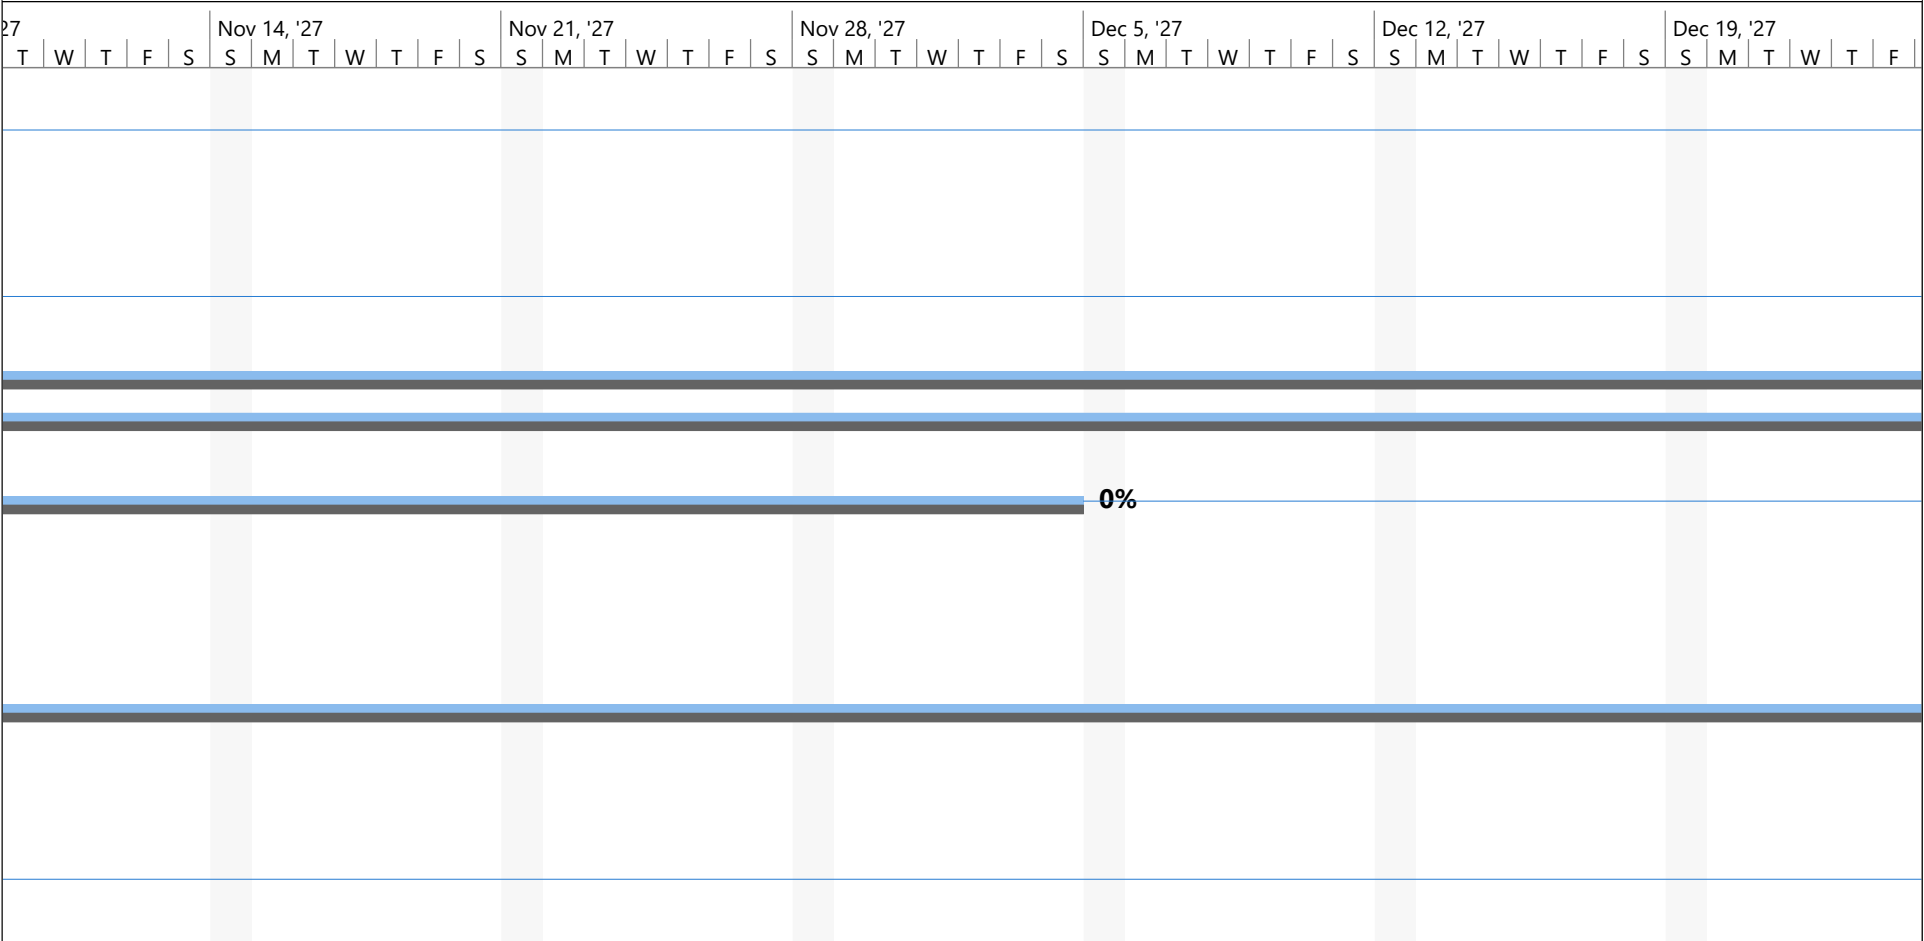

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

27

T

W

T

F

S

Nov 14, '27

S

M

T

W

T

F

S

Nov 21, '27

S

M

T

W

T

F

S

Nov 28, '27

S

M

T

W

T

F

S

Dec 5, '27

S

M

T

W

T

F

S

Dec 12, '27

S

M

T

W

T

F

S

Dec 19, '27

S



M

T

W


T

F




Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

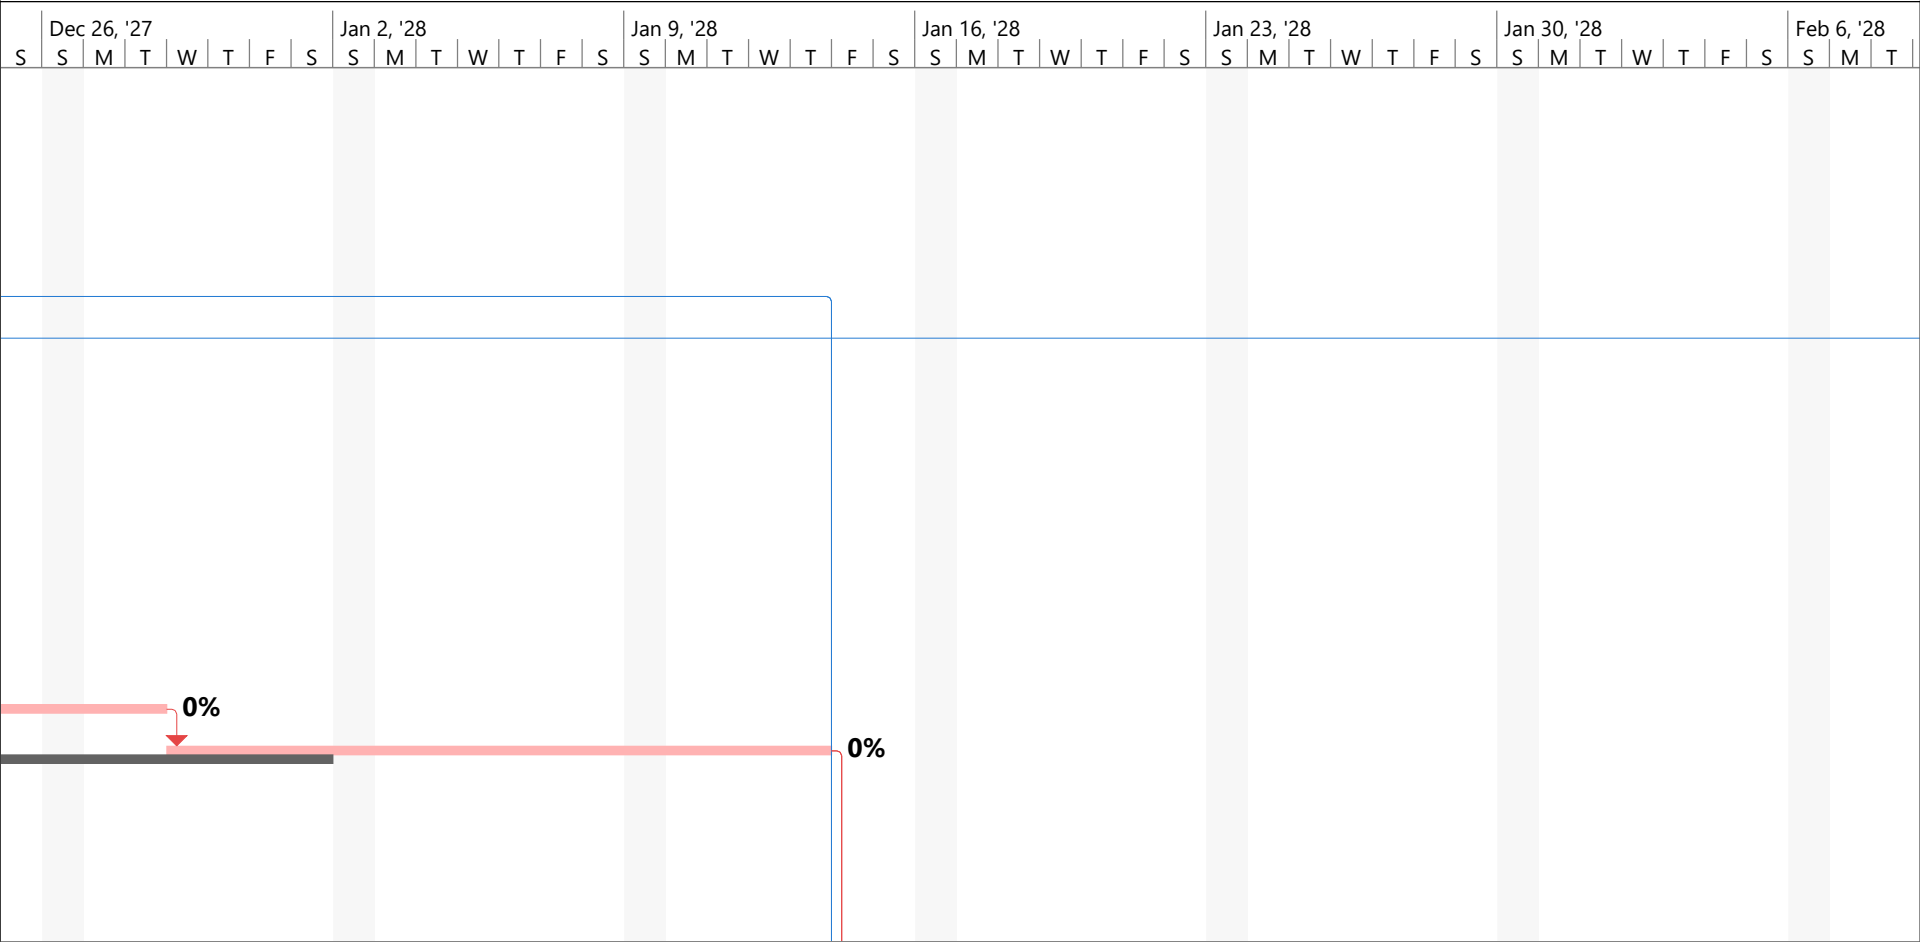


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

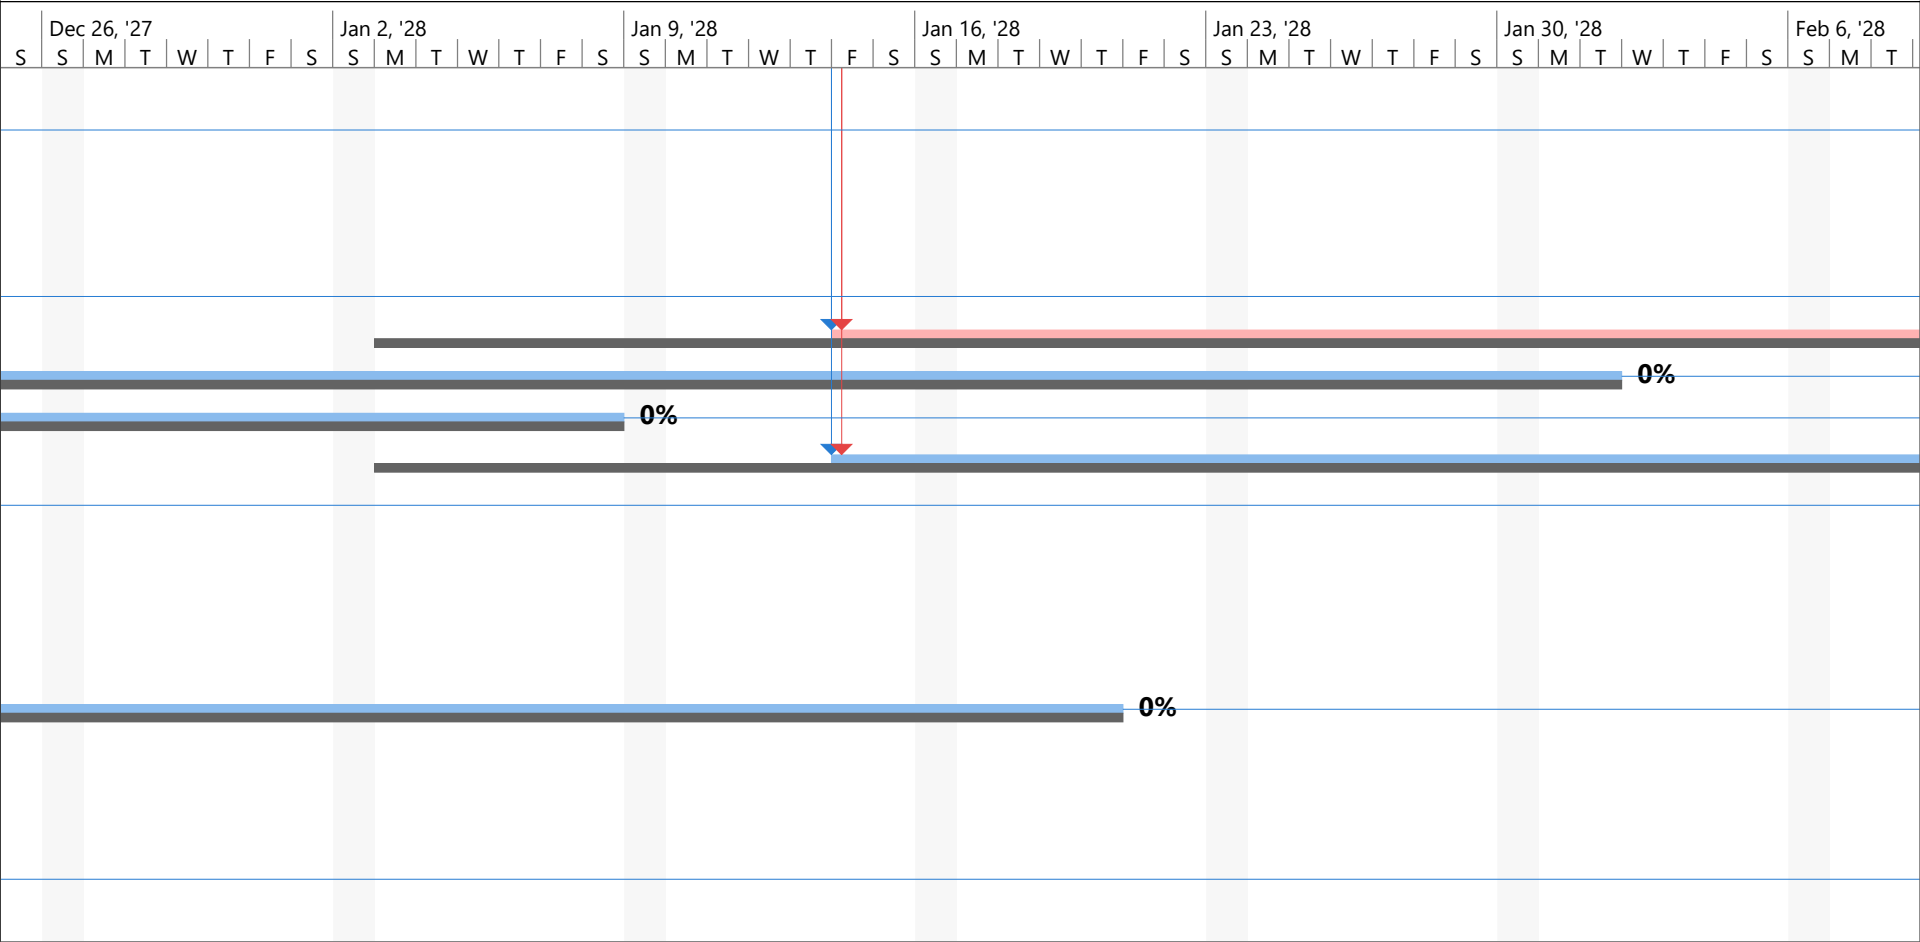

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

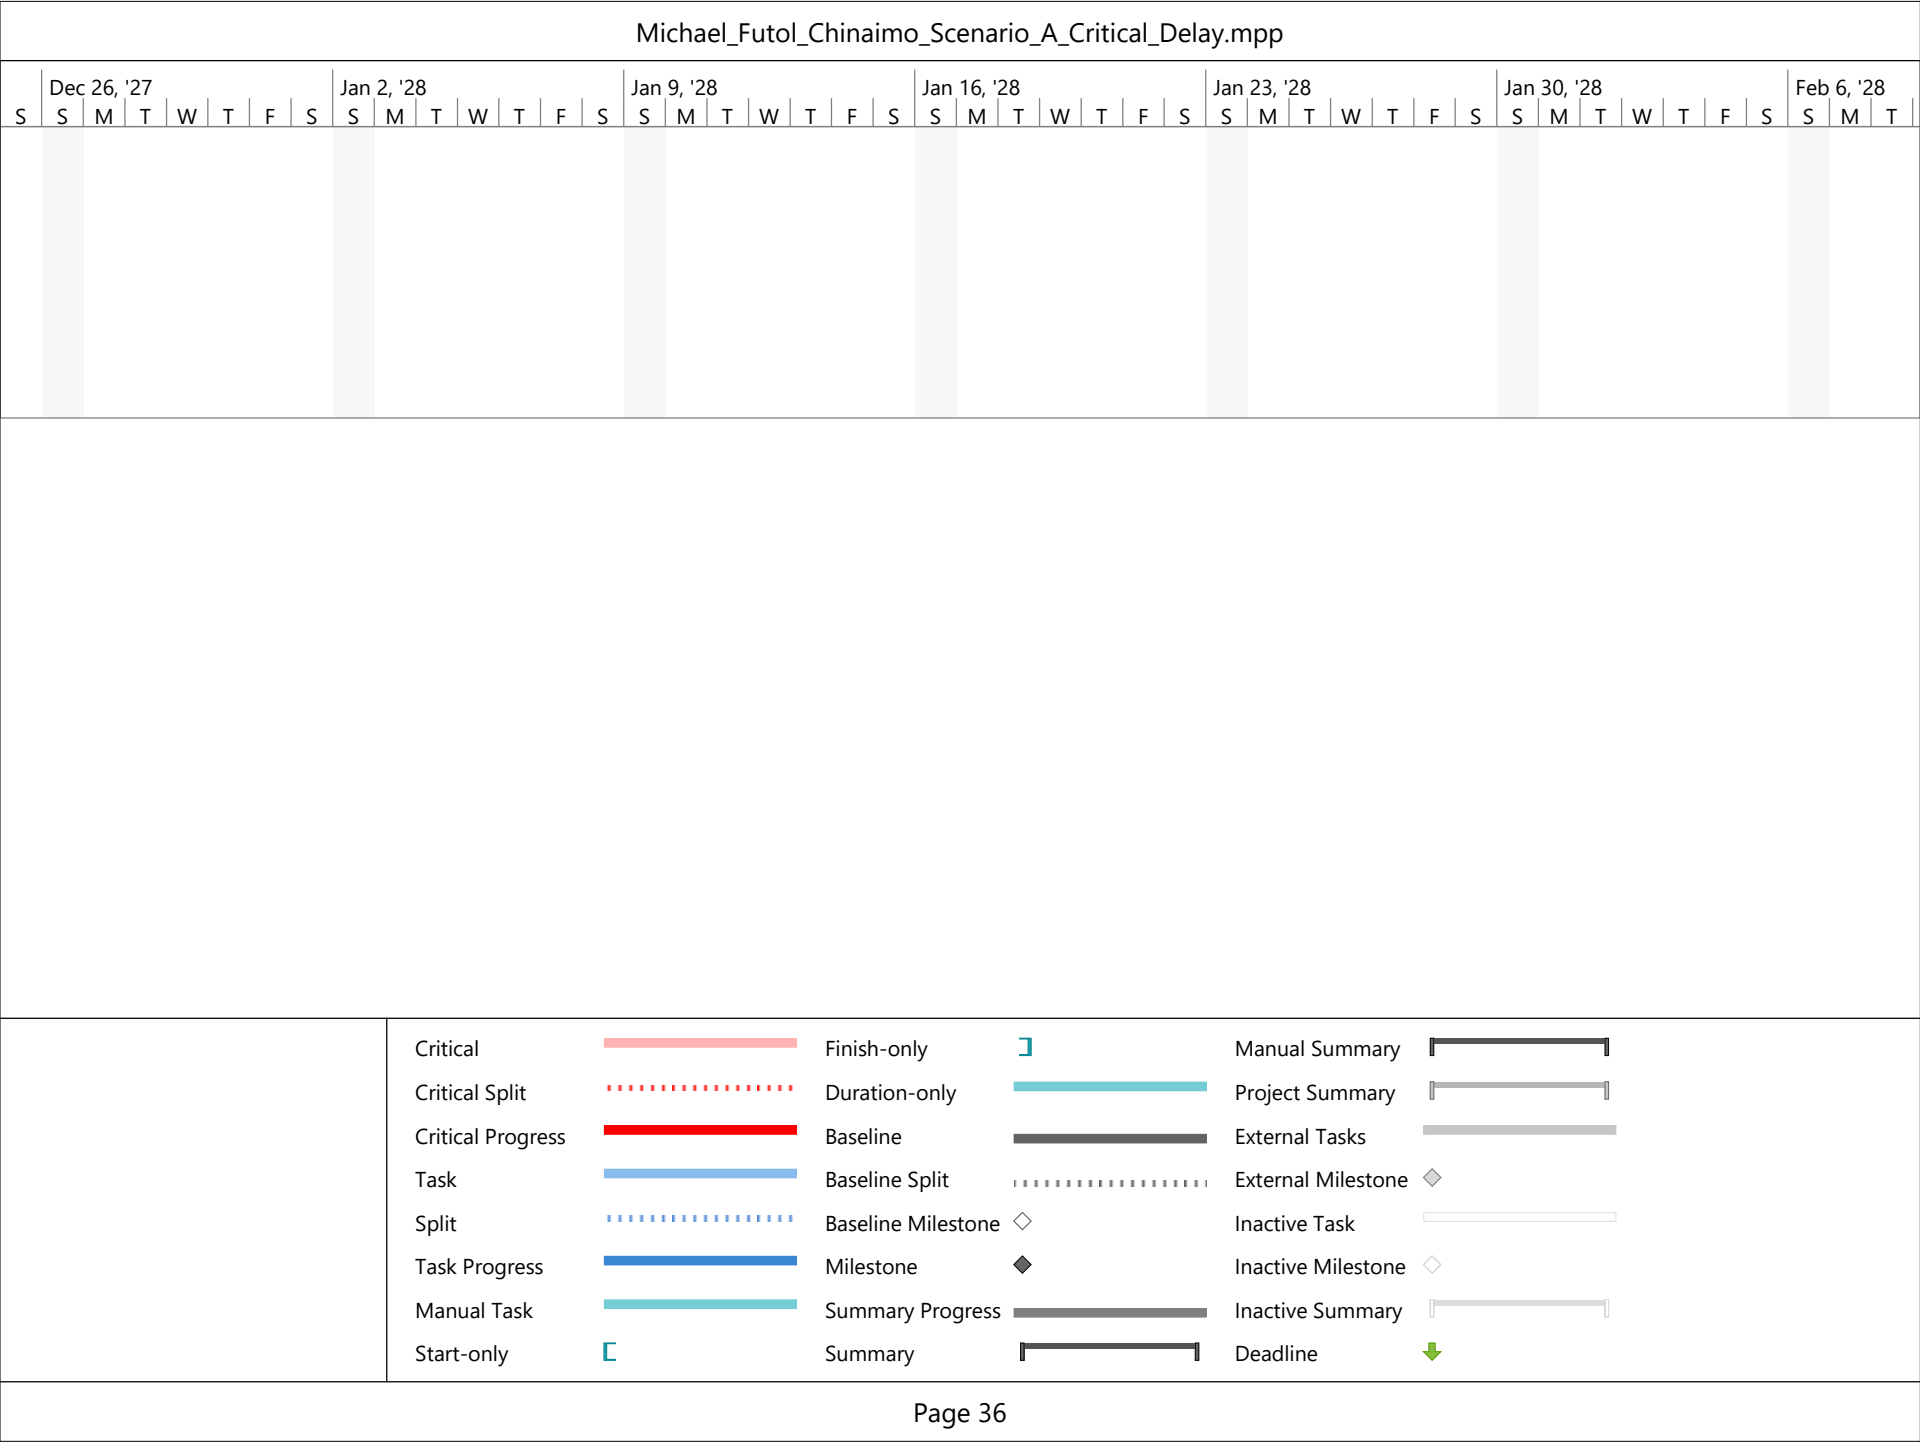


Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp


The Gantt chart displays a project schedule from February 13, 2028, to March 19, 2028. The timeline is marked with weekly intervals. The legend at the bottom defines the following task types and their visual representations:

- Critical:** Solid red line
- Critical Split:** Dotted red line
- Critical Progress:** Solid red line with a red arrowhead
- Task:** Solid blue line
- Split:** Dotted blue line
- Task Progress:** Solid blue line with a blue arrowhead
- Manual Task:** Solid teal line
- Start-only:** Teal line with a square start marker
- Finish-only:** Red line with a square end marker
- Duration-only:** Dotted red line
- Baseline:** Solid black line
- Baseline Split:** Dotted black line
- Baseline Milestone:** Diamond marker
- Milestone:** Diamond marker
- Summary Progress:** Solid black line with a black arrowhead
- Summary:** Solid black line with square start and end markers
- Manual Summary:** Solid black line with a black arrowhead
- Project Summary:** Solid black line with square start and end markers
- External Tasks:** Solid black line
- External Milestone:** Diamond marker
- Inactive Task:** Solid black line
- Inactive Milestone:** Diamond marker
- Inactive Summary:** Solid black line with square start and end markers
- Deadline:** Green arrow pointing down

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

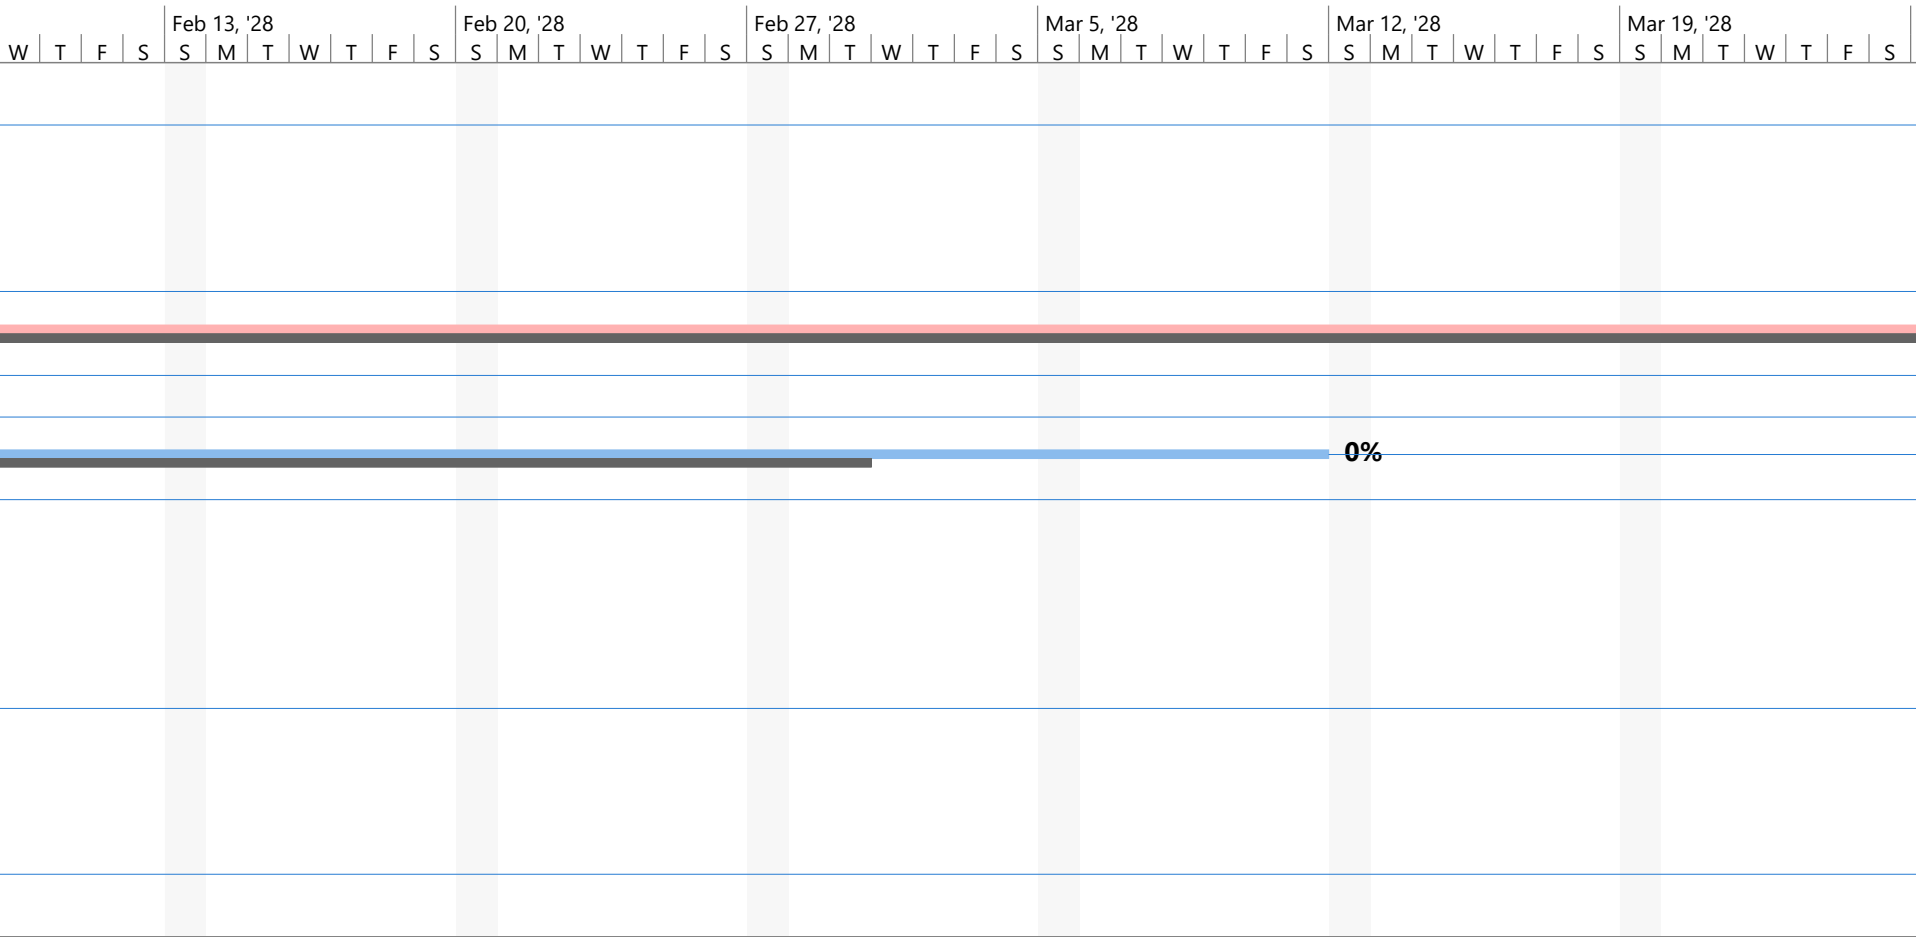


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

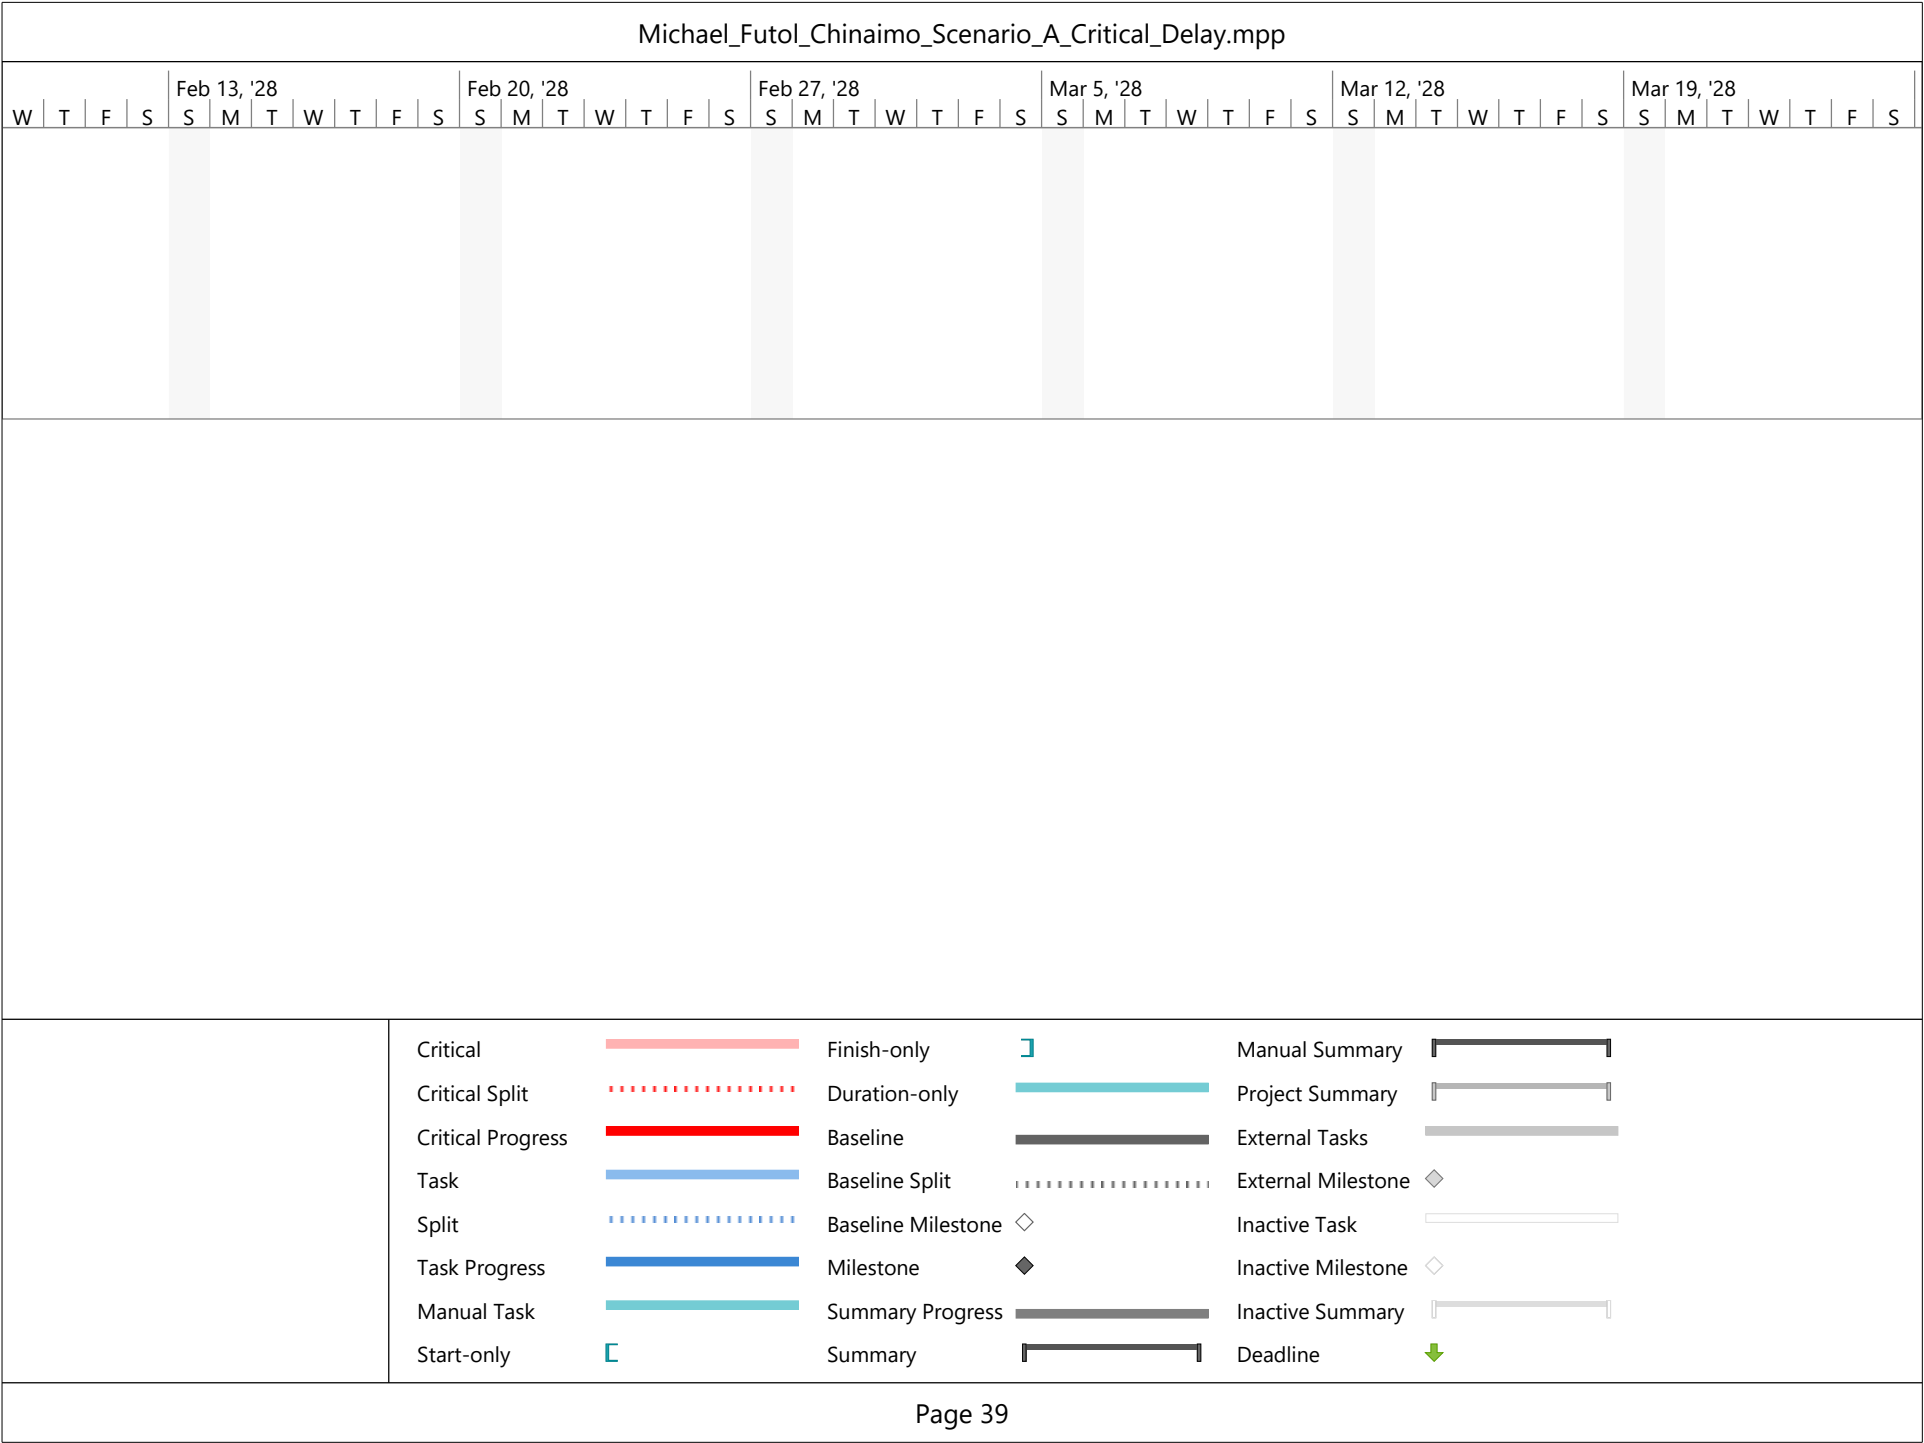


Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

Mar 26, '28							Apr 2, '28							Apr 9, '28							Apr 16, '28							Apr 23, '28							Apr 30, '28							May 7, '28			
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W							

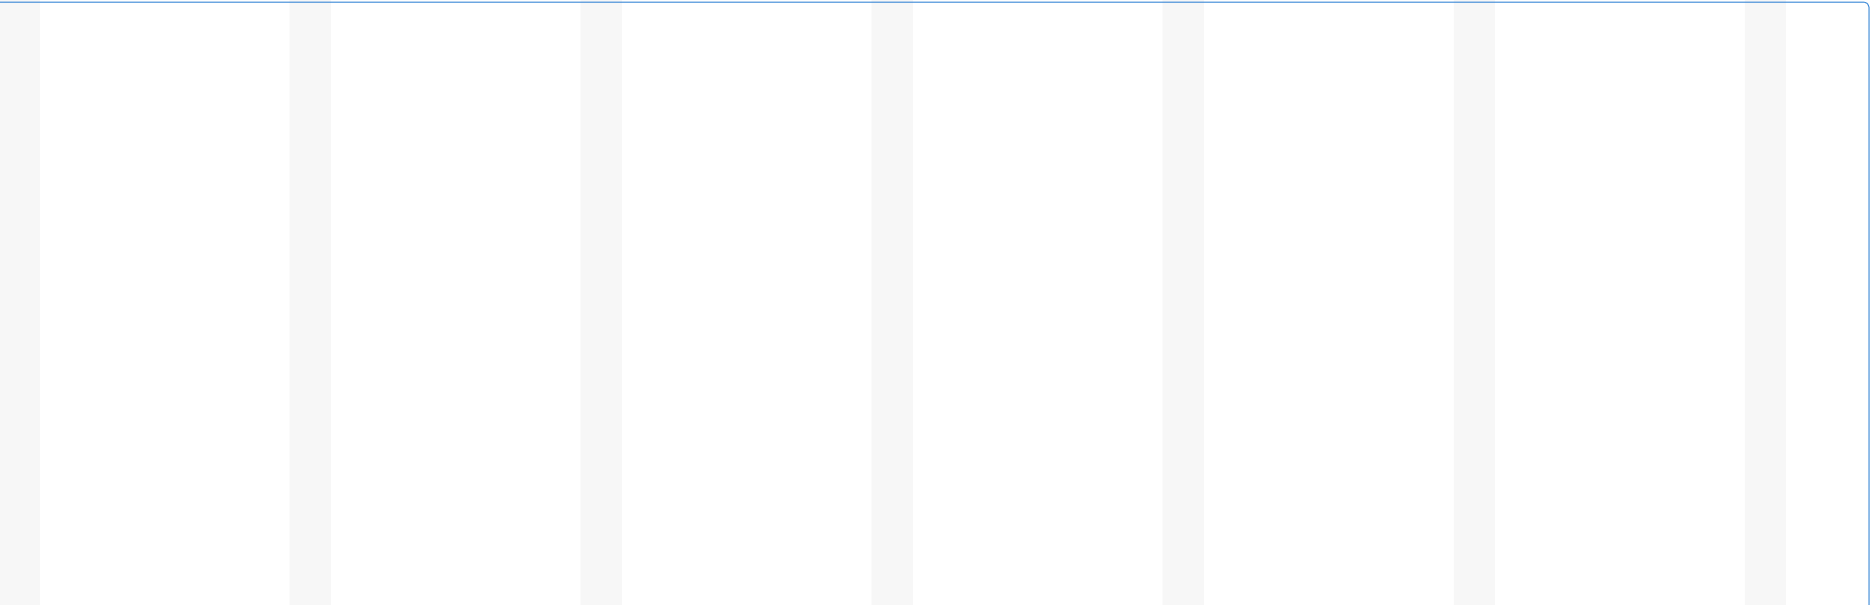

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

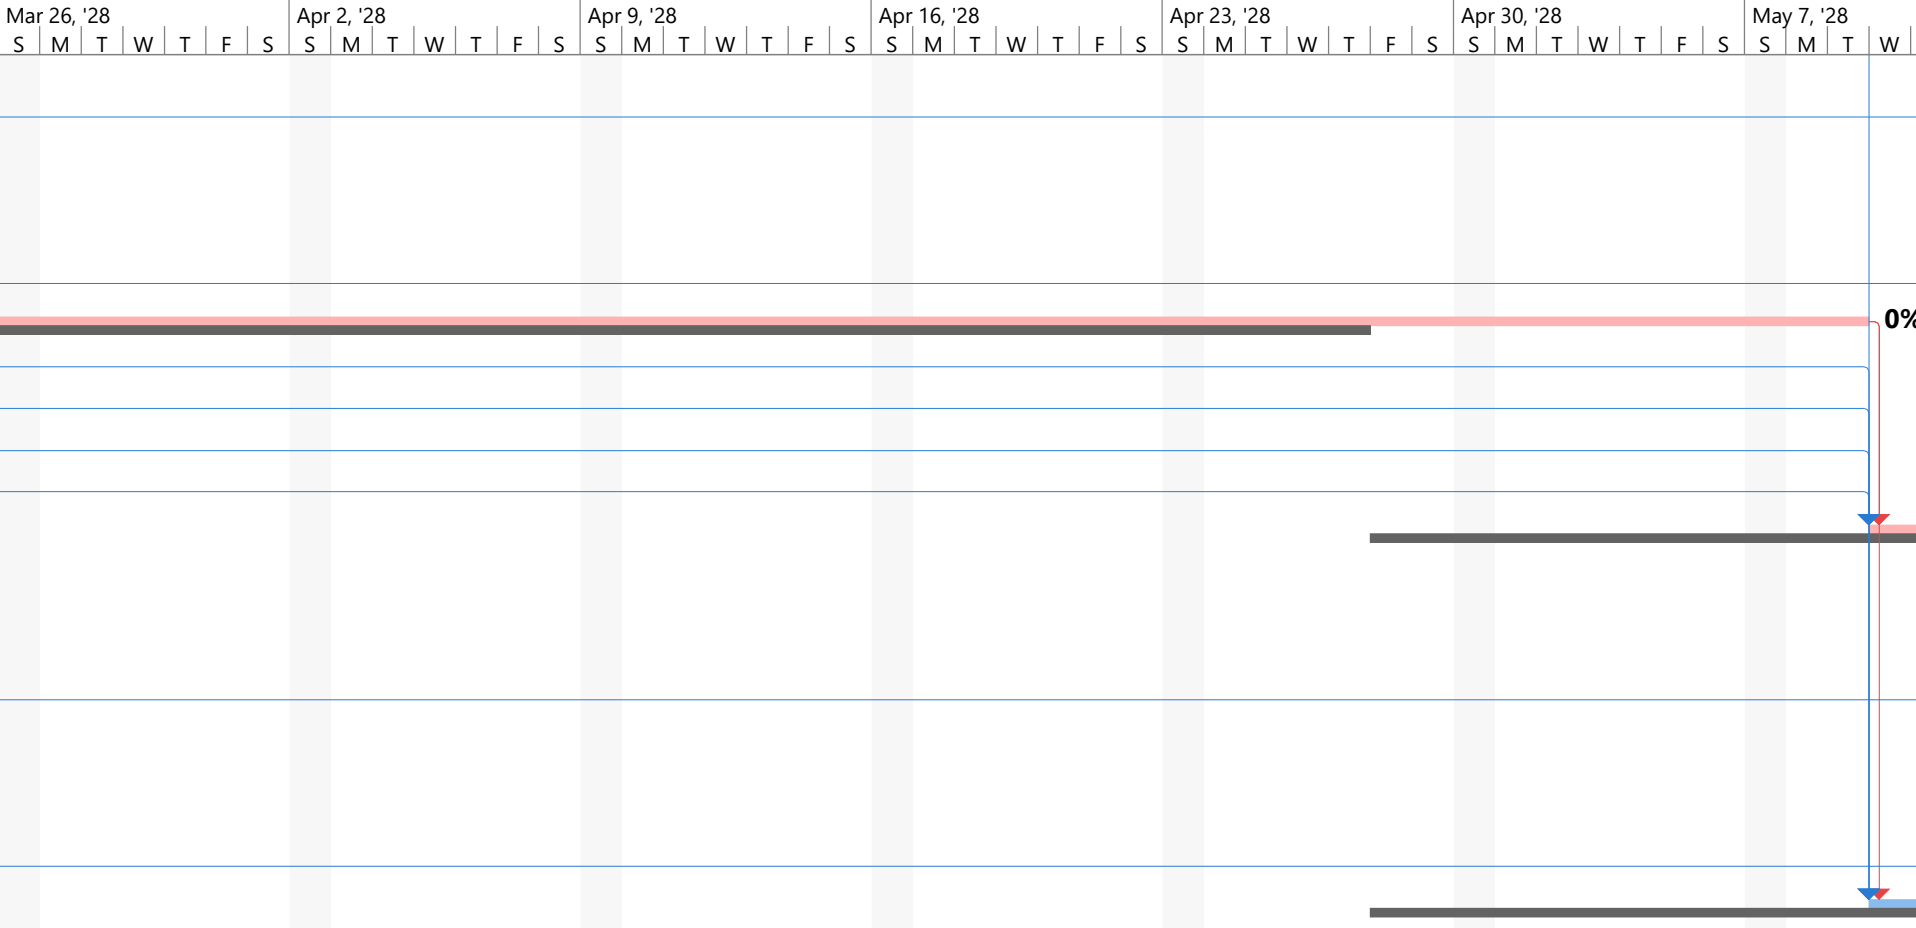



Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

Mar 26, '28							Apr 2, '28							Apr 9, '28							Apr 16, '28							Apr 23, '28							Apr 30, '28							May 7, '28			
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W							

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

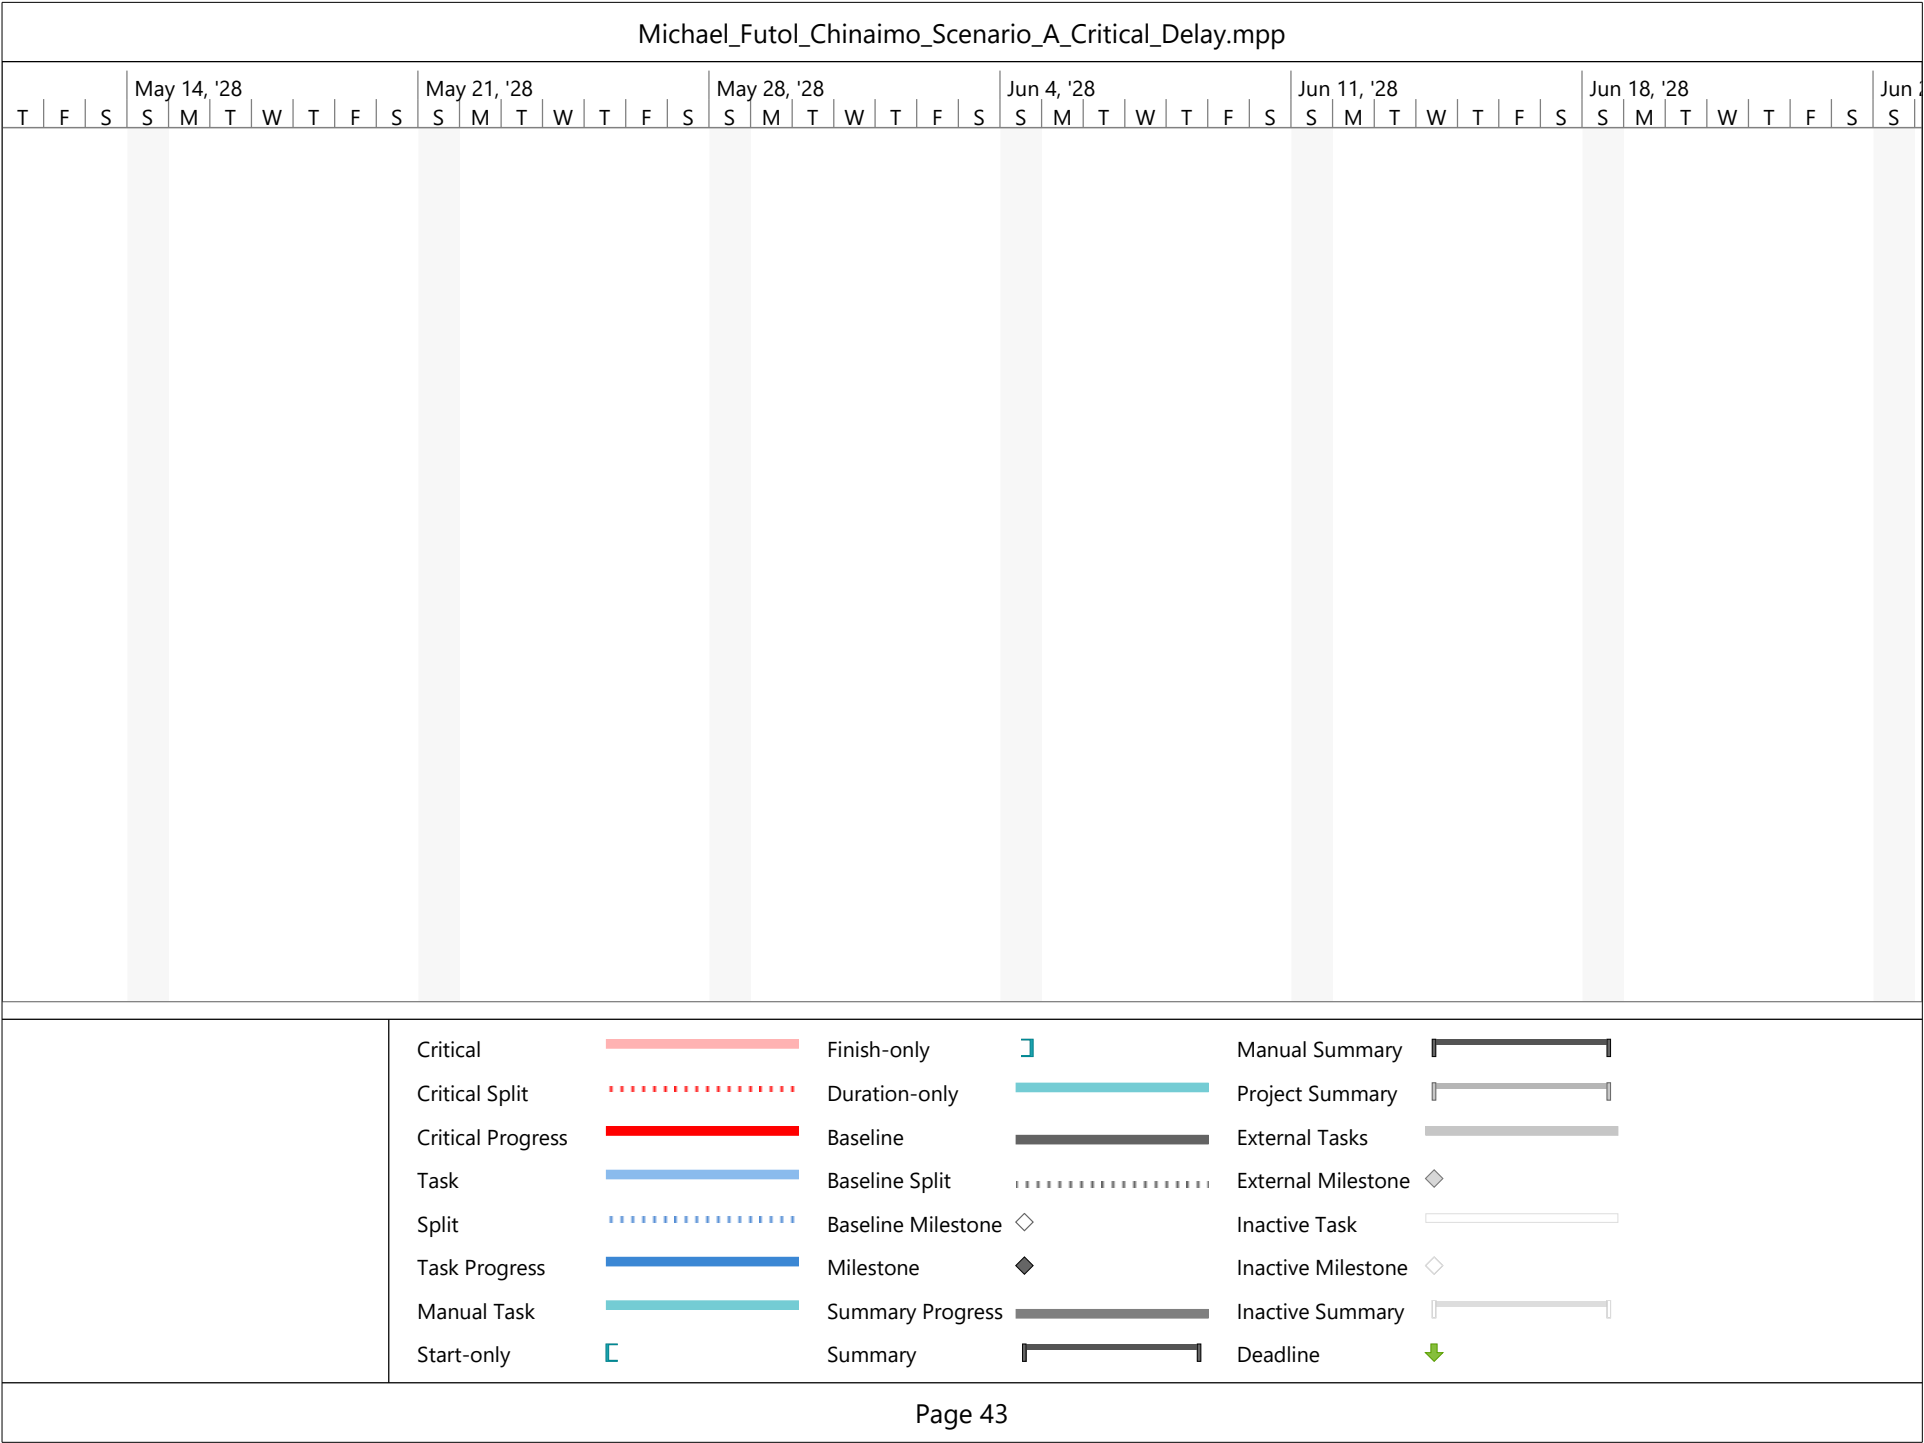

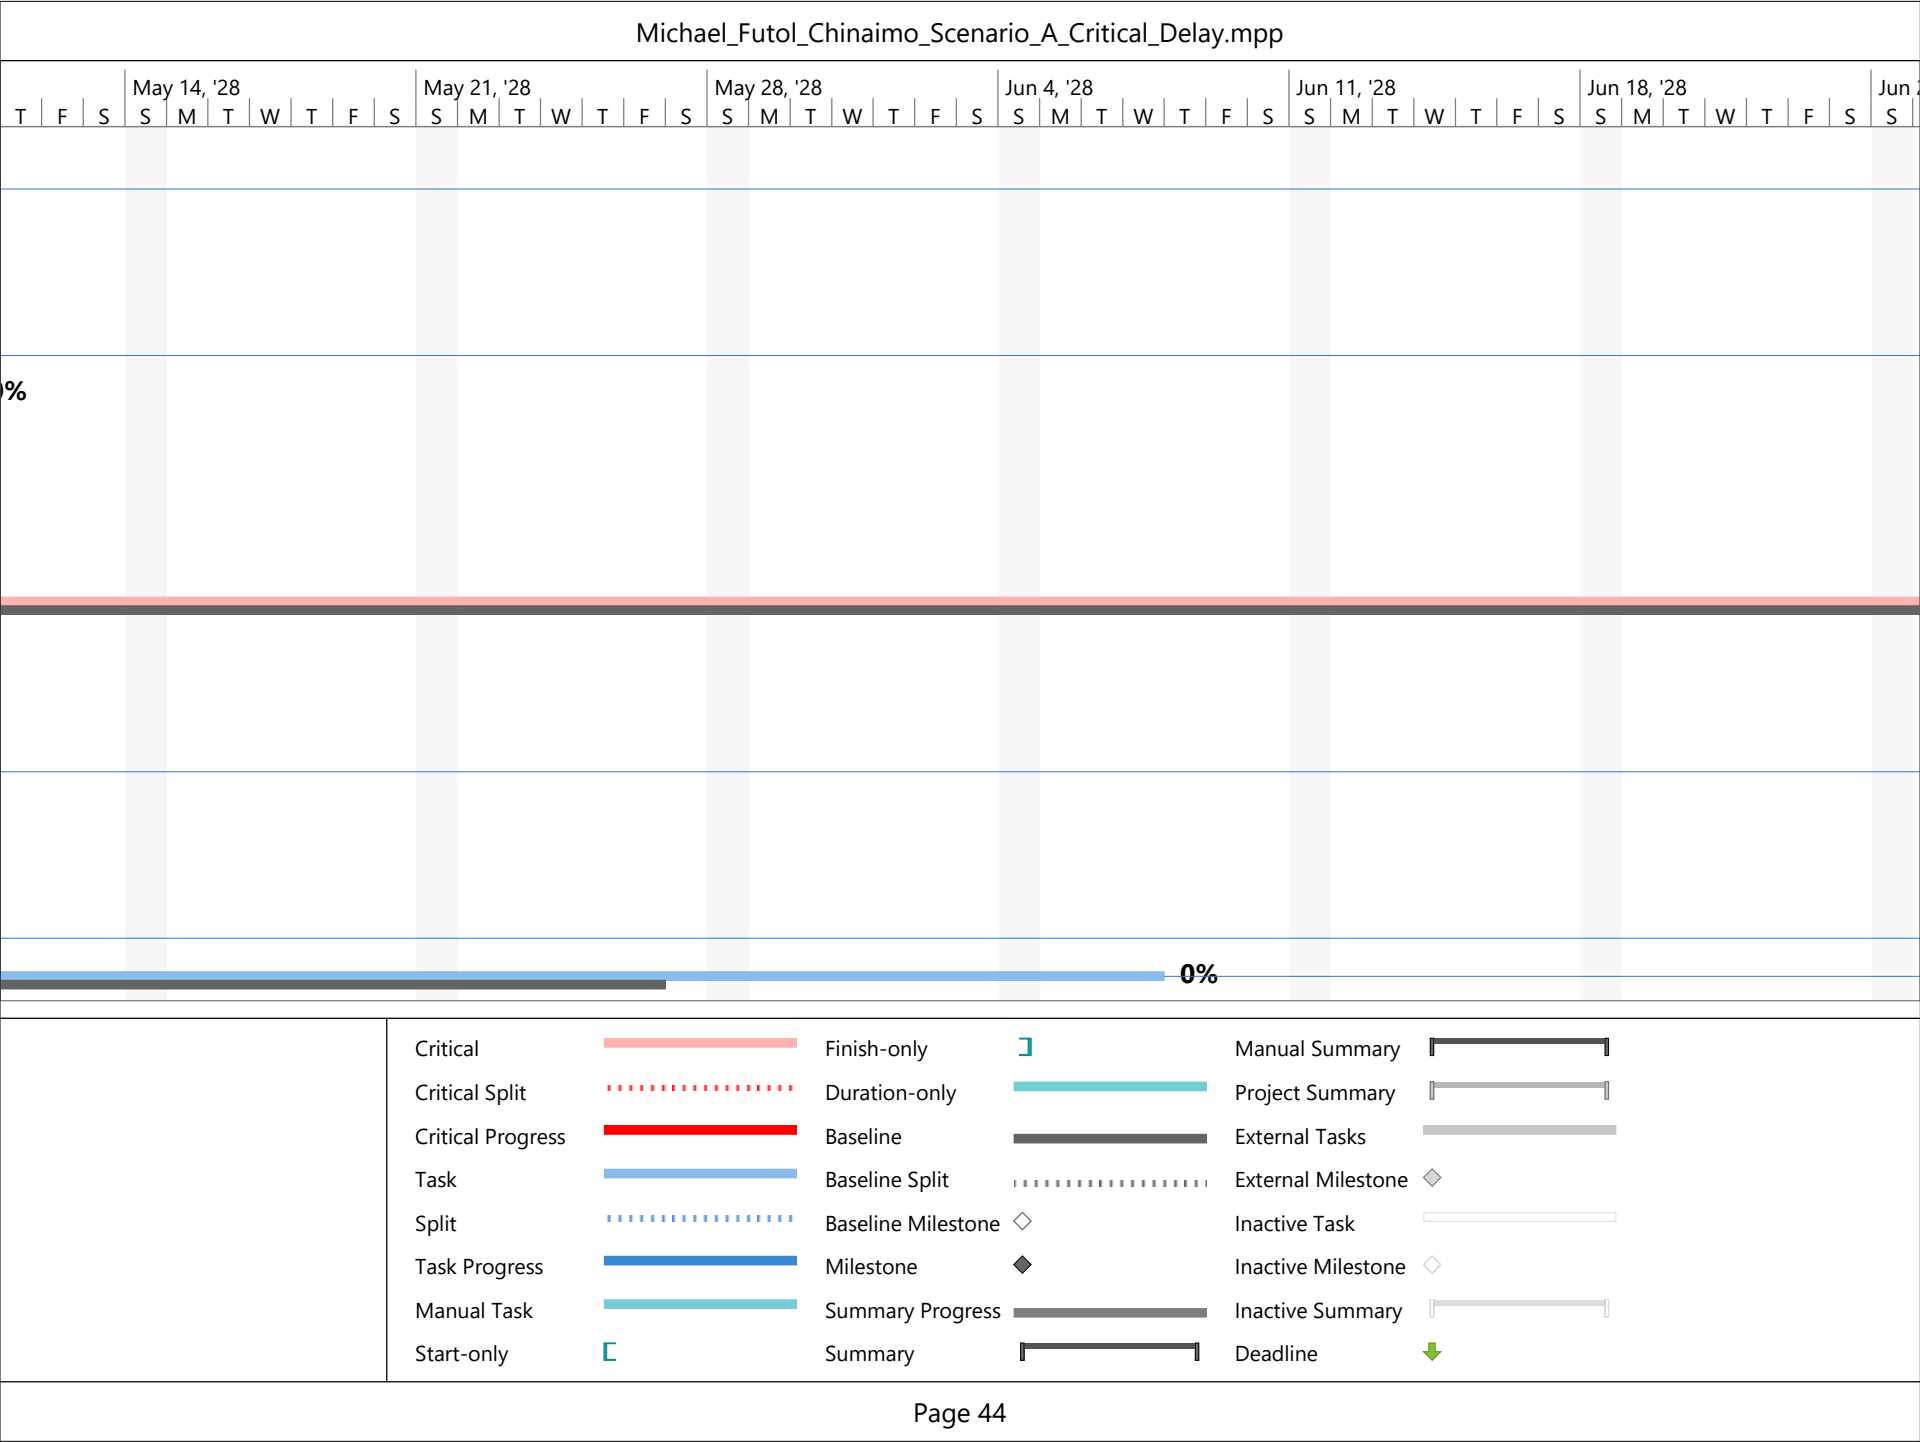

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp																																													
T	F	S	May 14, '28							May 21, '28							May 28, '28							Jun 4, '28							Jun 11, '28							Jun 18, '28							Jun
			S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S							
			Critical				Finish-only				Manual Summary																																		
			Critical Split				Duration-only				Project Summary																																		
			Critical Progress				Baseline				External Tasks																																		
			Task				Baseline Split				External Milestone																																		
			Split				Baseline Milestone				Inactive Task																																		
			Task Progress				Milestone				Inactive Milestone																																		
			Manual Task				Summary Progress				Inactive Summary																																		
			Start-only				Summary				Deadline																																		

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp



Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

25, '28 Jul 2, '28 Jul 9, '28 Jul 16, '28 Jul 23, '28 Jul 30, '28 Aug 6, '28


M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T

Task Type	Symbol/Color	Task Type	Symbol/Color	Task Type	Symbol/Color
Critical	Thick Red Bar	Finish-only	Red Bracket	Manual Summary	Thick Black Bar
Critical Split	Dotted Red Bar	Duration-only	Thick Cyan Bar	Project Summary	Thin Grey Bar
Critical Progress	Thick Red Bar	Baseline	Thick Black Bar	External Tasks	Thin Grey Bar
Task	Thick Blue Bar	Baseline Split	Dotted Black Bar	External Milestone	Grey Diamond
Split	Dotted Blue Bar	Baseline Milestone	White Diamond	Inactive Task	Thin White Bar
Task Progress	Thick Blue Bar	Milestone	Black Diamond	Inactive Milestone	White Diamond
Manual Task	Thick Cyan Bar	Summary Progress	Thick Black Bar	Inactive Summary	Thin Grey Bar
Start-only	Red Bracket	Summary	Thick Black Bar	Deadline	Green Arrow

Page 47


Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

25, '28							Jul 2, '28							Jul 9, '28							Jul 16, '28							Jul 23, '28							Jul 30, '28							Aug 6, '28						
M	T	W	T	F	S		S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T		




Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

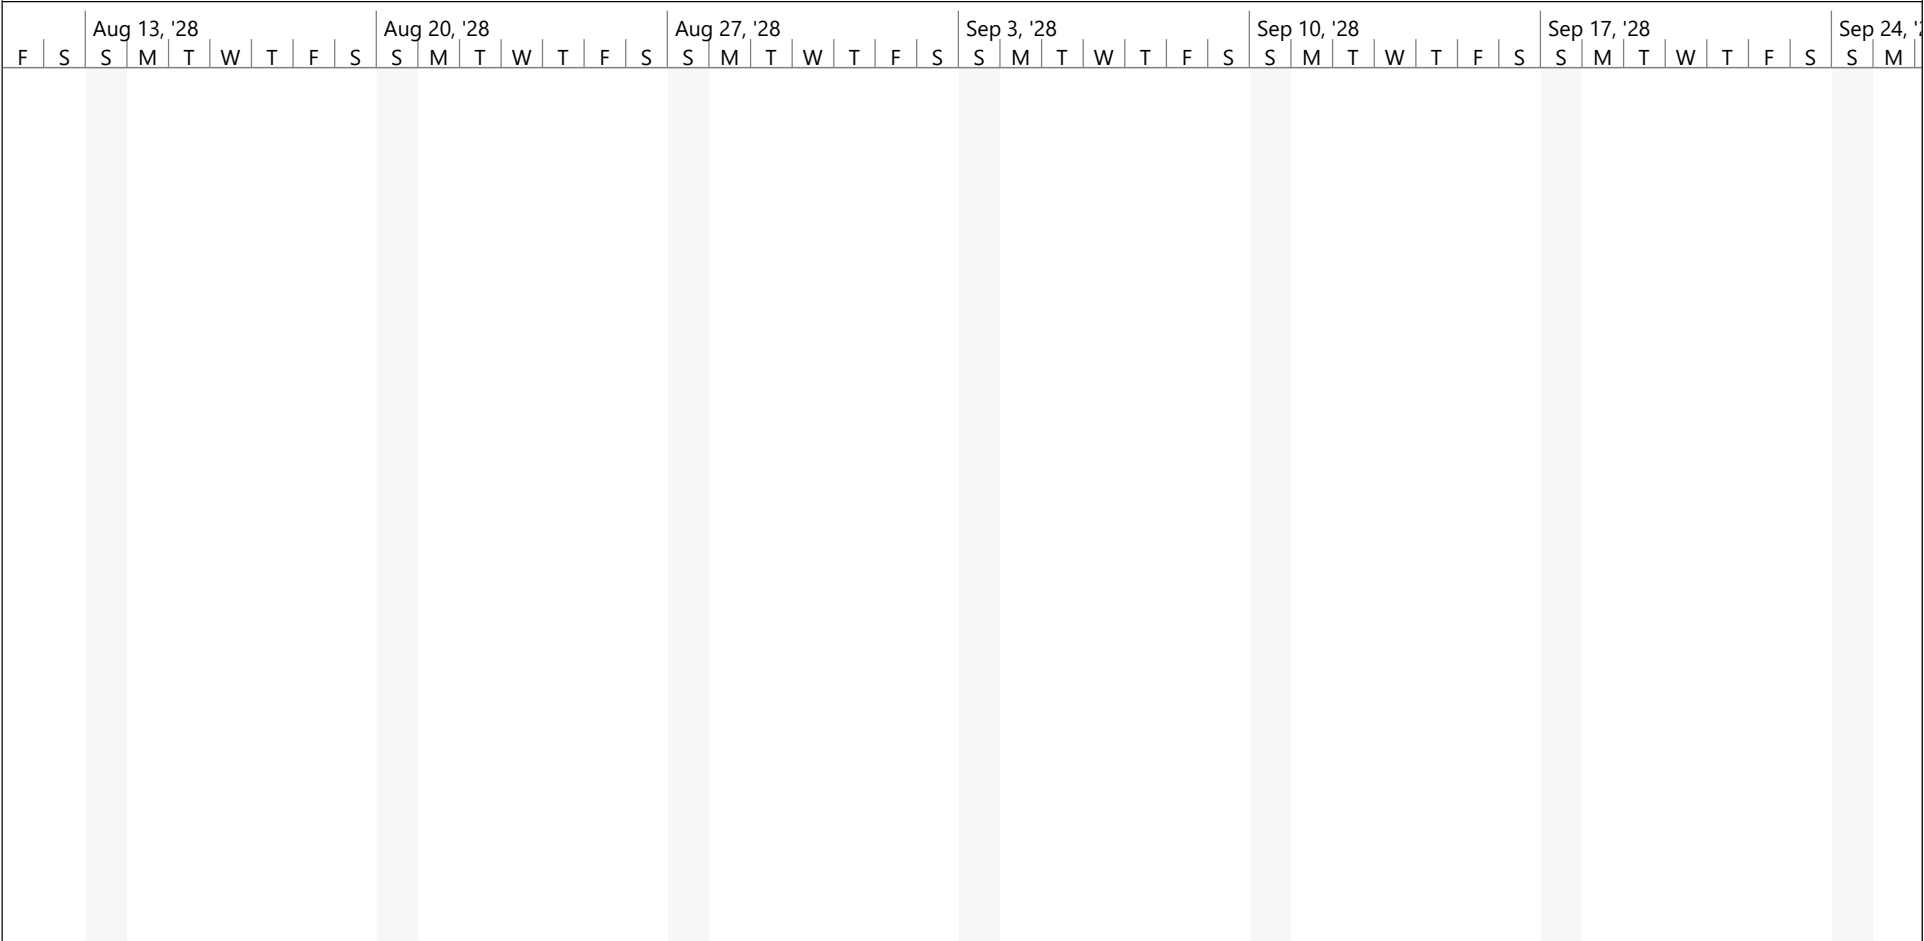

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

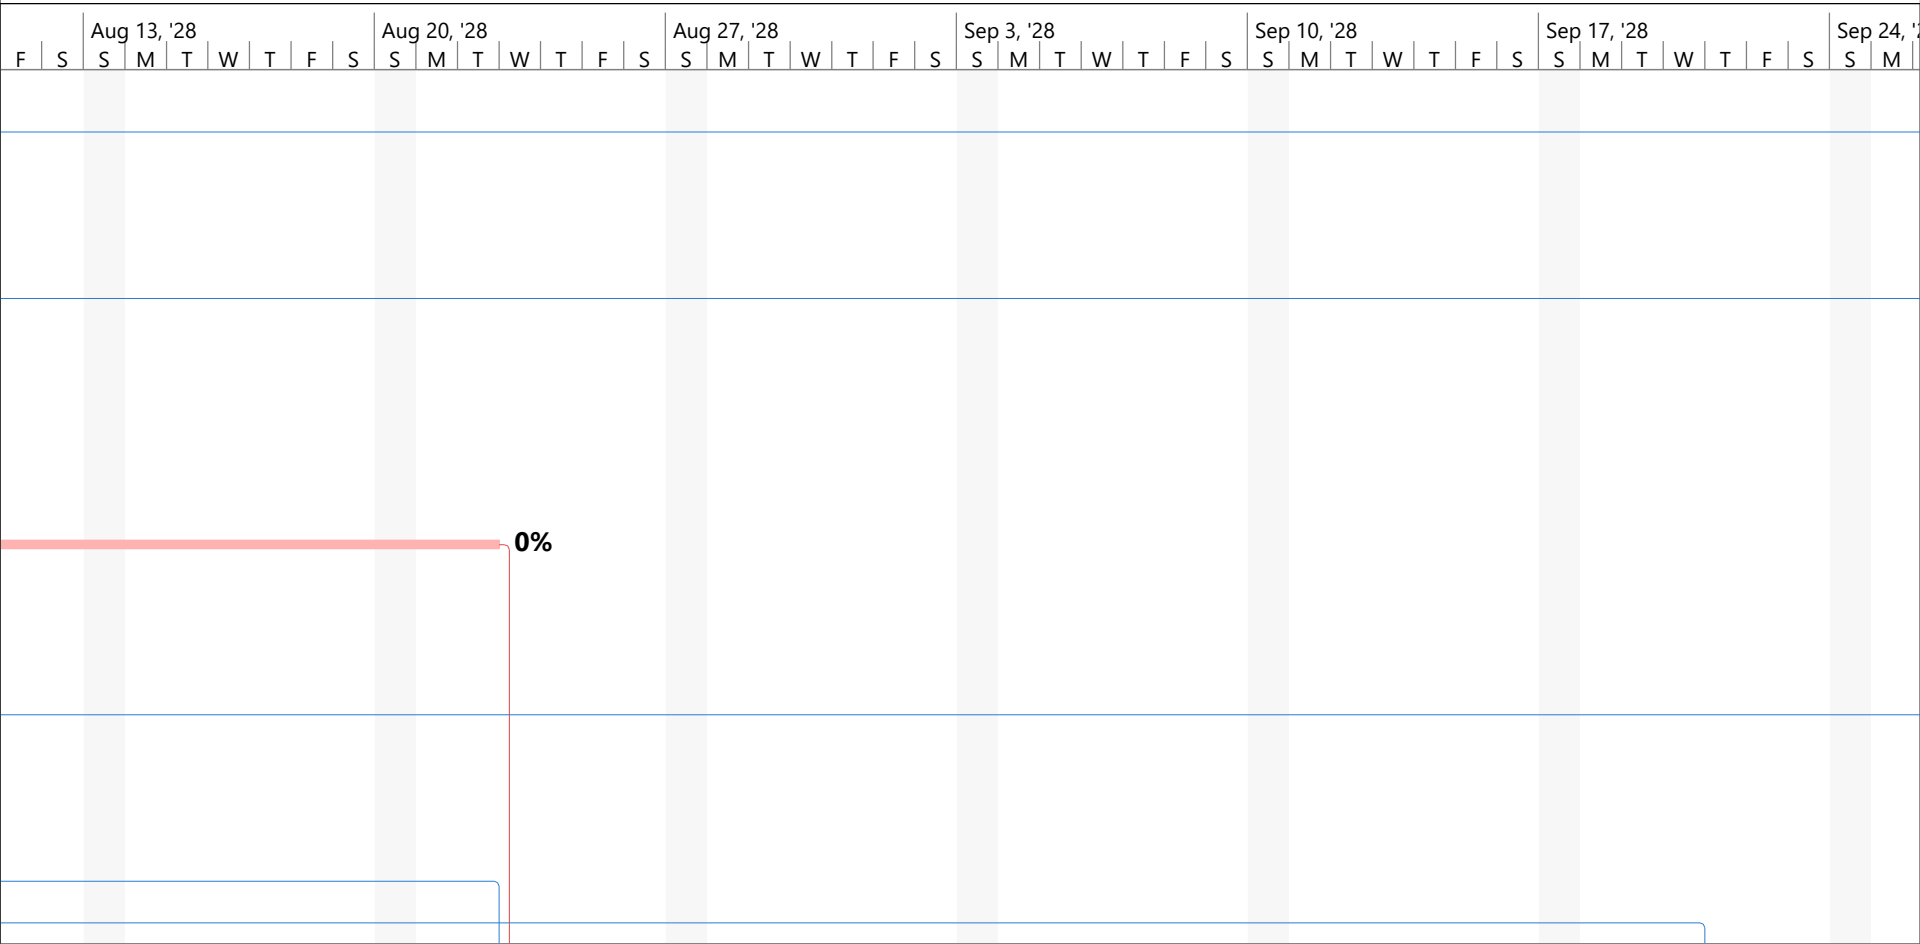

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

The Gantt chart displays a project schedule from August 13, 2028, to September 24, 2028. The critical path is highlighted in red, starting on August 20 and ending on September 3. A task is shown as a blue bar from August 20 to August 27. A summary task is shown as a grey bar from August 27 to September 3. A milestone is marked on September 3. The chart includes a legend at the bottom with 14 items: Critical, Critical Split, Critical Progress, Task, Split, Task Progress, Manual Task, Start-only, Finish-only, Duration-only, Baseline, Baseline Split, Baseline Milestone, Milestone, Summary Progress, Summary, Manual Summary, Project Summary, External Tasks, External Milestone, Inactive Task, Inactive Milestone, Inactive Summary, and Deadline.

Task Name	Start Date	End Date	Task Type
Task	Aug 20, '28	Aug 27, '28	Task
Summary Task	Aug 27, '28	Sep 3, '28	Summary Task
Critical Path	Aug 20, '28	Sep 3, '28	Critical Path


Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

28					Oct 1, '28					Oct 8, '28					Oct 15, '28					Oct 22, '28					Oct 29, '28					Nov 5, '28								
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	


Page 52

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

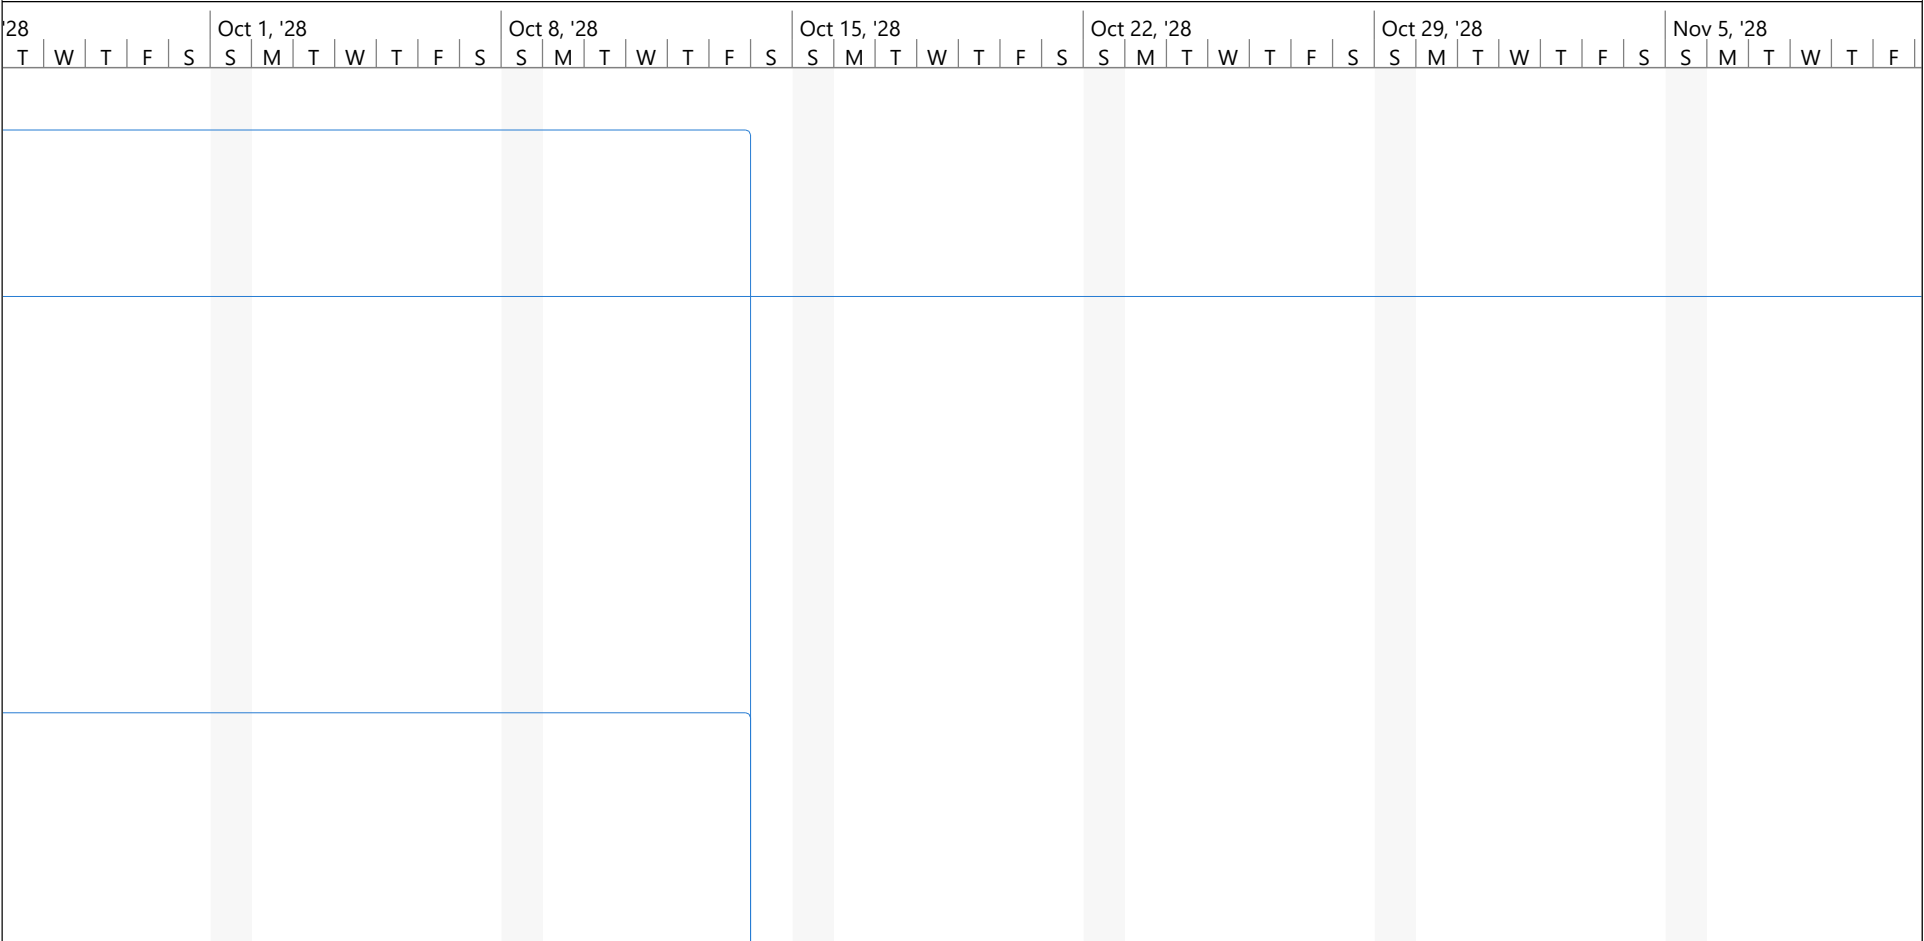


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

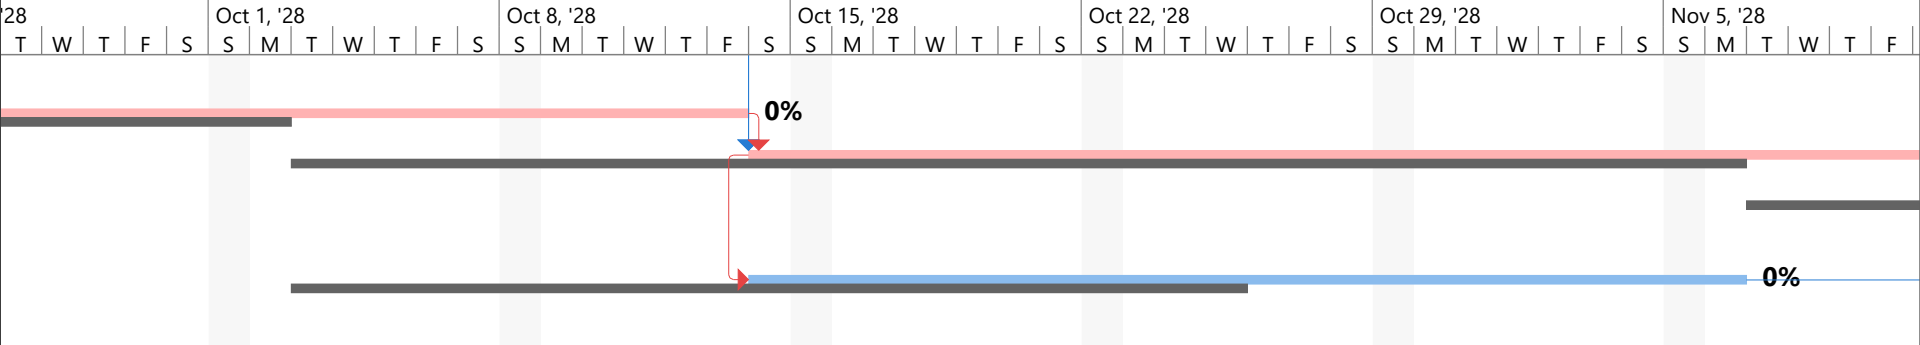

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

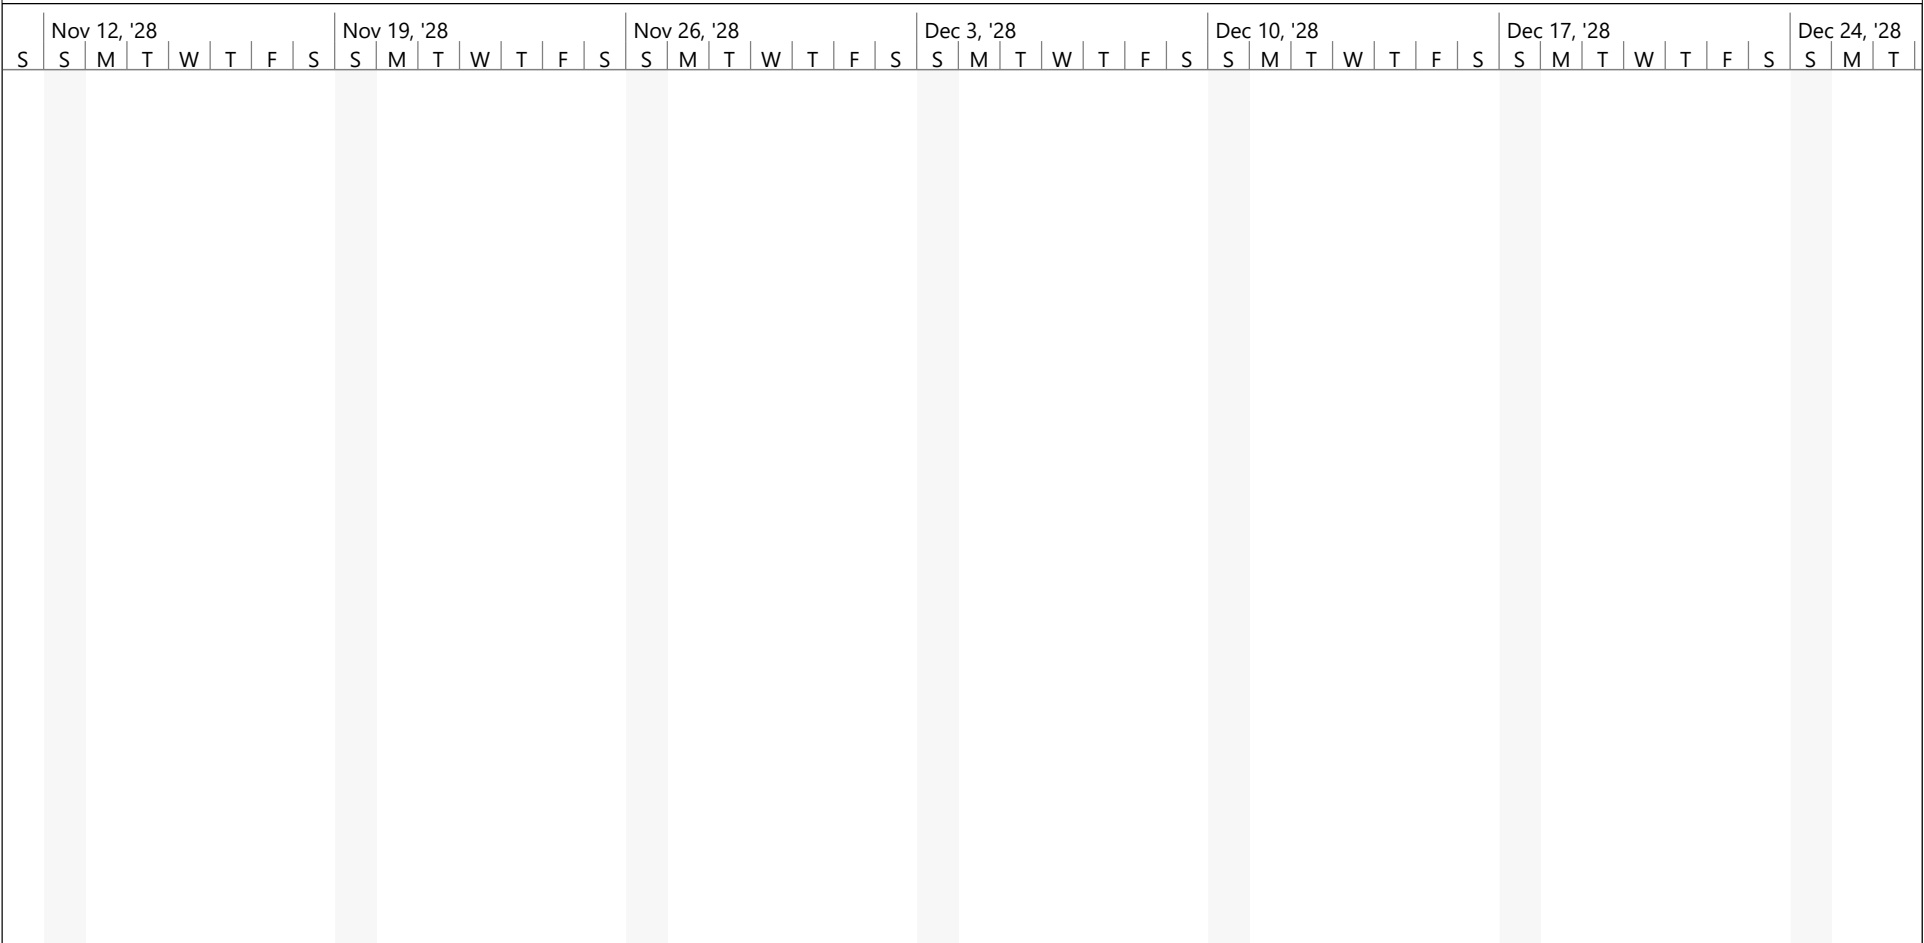


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

Nov 12, '28							Nov 19, '28							Nov 26, '28							Dec 3, '28							Dec 10, '28							Dec 17, '28							Dec 24, '28		
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T						


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

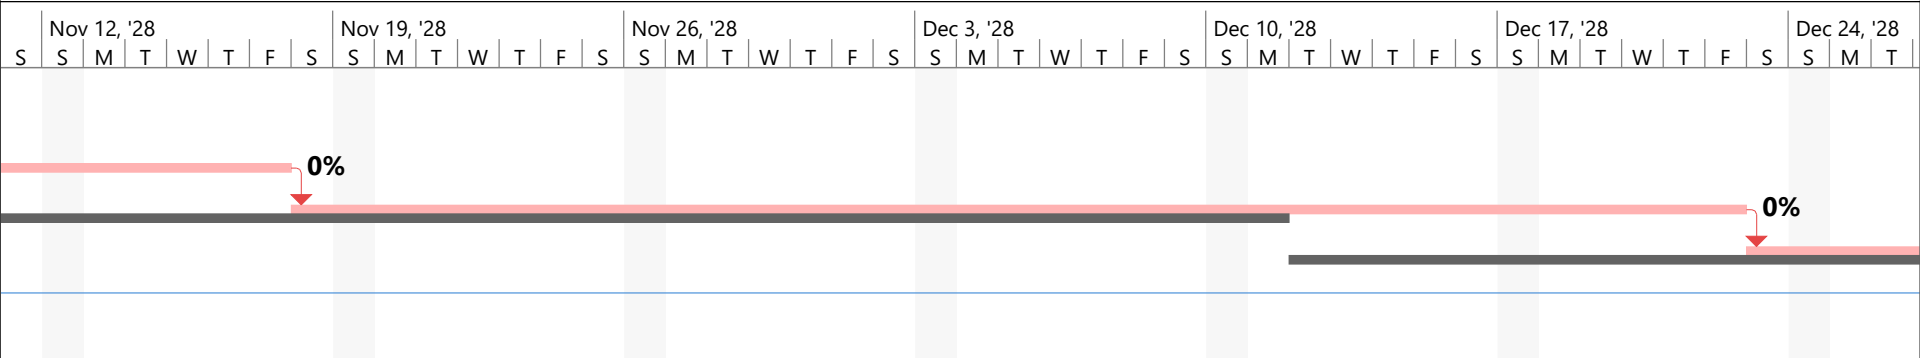


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

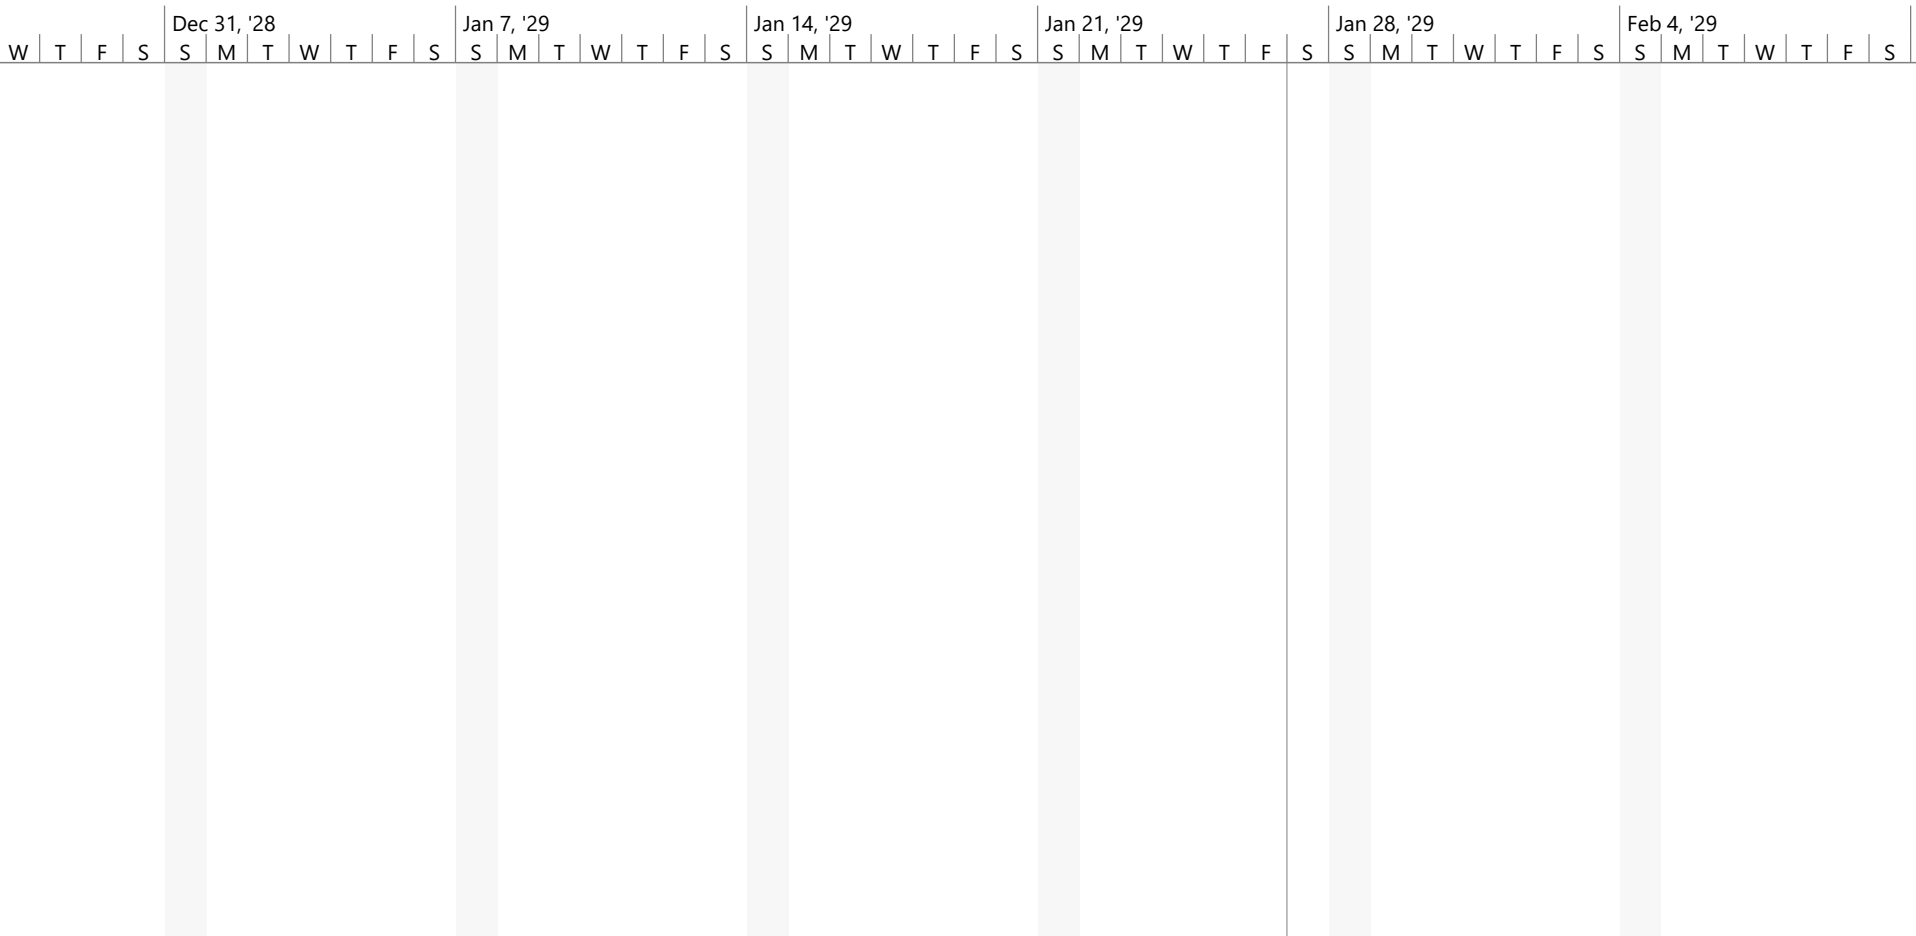


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

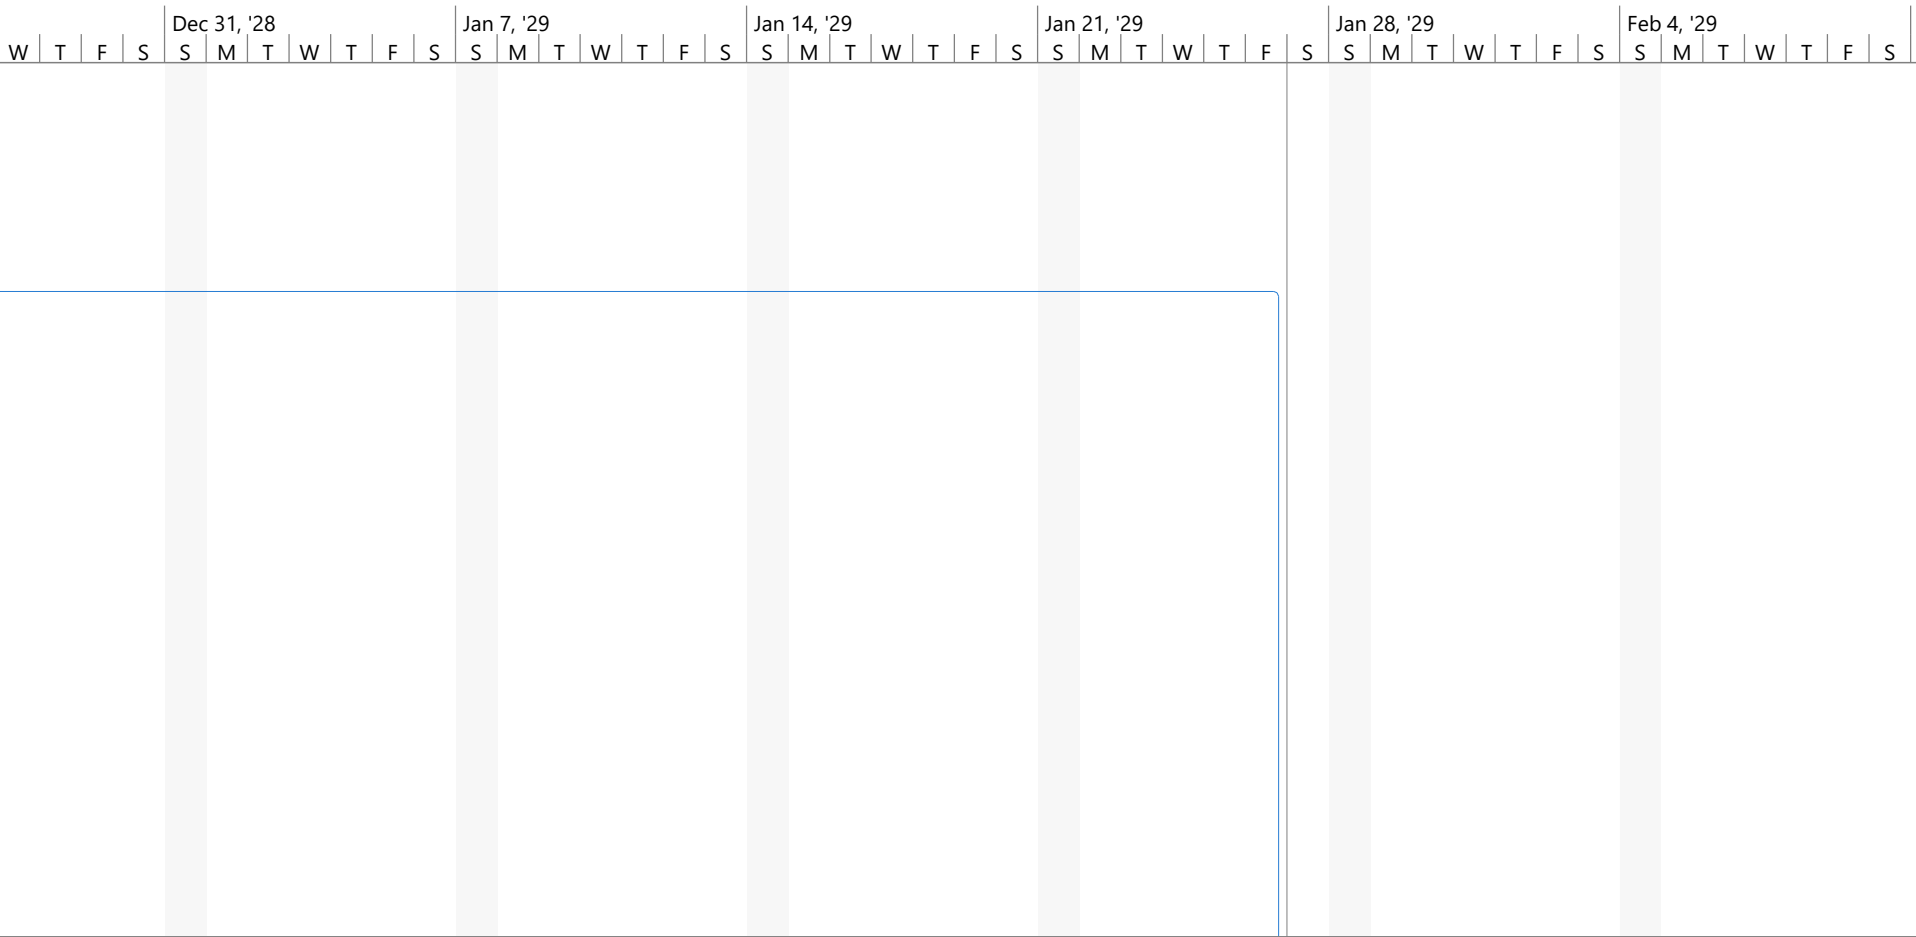

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Michael_Futol_Chinaimo_Scenario_A_Critical_Delay.mpp

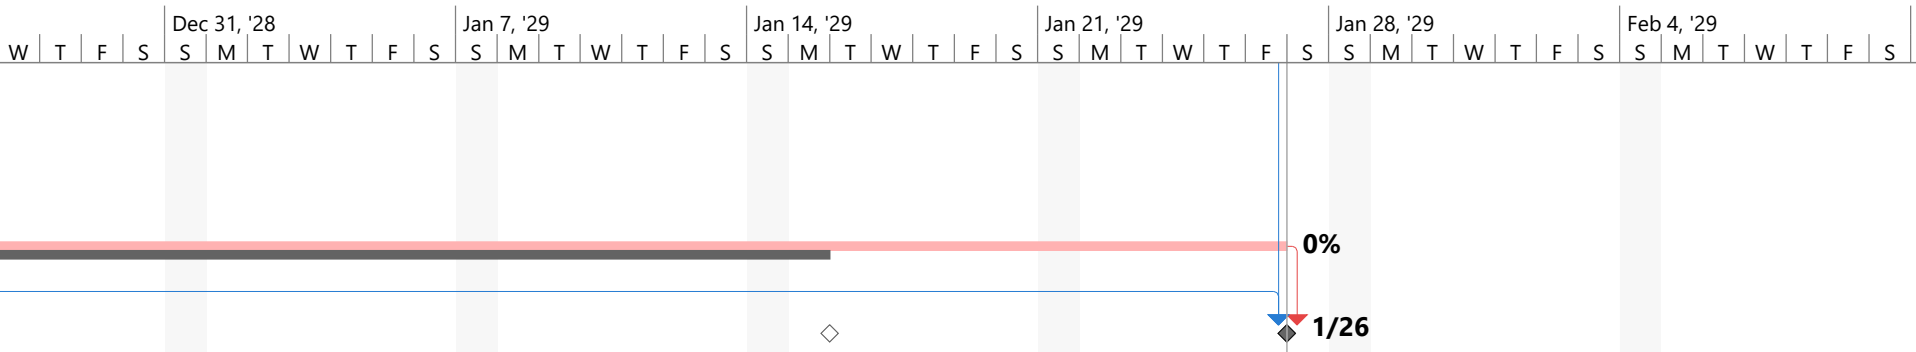

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	
