

Michael_Futol_Chinaimo_Actual_Progress.mpp

ID	Task Name	Act. Start	Act. Finish	% Comp.	Phys. % Comp.	Act. Dur.
5	Method Statement	on 10/13/25	NA	90%	90%	10.5 days
11	WTP Foundation	on 12/22/25	NA	75%	75%	45 days
13	Sedimentation Basins	Wed 3/25/26	NA	25%	25%	25 days
14	Rapid Sand Filter	NA	NA	0%	0%	0 days
15	Internal Channels	NA	NA	0%	0%	0 days
16	Waterproofing /	NA	NA	0%	0%	0 days
17	Hydrostatic / Structural	NA	NA	0%	0%	0 days
19	Reservoir Foundations	Wed 12/10/25	NA	80%	80%	48 days
20	Reservoir Walls /	Wed 2/18/26	NA	45%	45%	45 days
26	Administration & Training	Fri 12/4/25	NA	22%	22%	16.4 days
28	Process Piping Installation	NA	NA	0%	0%	0 days
33	Instrumentation	NA	NA	0%	0%	0 days
39	Pole / Foundation	Wed 12/16/25	NA	40%	40%	40 days
43	Electrical / I&C Preparation	NA	NA	0%	0%	0 days
44	Dry Commissioning	NA	NA	0%	0%	0 days
45	Wet Commissioning	NA	NA	0%	0%	0 days
46	Performance / Verification	NA	NA	0%	0%	0 days
47	Punch List / Rectification	NA	NA	0%	0%	0 days
49	Taking Over / Closeout	NA	NA	0%	0%	0 days

Critical

Critical Split

Critical Progress

Task

Split

Task Progress

Manual Task

Start-only

Finish-only

Duration-only

Baseline

Baseline Split

Baseline Milestone

Milestone

Summary Progress

Summary

Manual Summary

Project Summary

External Tasks

External Milestone

Inactive Task


Inactive Milestone


Inactive Summary


Deadline










CURRENT CRITICAL PATH | Critical-filtered current programme; activities shown control forecast finish.

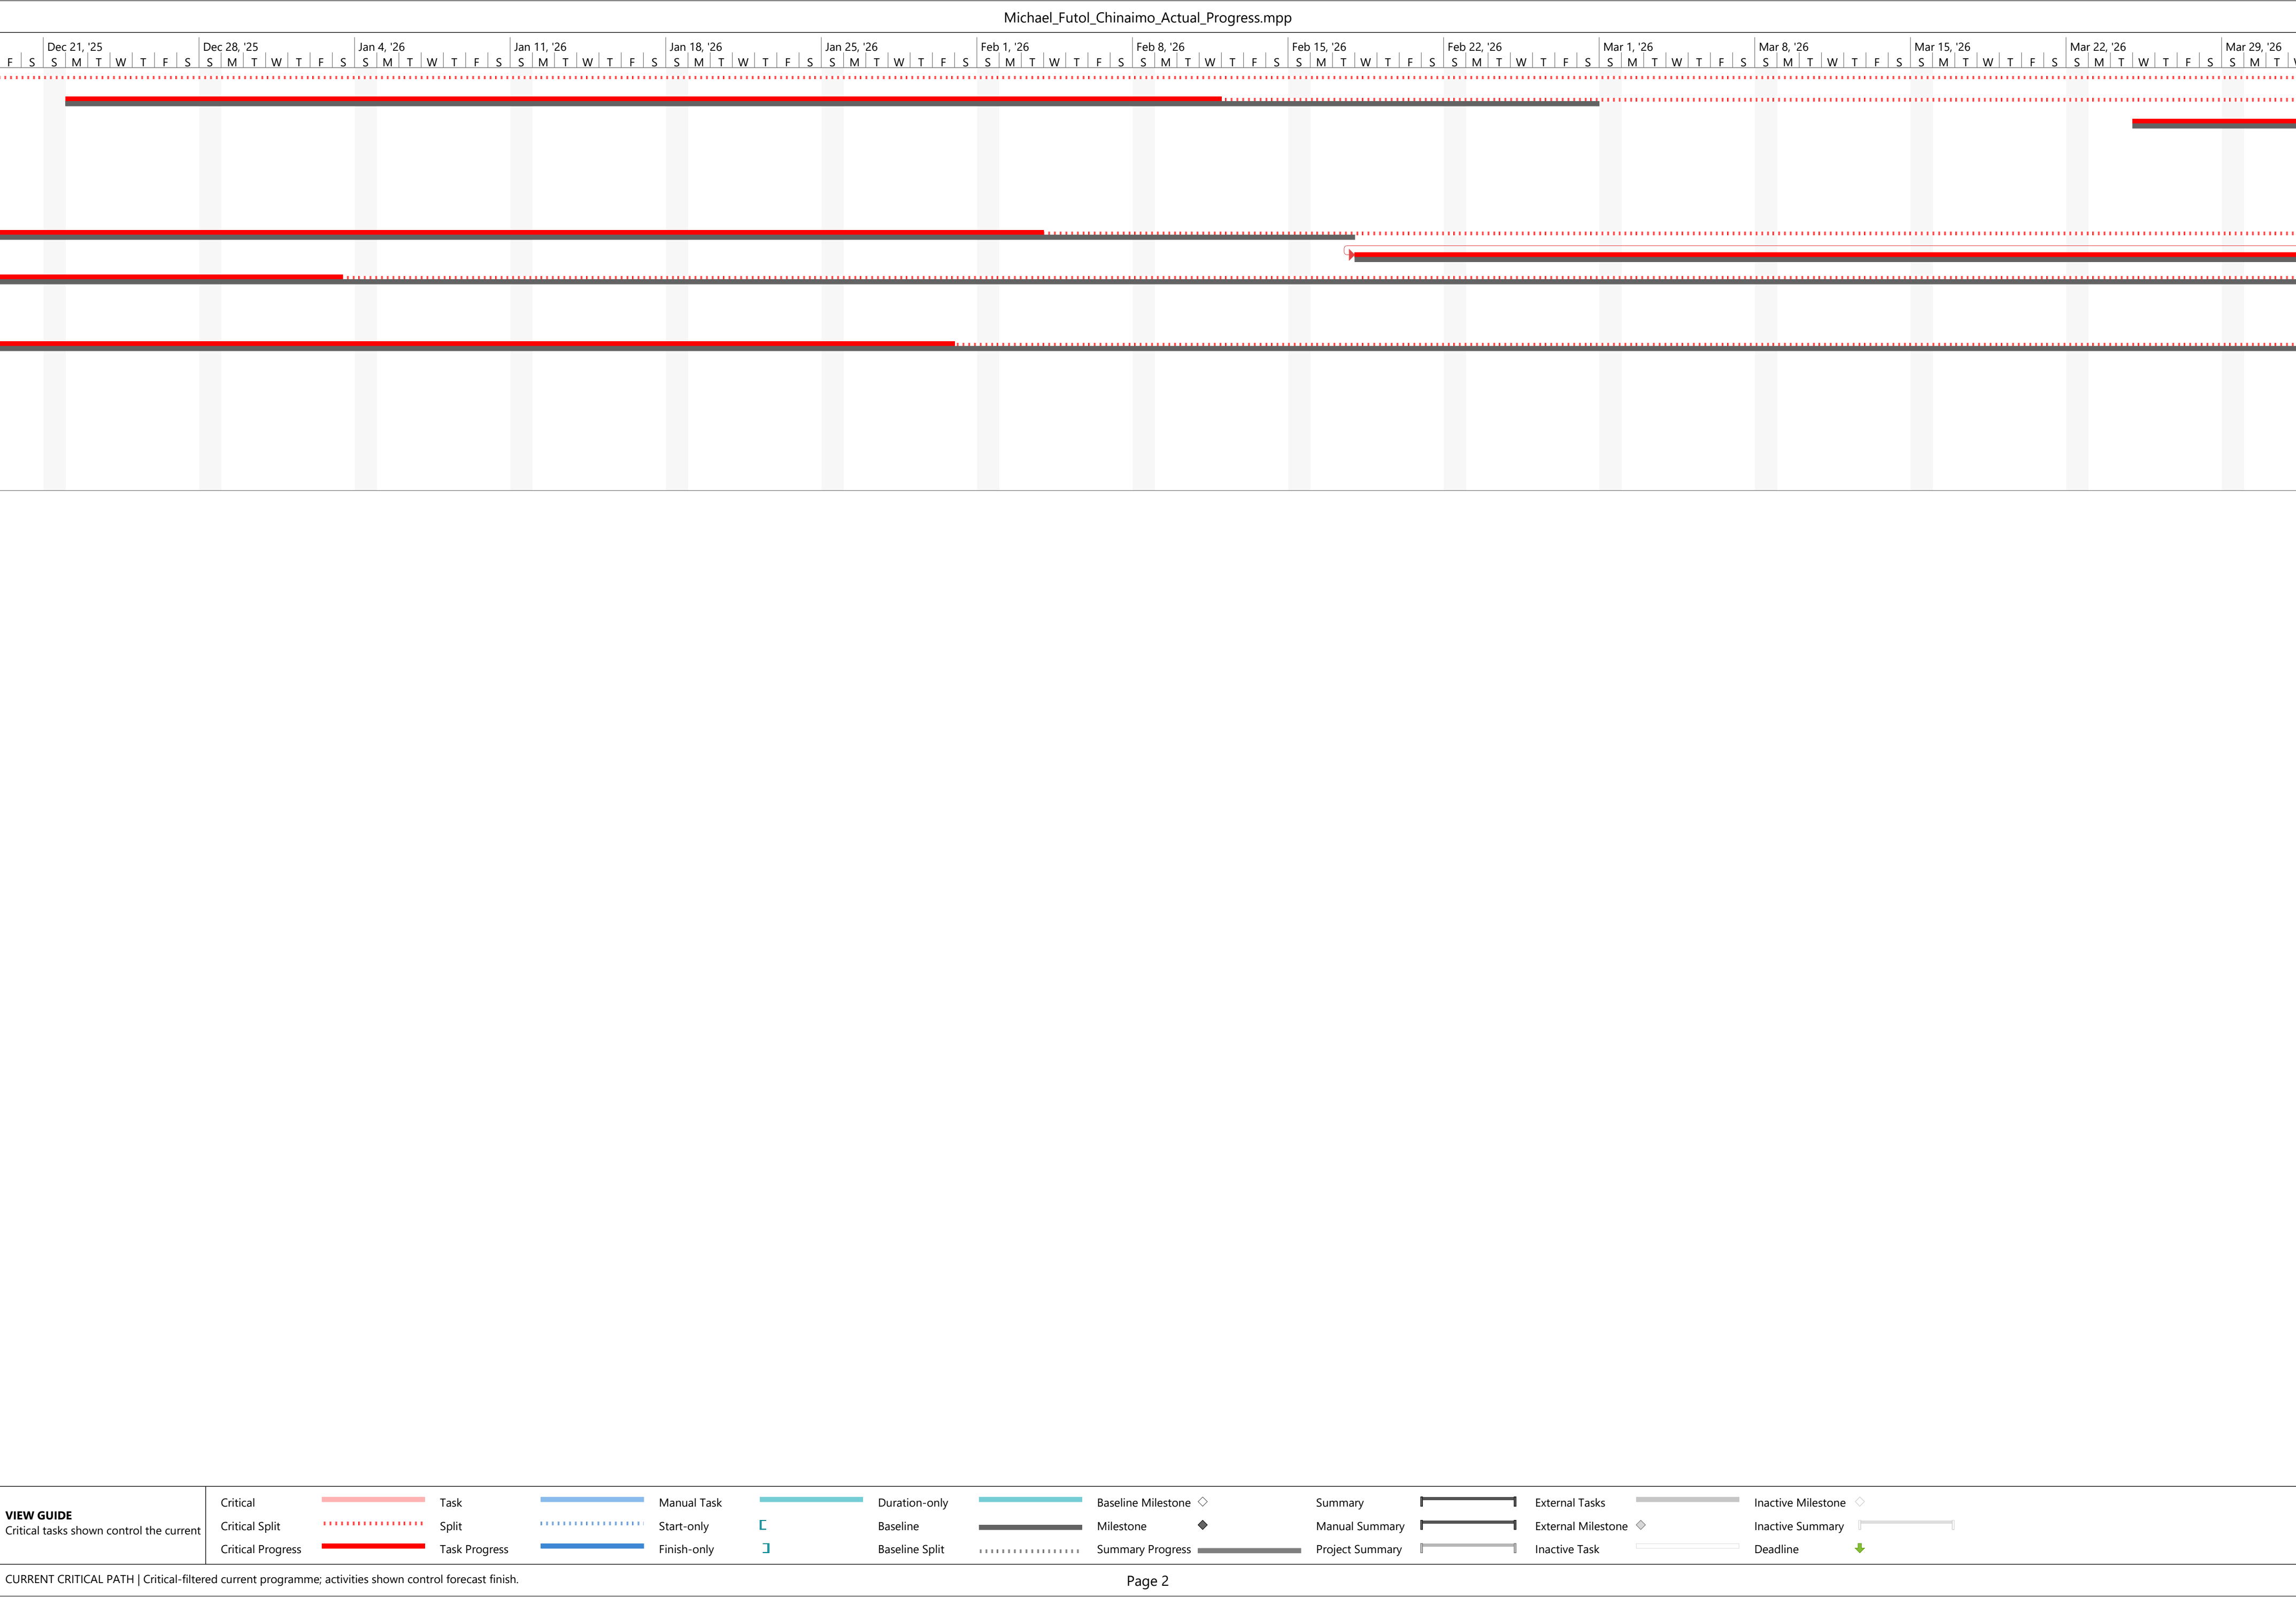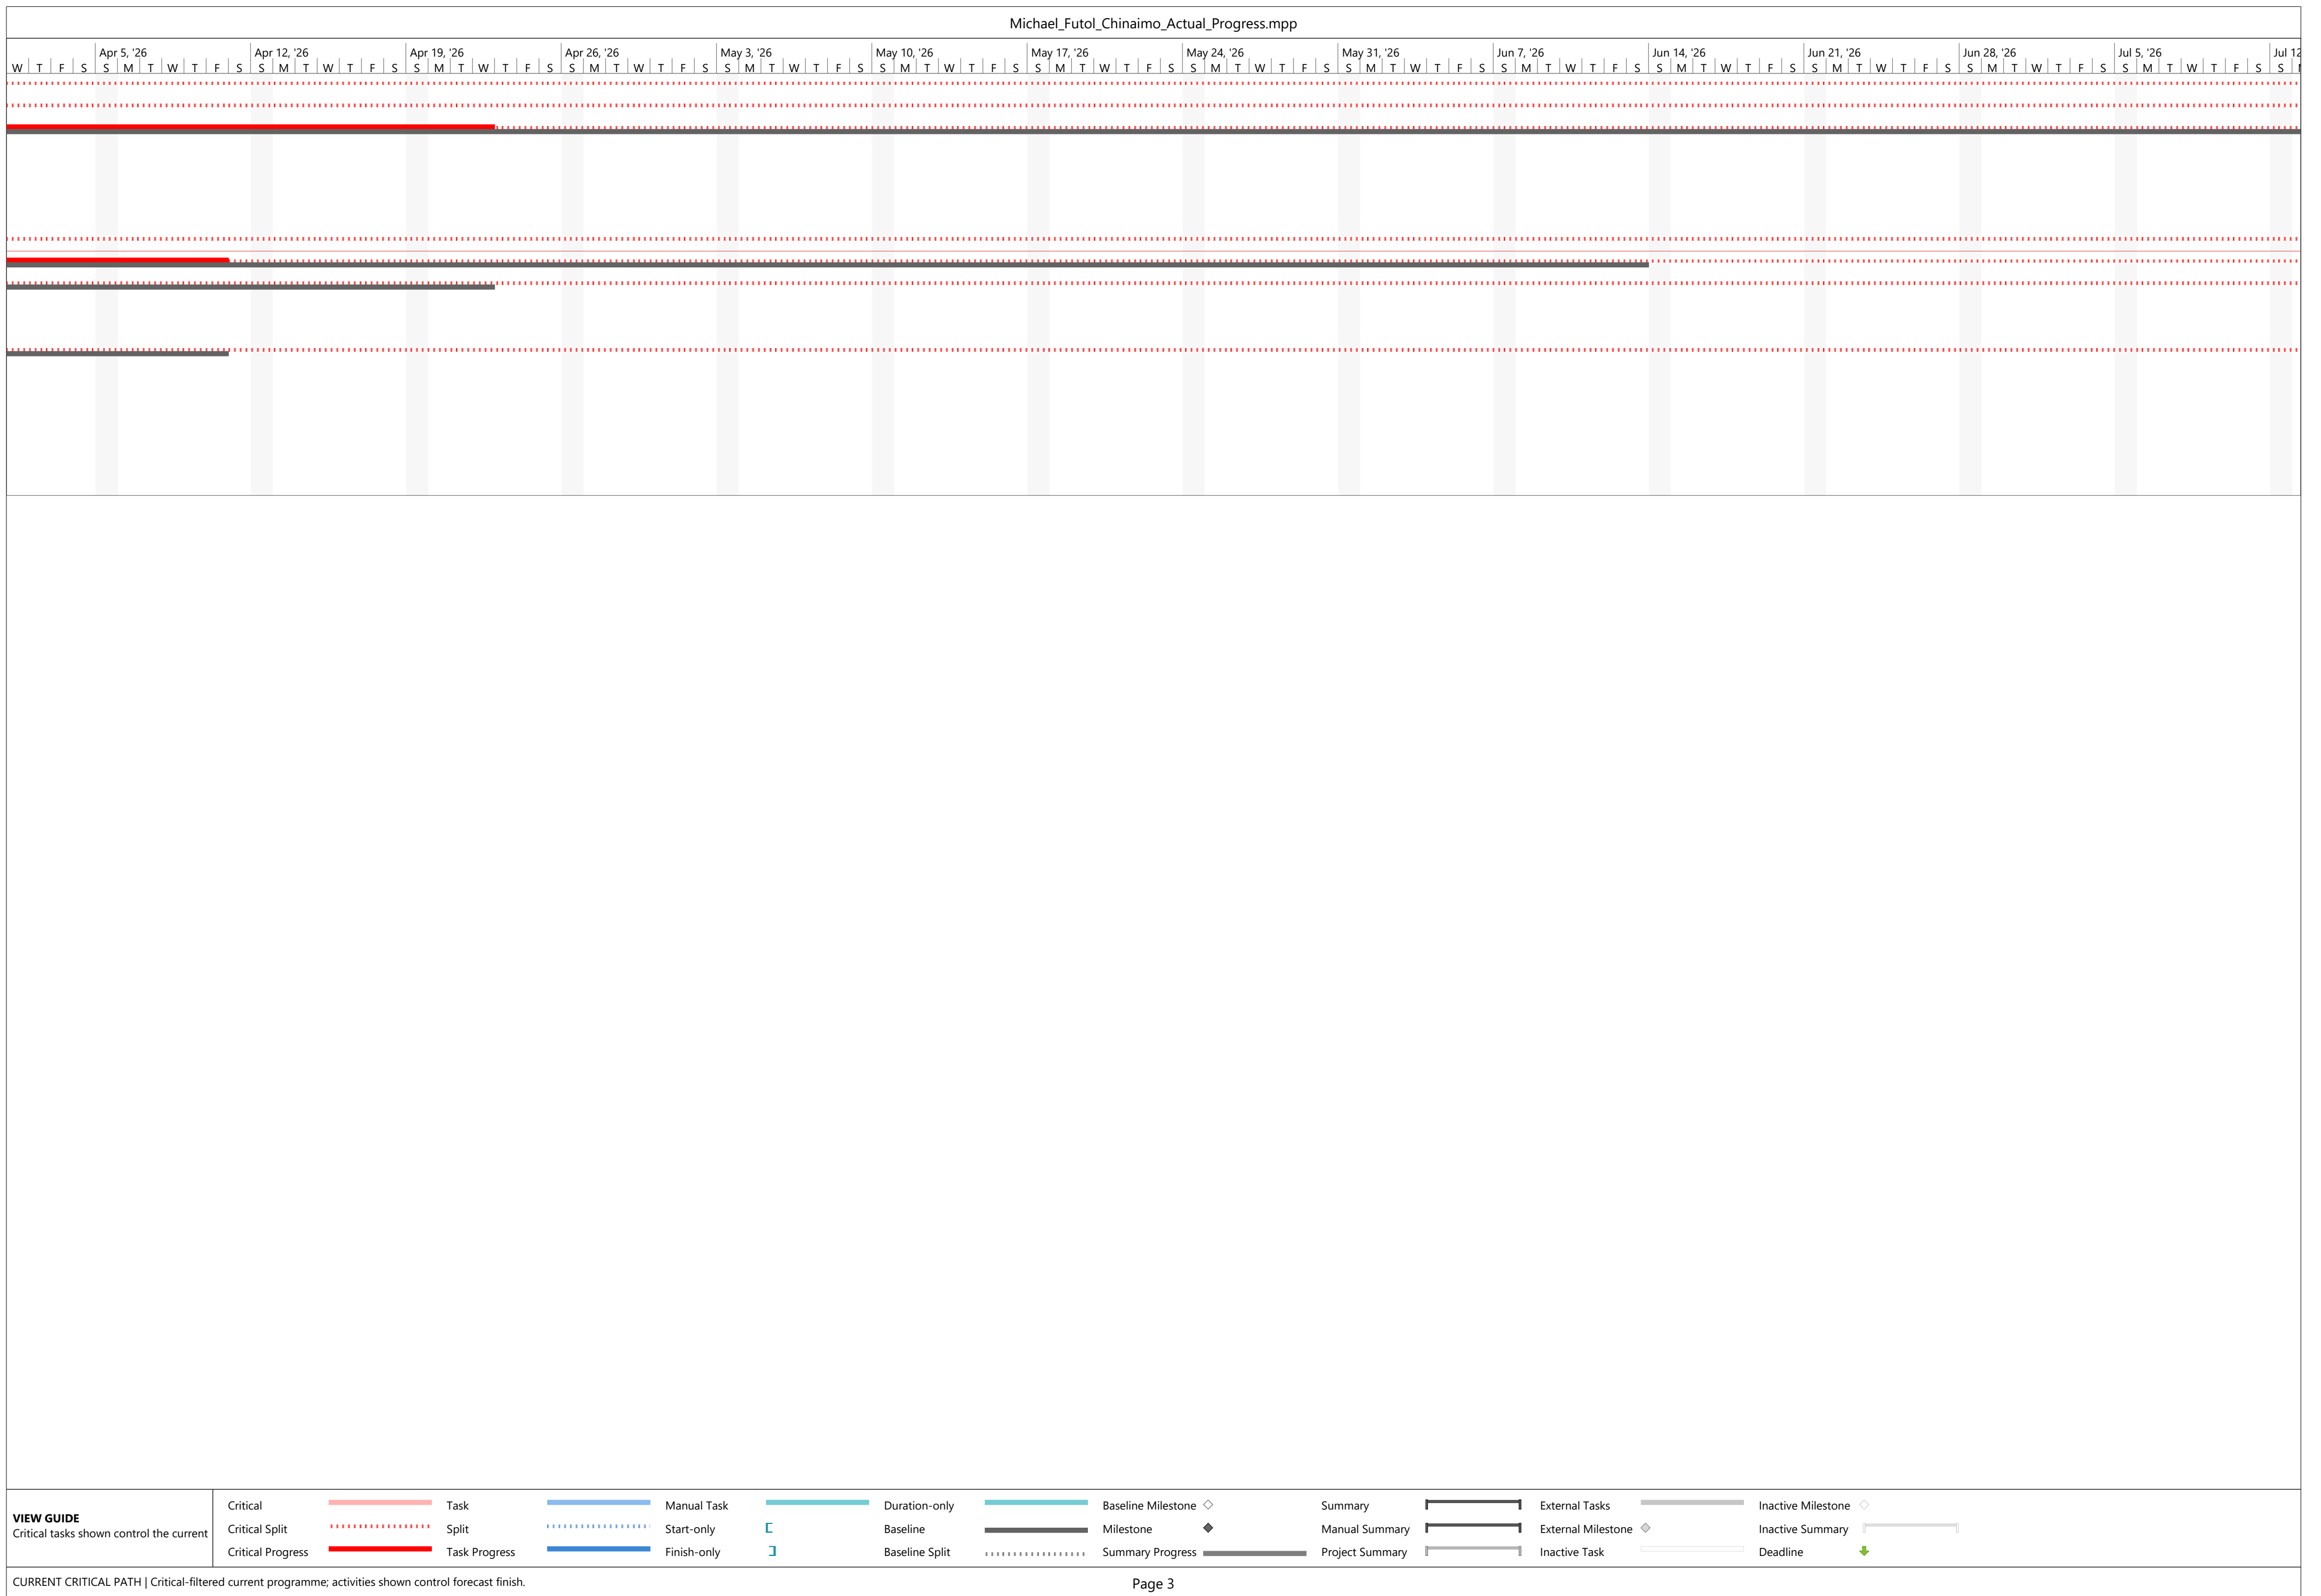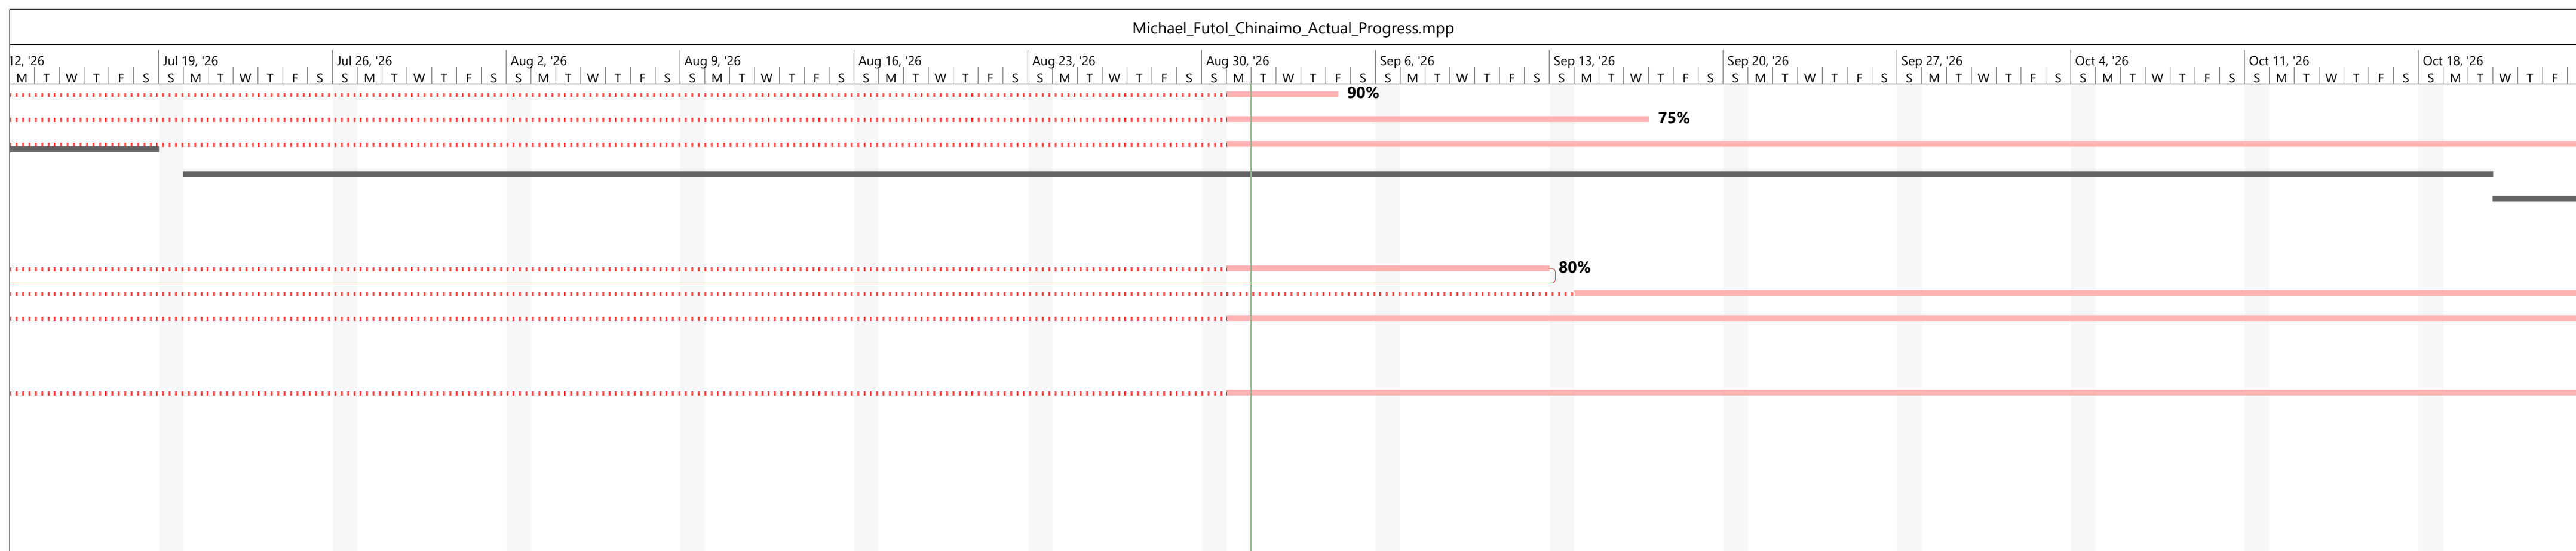
Page 1









VIEW GUIDE Critical tasks shown control the current	Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
	Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
	Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

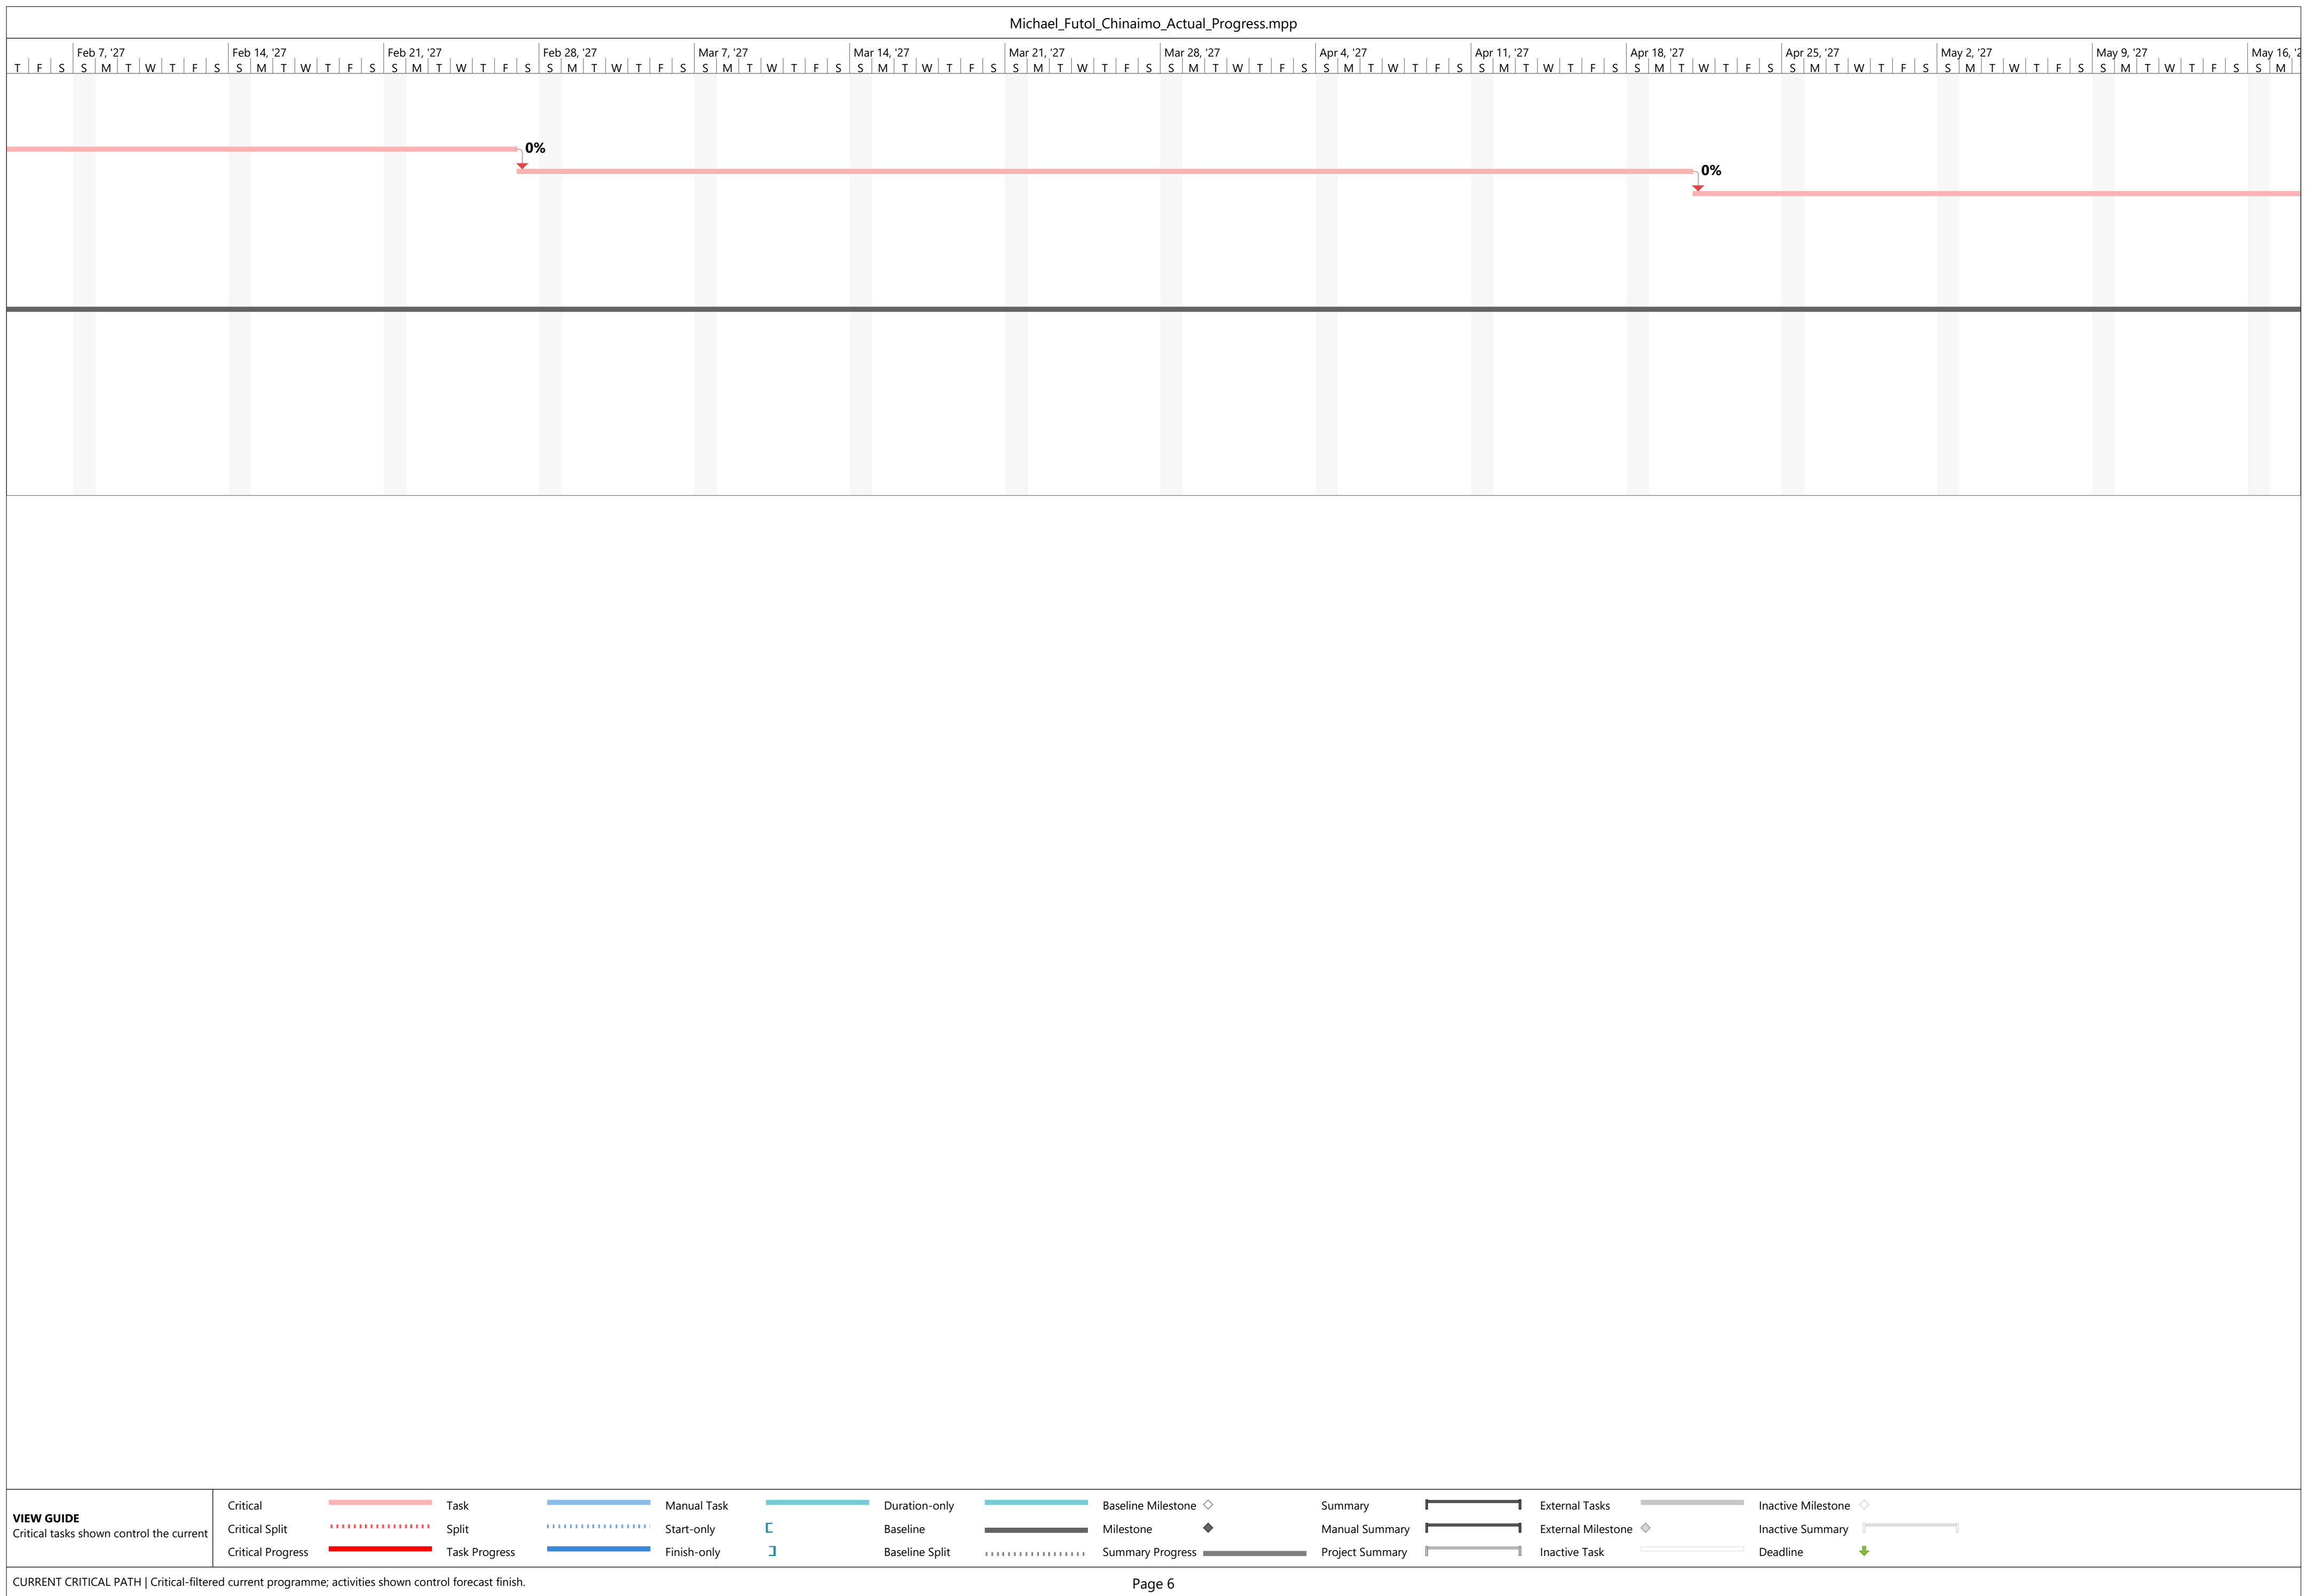

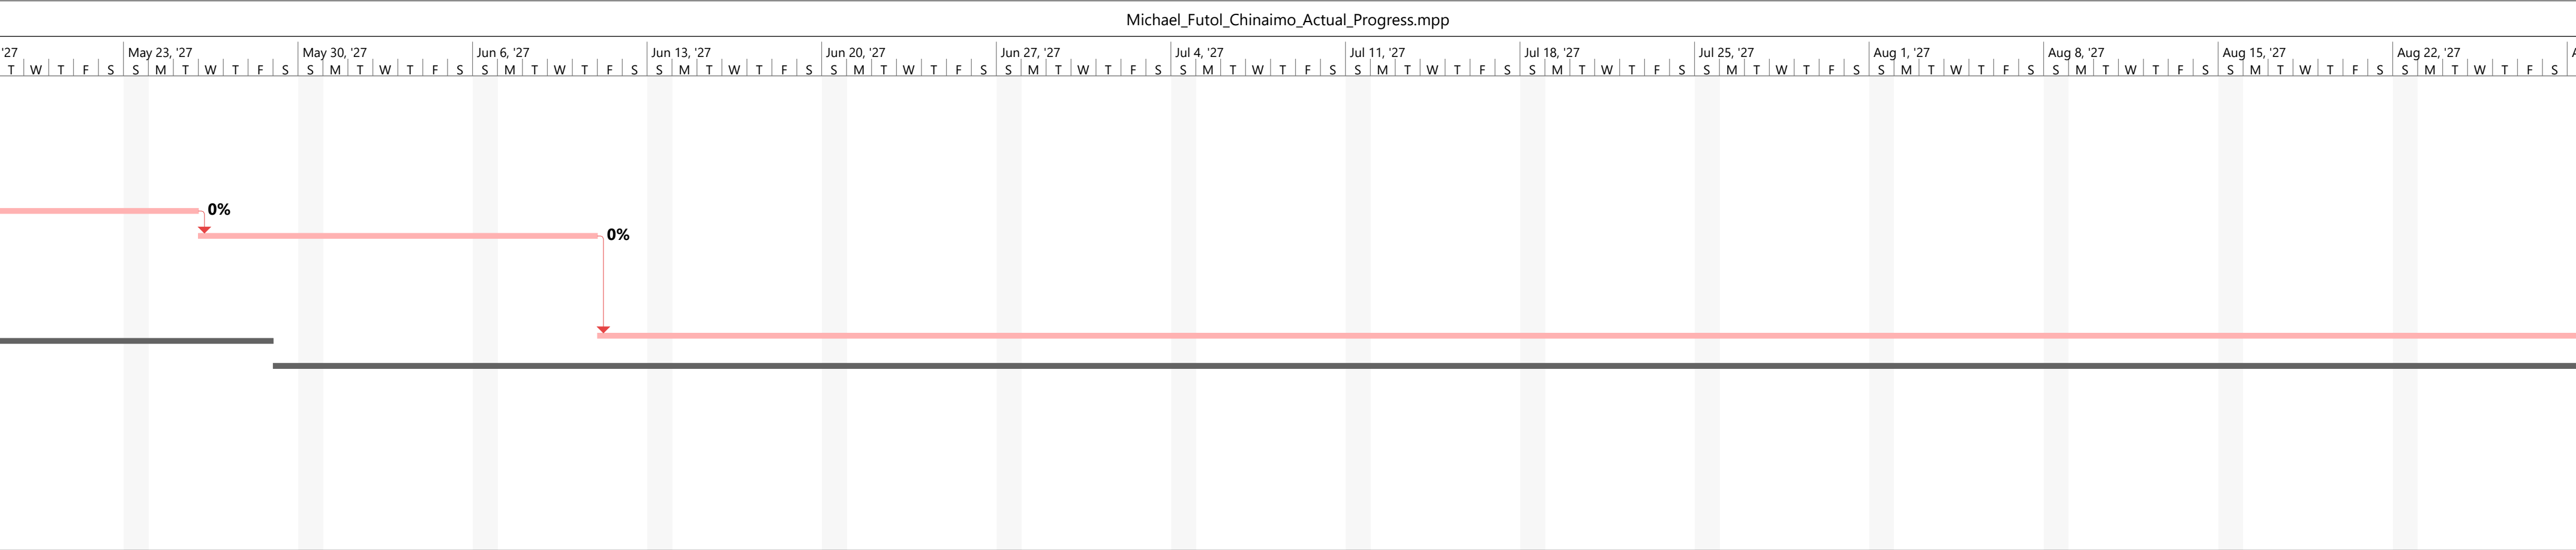

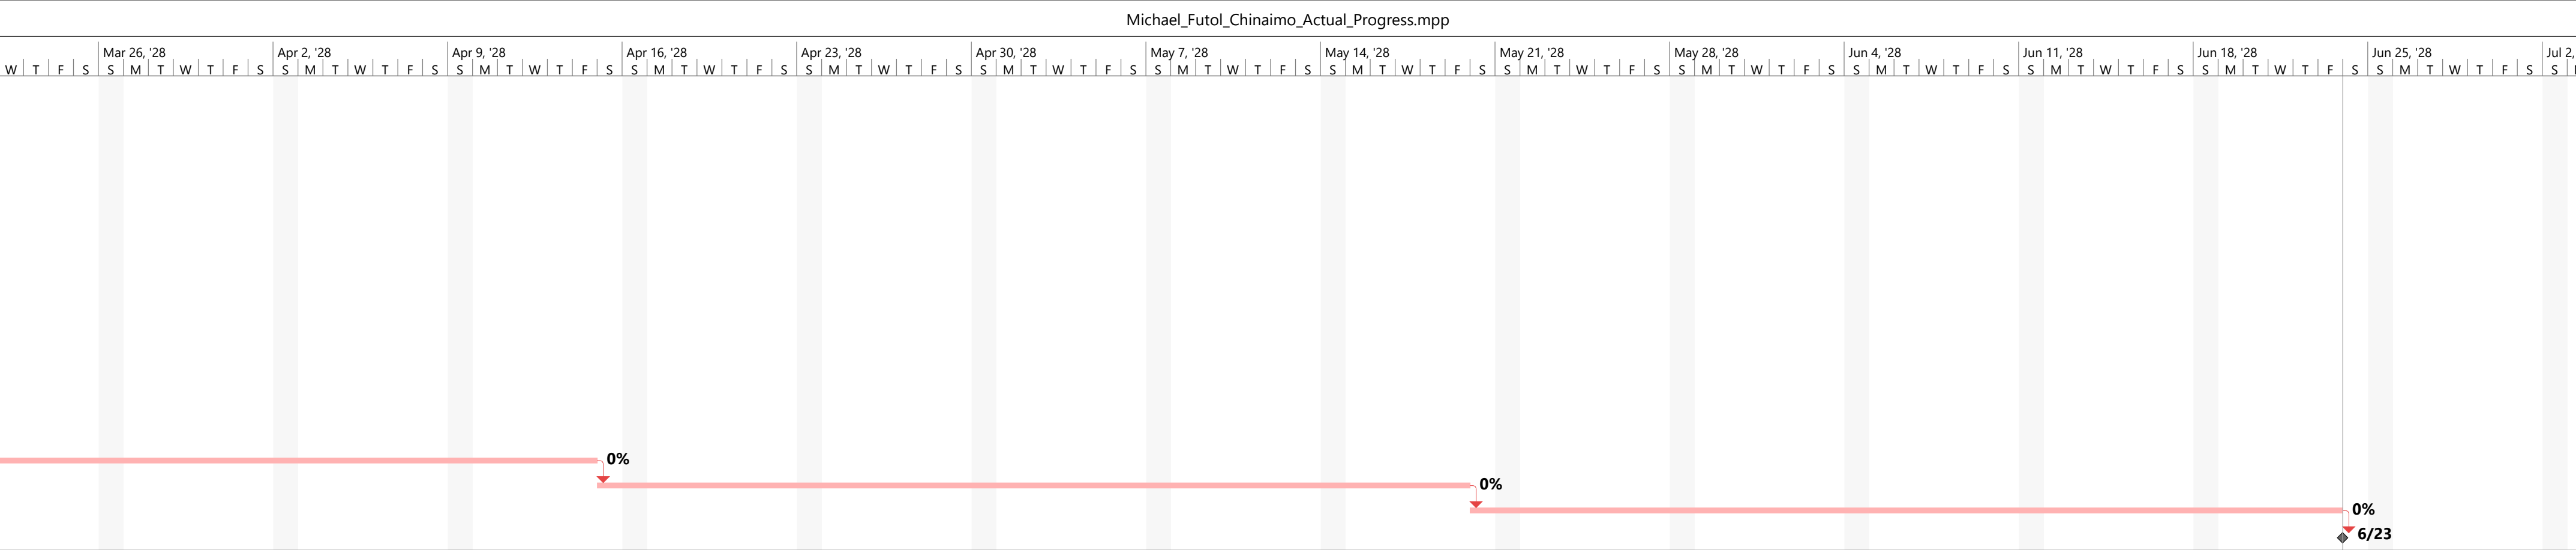

VIEW GUIDE Critical tasks shown control the current	Critical		Task		Manual Task		Duration-only		Baseline Milestone	◇	Summary		External Tasks		Inactive Milestone	◇
	Critical Split		Split		Start-only		Baseline		Milestone	◆	Manual Summary		External Milestone	◆	Inactive Summary	
	Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	↓
