

Michael_Futol_Chinaimo_Recovery.mpp

ID	Task Name	Act. Start	Act. Finish	% Comp.	Phys. % Comp.	Act. Dur.
5	Method Statement	on 10/13/25	NA	90%	90%	10.5 days
11	WTP Foundation	n 12/22/25	NA	75%	75%	45 days
13	Sedimentation Basins	d 3/25/26	NA	31%	25%	25 days
14	Rapid Sand Filter	NA	NA	0%	0%	0 days
15	Internal Channels	NA	NA	0%	0%	0 days
16	Waterproofing / Sealing	NA	NA	0%	0%	0 days
17	Hydrostatic Testing	NA	NA	0%	0%	0 days
19	Reservoir Foundations	d 12/10/25	NA	80%	80%	48 days
20	Reservoir Walls / Linings	d 2/18/26	NA	45%	45%	45 days
26	Administration & Training	Thu 12/4/25	NA	22%	22%	16.4 days
28	Process Piping Installation	NA	NA	0%	0%	0 days
33	Instrumentation	NA	NA	0%	0%	0 days
39	Pole / Foundation	e 12/16/25	NA	40%	40%	40 days
43	Electrical / I&C Preparation	NA	NA	0%	0%	0 days
44	Dry Commissioning	NA	NA	0%	0%	0 days
45	Wet Commissioning	NA	NA	0%	0%	0 days
46	Performance / Verification	NA	NA	0%	0%	0 days
47	Punch List / Rectification	NA	NA	0%	0%	0 days
49	Taking Over / Closeout	NA	NA	0%	0%	0 days

Critical Chain Controlling the Recovery Process

VIEW GUIDE

Residual critical chain controlling the recovery process.

Critical

Critical Split

Critical Progress

Task

Split

Task Progress

Manual Task

Start-only

Finish-only

Duration-only

Baseline

Baseline Split

Baseline Milestone

Milestone

Summary Progress

Summary

Manual Summary

Project Summary

External Tasks

External Milestone

Inactive Task


Inactive Milestone


Inactive Summary


Deadline

RECOVERY CRITICAL PATH | Residual critical sequence controlling the partial-recovery finish.

Page 1

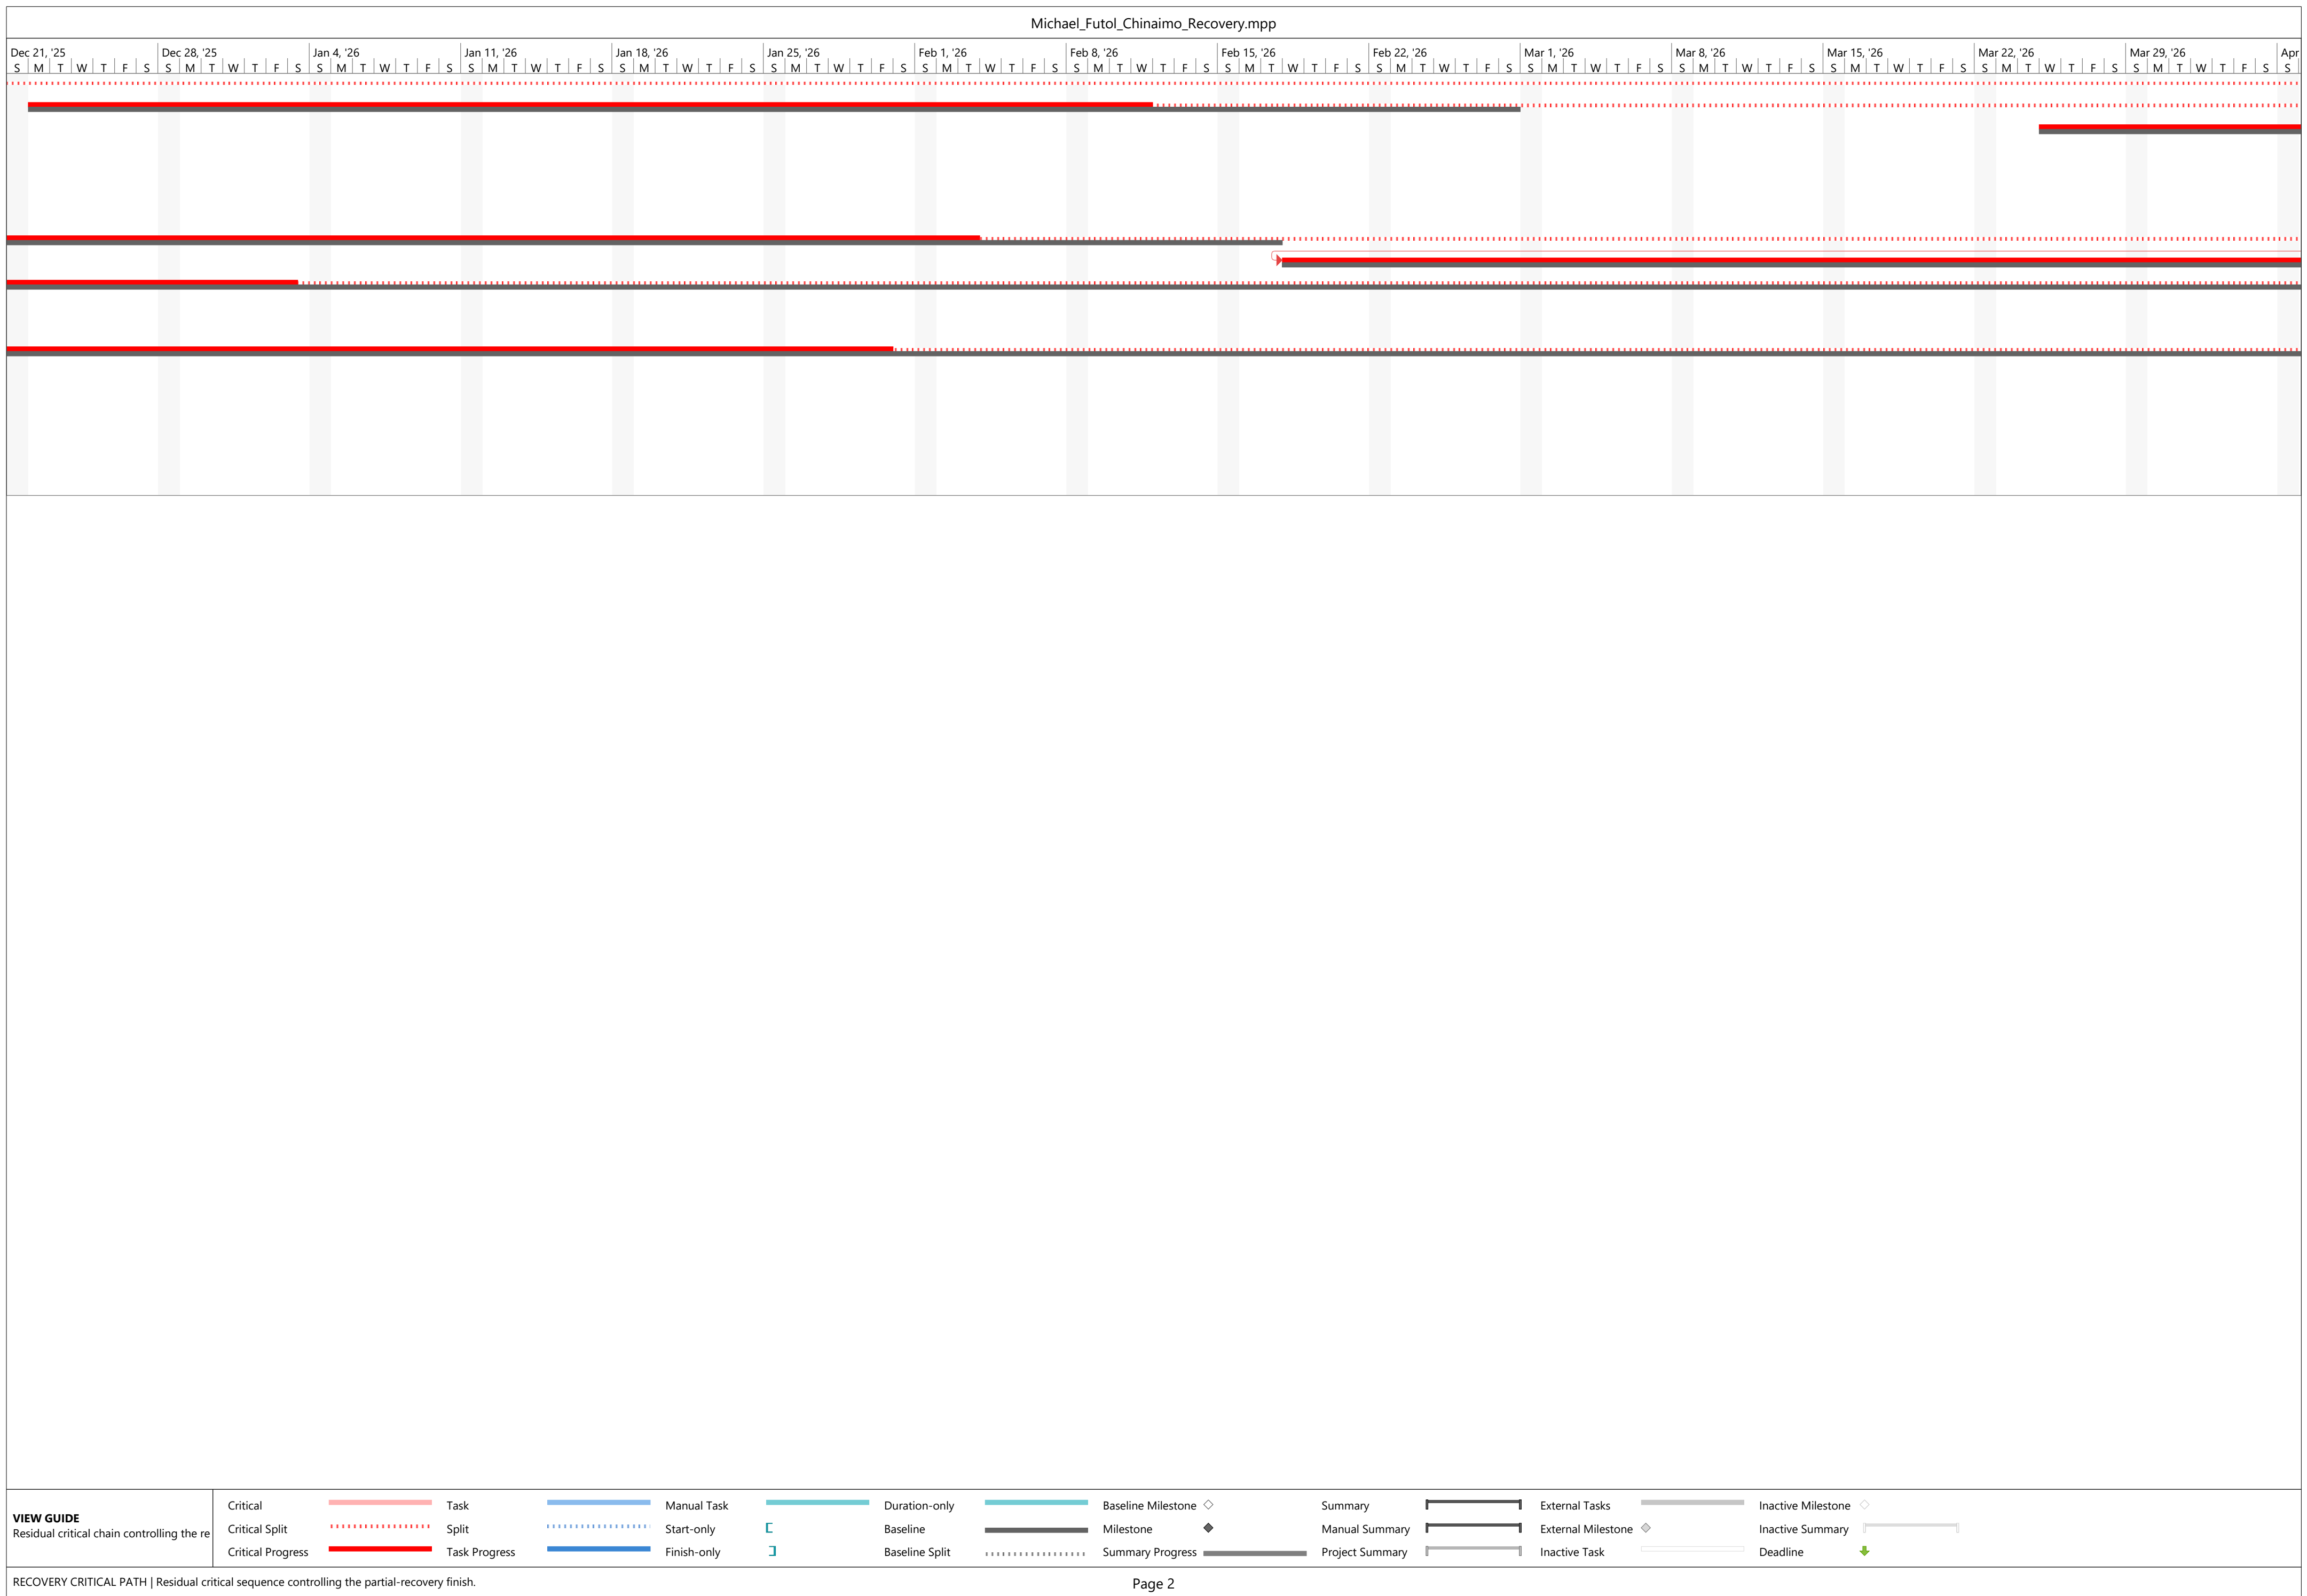

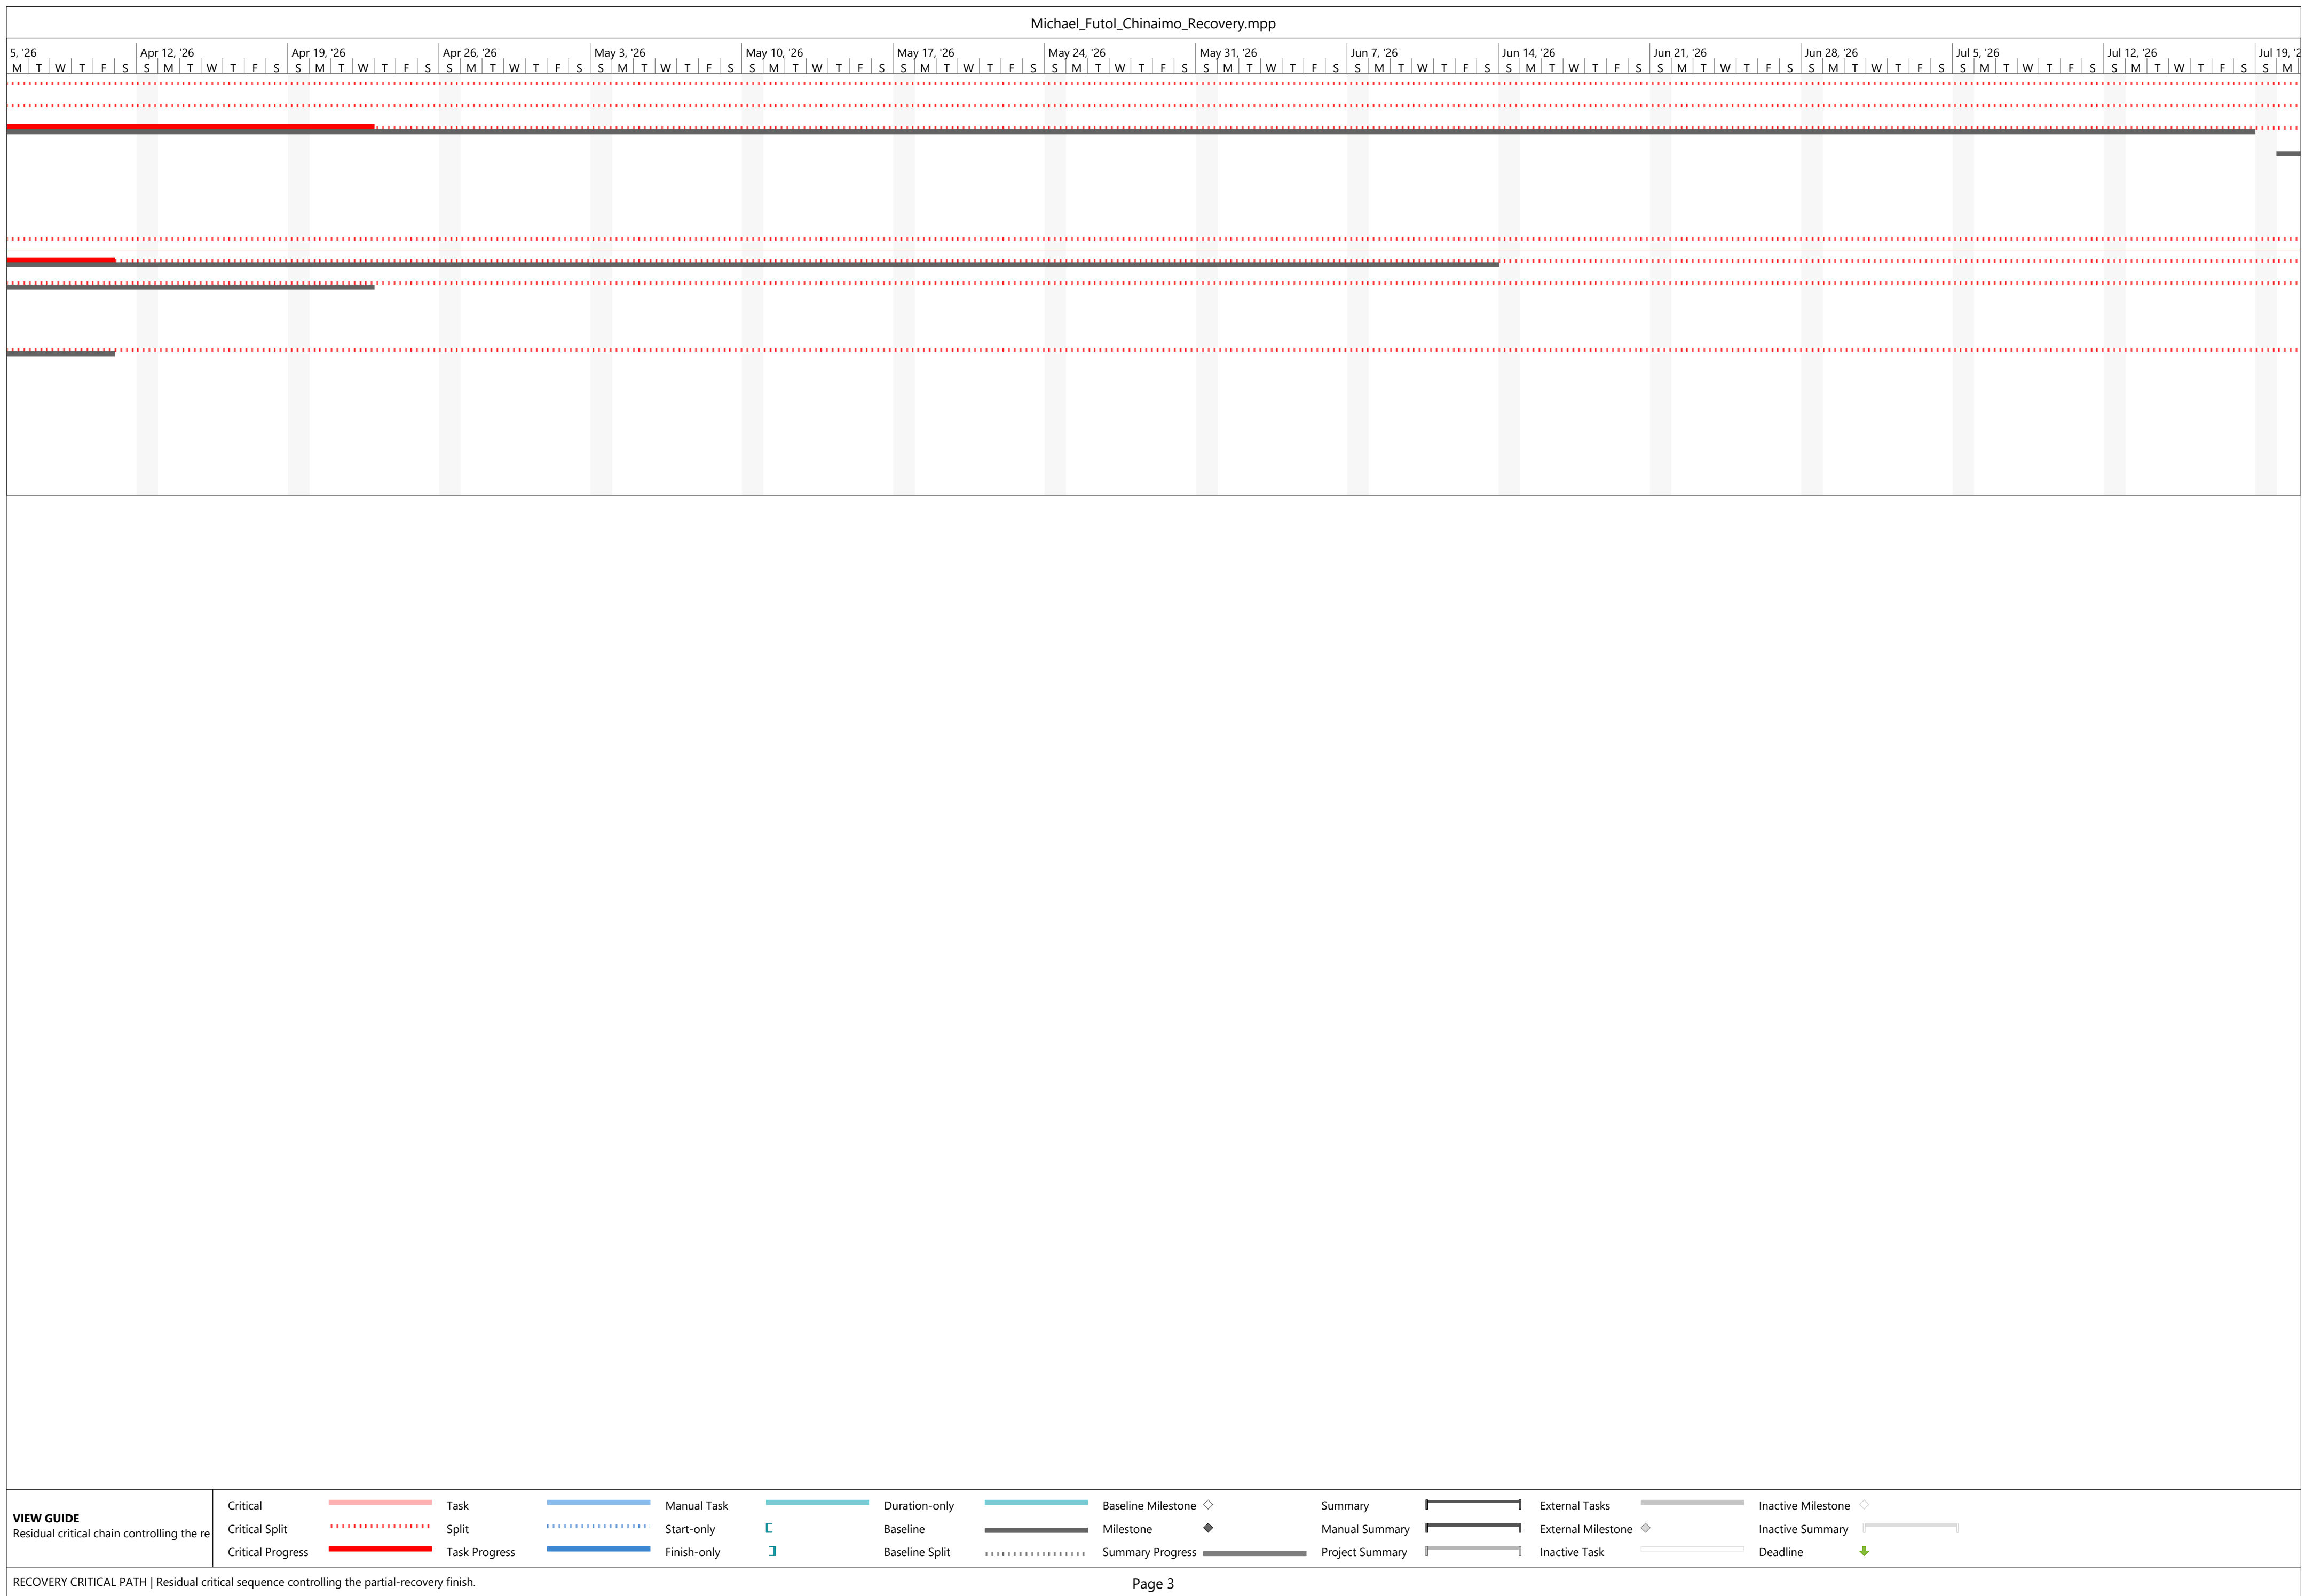

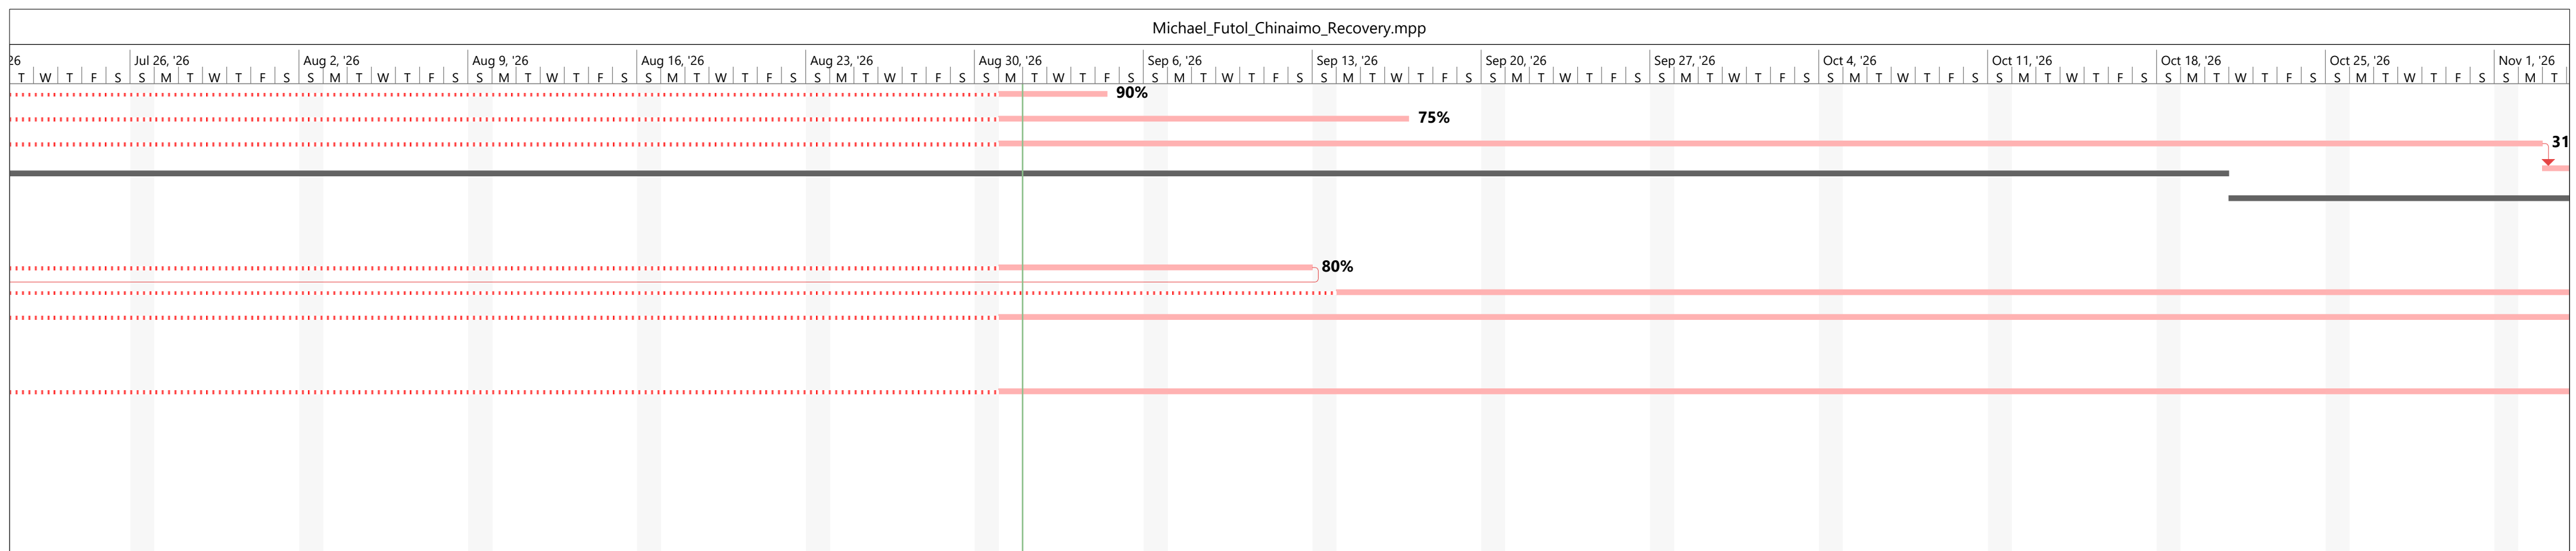

VIEW GUIDE Residual critical chain controlling the re	Critical  Task  Manual Task  Duration-only  Baseline Milestone  Summary  External Tasks Inactive Milestone
	Critical Split Split Start-only Baseline Milestone Manual Summary External Milestone Inactive Summary
	Critical Progress  Task Progress  Finish-only  Baseline Split  Summary Progress  Project Summary Inactive Task Deadline
RECOVERY CRITICAL PATH Residual critical sequence controlling the partial-recovery finish.	

