ID	Task Name	Duration	Start	Finish
1	Notice to Proceed	0 days	Wed 10/1/25	Wed 10/1/25
2	Mobilization & Temporary Facilities	20 days	Wed 10/1/25	Thu 10/23/25
3	Survey / Setting Out	15 days	Tue 10/7/25	Thu 10/23/25
4	Review IFC Drawings / Interfaces	30 days	Wed 10/1/25	Tue 11/4/25
5	Method Statements & Material	45 days	Mon 10/13/25	Wed 12/3/25
6	Long-Lead M&E Procurement	300 days	Thu 12/4/25	Wed 11/18/26
7	SCADA / Instrumentation Procurement	260 days	Thu 12/4/25	Fri 10/2/26
8	Electrical / Receiving Equipment Procurement	240 days	Thu 12/4/25	Wed 9/9/26
9	Site Clearing / Excavation / Dewatering	35 days	Fri 10/24/25	Wed 12/3/25
10	Ground Preparation / Blinding	15 days	Thu 12/4/25	Sat 12/20/25
11	WTP Foundations / Base Slabs	60 days	Mon 12/22/25	Sat 2/28/26
12	Mixing / Flocculation Basin RC Works	70 days	Mon 3/2/26	Thu 5/21/26
13	Sedimentation Basin RC Works	100 days	Wed 3/25/26	Sat 7/18/26
14	Rapid Sand Filter Structure	80 days	Mon 7/20/26	Tue 10/20/26
15	Internal Channels / Pipe Galleries	45 days	Wed 10/21/26	Fri 12/11/26
16	Waterproofing / Prot	30 days	Sat 12/12/26	Fri 1/15/27
17	Hydrostatic / Structur	14 days	Sat 1/16/27	Mon 2/1/27
18	10,000 mÂ³ Reservoir	40 days	Fri 10/24/25	Tue 12/9/25
19	Reservoir Foundation	60 days	Wed 12/10/2	Tue 2/17/26
20	Reservoir Walls / Col	100 days	Wed 2/18/26	Sat 6/13/26
21	Reservoir Roof Slab	60 days	Mon 6/15/26	Sat 8/22/26
22	Reservoir Waterproo	30 days	Mon 8/24/26	Sat 9/26/26
23	Reservoir Hydrostatic	14 days	Mon 9/28/26	Tue 10/13/26
24	Pump Room Civil / St	75 days	Wed 1/14/26	Fri 4/10/26
25	Chemical Building Civ	90 days	Mon 1/26/26	Sat 5/9/26
26	Administration & Lab	120 days	Thu 12/4/25	Wed 4/22/26
27	Building MEP / Archit	70 days	Thu 4/23/26	Mon 7/13/26
28	Process Piping Installa	100 days	Tue 2/2/27	Fri 5/28/27
29	Pumps & Mechanical	90 days	Thu 11/19/26	Wed 3/3/27
30	Chemical Dosing Equi	70 days	Thu 11/19/26	Mon 2/8/27
31	Filter Media / Underd	50 days	Tue 2/2/27	Wed 3/31/27
32	Electrical Installation	100 days	Thu 9/10/26	Mon 1/4/27
33	Instrumentation & SC	90 days	Sat 5/29/27	Fri 9/10/27
34	Salakham Site Prepar	40 days	Fri 10/24/25	Tue 12/9/25
35	7,100 mÂ³ Reservoir I	180 days	Wed 12/10/2	Tue 7/7/26
36	Salakham Pump Roor	90 days	Fri 11/28/25	Thu 3/12/26
37	Salakham M&E Install	80 days	Thu 11/19/26	Fri 2/19/27
38	22-kV Route Survey /	45 days	Fri 10/24/25	Mon 12/15/2
39	Pole / Foundation Wc	100 days	Tue 12/16/25	Fri 4/10/26
40	22-kV Line Installatior	120 days	Sat 4/11/26	Fri 8/28/26
41	Receiving Equipment	30 days	Thu 9/10/26	Wed 10/14/2
42	Mechanical Pre-Comr	25 days	Sat 5/29/27	Sat 6/26/27
43	Electrical / I&C Pre-Cc	25 days	Sat 9/11/27	Sat 10/9/27
44	Dry Commissioning	20 days	Mon 10/11/2	Tue 11/2/27
45	Wet Commissioning /	30 days	Wed 11/3/27	Tue 12/7/27
46	Performance / Water	30 days	Wed 12/8/27	Tue 1/11/28
47	Punch List / Rectificat	30 days	Wed 1/12/28	Tue 2/15/28
48	Training / O&M Docu	20 days	Wed 11/3/27	Thu 11/25/27
49	Taking Over / Comple	0 days	Tue 2/15/28	Tue 2/15/28

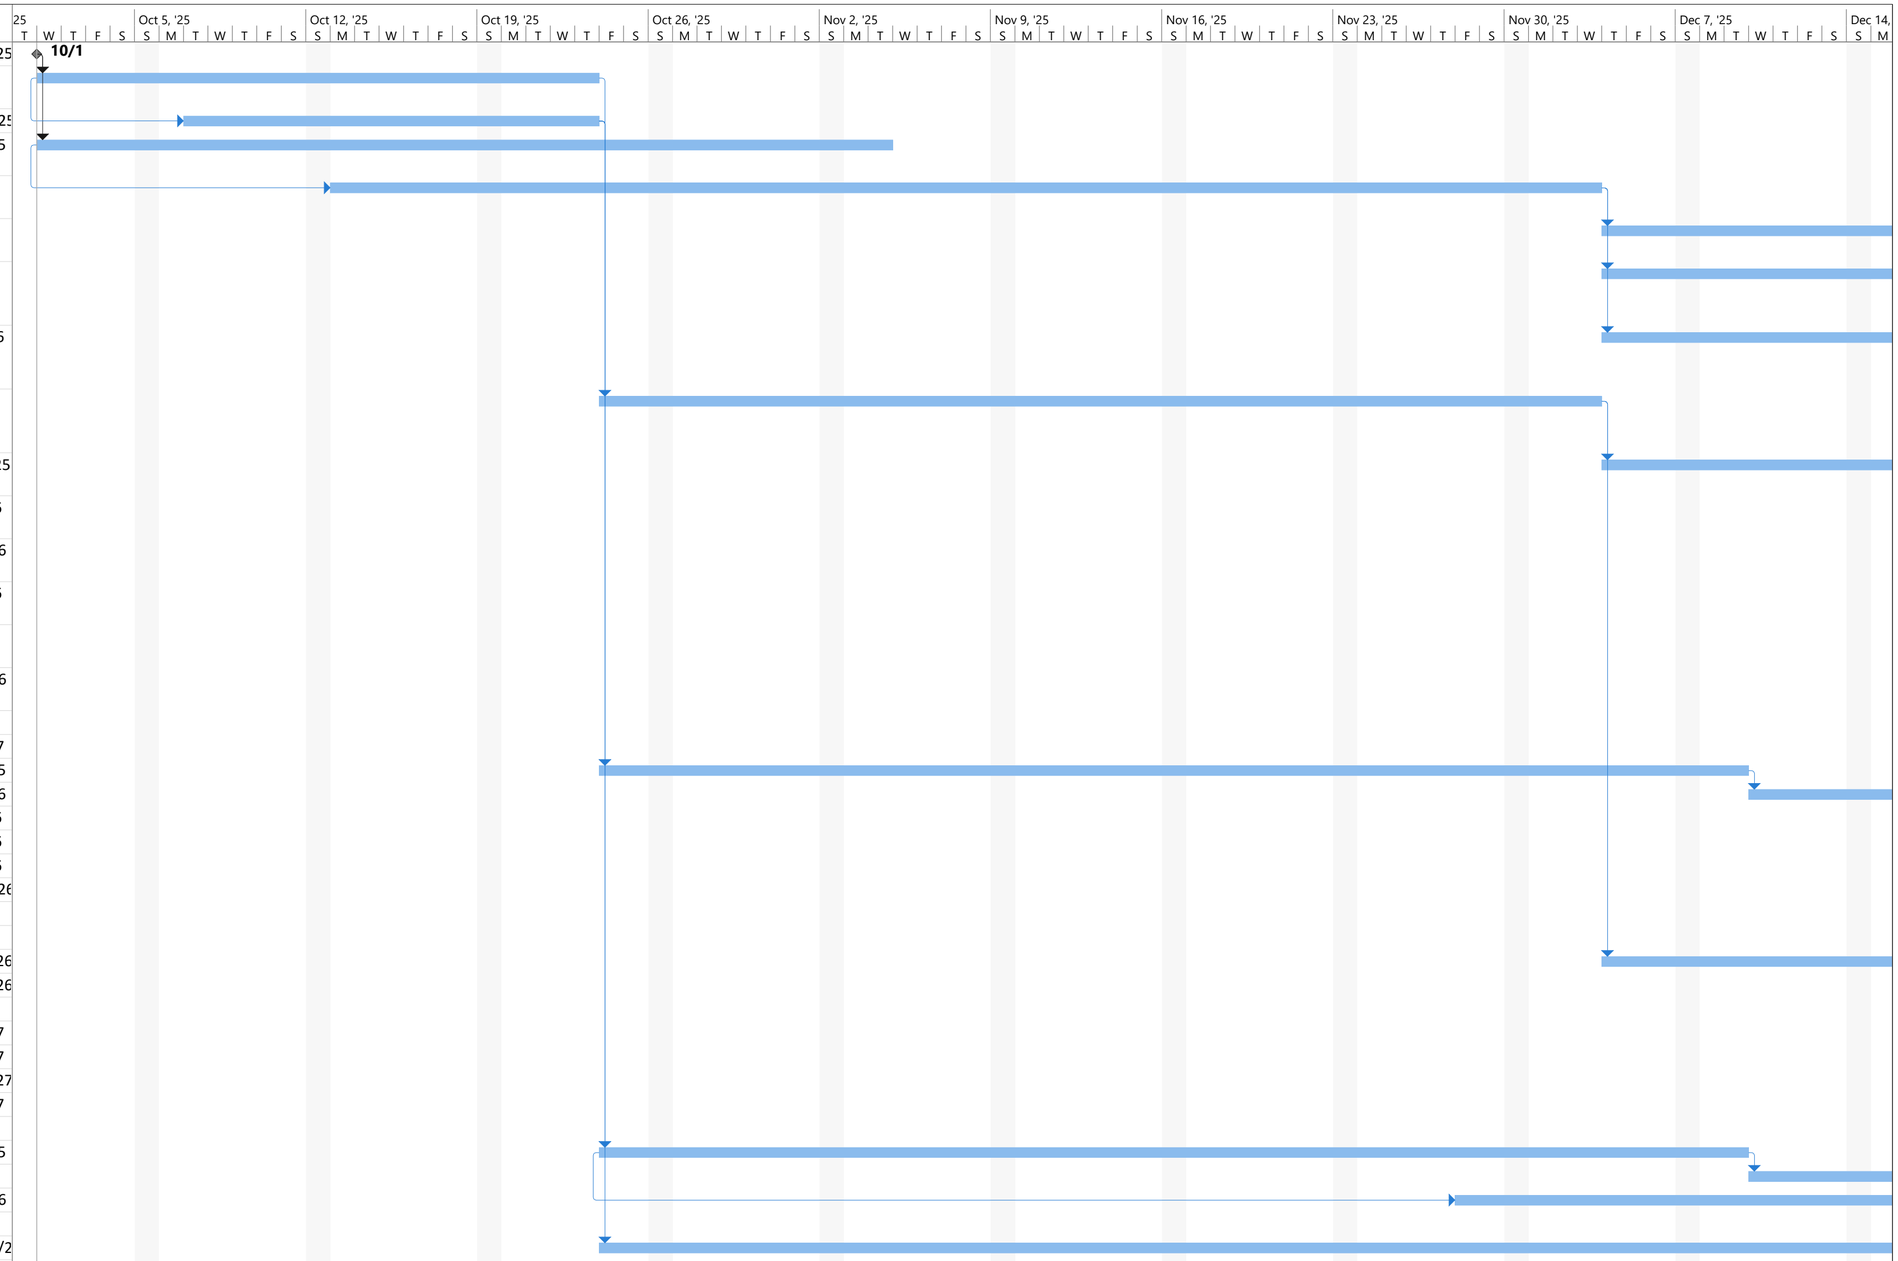

Project: Michael_Futol_Chinaim
Date: Tue 9/1/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

BASELINE | Reference programme; planned dates and logic are the comparison basis.

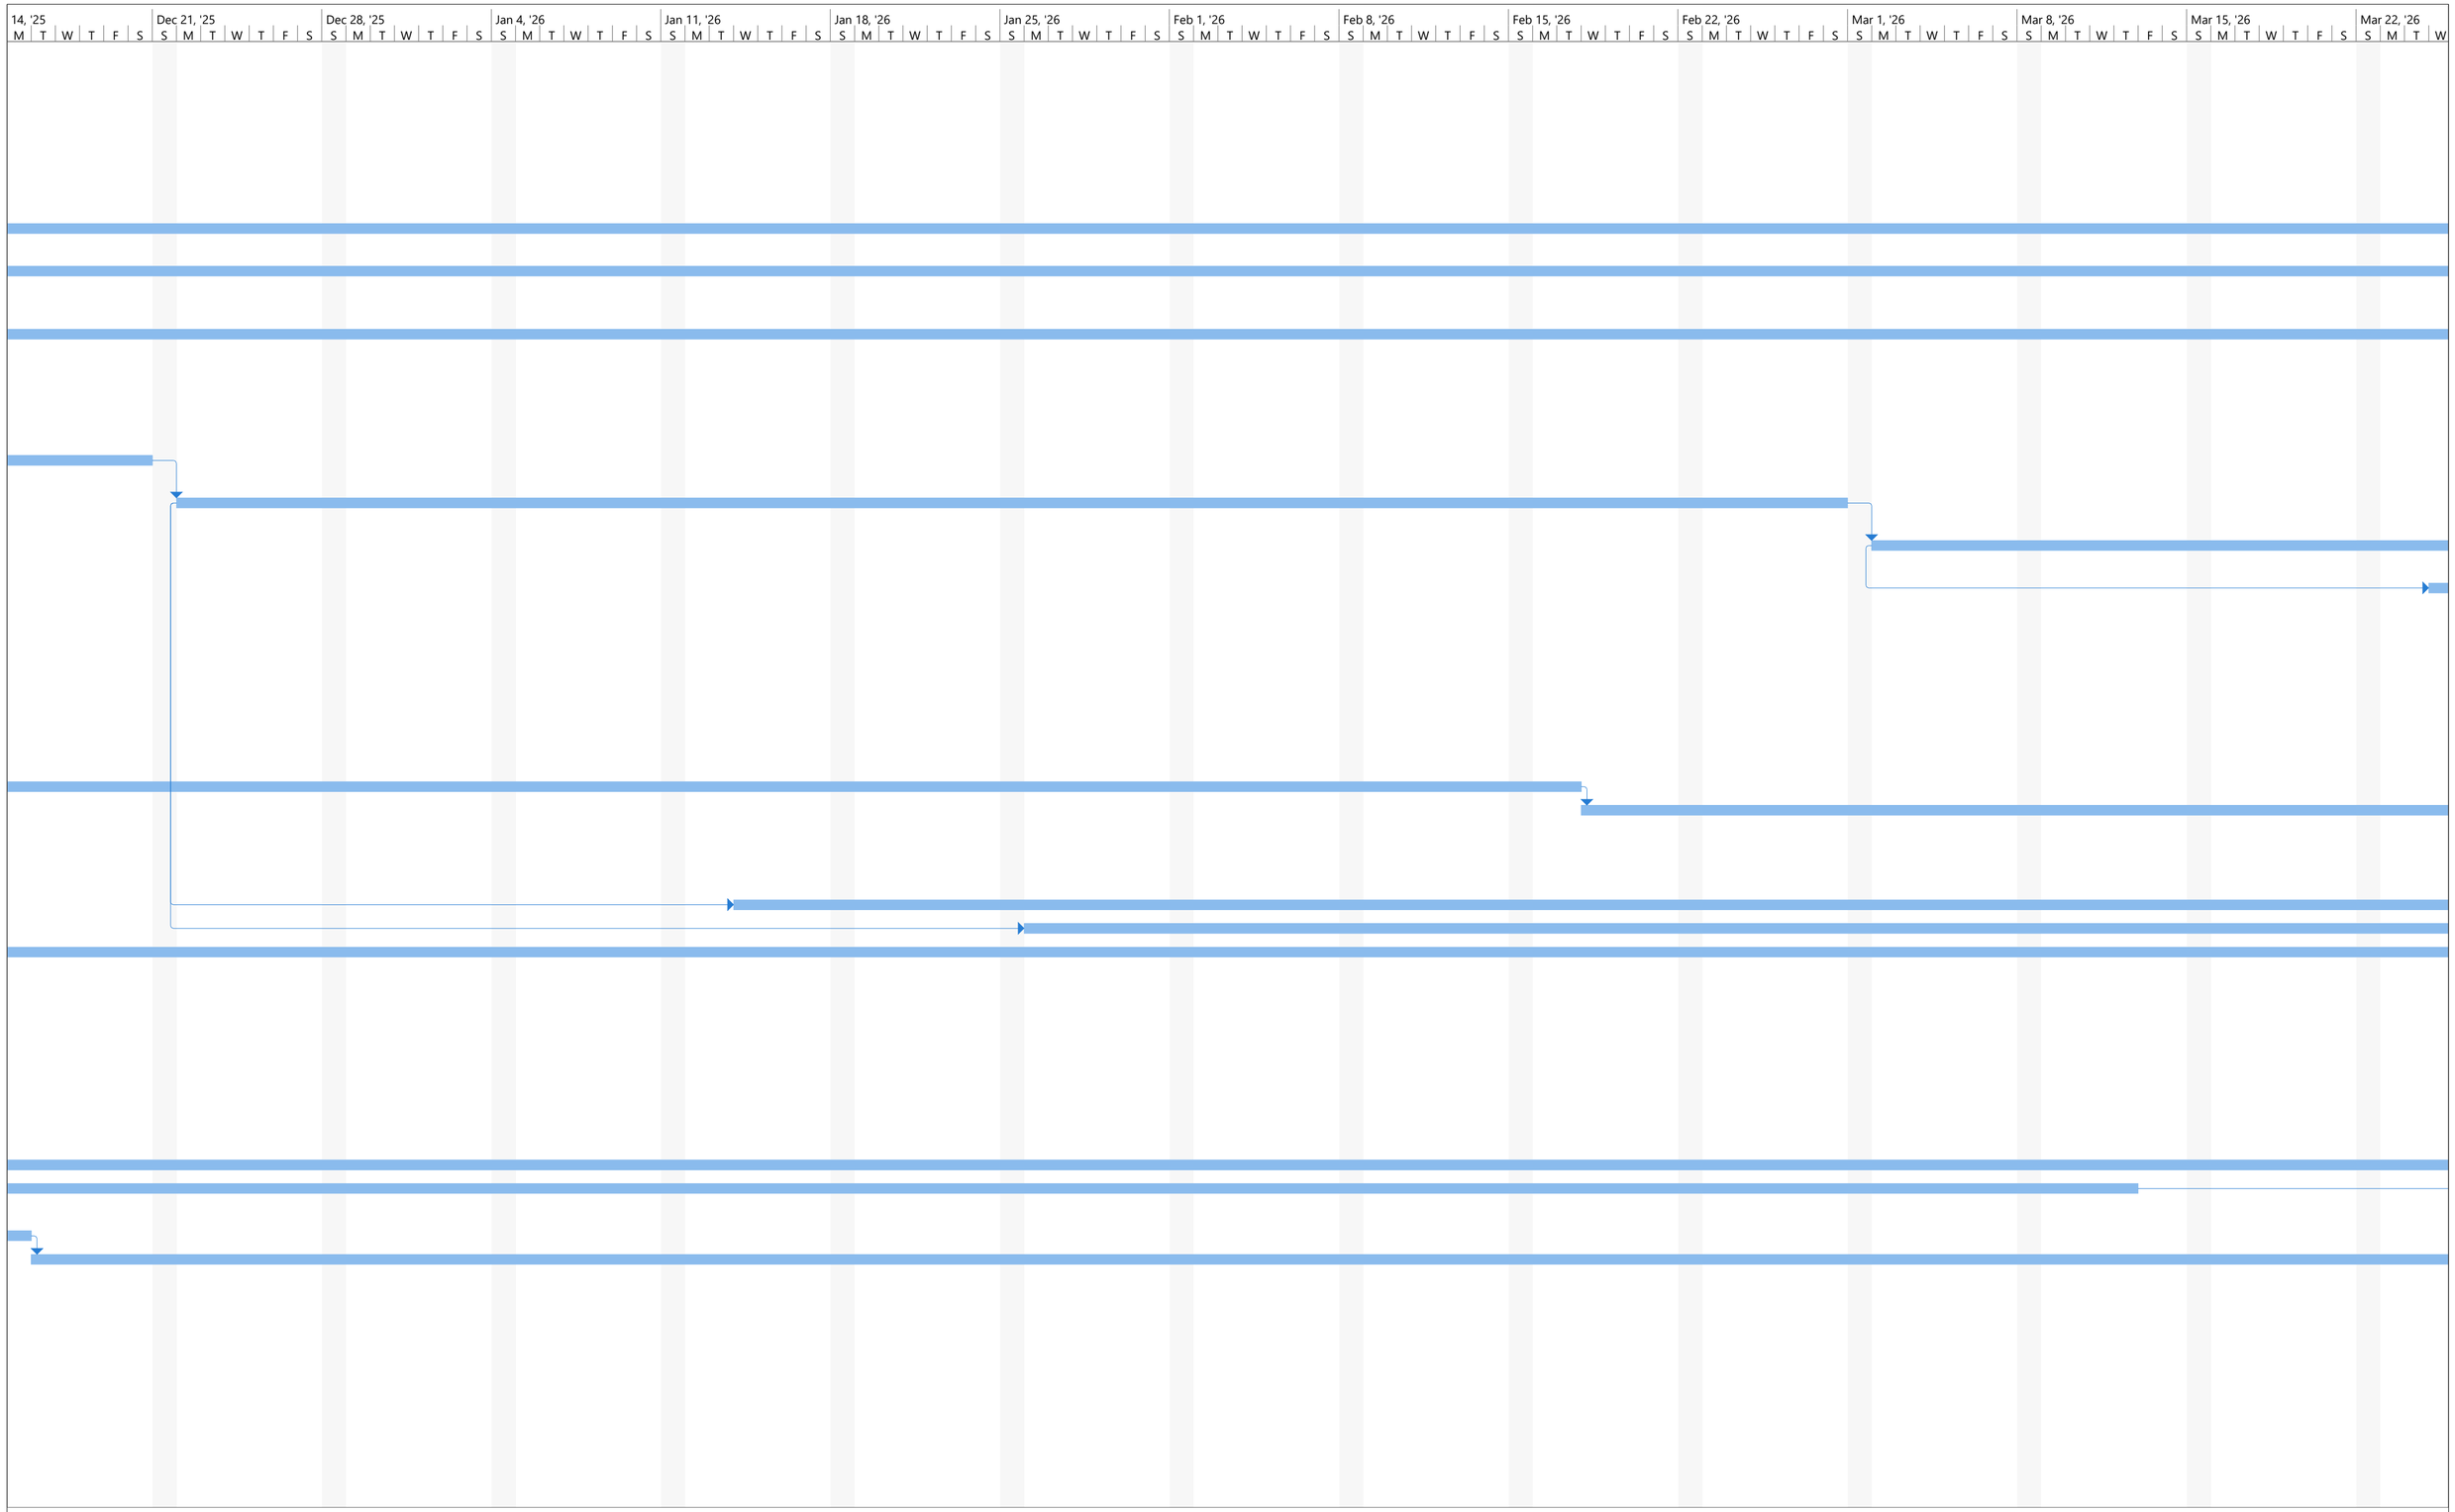

Project: Michael_Futol_Chinaim
Date: Tue 9/1/26

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

BASELINE | Reference programme; planned dates and logic are the comparison basis.

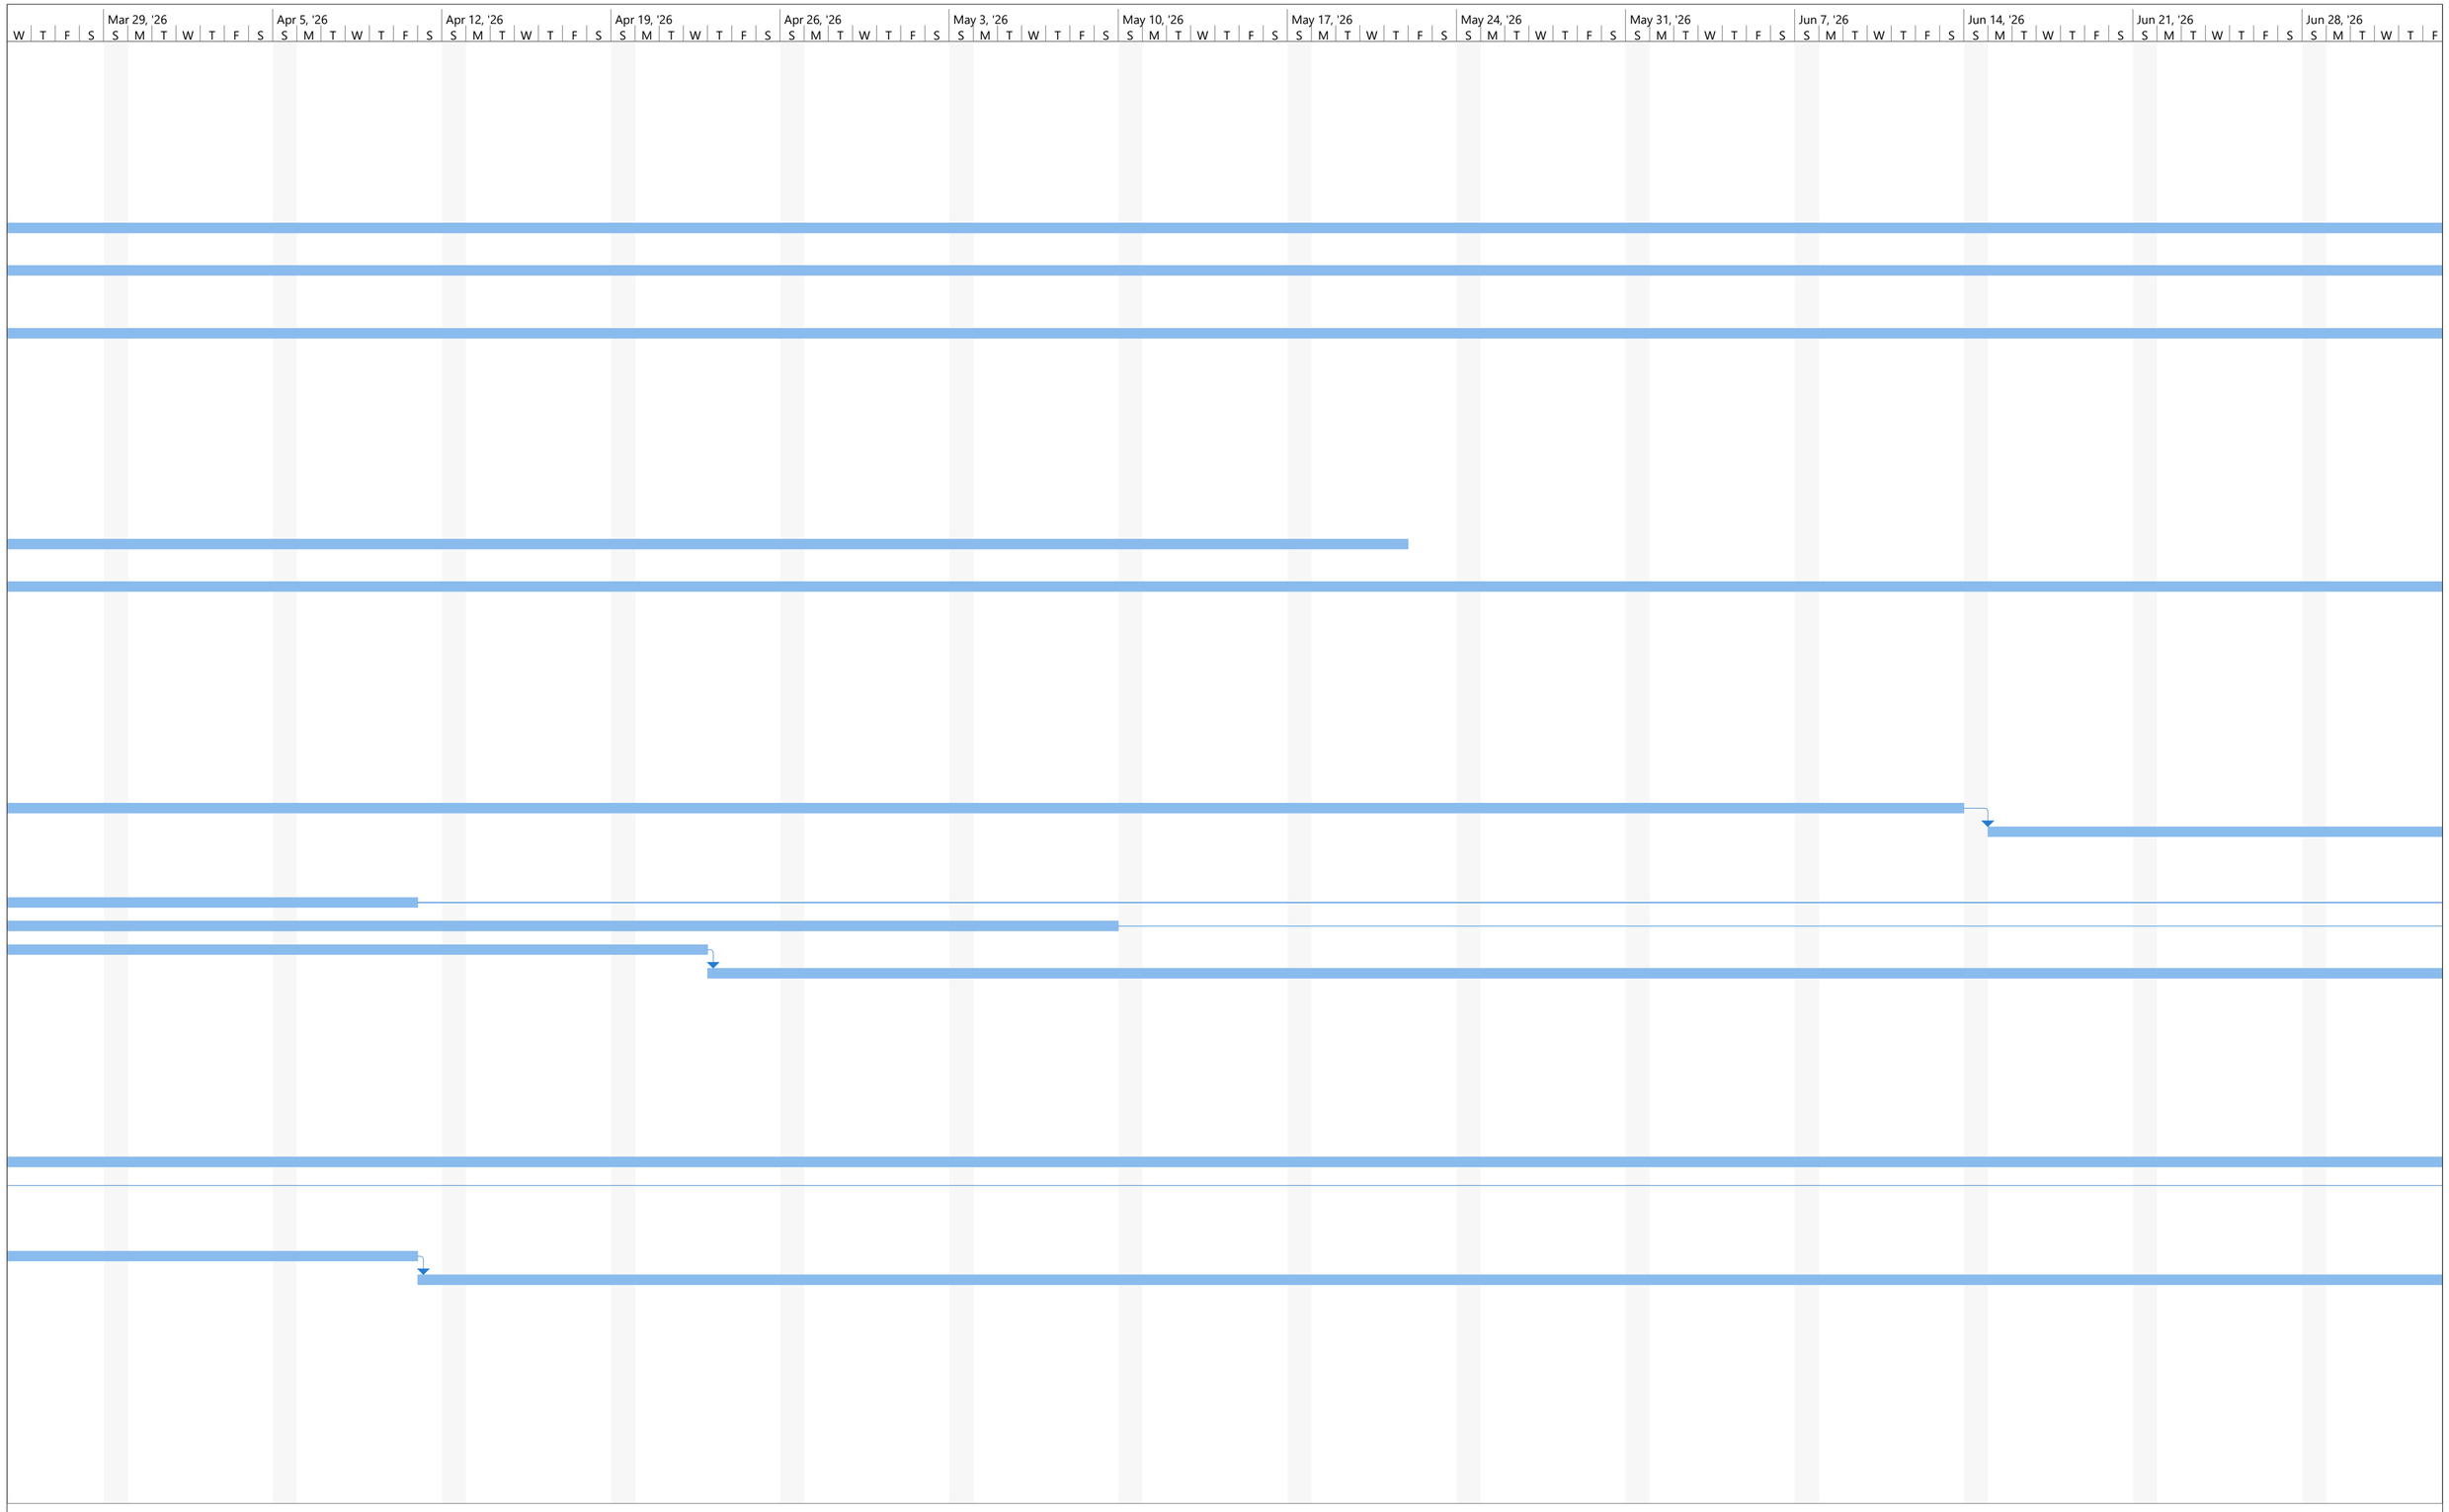

Project: Michael_Futol_Chinaim
Date: Tue 9/1/26

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

BASELINE | Reference programme; planned dates and logic are the comparison basis.

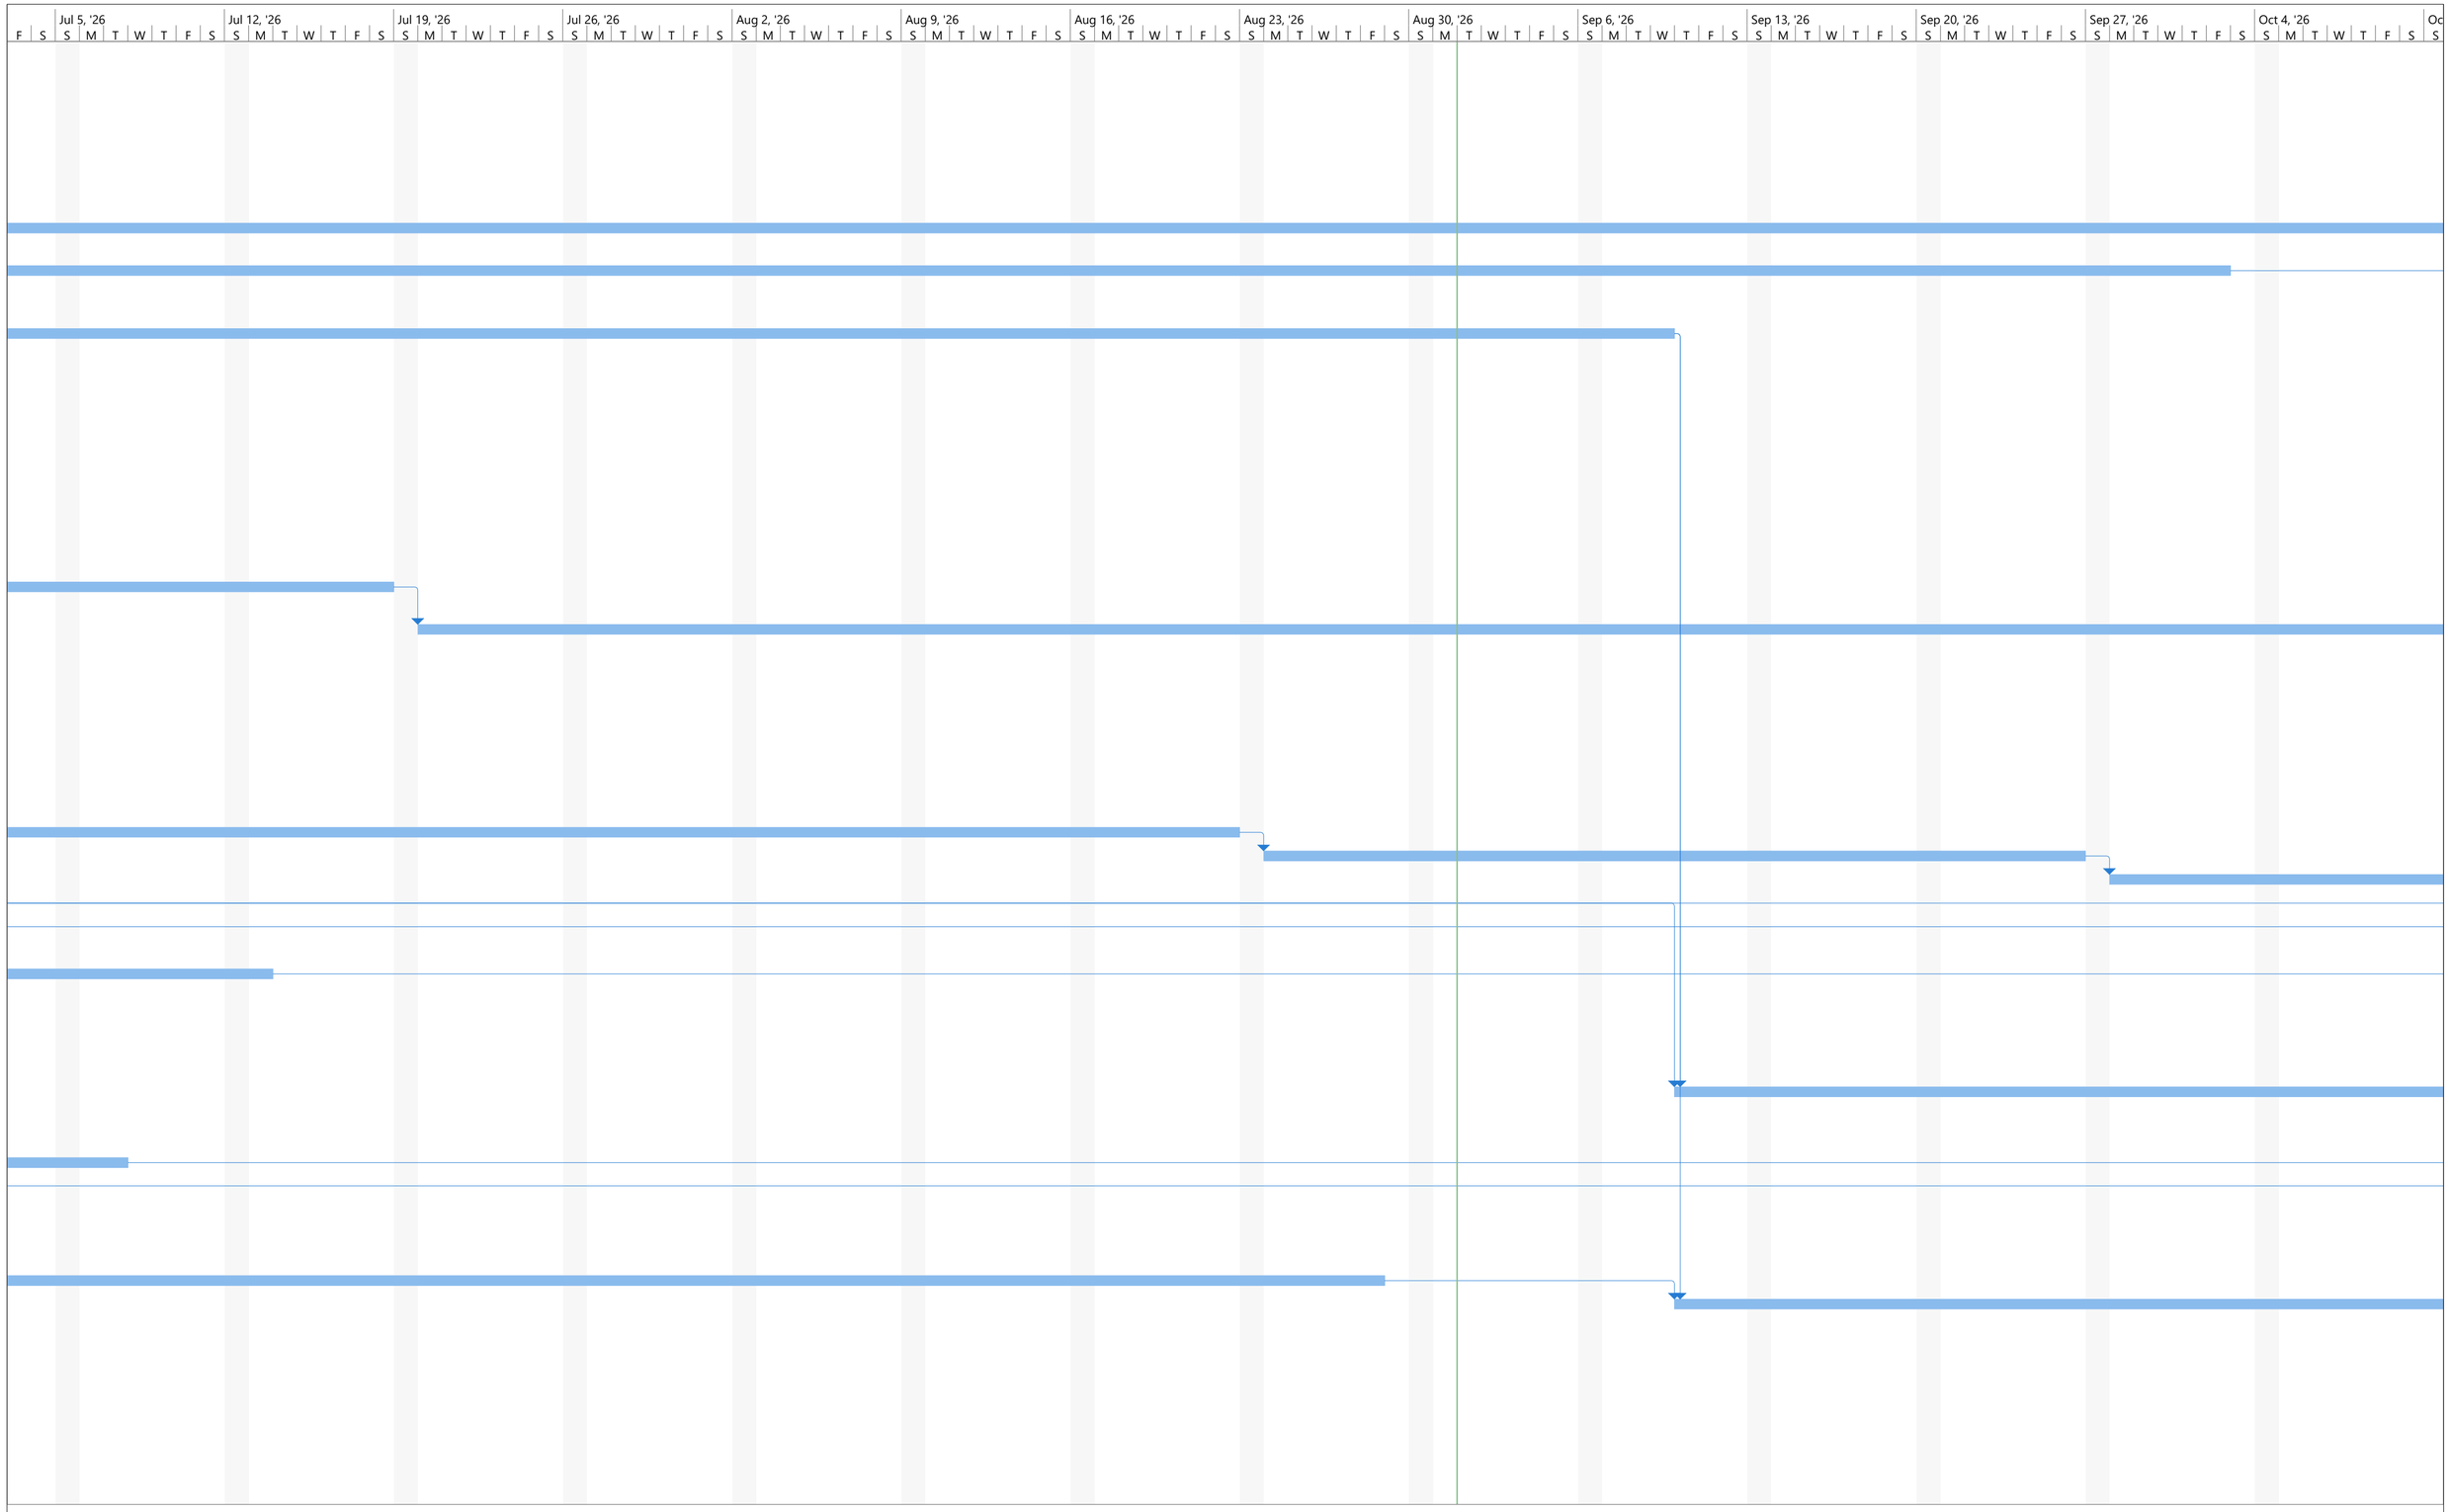

Project: Michael_Futol_Chinaim
Date: Tue 9/1/26

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

BASELINE | Reference programme; planned dates and logic are the comparison basis.

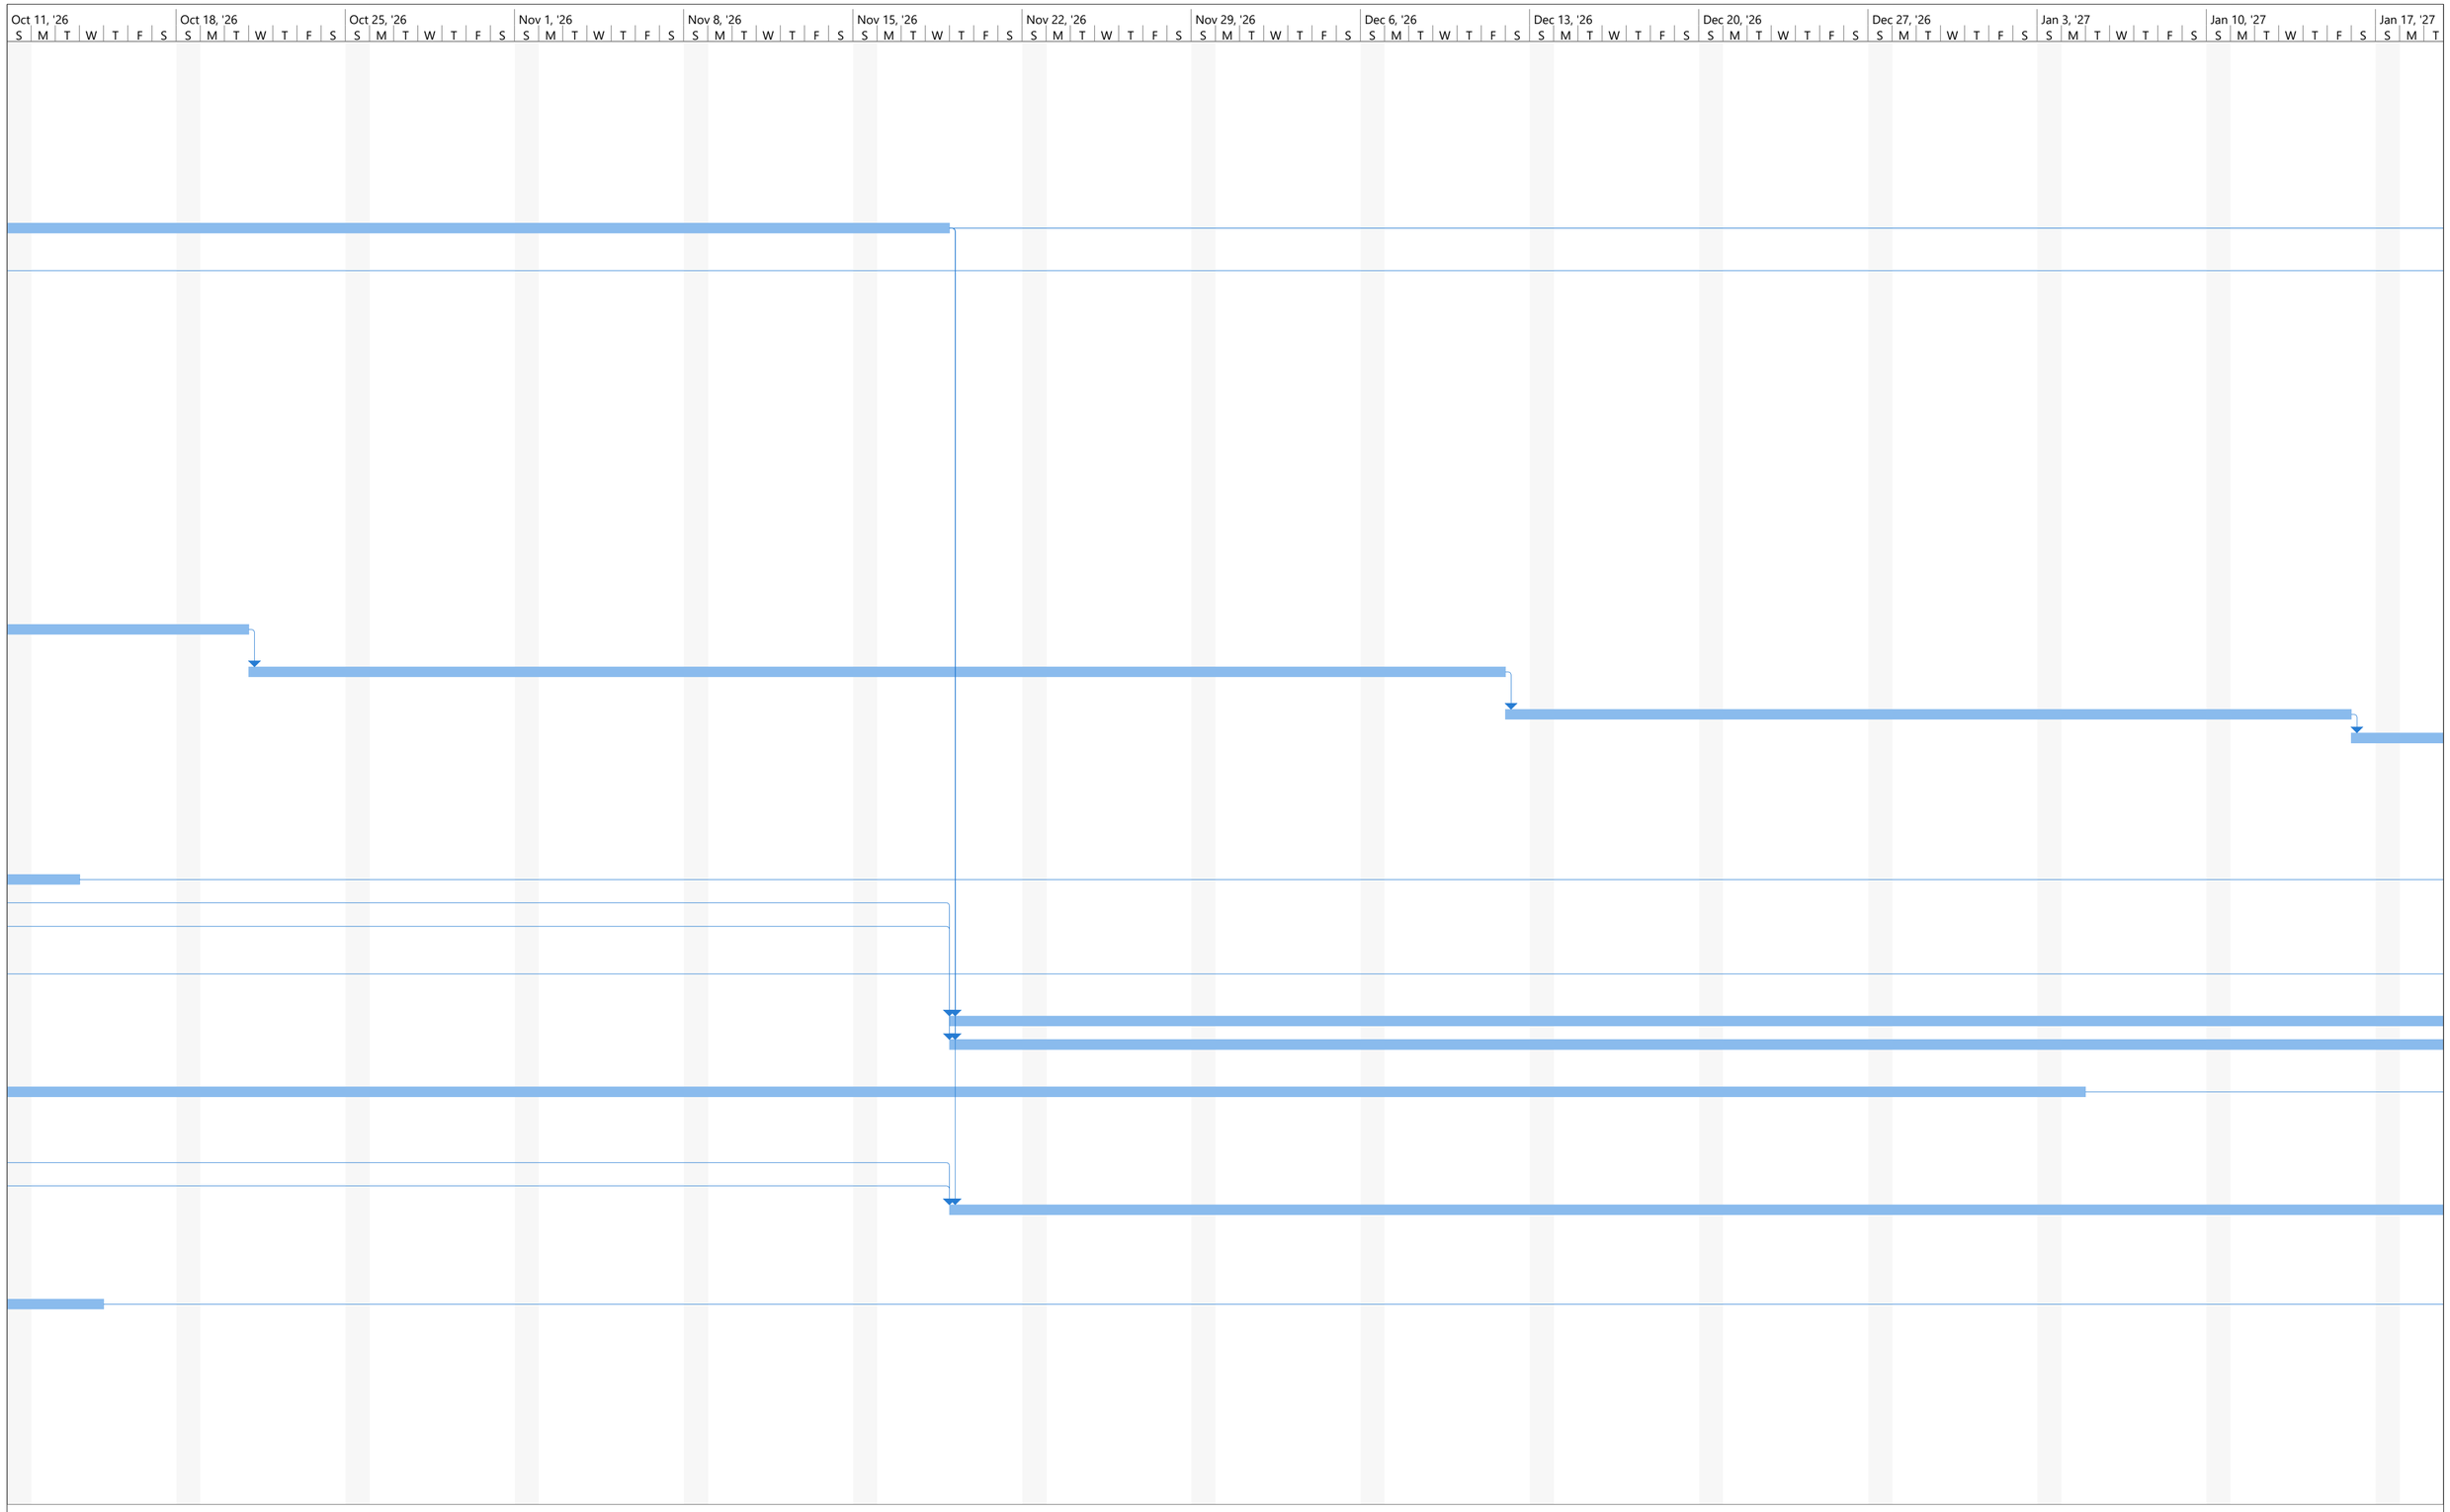

Project: Michael_Futol_Chinaim
Date: Tue 9/1/26

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

BASELINE | Reference programme; planned dates and logic are the comparison basis.

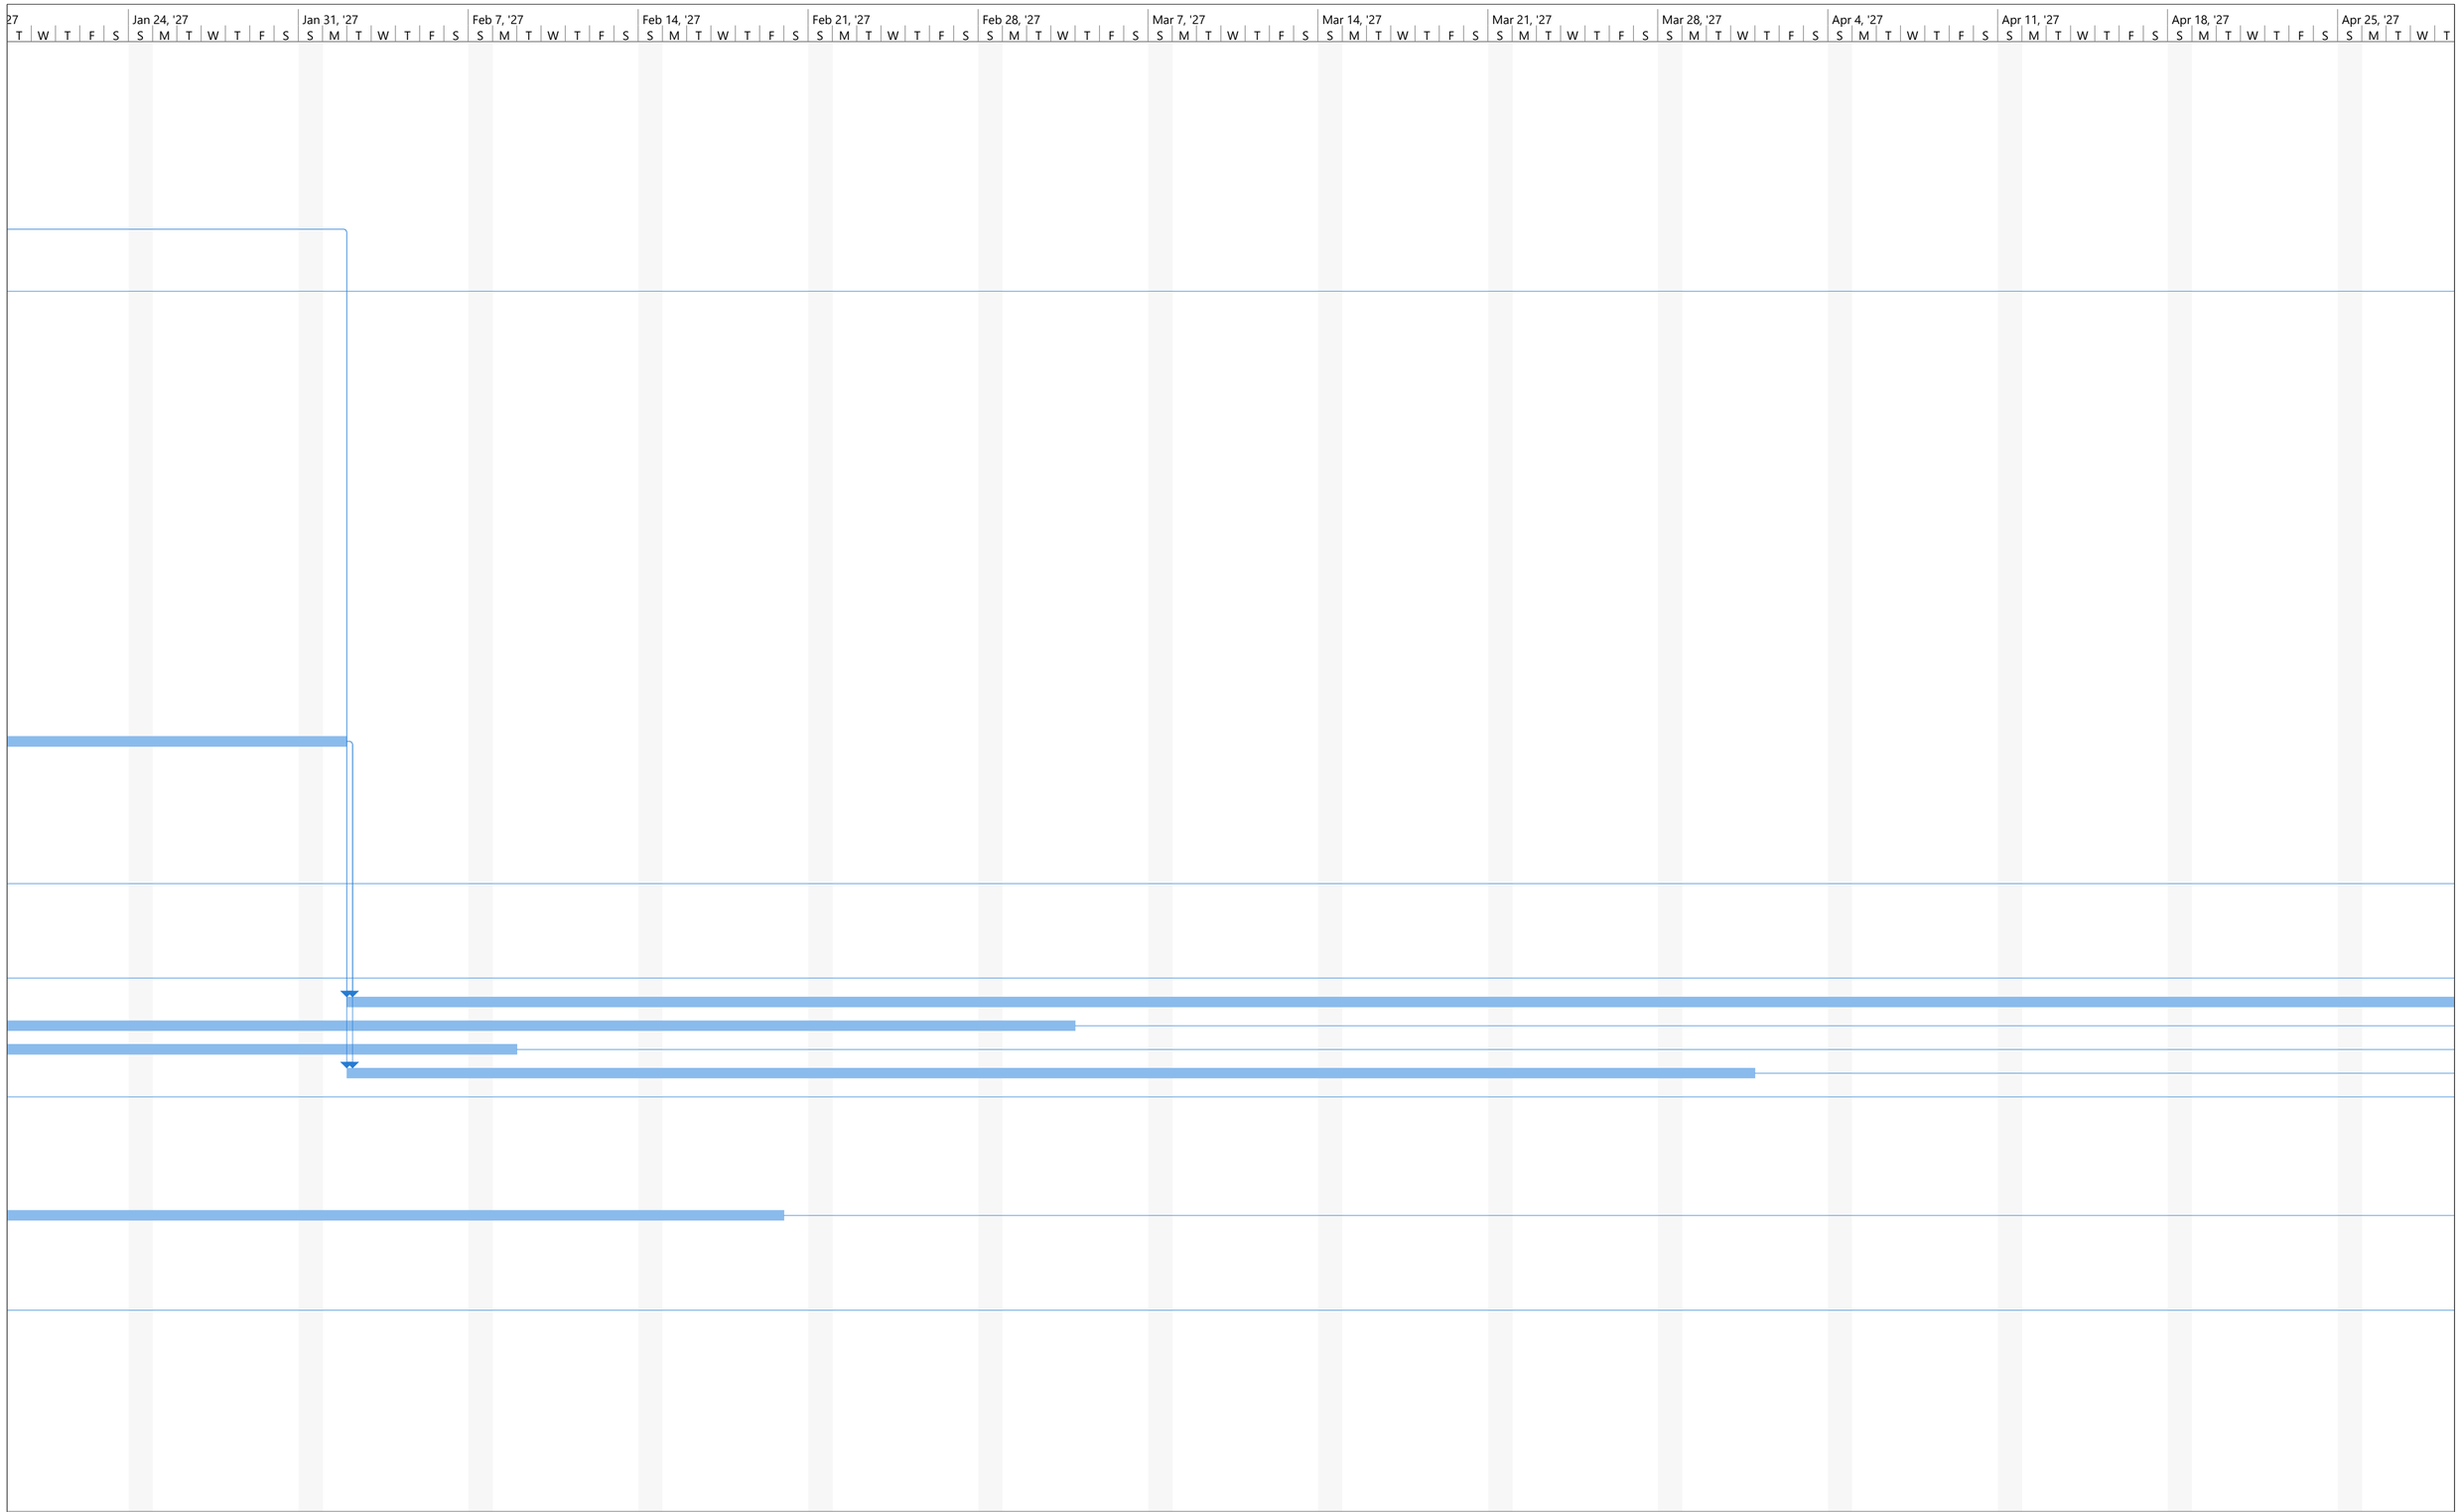

Project: Michael_Futol_Chinaim
Date: Tue 9/1/26

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

BASELINE | Reference programme; planned dates and logic are the comparison basis.

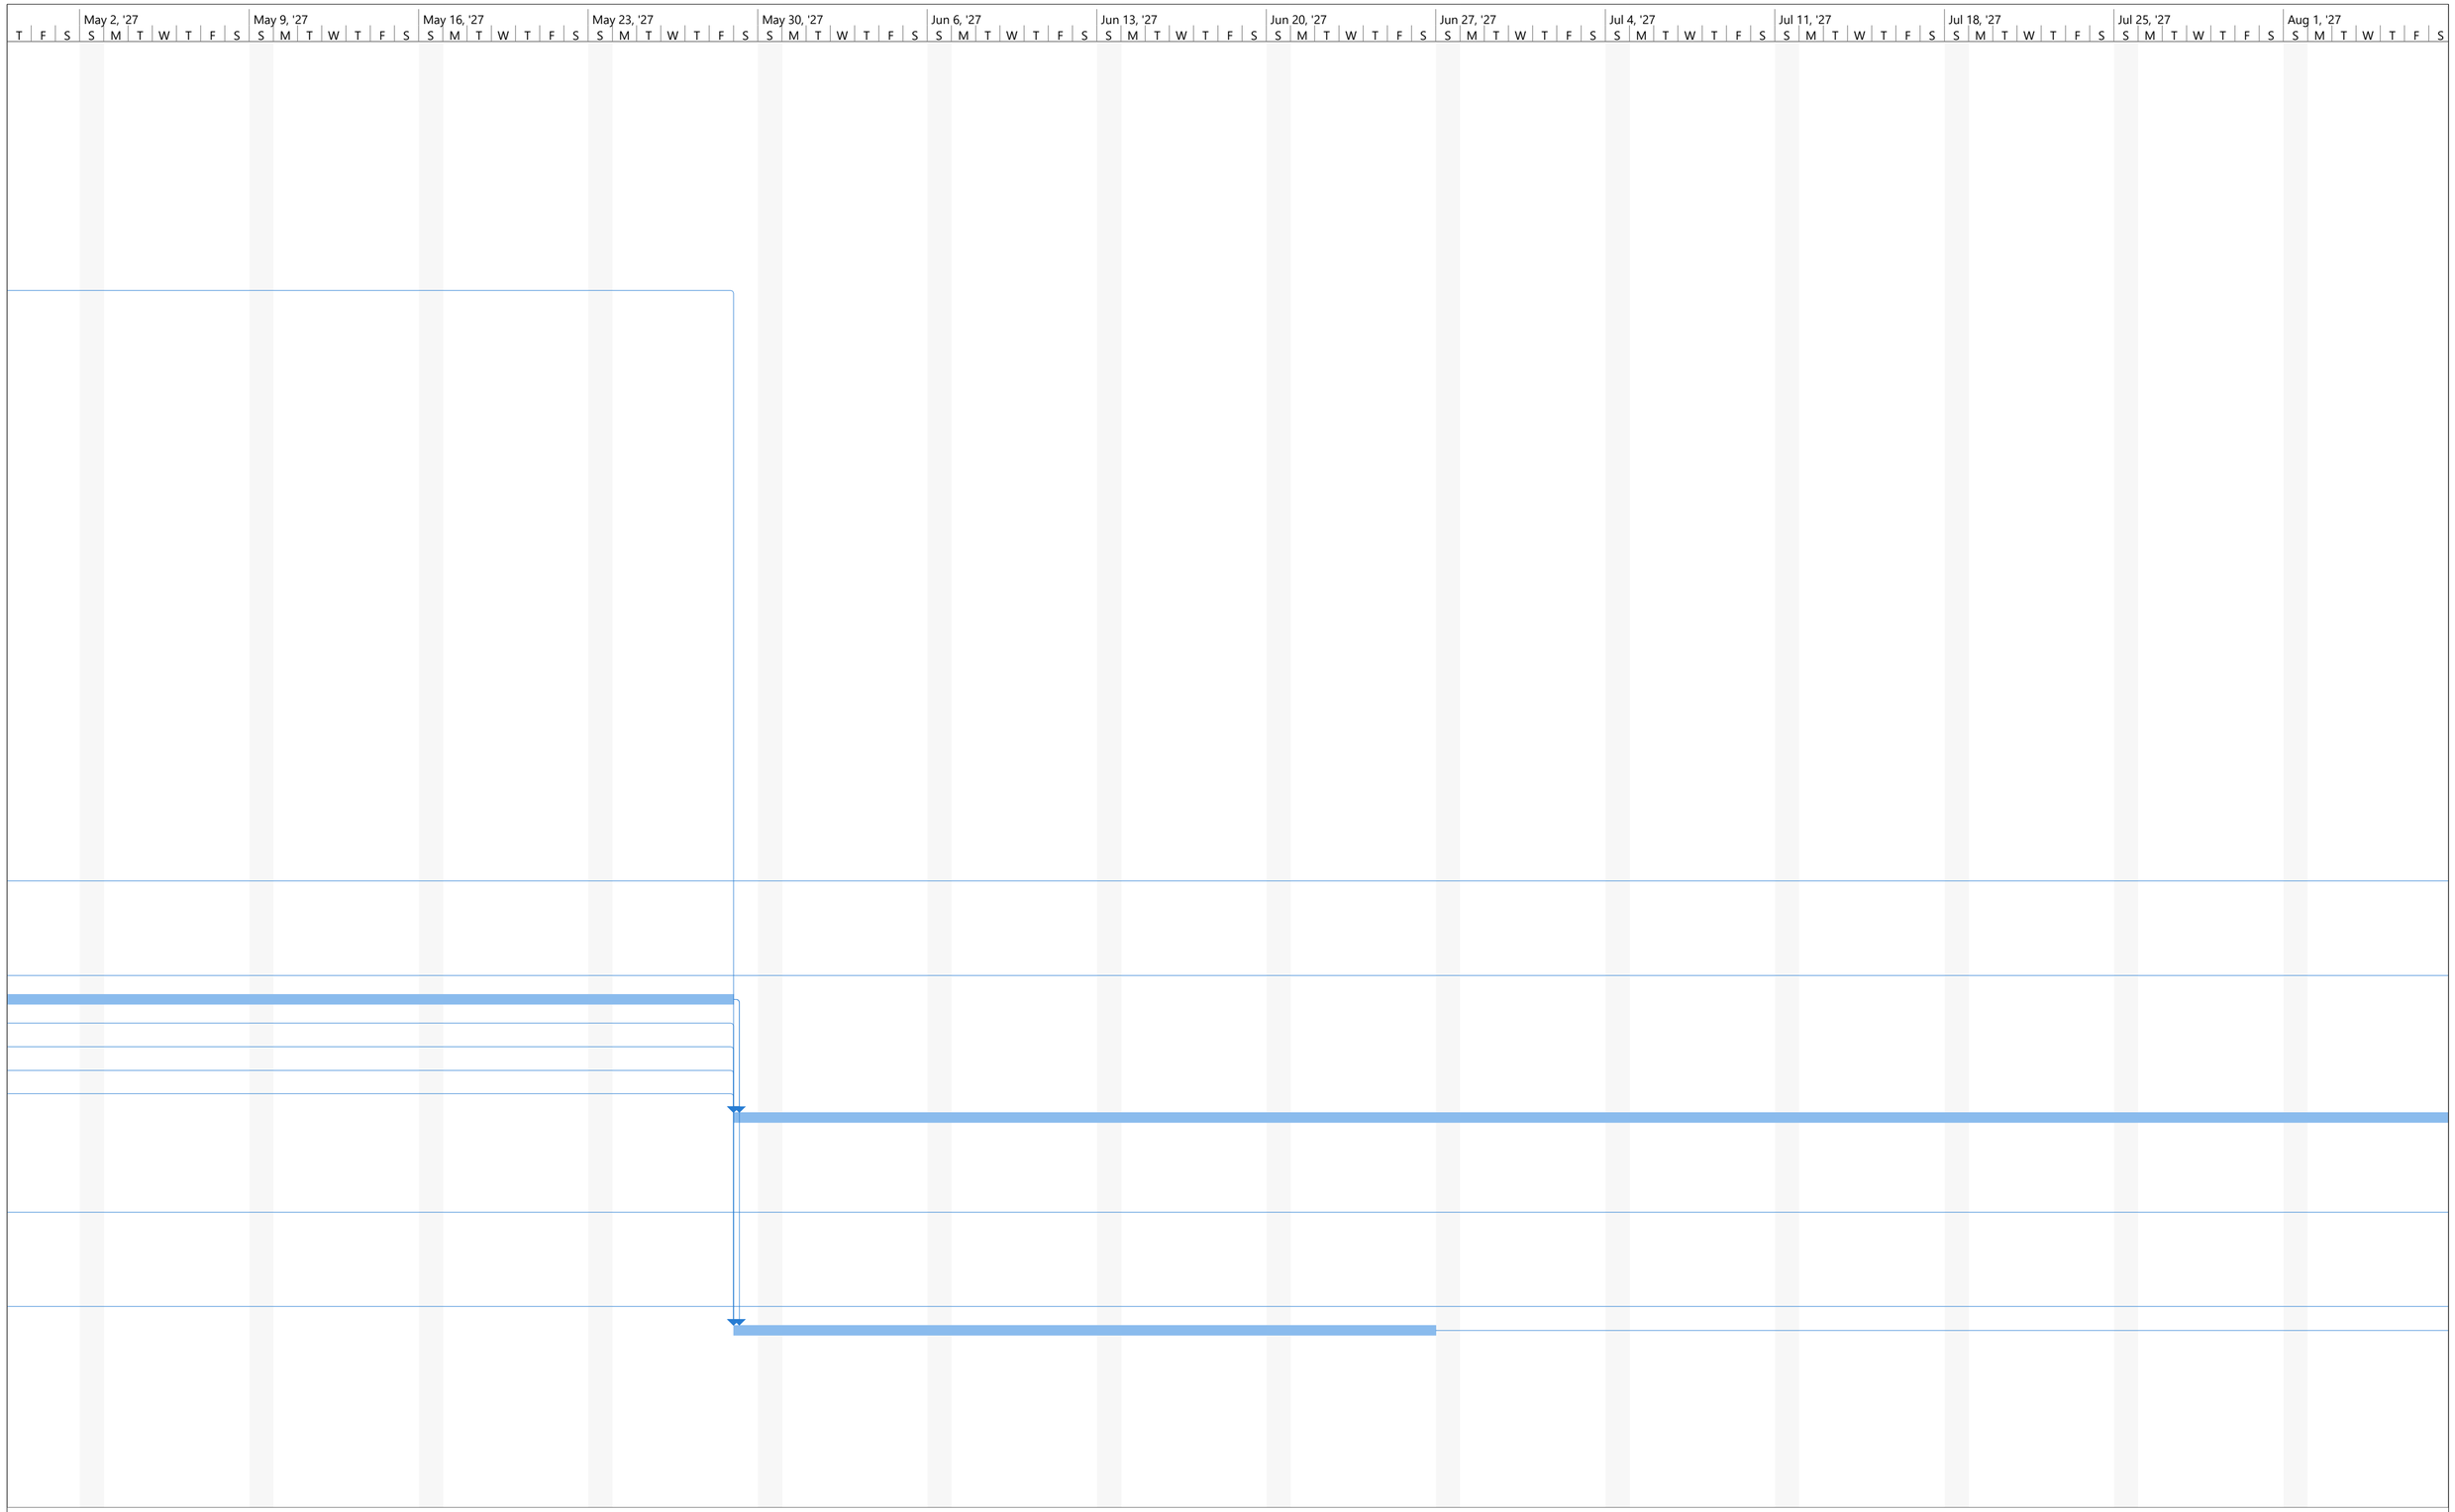

Project: Michael_Futol_Chinaim
Date: Tue 9/1/26

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

BASELINE | Reference programme; planned dates and logic are the comparison basis.

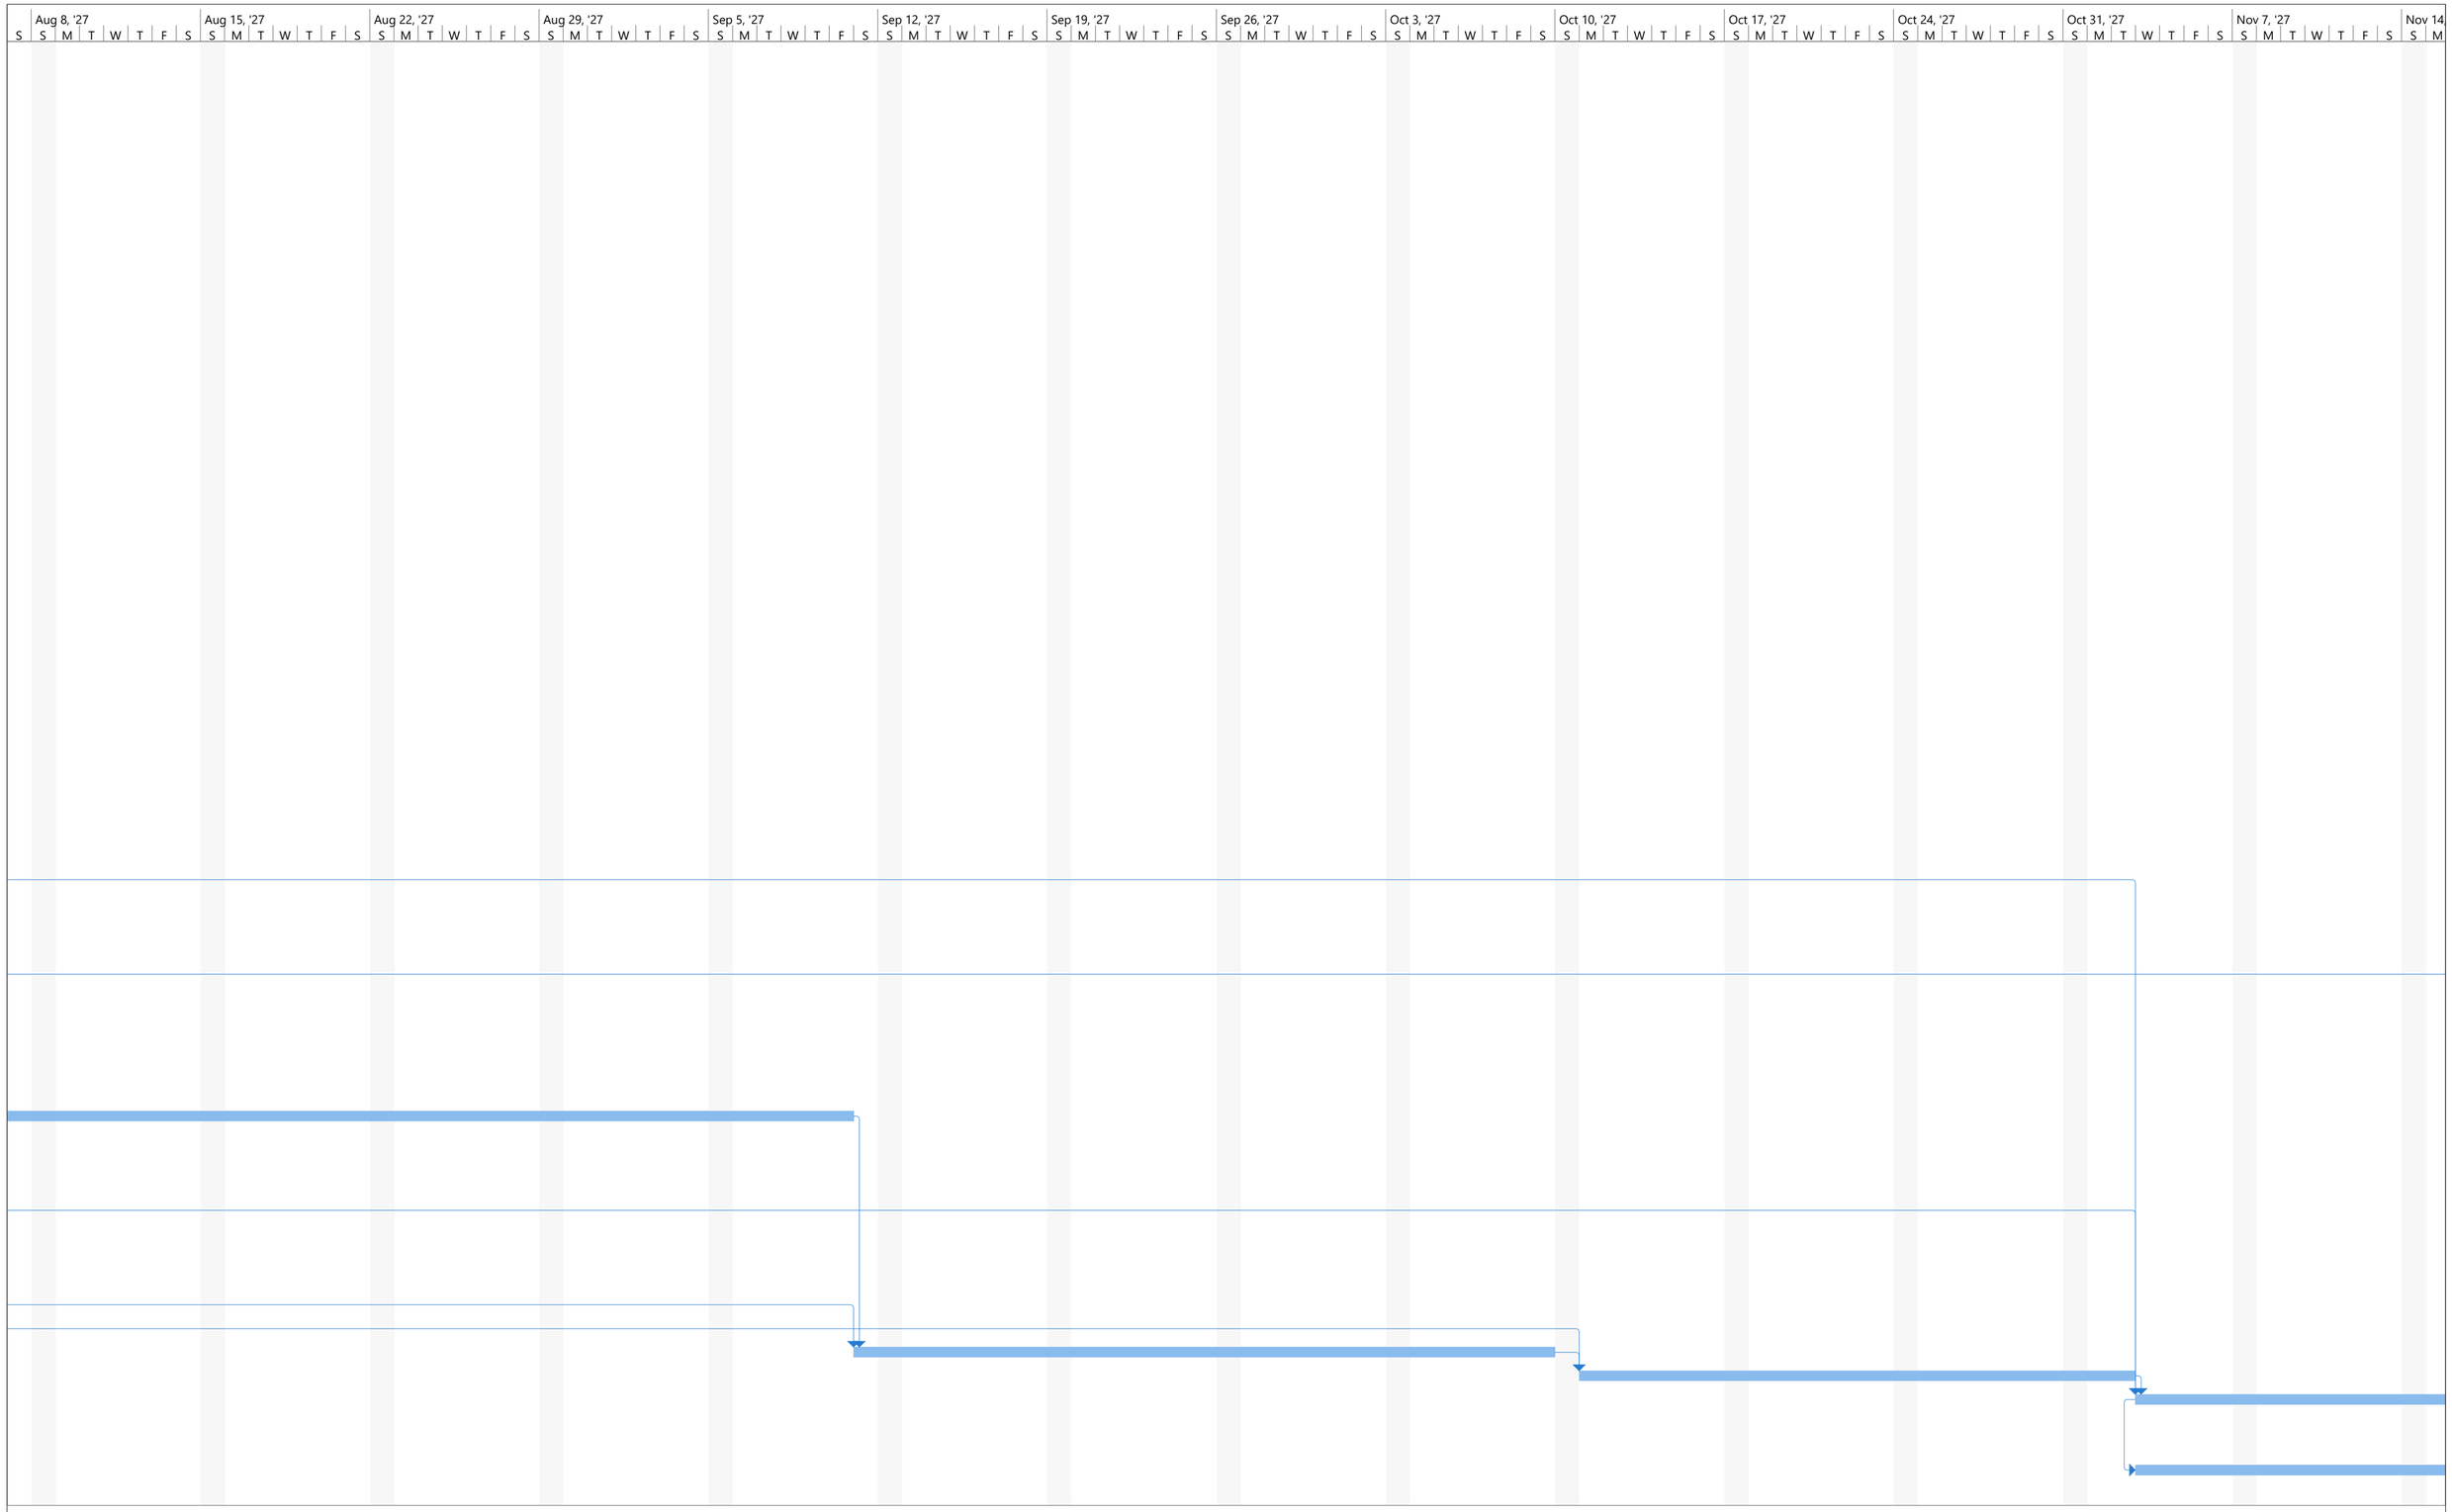

Project: Michael_Futol_Chinaim
Date: Tue 9/1/26

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

BASELINE | Reference programme; planned dates and logic are the comparison basis.

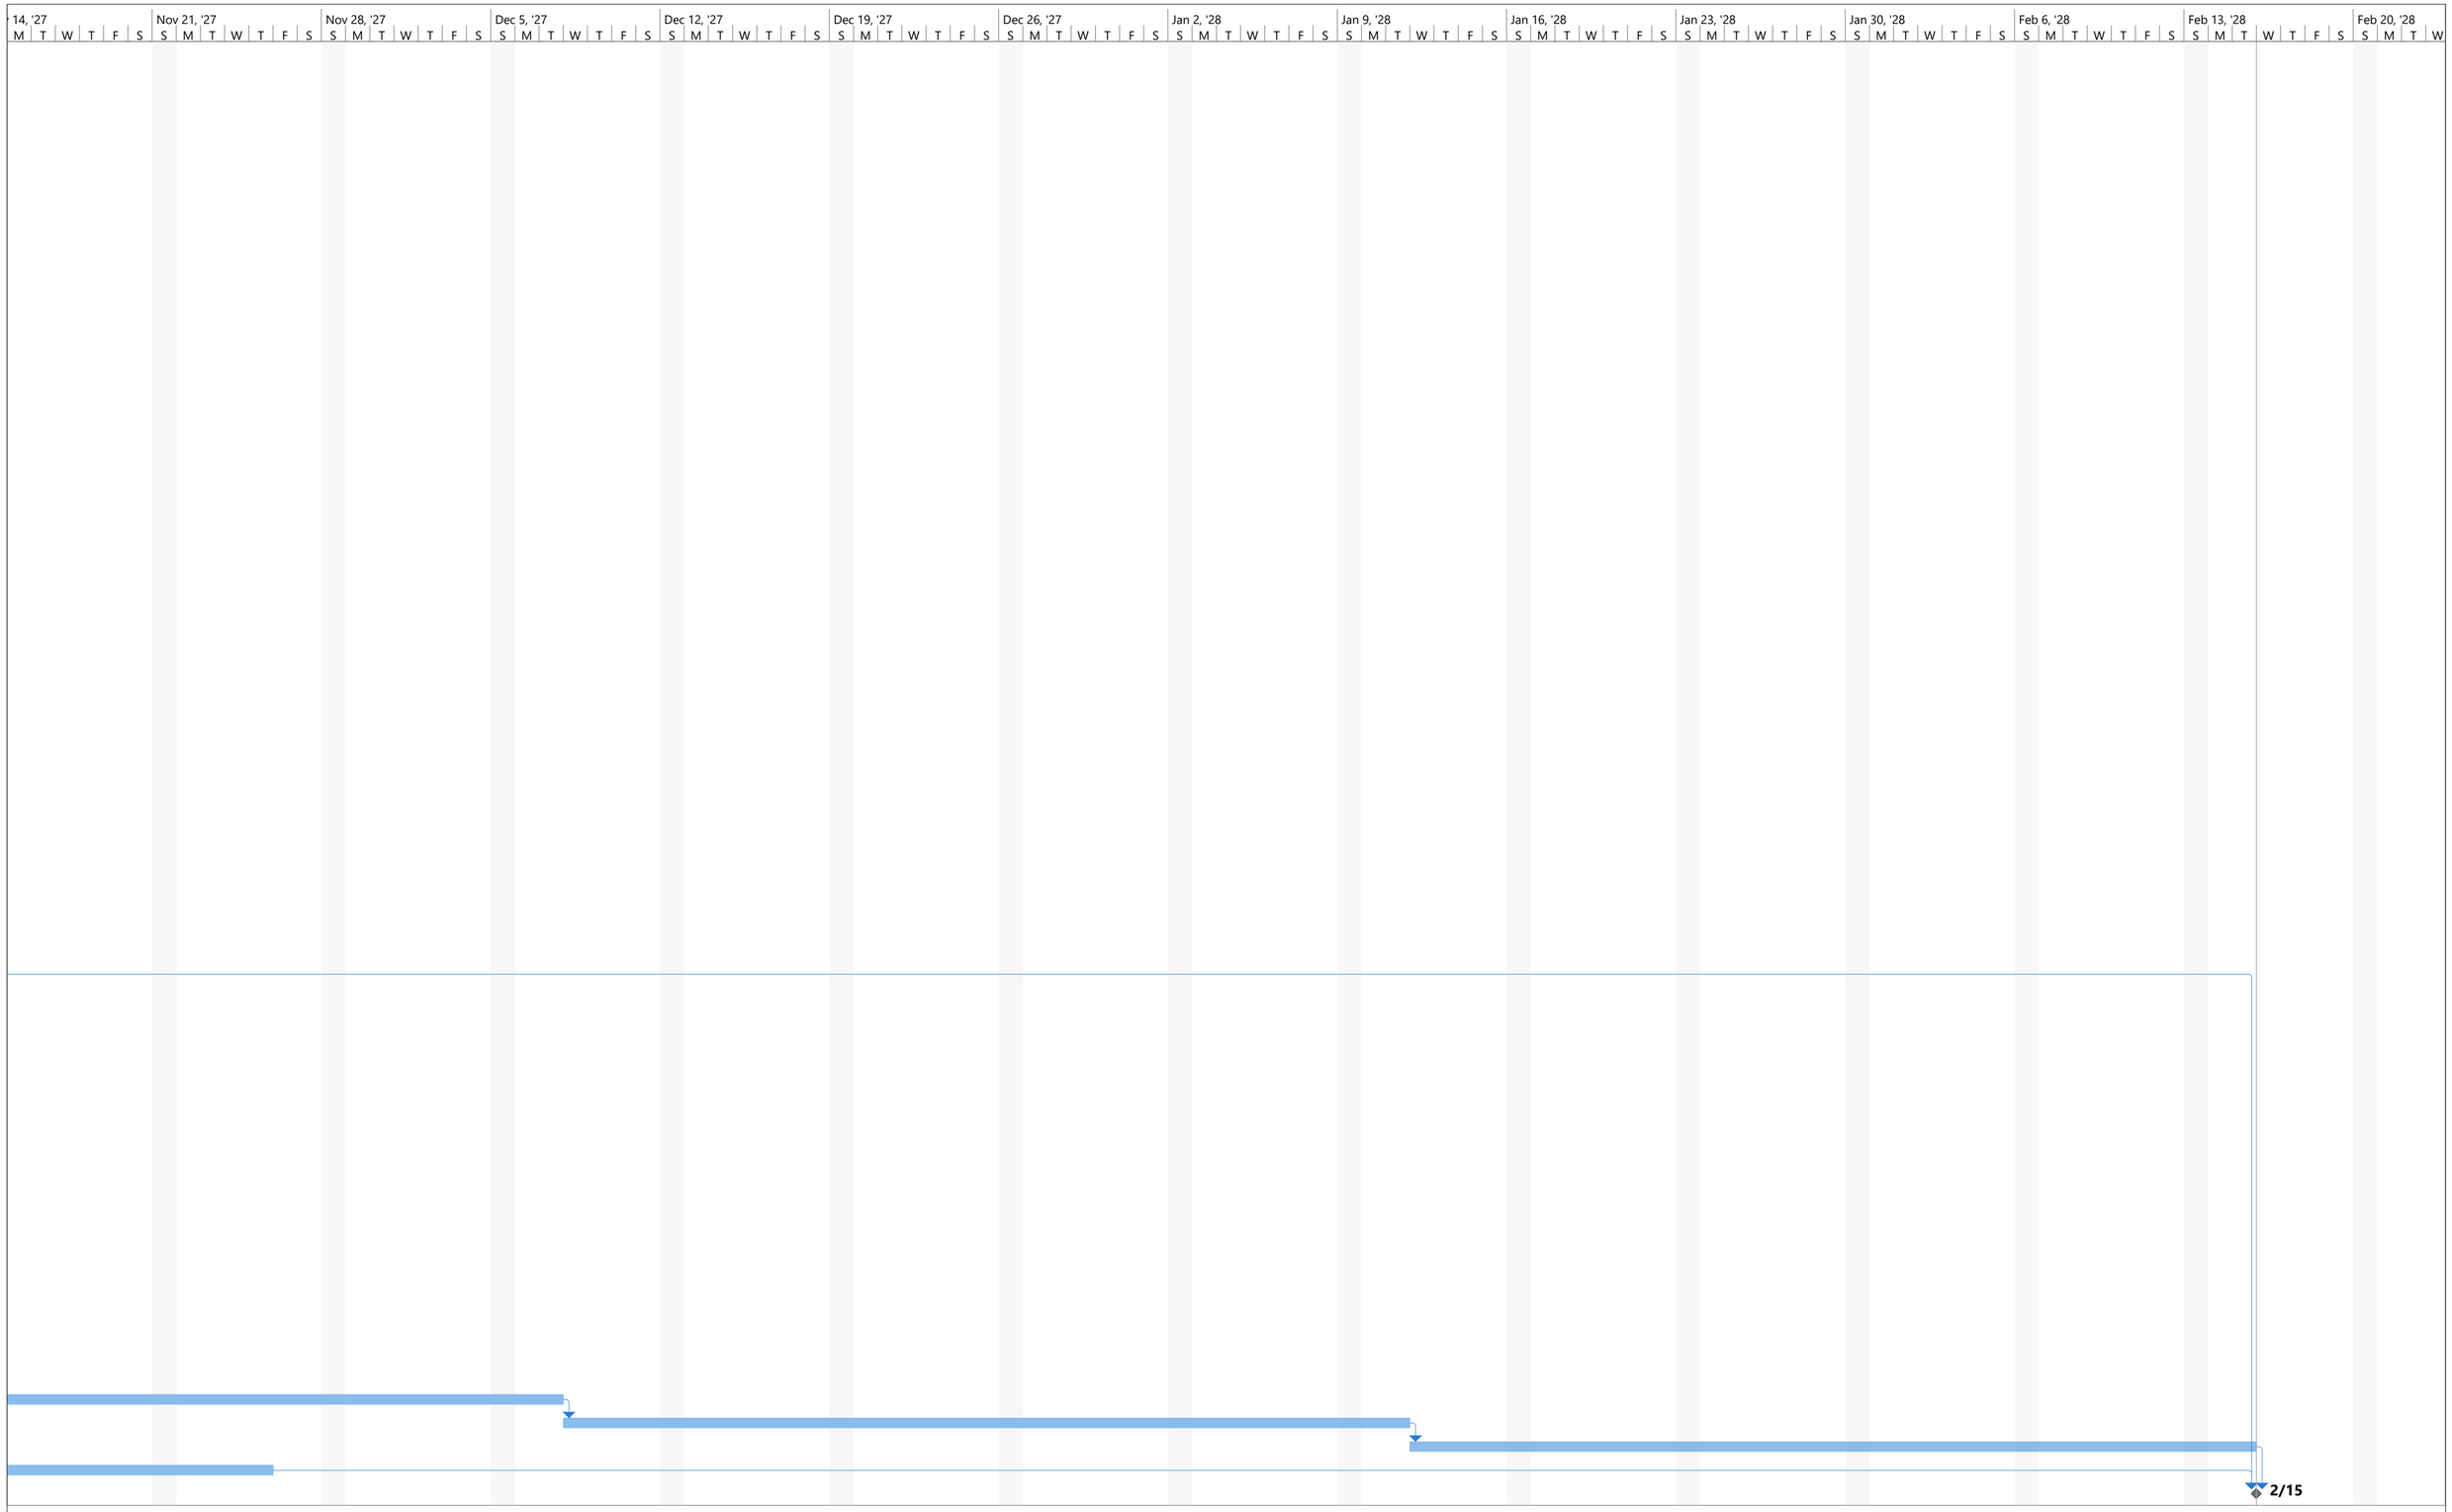

Project: Michael_Futol_Chinaim
Date: Tue 9/1/26

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

BASELINE | Reference programme; planned dates and logic are the comparison basis.
