Michael_Futol_Chinaimo_Recovery.mpp

ID	Task Name	Act. Start	Act. Finish	% Comp.	Phys. % Comp.	Act. Dur.
1	Notice to Procee	Wed 10/1/25	Wed 10/1/25	100%	100%	0 days
2	Mobilization & Te	Wed 10/1/25	Thu 10/23/25	100%	100%	20 days
3	Survey / Setting (	Tue 10/7/25	Thu 10/23/25	100%	100%	15 days
4	Review IFC Draw	Wed 10/1/25	Tue 11/4/25	100%	100%	30 days
5	Method Statemen	Mon 10/13/25	NA	90%	90%	40.5 days
6	Long-Lead M&E E	Thu 12/4/25	NA	45%	45%	135 days
7	SCADA / Instrum	Thu 12/4/25	NA	40%	40%	104 days
8	Electrical / Recei	Thu 12/4/25	NA	55%	55%	132 days
9	Site Clearing / Ex	Fri 10/24/25	Wed 12/3/25	100%	100%	35 days
10	Ground Preparat	Thu 12/4/25	Sat 12/20/25	100%	100%	15 days
11	WTP Foundation	Mon 12/22/25	NA	75%	75%	45 days
12	Mixing / Floccula	Mon 3/2/26	NA	45%	45%	31.5 days
13	Sedimentation B	Wed 3/25/26	NA	31%	25%	25 days
14	Rapid Sand Filter	NA	NA	0%	0%	0 days
15	Internal Channels	NA	NA	0%	0%	0 days
16	Waterproofing /	NA	NA	0%	0%	0 days
17	Hydrostatic / Stru	NA	NA	0%	0%	0 days
18	10,000 mÂ³ Rese	Fri 10/24/25	Tue 12/9/25	100%	100%	40 days
19	Reservoir Foundat	Wed 12/10/25	NA	80%	80%	48 days
20	Reservoir Walls /	Wed 2/18/26	NA	45%	45%	45 days
21	Reservoir Roof Sl	Mon 6/15/26	NA	10%	10%	6 days
22	Reservoir Waterp	NA	NA	0%	0%	0 days
23	Reservoir Hydros	NA	NA	0%	0%	0 days
24	Pump Room Civil	Wed 1/14/26	NA	30%	30%	22.5 days
25	Chemical Building	Mon 1/26/26	NA	25%	25%	22.5 days
26	Administration &	Thu 12/4/25	NA	22%	22%	26.4 days
27	Building MEP / A	Thu 4/23/26	NA	5%	5%	3.5 days
28	Process Piping In	NA	NA	0%	0%	0 days
29	Pumps & Mechar	NA	NA	0%	0%	0 days
30	Chemical Dosing	NA	NA	0%	0%	0 days
31	Filter Media / Un	NA	NA	0%	0%	0 days
32	Electrical Installa	NA	NA	0%	0%	0 days
33	Instrumentation	NA	NA	0%	0%	0 days
34	Salakham Site Pr	Fri 10/24/25	Tue 12/9/25	100%	100%	40 days
35	7,100 mÂ³ Reserv	Wed 12/10/25	NA	25%	25%	45 days
36	Salakham Pump I	Fri 11/28/25	NA	40%	40%	36 days
37	Salakham M&E Ir	NA	NA	0%	0%	0 days
38	22-kV Route Surv	Fri 10/24/25	Mon 12/15/25	100%	100%	45 days
39	Pole / Foundatio	Tue 12/16/25	NA	40%	40%	40 days
40	22-kV Line Install	Sat 4/11/26	NA	15%	15%	18 days
41	Receiving Equipr	NA	NA	0%	0%	0 days
42	Mechanical Pre-(	NA	NA	0%	0%	0 days
43	Electrical / I&C Pr	NA	NA	0%	0%	0 days
44	Dry Commissioni	NA	NA	0%	0%	0 days
45	Wet Commission	NA	NA	0%	0%	0 days
46	Performance / W	NA	NA	0%	0%	0 days
47	Punch List / Recti	NA	NA	0%	0%	0 days
48	Training / O&M D	NA	NA	0%	0%	0 days
49	Taking Over / Co	NA	NA	0%	0%	0 days

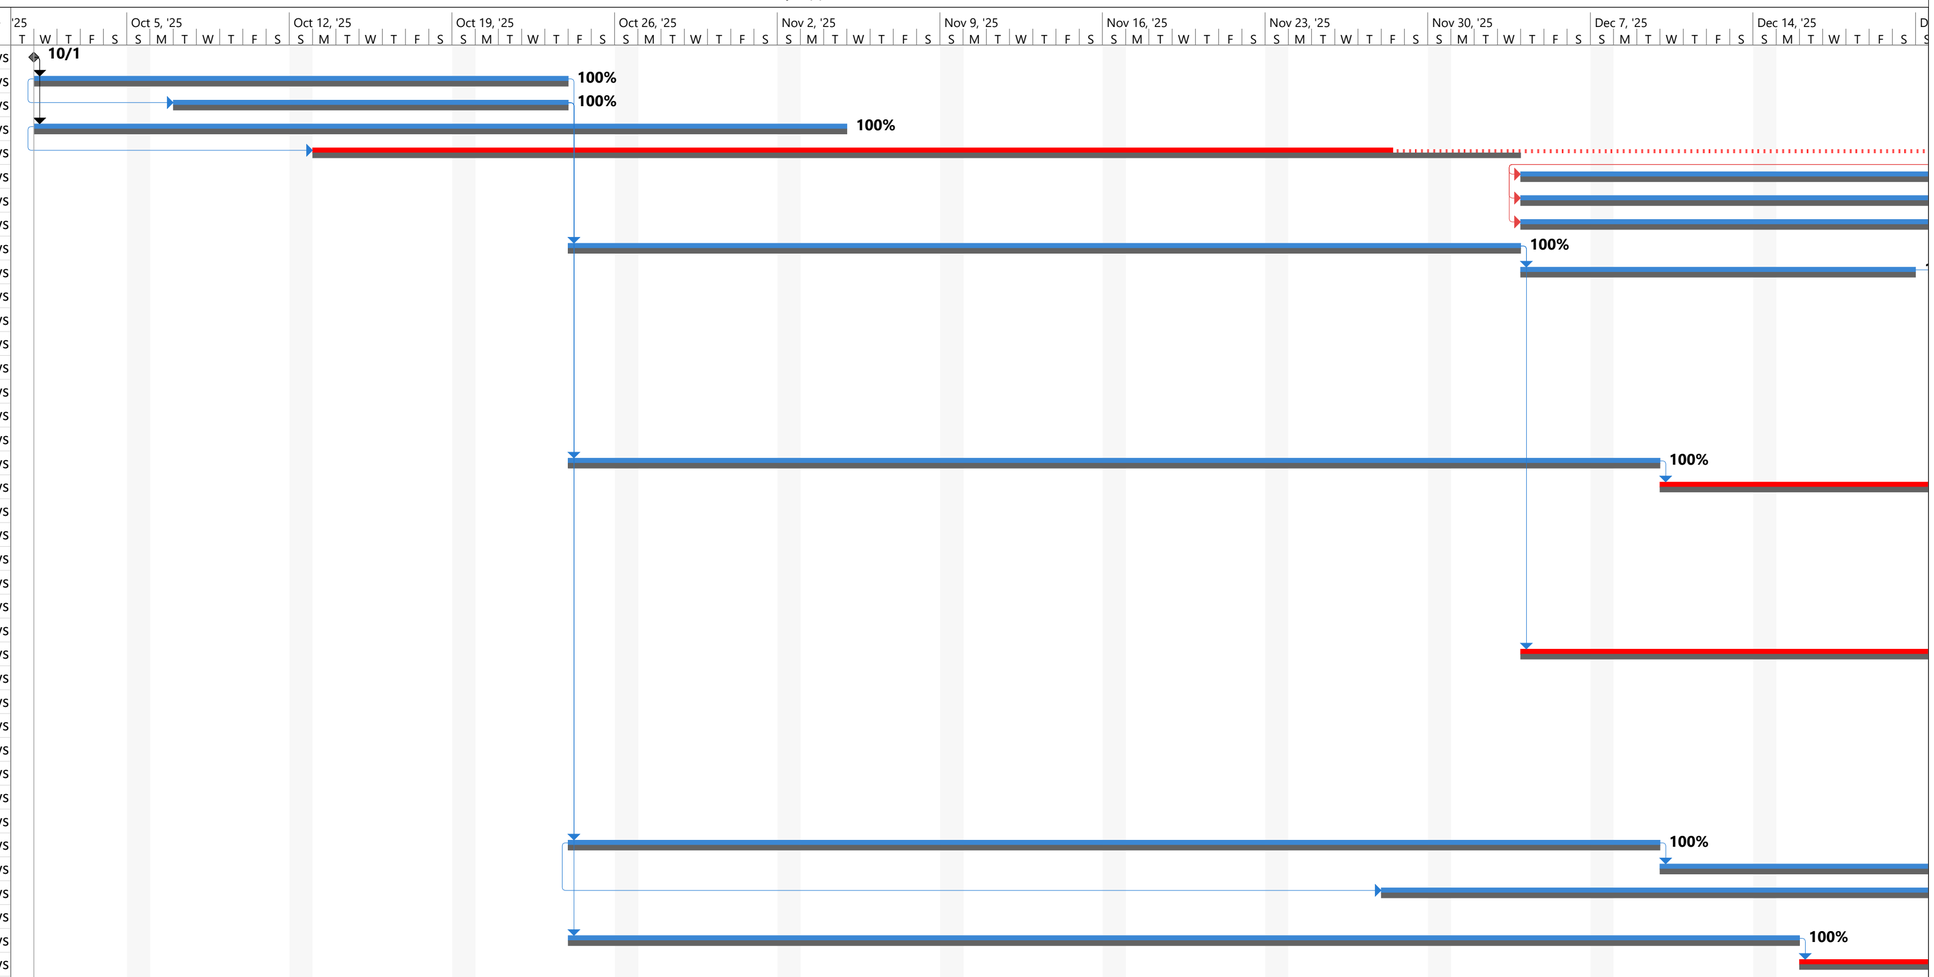

Critical | Task | Manual Task | Duration-only | Baseline Milestone | Summary | External Tasks | Inactive Milestone
Critical Split | Split | Start-only | Baseline | Milestone | Manual Summary | External Milestone | Inactive Summary
Critical Progress | Task Progress | Finish-only | Baseline Split | Summary Progress | Project Summary | Inactive Task | Deadline

RECOVERY TRACKING | Partial recovery compared with baseline/current forecast; residual delay remains visible.

Michael_Futol_Chinaimo_Recovery.mpp

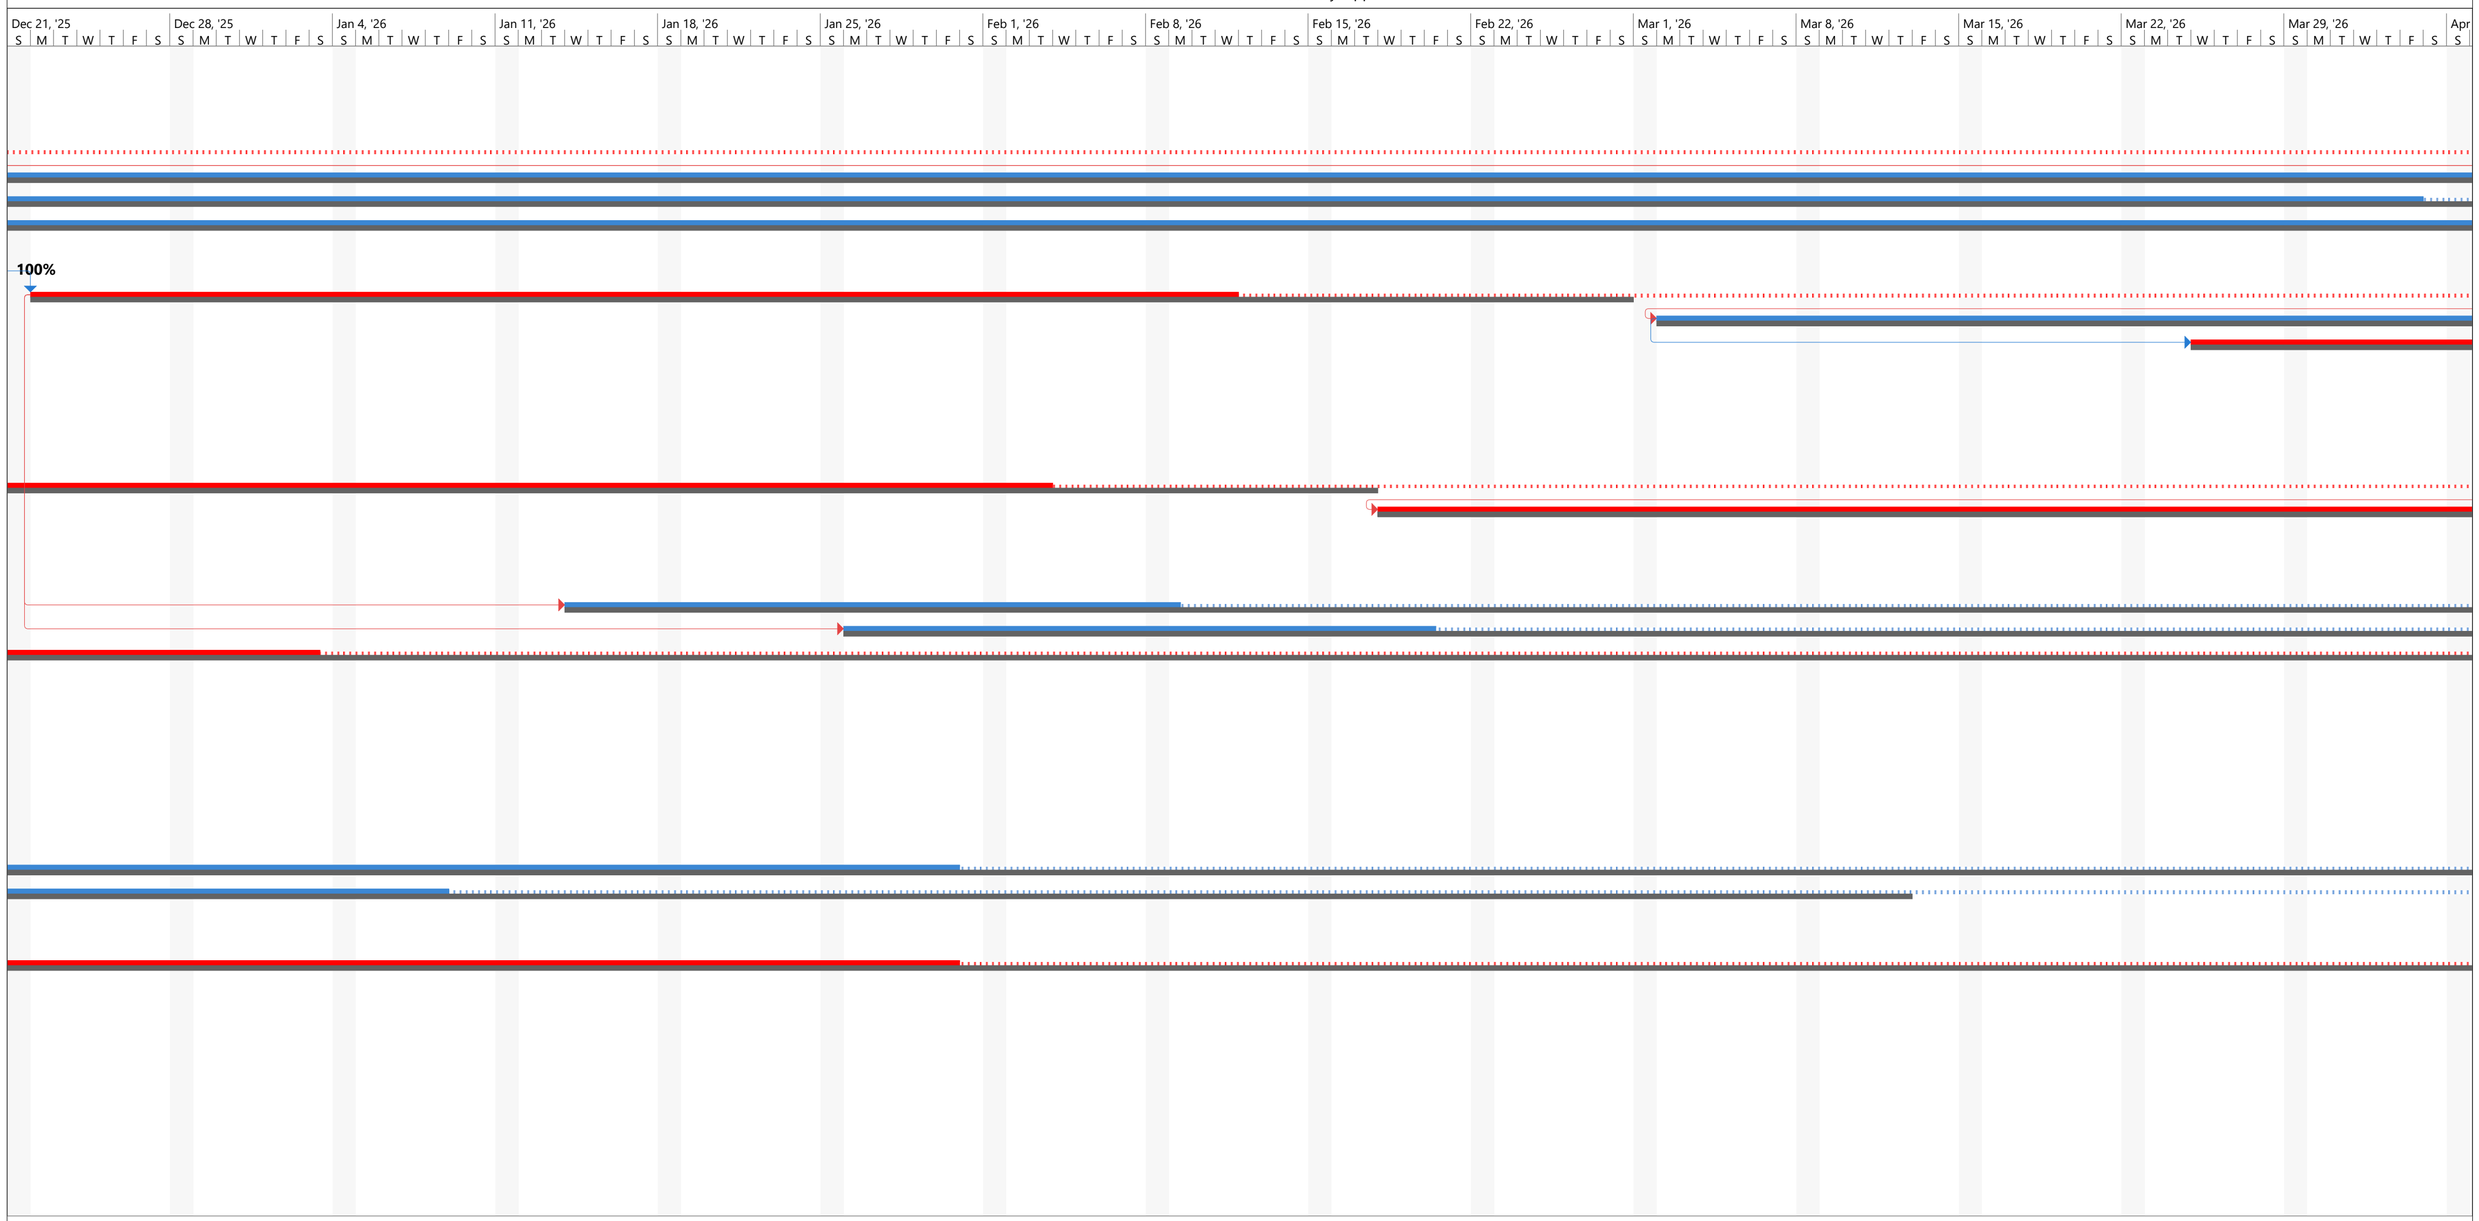

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

RECOVERY TRACKING | Partial recovery compared with baseline/current forecast; residual delay remains visible.

Michael_Futol_Chinaimo_Recovery.mpp

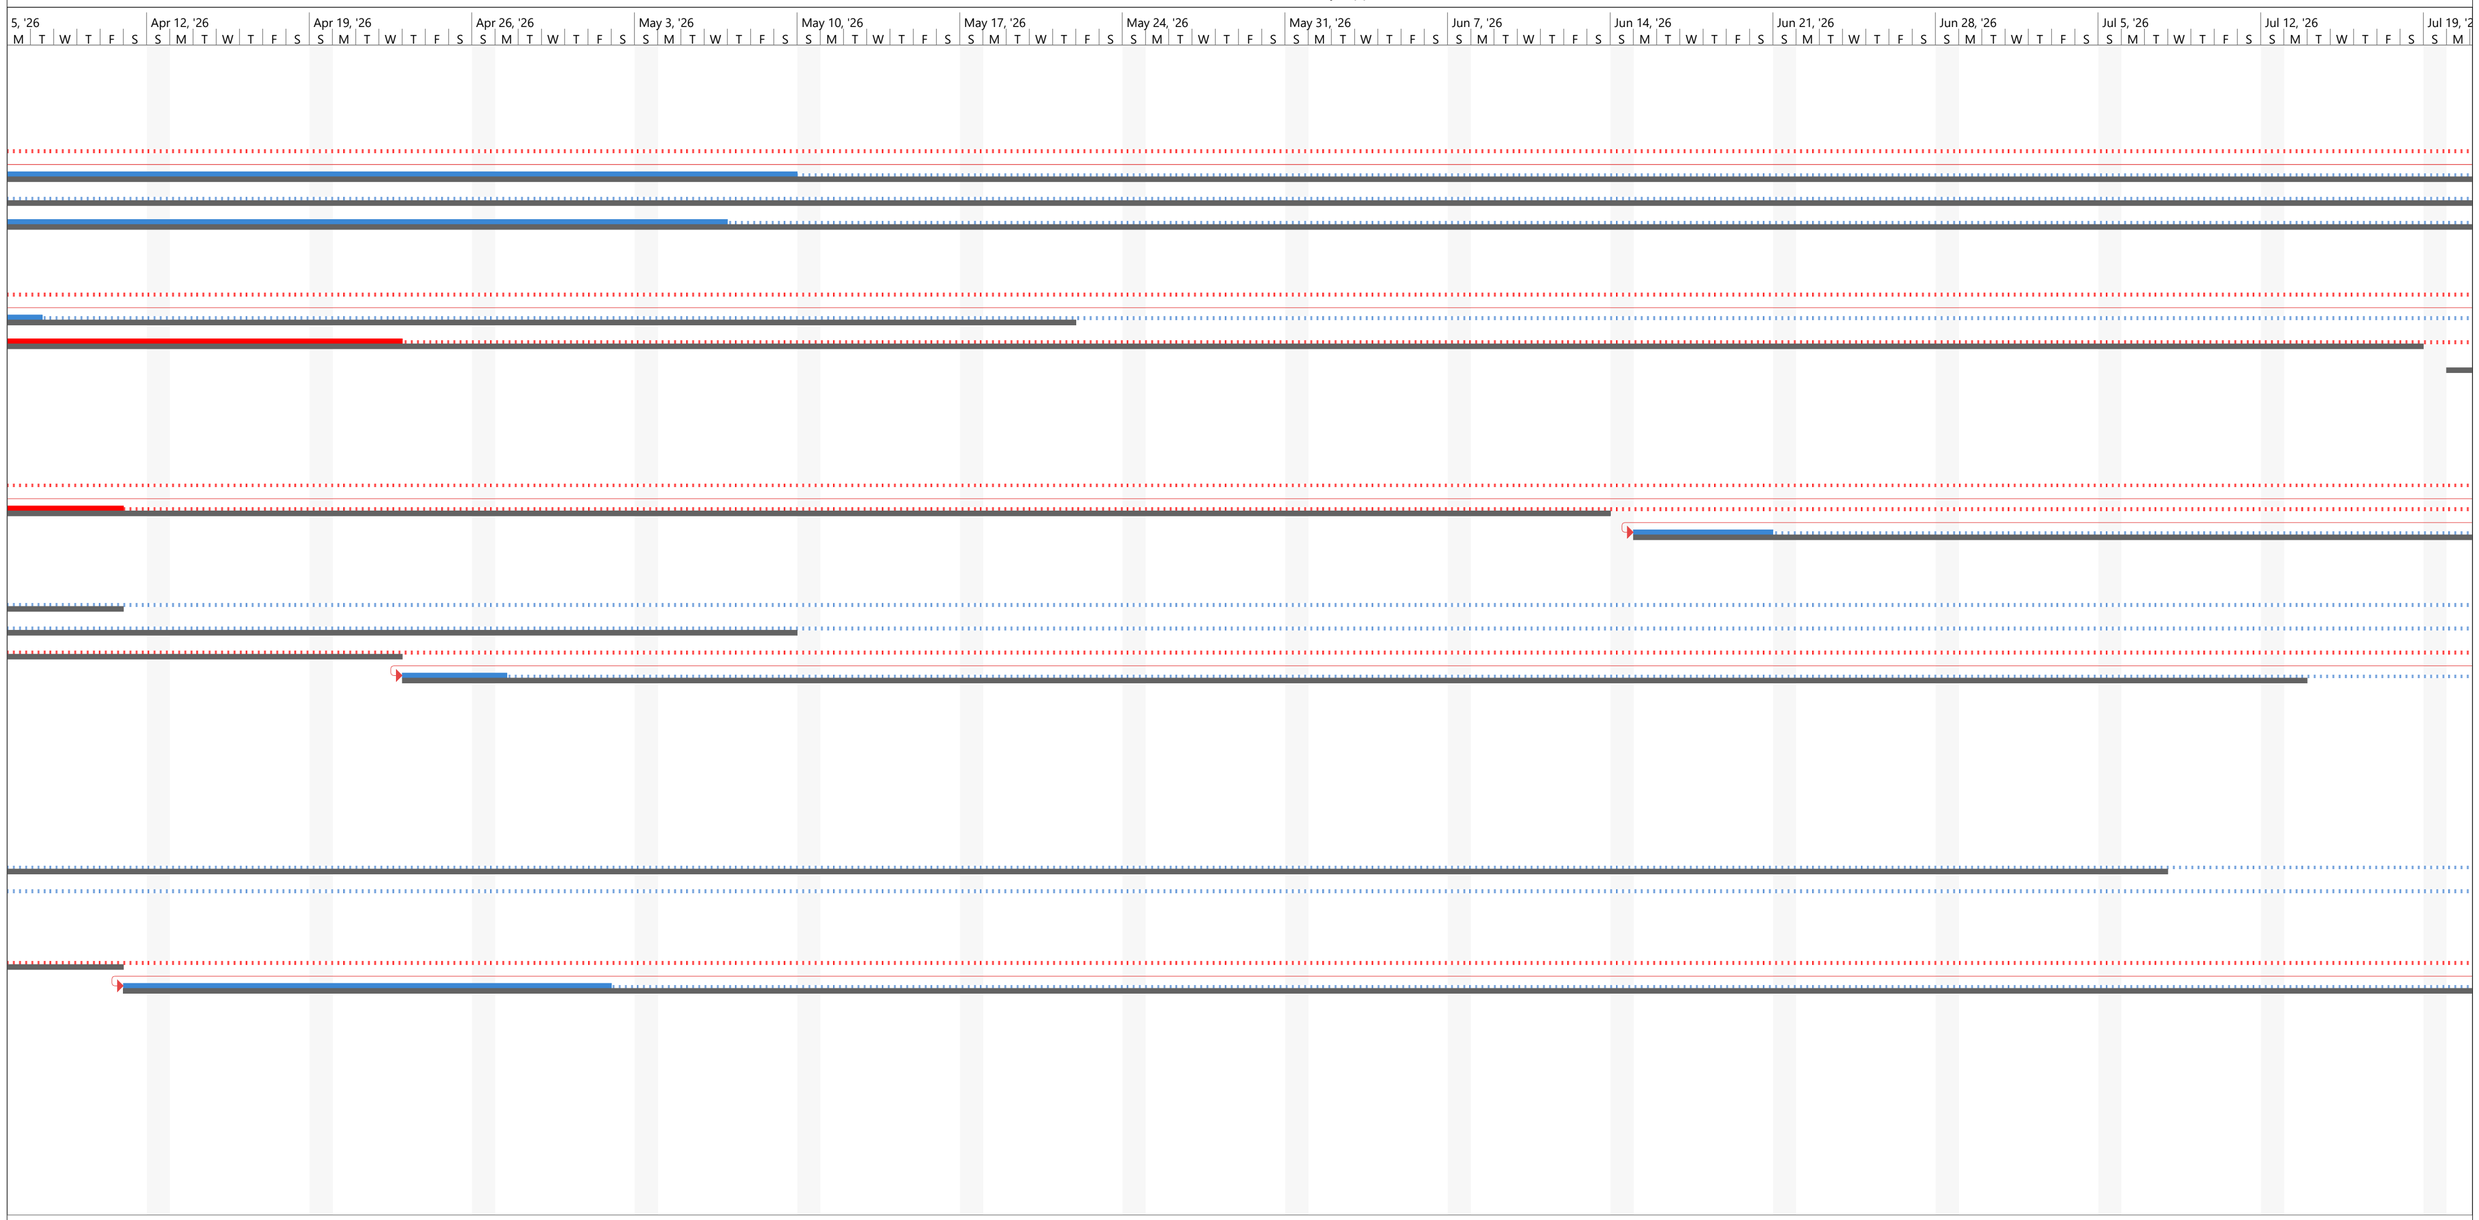

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

RECOVERY TRACKING | Partial recovery compared with baseline/current forecast; residual delay remains visible.

Michael_Futol_Chinaimo_Recovery.mpp

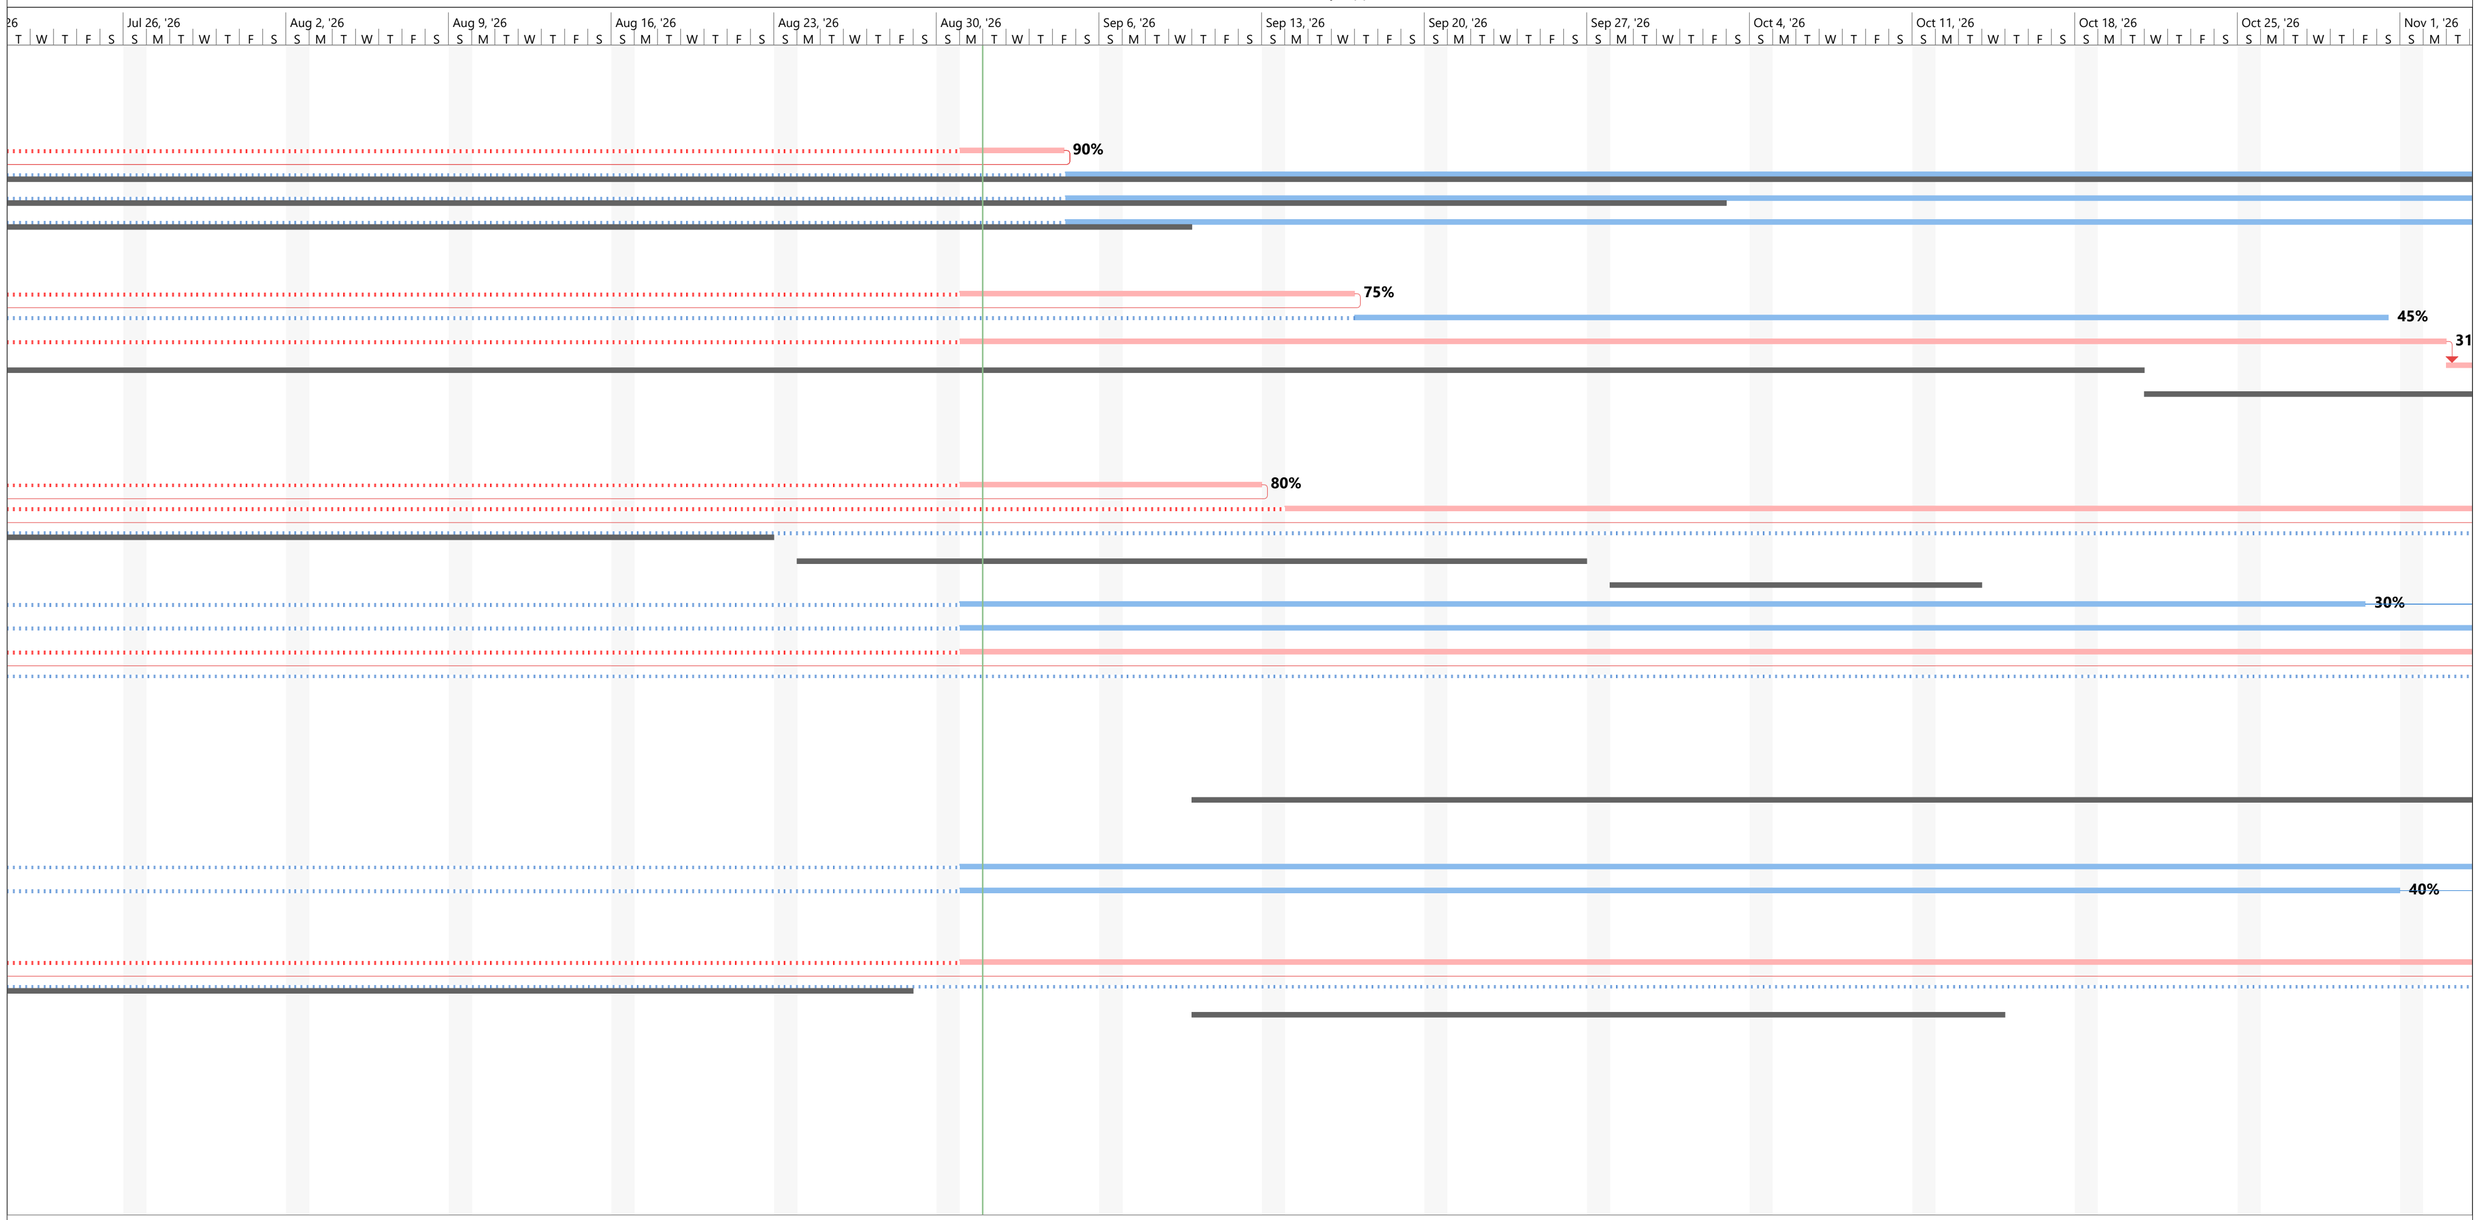

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

RECOVERY TRACKING | Partial recovery compared with baseline/current forecast; residual delay remains visible.

Michael_Futol_Chinaimo_Recovery.mpp

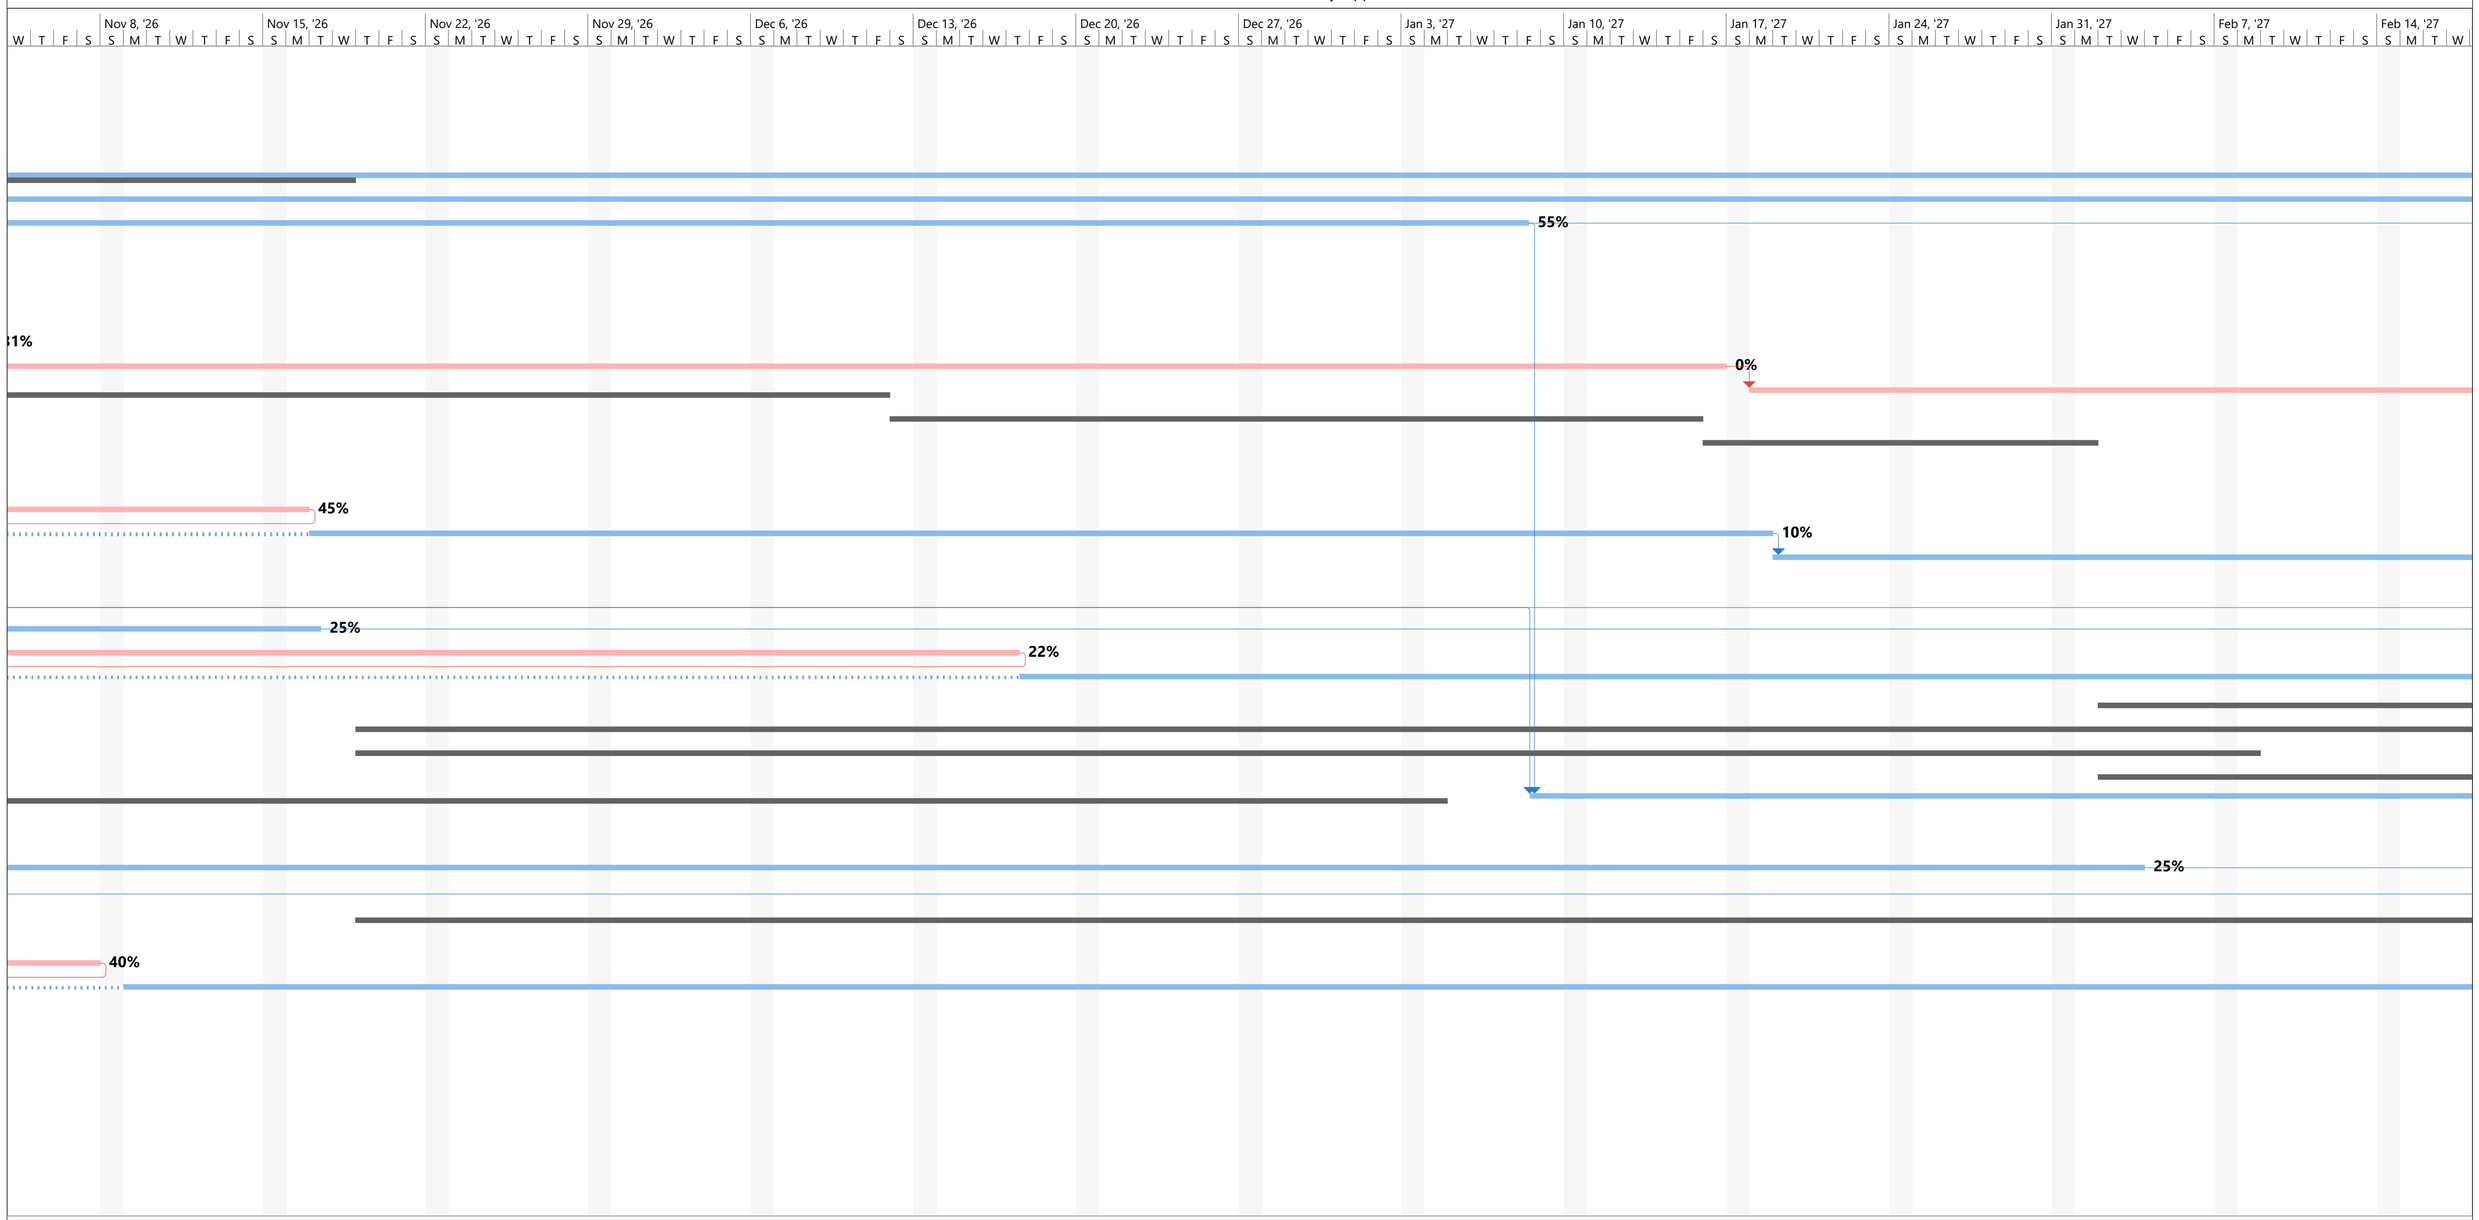

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

RECOVERY TRACKING | Partial recovery compared with baseline/current forecast; residual delay remains visible.

Michael_Futol_Chinaimo_Recovery.mpp

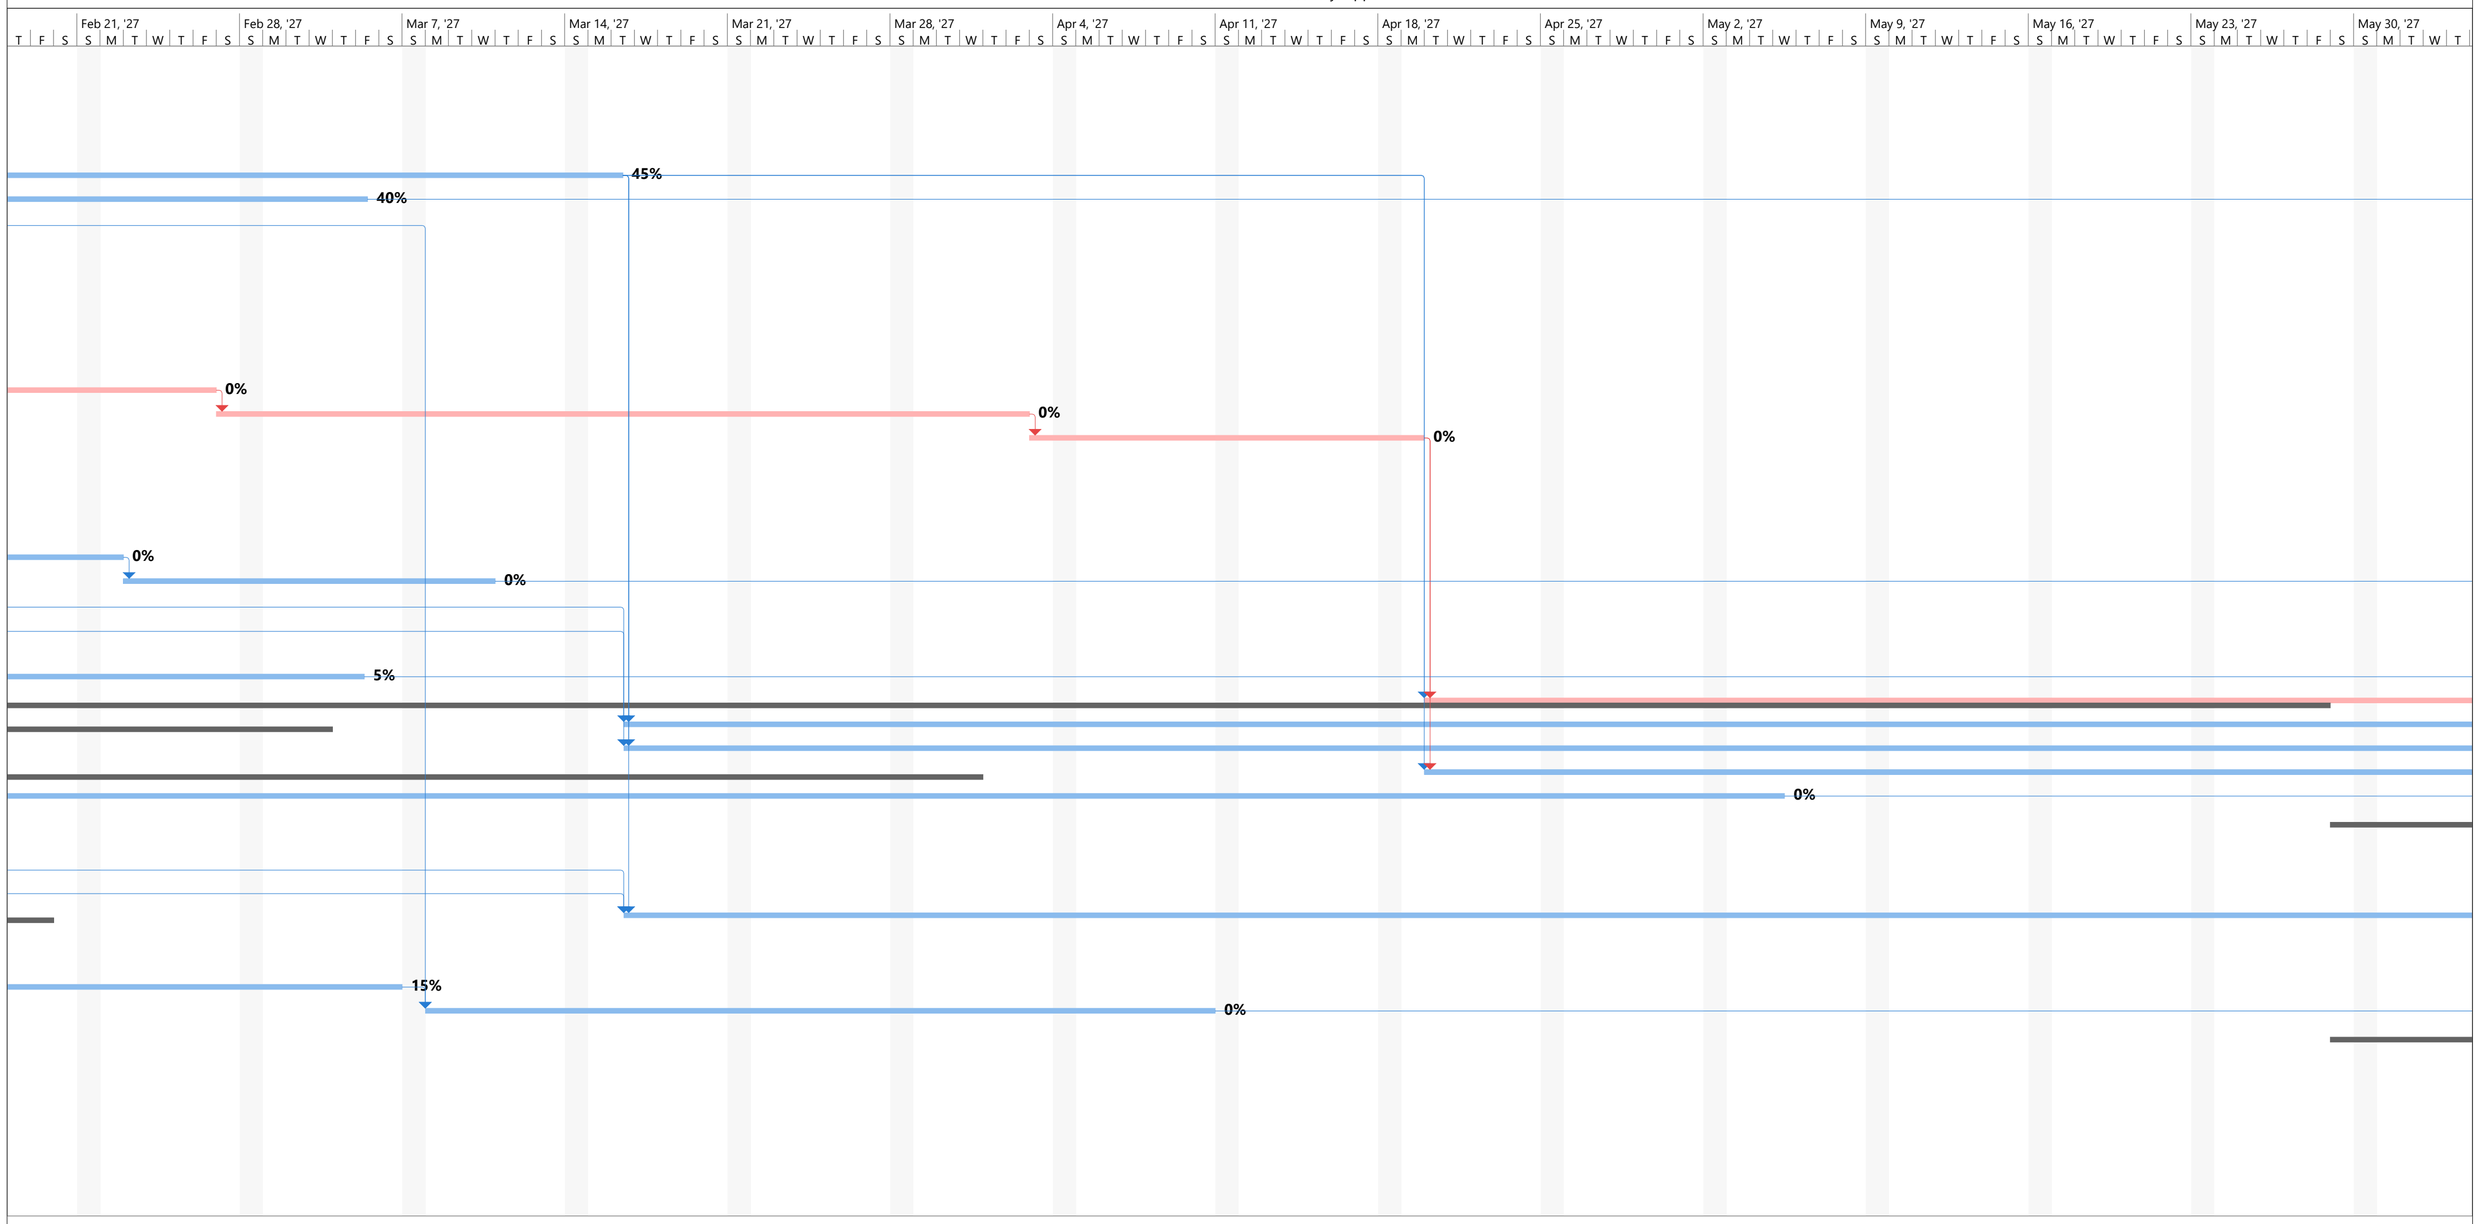

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

RECOVERY TRACKING | Partial recovery compared with baseline/current forecast; residual delay remains visible.

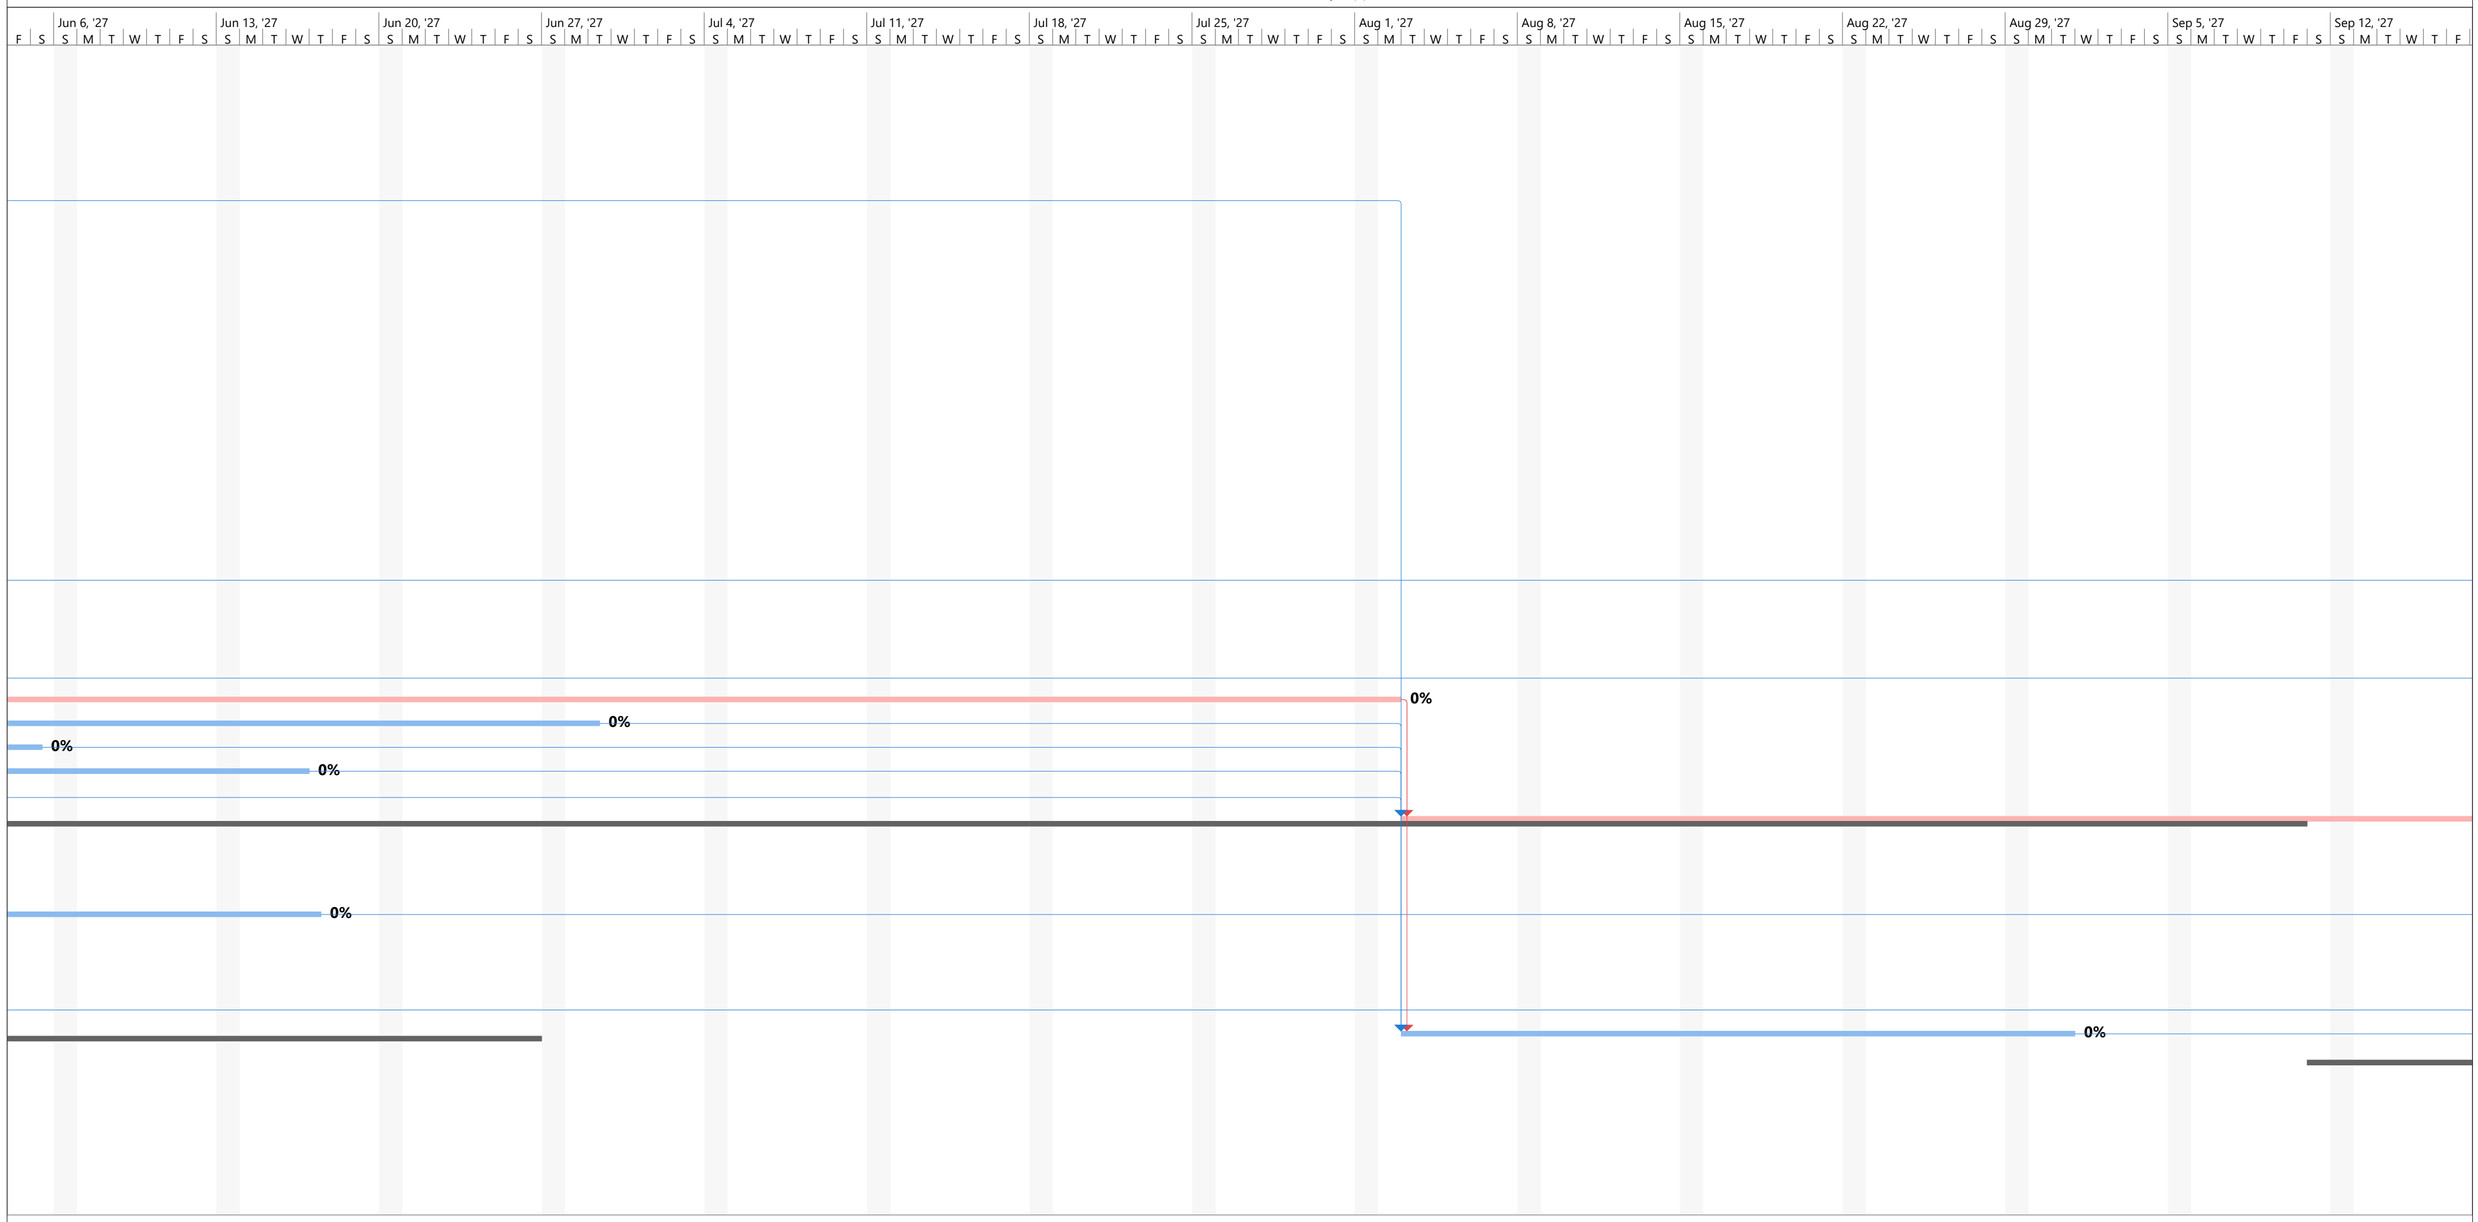

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

RECOVERY TRACKING | Partial recovery compared with baseline/current forecast; residual delay remains visible.

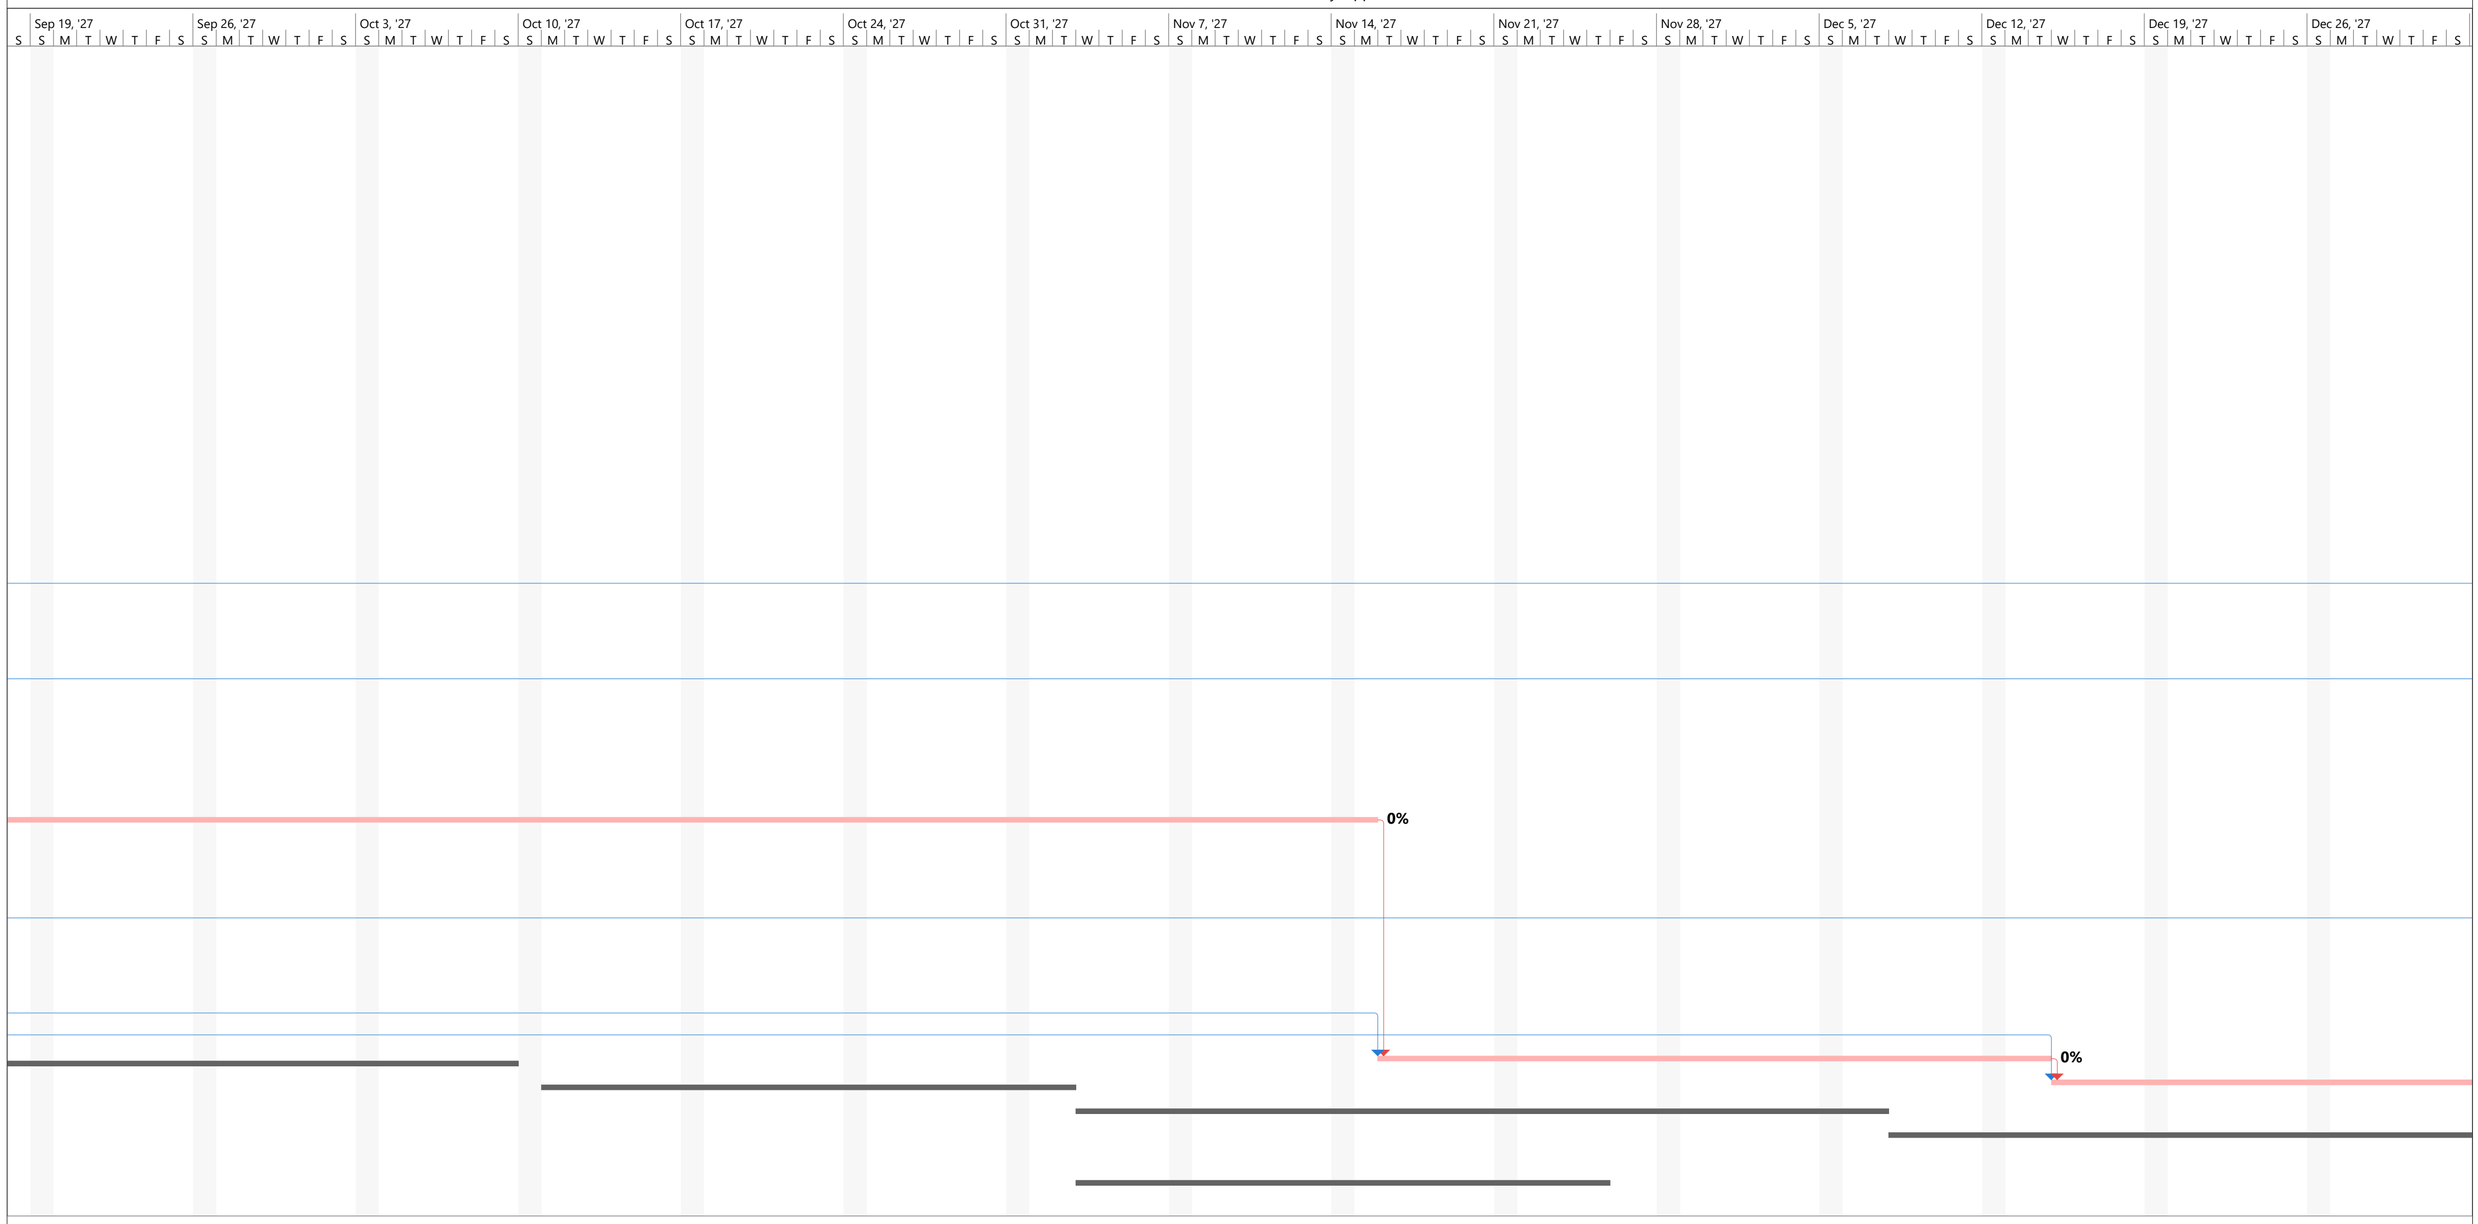

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

RECOVERY TRACKING | Partial recovery compared with baseline/current forecast; residual delay remains visible.

Critical	Task	Manual Task	Duration-only	Baseline Milestone	Summary	External Tasks	Inactive Milestone
Critical Split	Split	Start-only	Baseline	Milestone	Manual Summary	External Milestone	Inactive Summary
Critical Progress	Task Progress	Finish-only	Baseline Split	Summary Progress	Project Summary	Inactive Task	Deadline

RECOVERY TRACKING | Partial recovery compared with baseline/current forecast; residual delay remains visible.
