Michael_Futol_Chinaimo_Actual_Progress.mpp

ID	Task Name	Act. Start	Act. Finish	% Comp.	Phys. % Comp.	Act. Dur.
5	Method Statemen	on 10/13/25	NA	90%	90%	40.5 days
11	WTP Foundation:	on 12/22/25	NA	75%	75%	45 days
13	Sedimentation Ba	Wed 3/25/26	NA	25%	25%	25 days
14	Rapid Sand Filter	NA	NA	0%	0%	0 days
15	Internal Channels	NA	NA	0%	0%	0 days
16	Waterproofing /	NA	NA	0%	0%	0 days
17	Hydrostatic / Stru	NA	NA	0%	0%	0 days
19	Reservoir Foundat	ed 12/10/25	NA	80%	80%	48 days
20	Reservoir Walls /	Wed 2/18/26	NA	45%	45%	45 days
26	Administration &	Thu 12/4/25	NA	22%	22%	26.4 days
28	Process Piping In	NA	NA	0%	0%	0 days
33	Instrumentation	NA	NA	0%	0%	0 days
39	Pole / Foundation	ue 12/16/25	NA	40%	40%	40 days
43	Electrical / I&C Pr	NA	NA	0%	0%	0 days
44	Dry Commissioni	NA	NA	0%	0%	0 days
45	Wet Commission	NA	NA	0%	0%	0 days
46	Performance / W	NA	NA	0%	0%	0 days
47	Punch List / Recti	NA	NA	0%	0%	0 days
49	Taking Over / Co	NA	NA	0%	0%	0 days

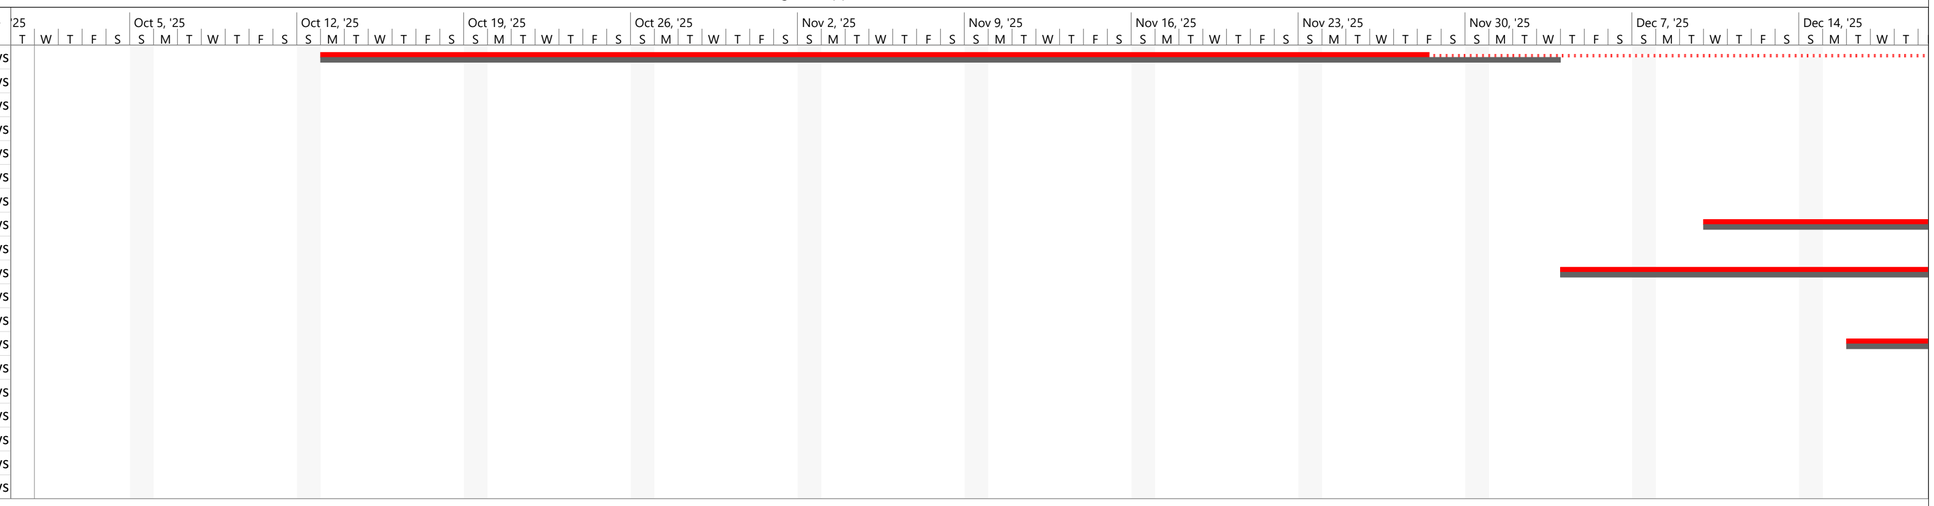

VIEW GUIDE
Critical tasks control forecast.

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

CURRENT CRITICAL PATH | Critical-filtered current programme; activities shown control forecast finish.

Michael_Futol_Chinaimo_Actual_Progress.mpp

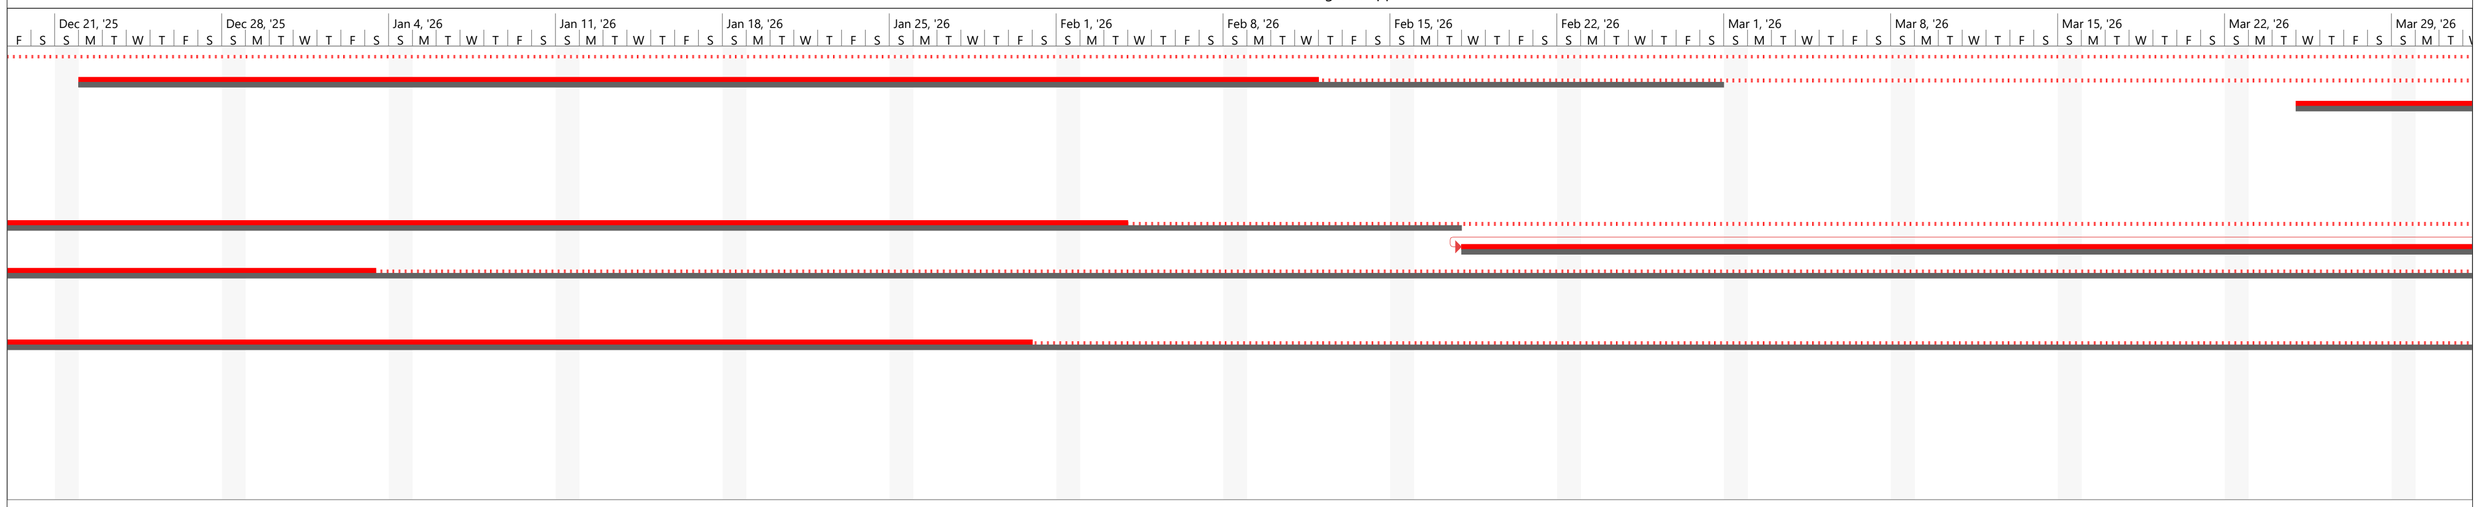

VIEW GUIDE
Critical tasks control forecast.

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

CURRENT CRITICAL PATH | Critical-filtered current programme; activities shown control forecast finish.

Michael_Futol_Chinaimo_Actual_Progress.mpp

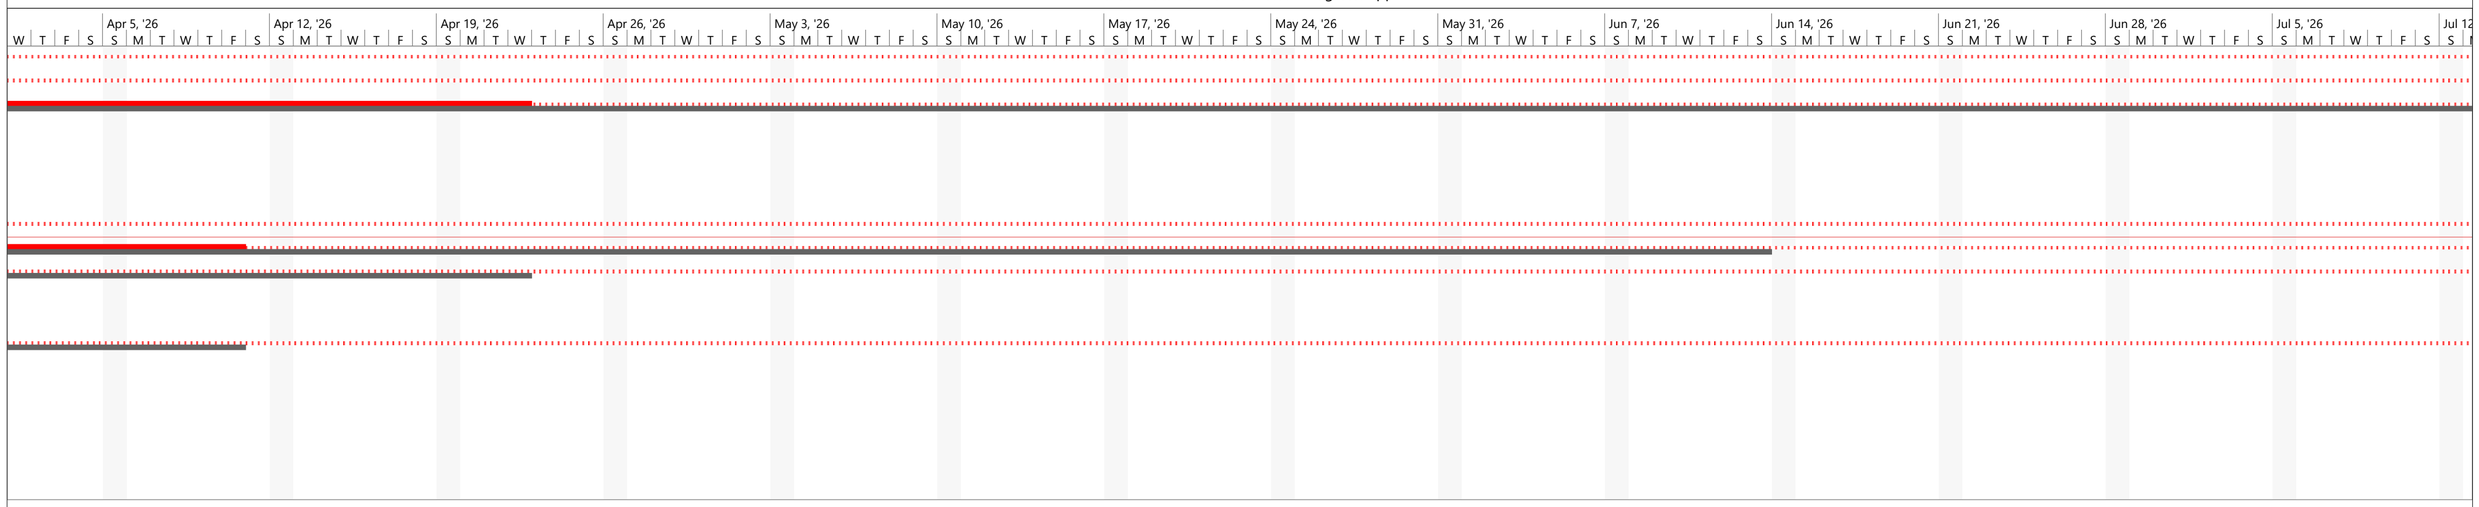

VIEW GUIDE
Critical tasks control forecast.

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

CURRENT CRITICAL PATH | Critical-filtered current programme; activities shown control forecast finish.

Michael_Futol_Chinaimo_Actual_Progress.mpp

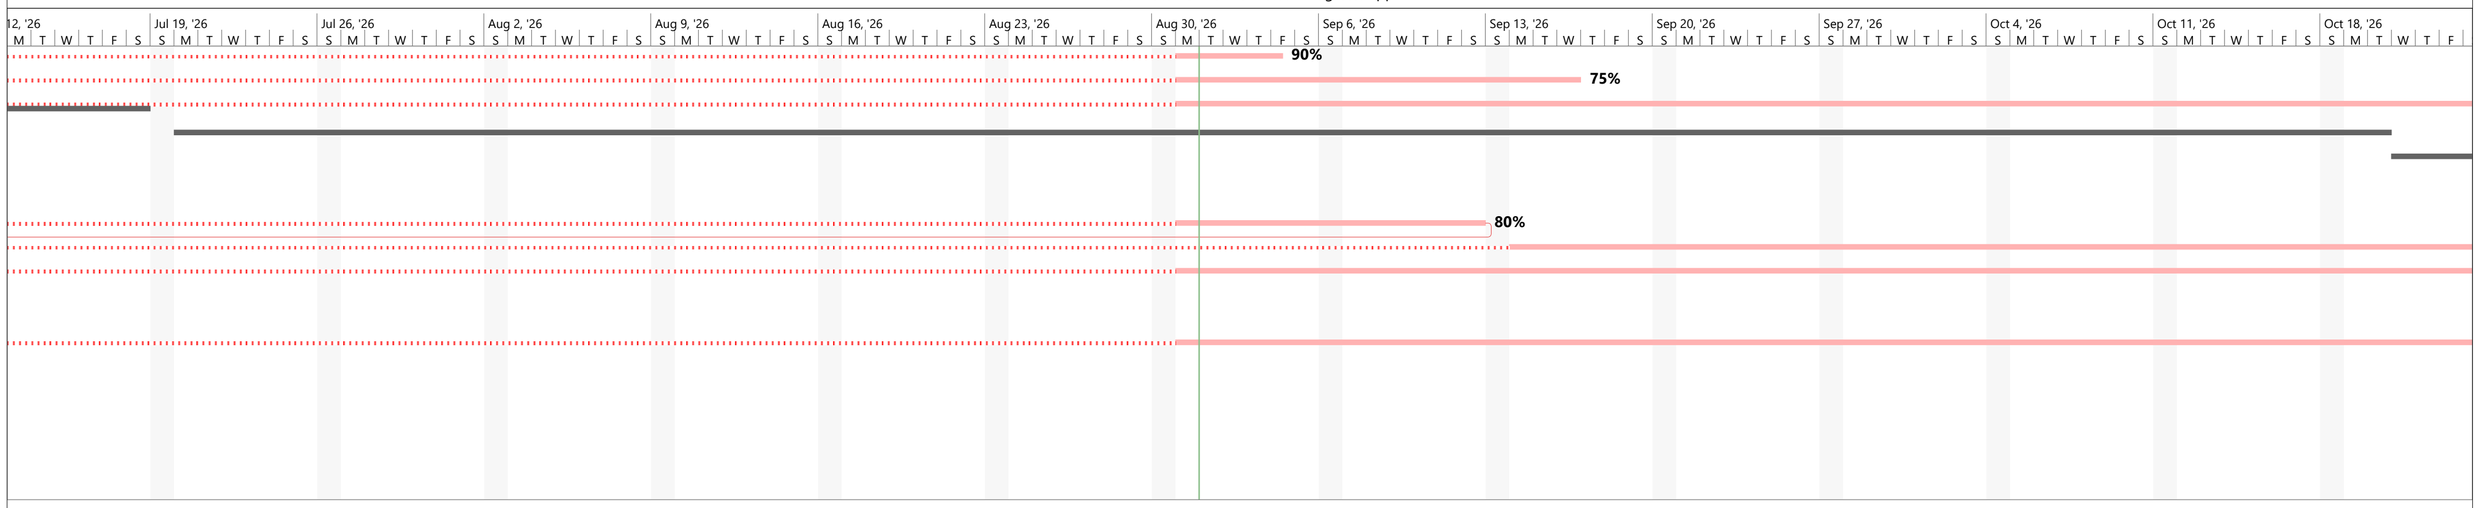

VIEW GUIDE
Critical tasks control forecast.

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

CURRENT CRITICAL PATH | Critical-filtered current programme; activities shown control forecast finish.

Michael_Futol_Chinaimo_Actual_Progress.mpp

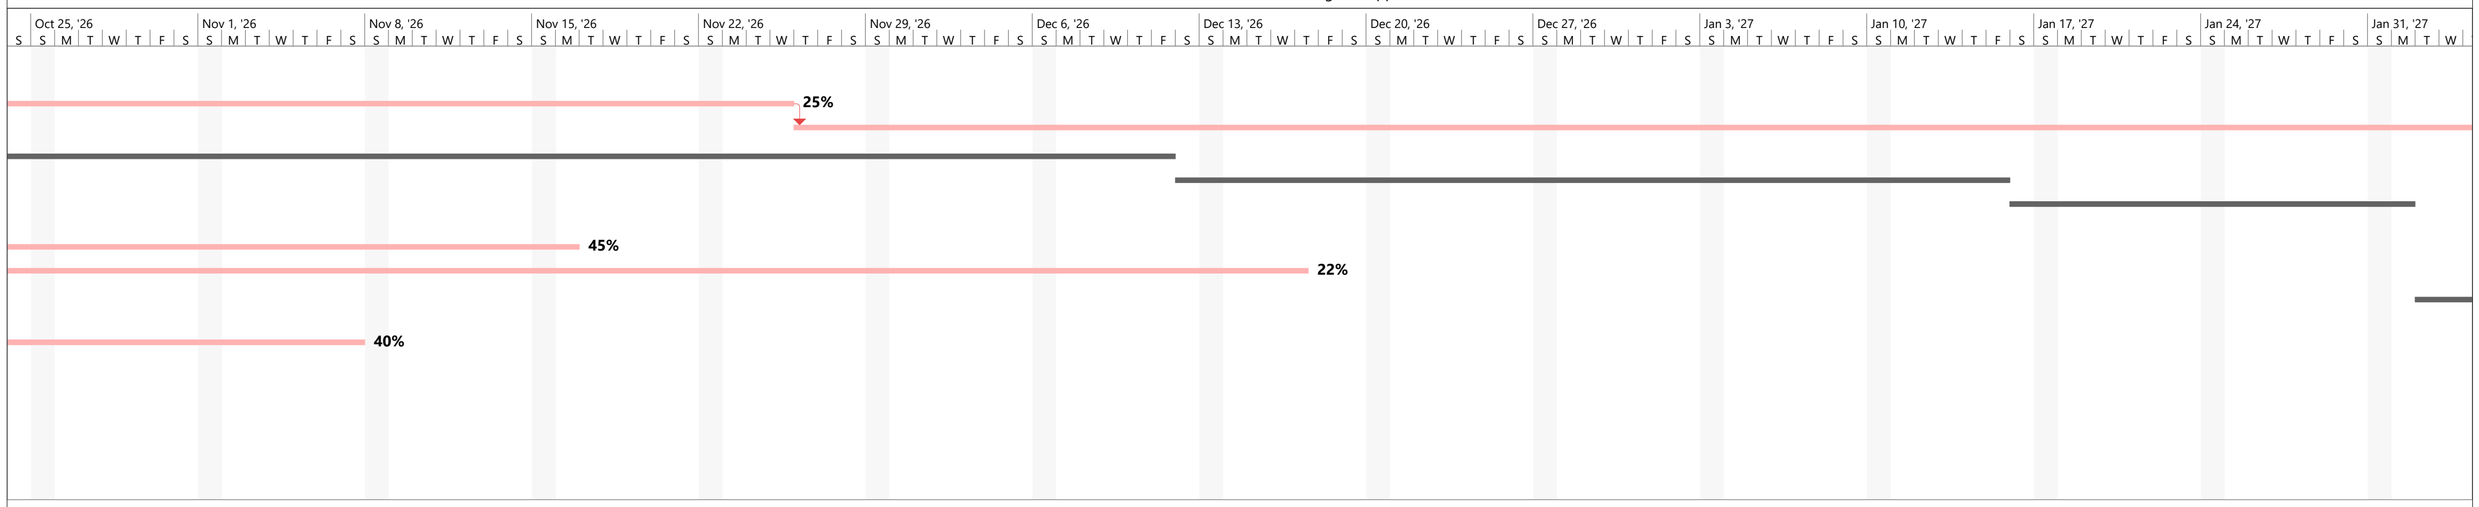

VIEW GUIDE
Critical tasks control forecast.

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

CURRENT CRITICAL PATH | Critical-filtered current programme; activities shown control forecast finish.

Michael_Futol_Chinaimo_Actual_Progress.mpp

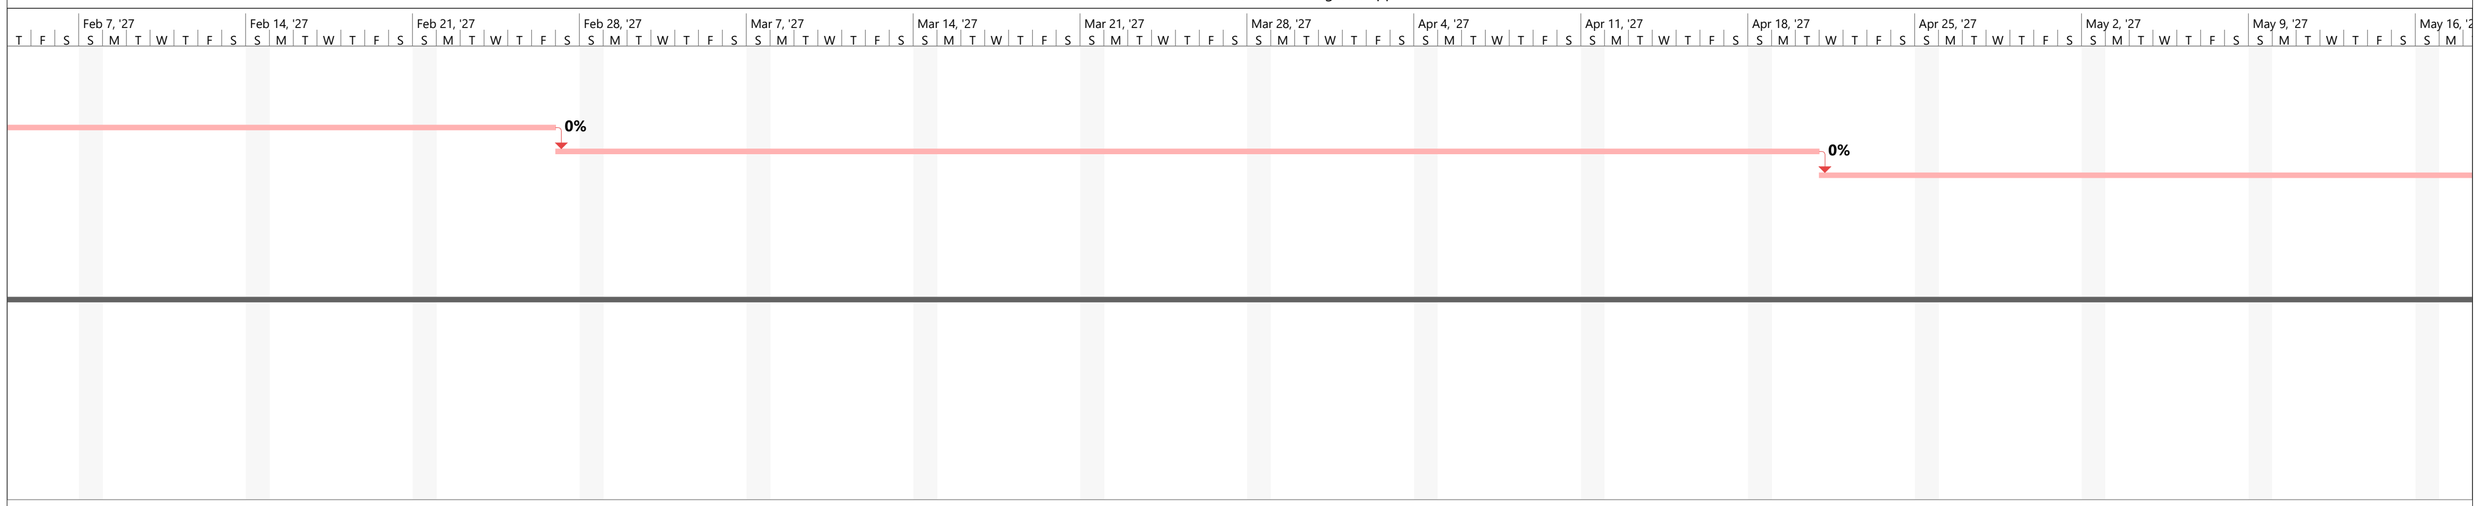

VIEW GUIDE
Critical tasks control forecast.

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

CURRENT CRITICAL PATH | Critical-filtered current programme; activities shown control forecast finish.

Michael_Futol_Chinaimo_Actual_Progress.mpp

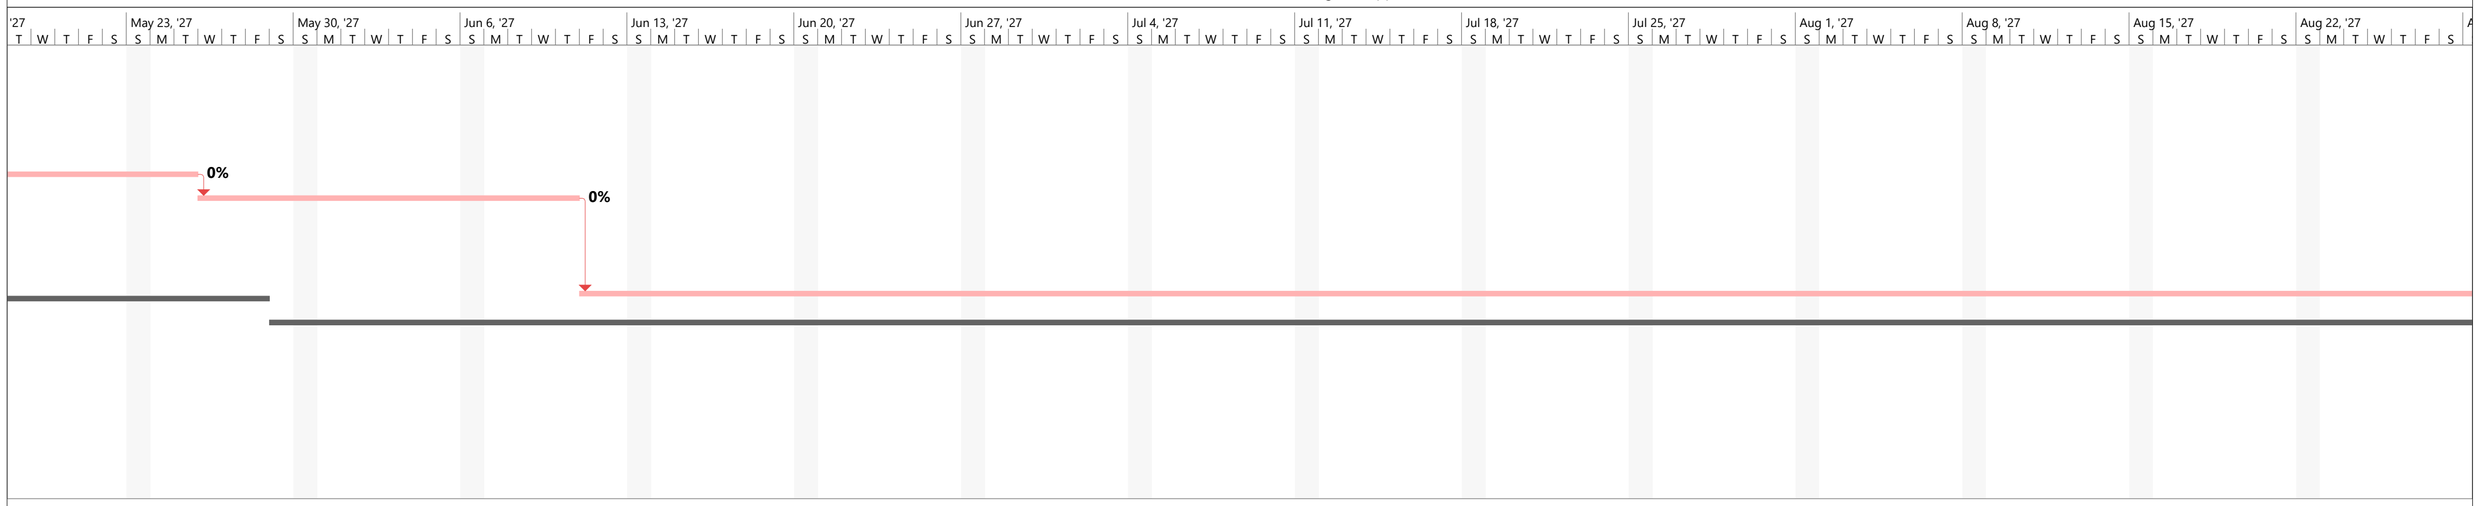

VIEW GUIDE
Critical tasks control forecast.

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

CURRENT CRITICAL PATH | Critical-filtered current programme; activities shown control forecast finish.

Michael_Futol_Chinaimo_Actual_Progress.mpp

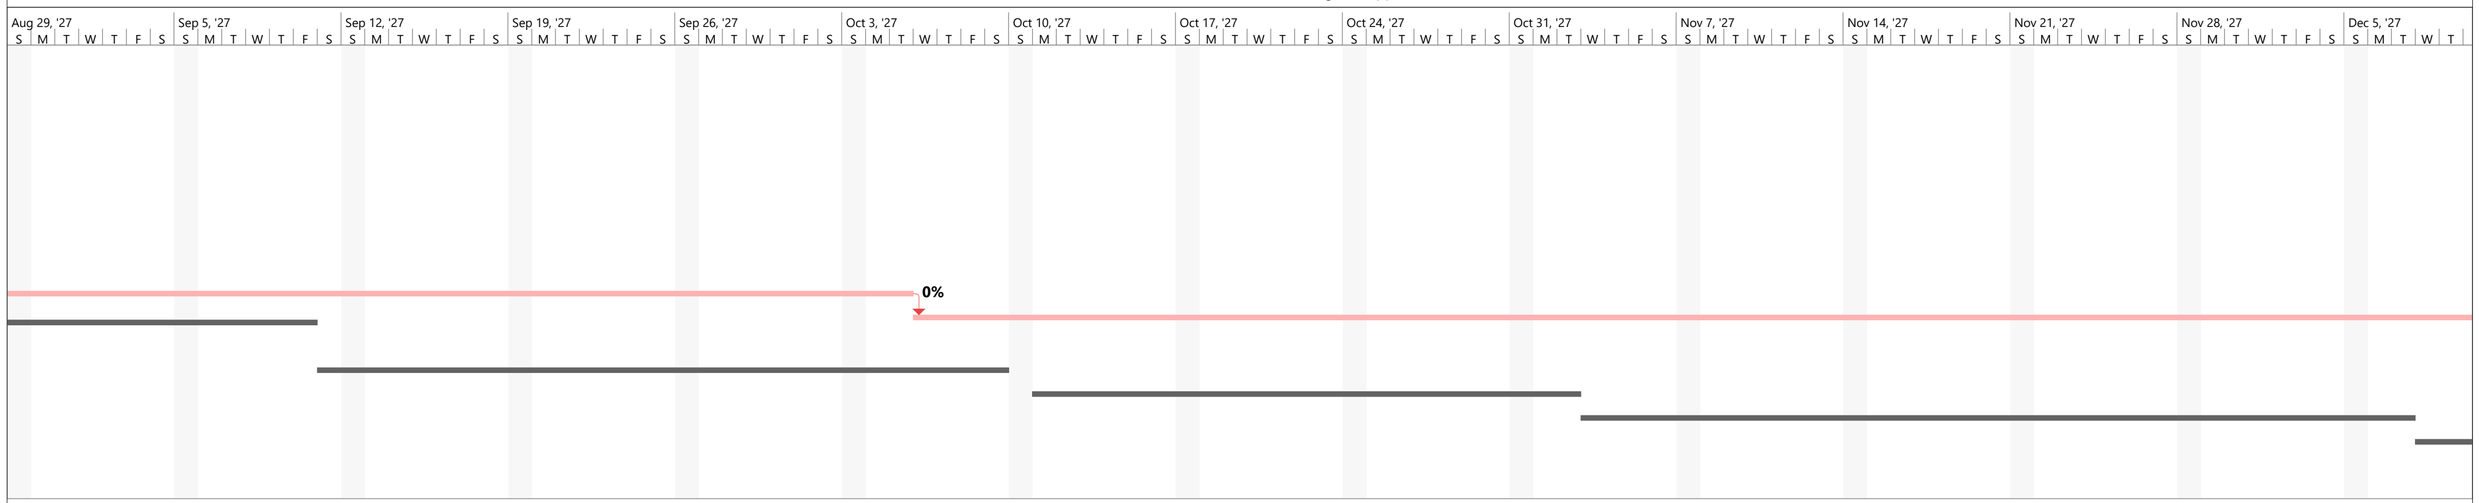

VIEW GUIDE
Critical tasks control forecast.

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

CURRENT CRITICAL PATH | Critical-filtered current programme; activities shown control forecast finish.

Michael_Futol_Chinaimo_Actual_Progress.mpp

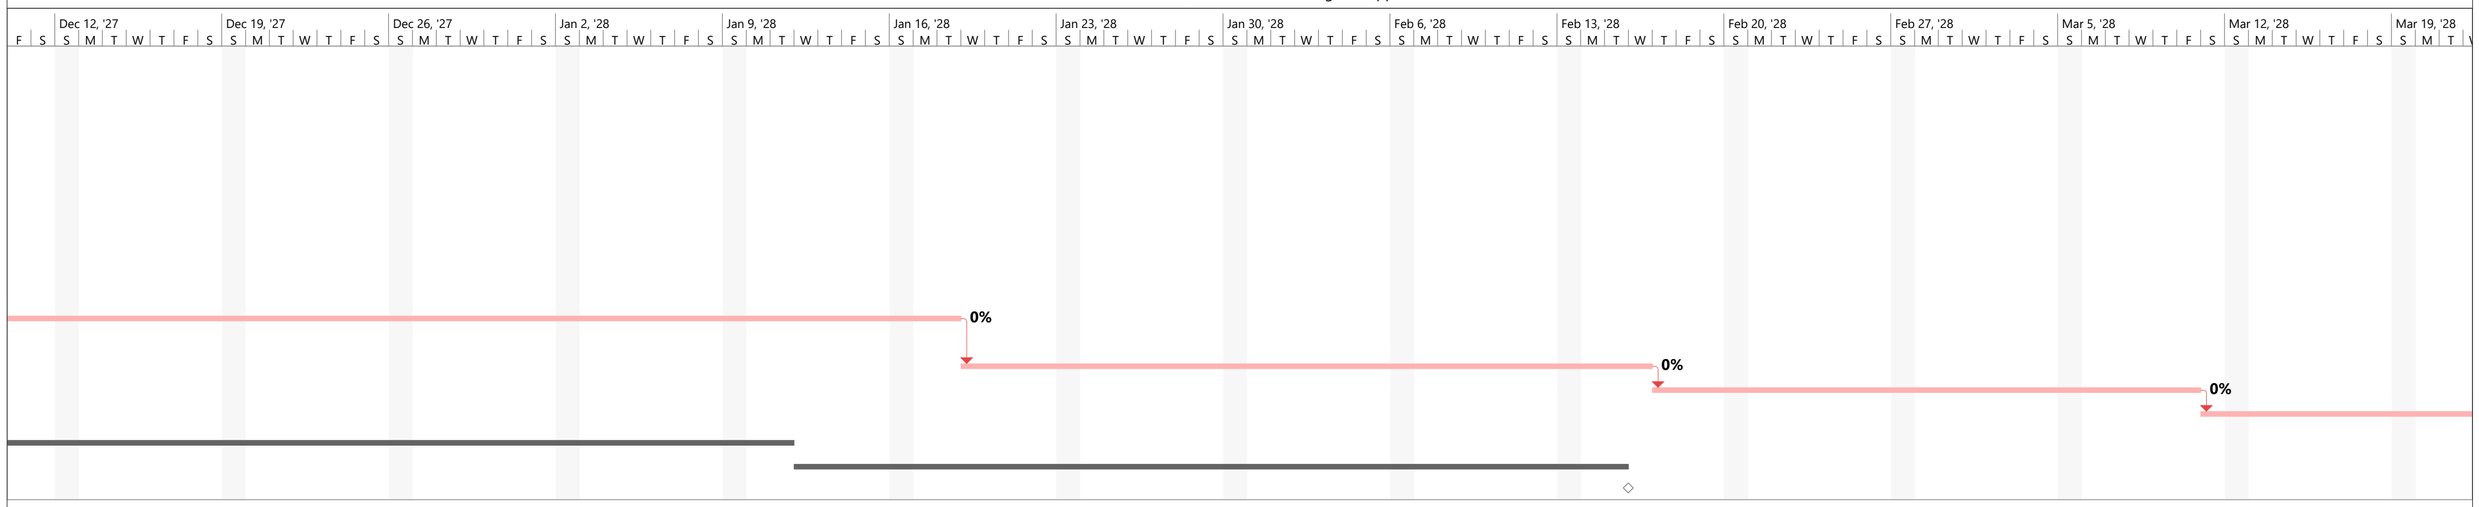

VIEW GUIDE
Critical tasks control forecast.

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	

CURRENT CRITICAL PATH | Critical-filtered current programme; activities shown control forecast finish.

Michael_Futol_Chinaimo_Actual_Progress.mpp

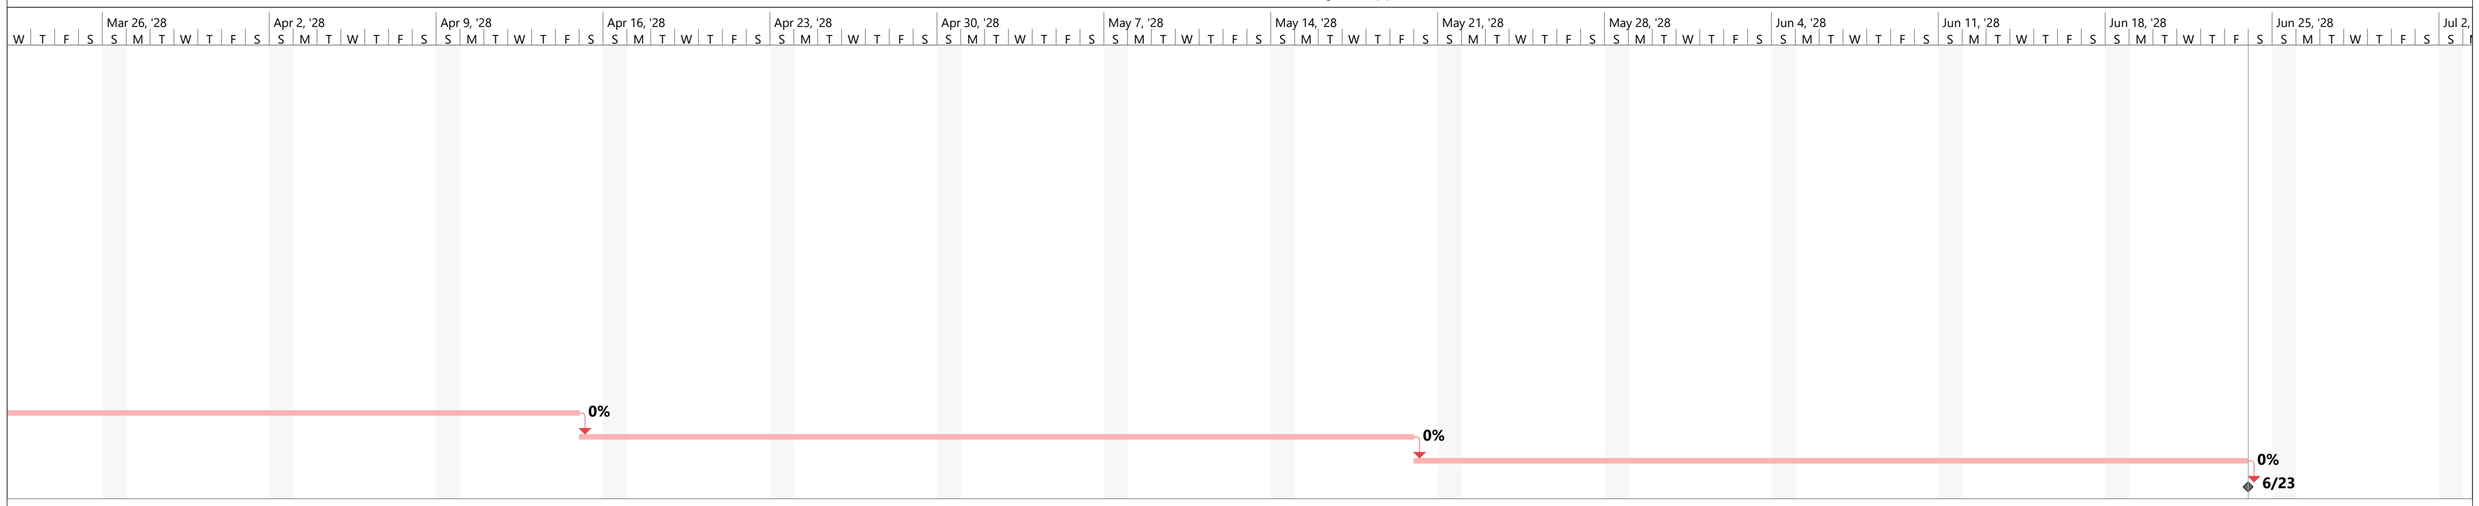

VIEW GUIDE
Critical tasks control forecast.

Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	
